



489th —————

Flash Report on Central Sector Infrastructure Projects —————



Scan the QR code to access
the PAIMANA Portal.

**(₹150 crore
& above)**

JULY 2026

<https://paimana.mospi.gov.in> @GoIStats f /GoIStats in GoIStats Ministry of Statistics & PI



CONTENTS

I. Overview*	2-4
II. North Eastern Region	5-6
III. As per Harmonized Master List (HML) 2022	7-13
IV. Major Infrastructure Central Ministries & Departments	14-19
V. Appendix : <i>List of Tables</i>	20 onwards
Table 1: Ministry-wise Ongoing Projects	
Table 2: State-wise Ongoing Projects	
Table 3: Completed Projects	
Table 4: Newly Added Projects	
Table 5: Ongoing Projects of North Eastern Region	
Table 6: All Ongoing Projects	

*Note: This report is web-generated from the PAIMANA portal (<https://paimana-proj.mospi.gov.in>) as of July 2026, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies on the CRIP portal (<https://paimana-crip.mospi.gov.in>) latest by 21st August 2026.





Overview





Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above

JULY 2026

1775 | 17

Ongoing Projects |
Line Ministries & Departments

₹ 33,70,138

Original Cost
(crores)

₹ 37,10,642

Revised Cost
(crores)

₹ 19,26,100

(51.91% of Revised Cost)
Cumulative Expenditure
(crores)

25


Commissioned during month

36

Newly Added during month


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

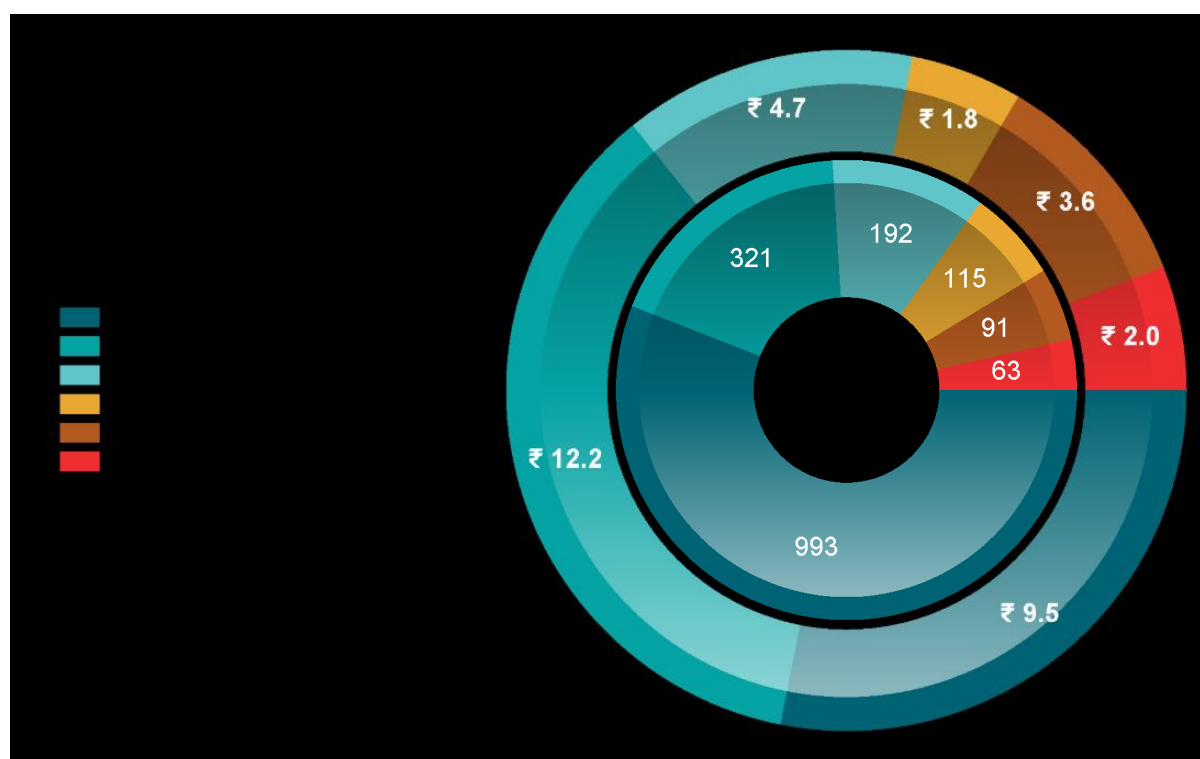


Ministry Comparison : Major Ministries*


[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

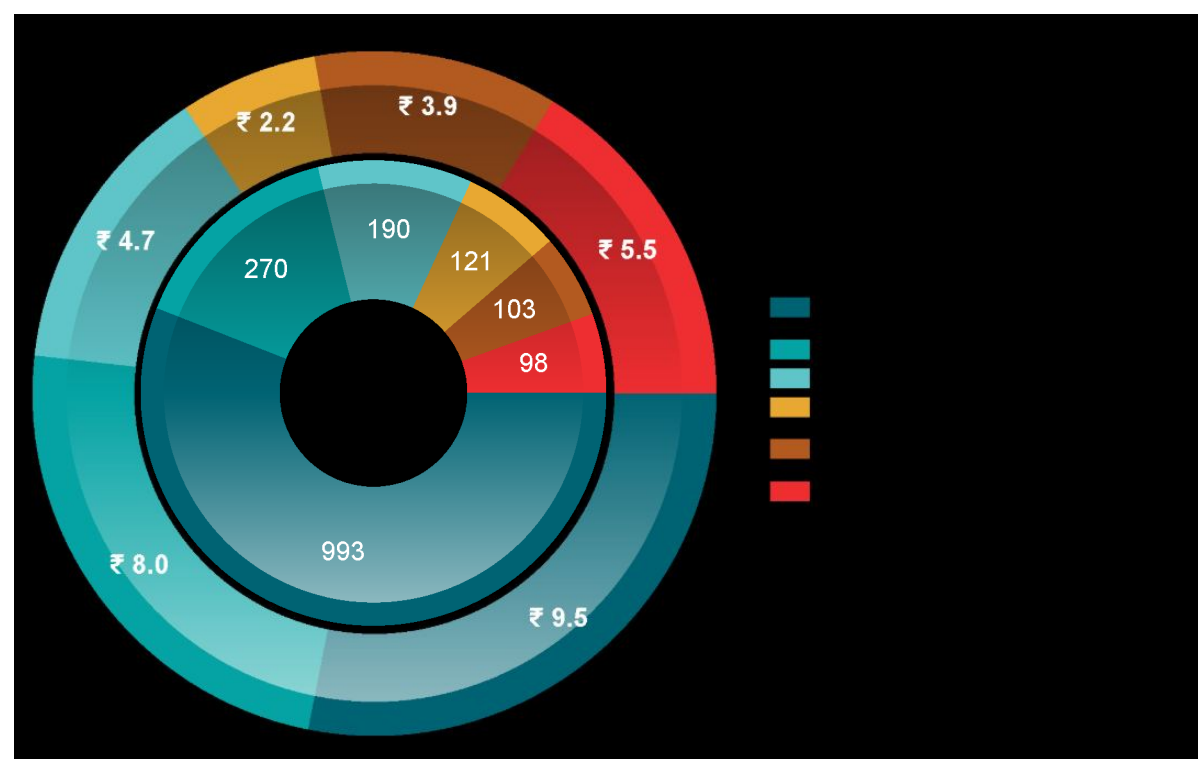

Cost Analytics : Major Sectors*

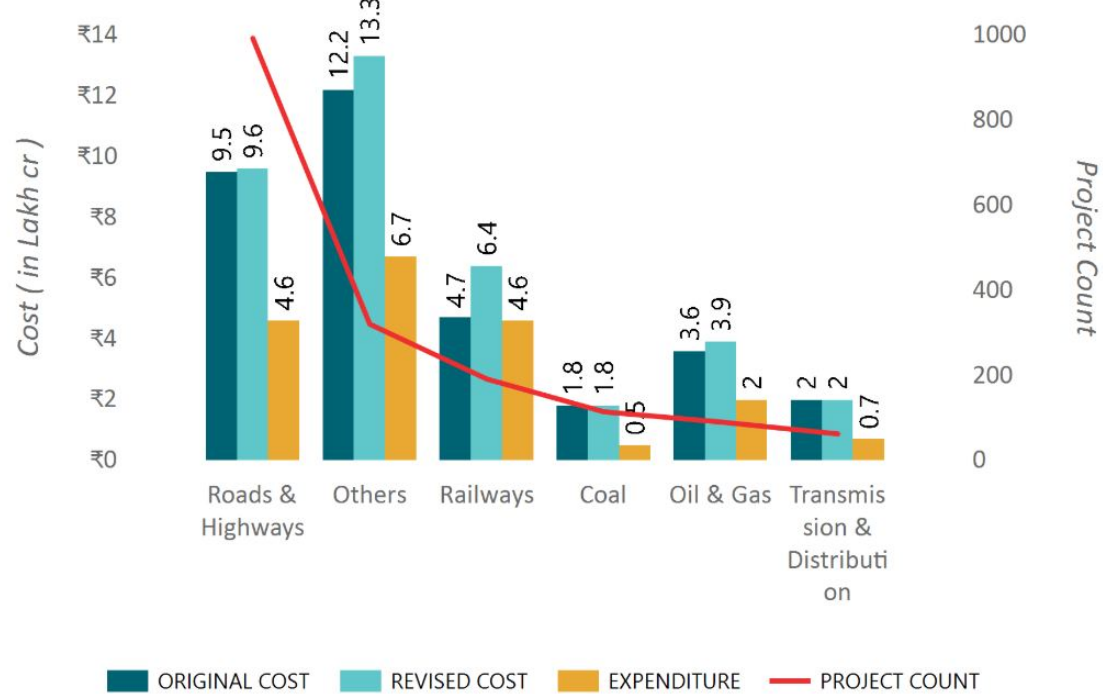


Cost Analytics : Major Ministries*

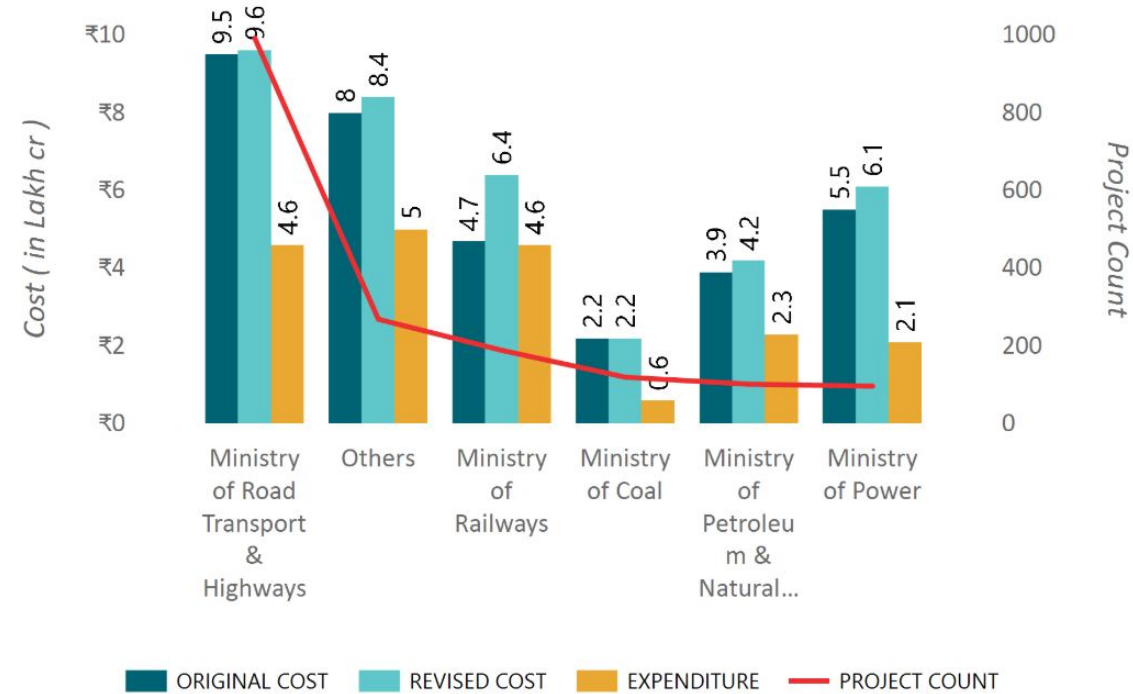


Note: * as per Project Count

Analytics: as per HML

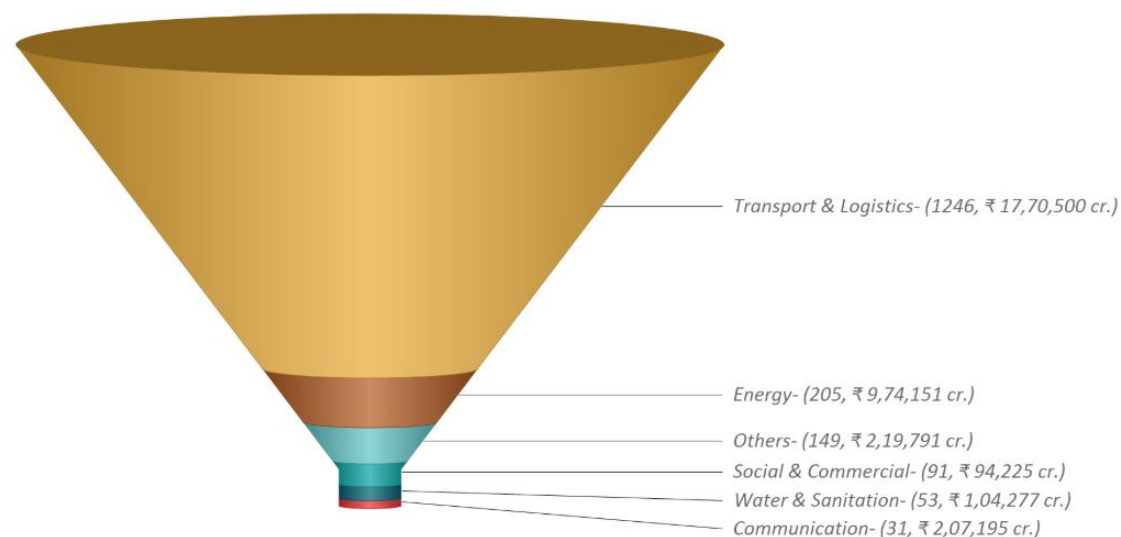


Note: all indicated legends are in format (Project count, Original Cost in crores)

Cumulative Physical & Financial progress (%) : Project count

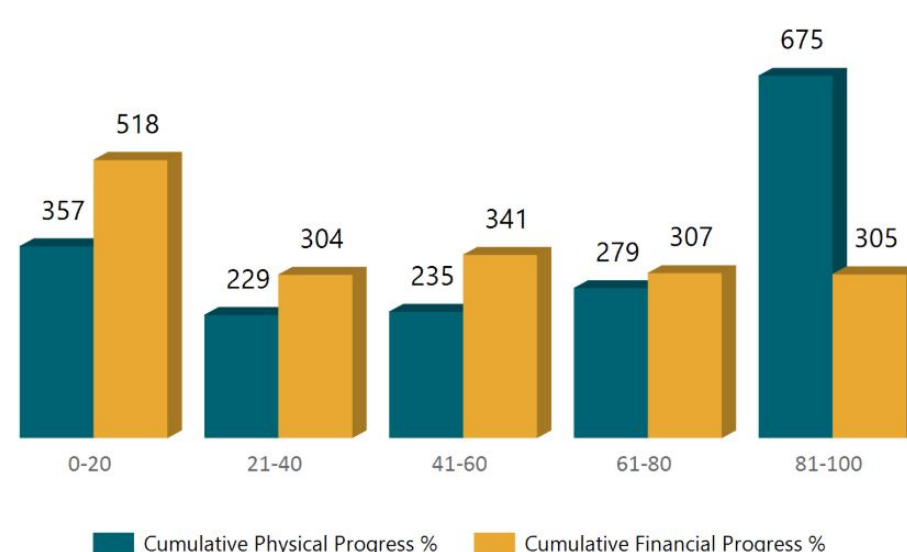




State Comparison : Major States*

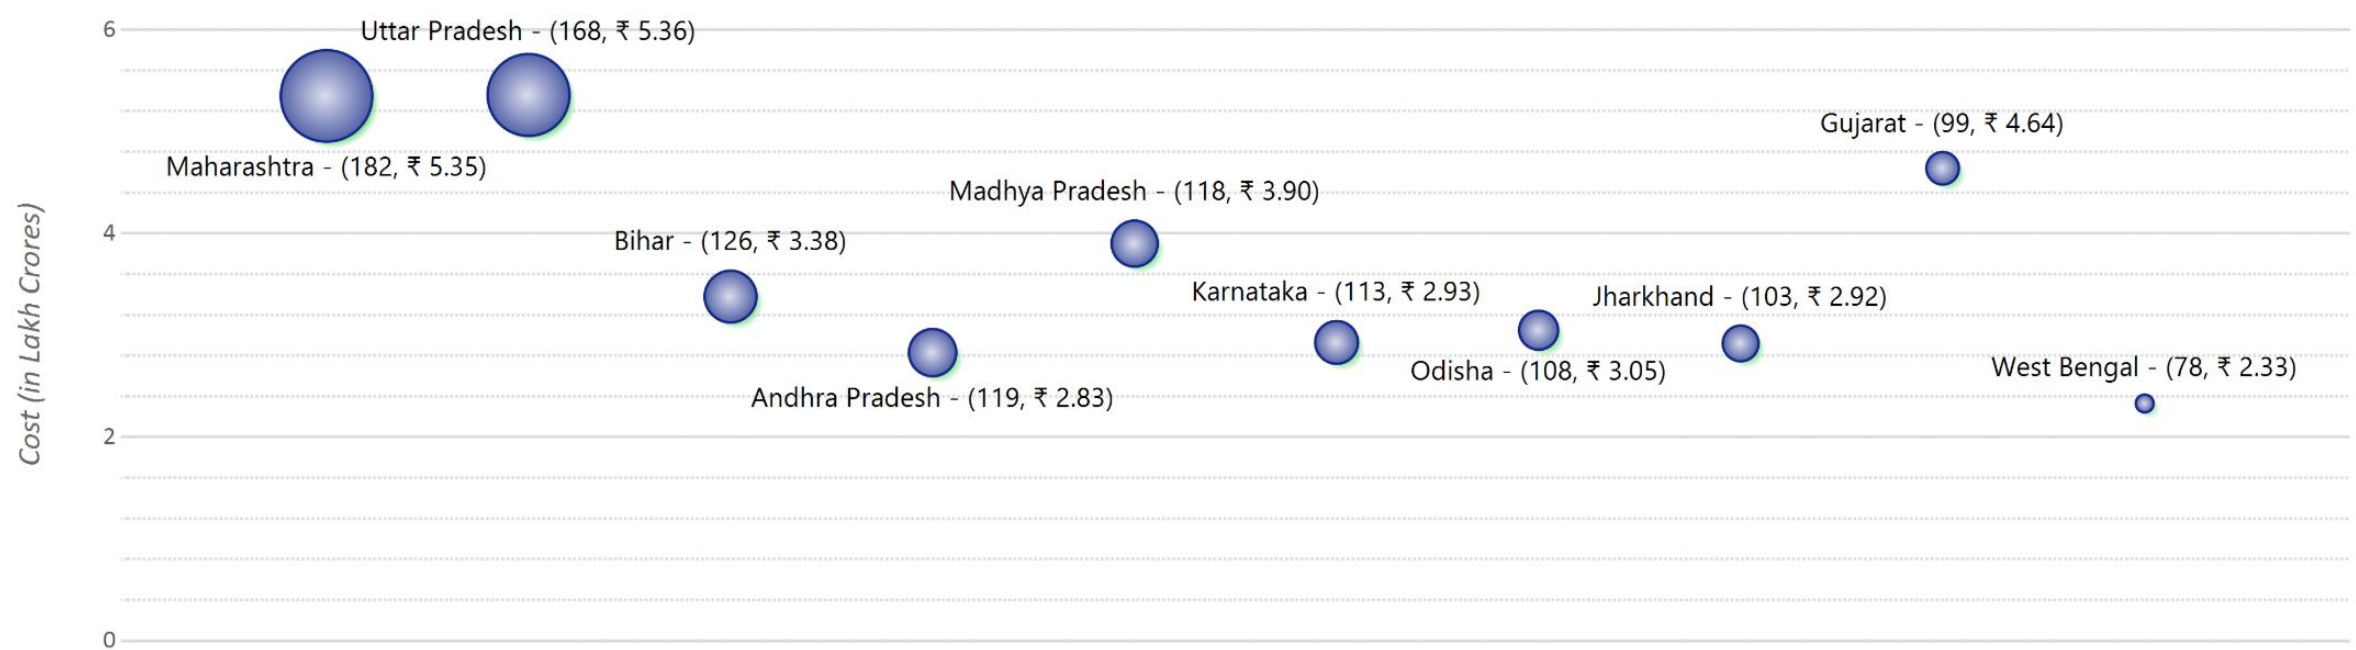

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count

Ministry-wise Distribution of total 675 projects with reported Physical Progress between 81-100%

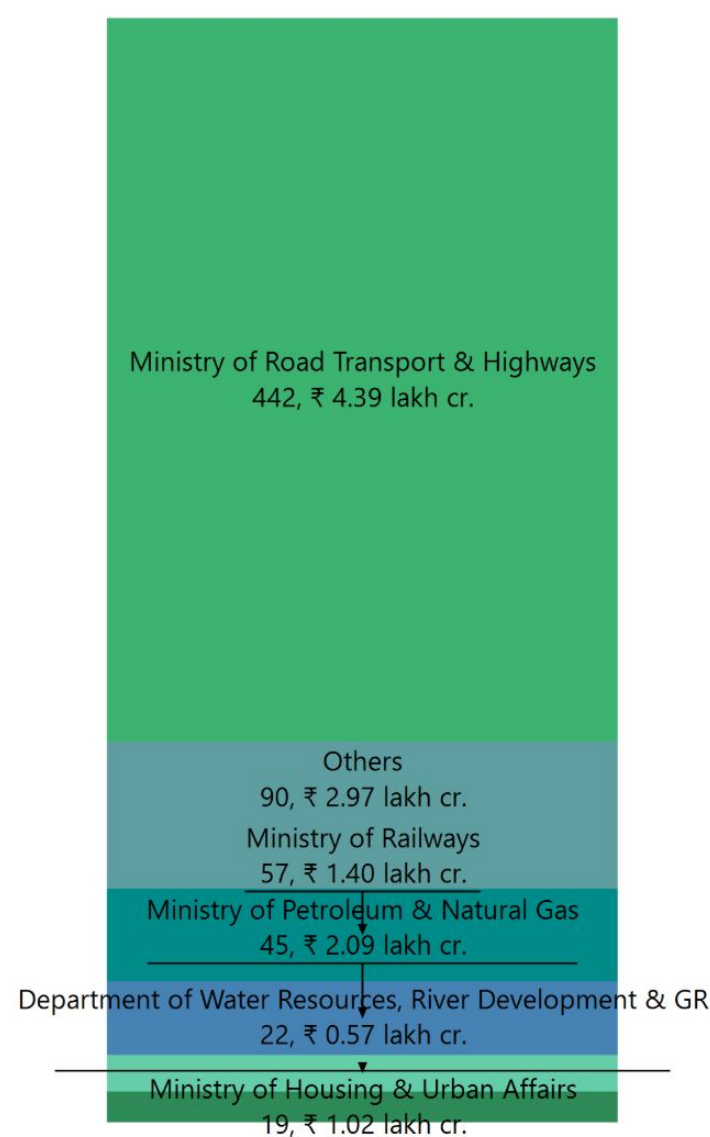

Total Ongoing Projects: Mega & Major




Total North East Region Ongoing Projects: Mega & Major



Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost $\geq$ 1000 crore
* Major project if having original cost $<$ 1000 crore

Project volume (nos.)

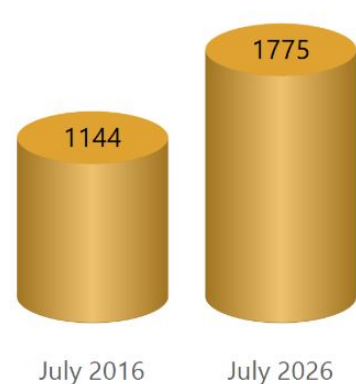

Change in Project Count : +55%

Total Project value (in lakh crore)



Change in Total Value : +143%

Cumulative Expenditure (in lakh crore)



Change in Expenditure : +218%



North Eastern Region





Special Focus : North Eastern Region

JULY 2026

211 | 11

Ongoing Projects |
Line Ministries & Departments

₹ 3,65,682

Original Cost
(crores)

₹ 3,68,586

Revised Cost
(crores)

₹ 2,51,885

(68.34% of Revised Cost)
Cumulative Expenditure
(crores)

3


Commissioned during month

6


Newly Added during month

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

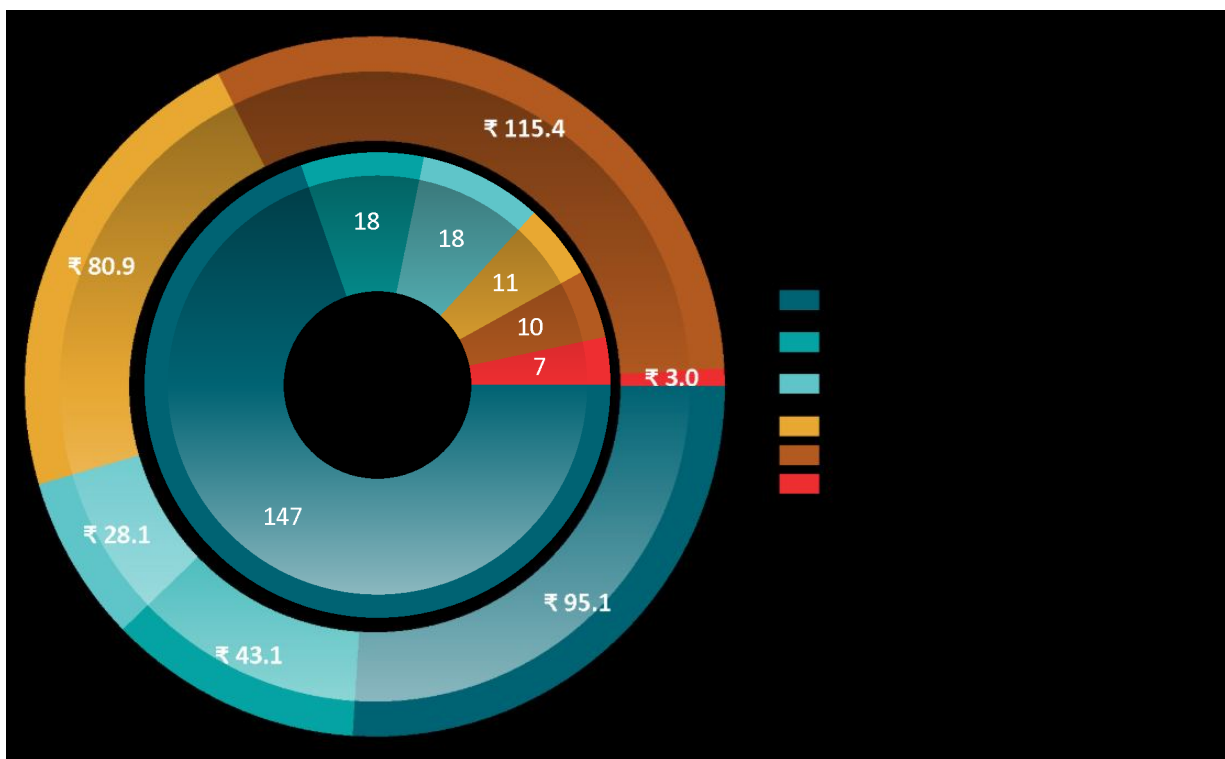


Cost Analytics : Major Ministries*

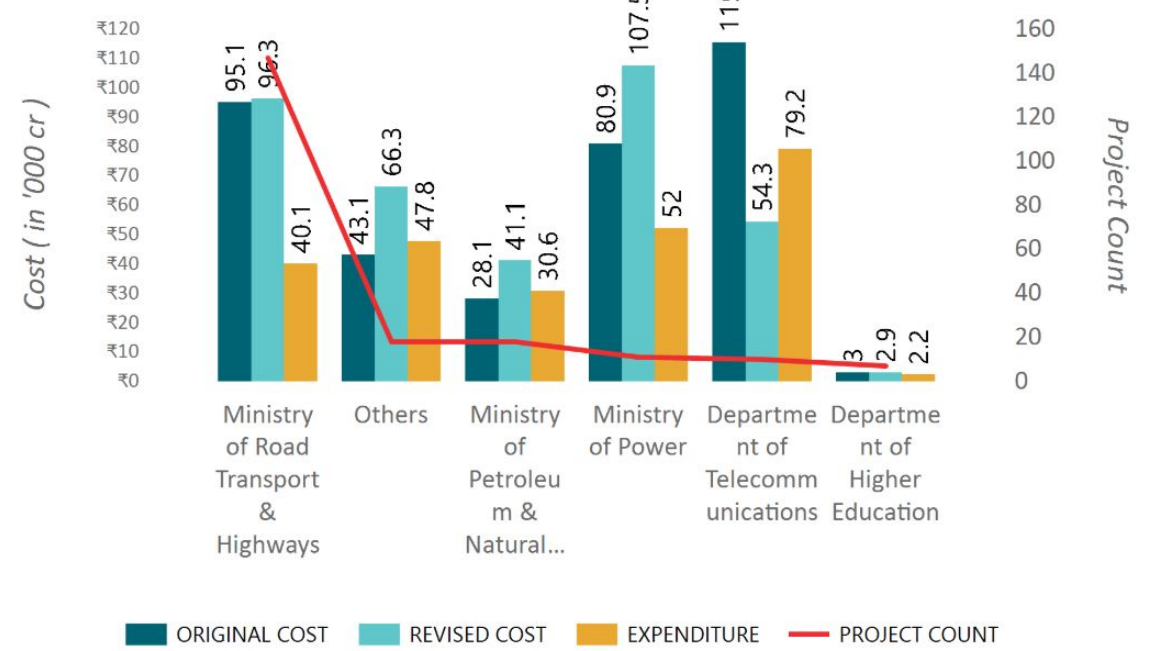


Note: * as per Project Count

Analytics: as per HML

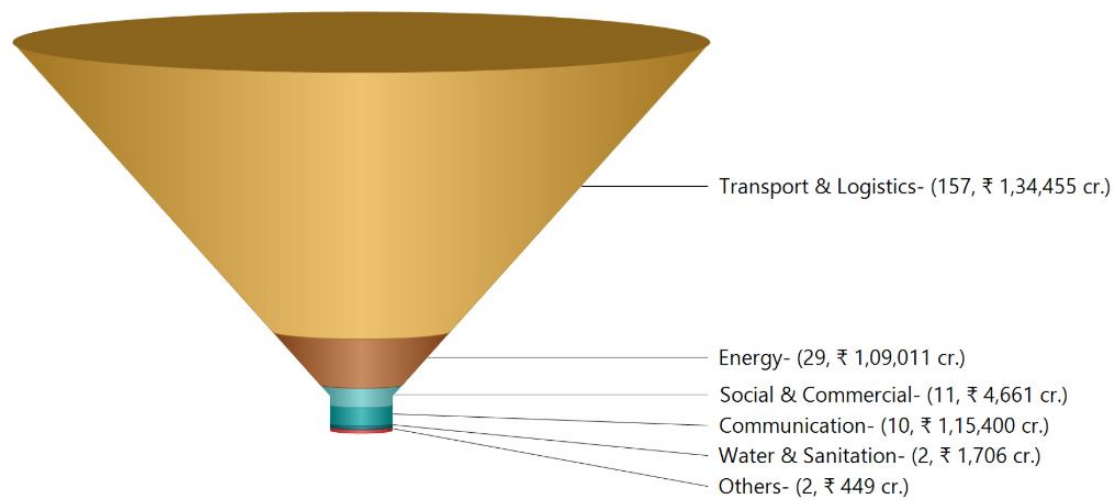


Note: all indicated legends are in format (Project count, Original Cost in crores)

Cumulative Physical & Financial progress (%) : Project count

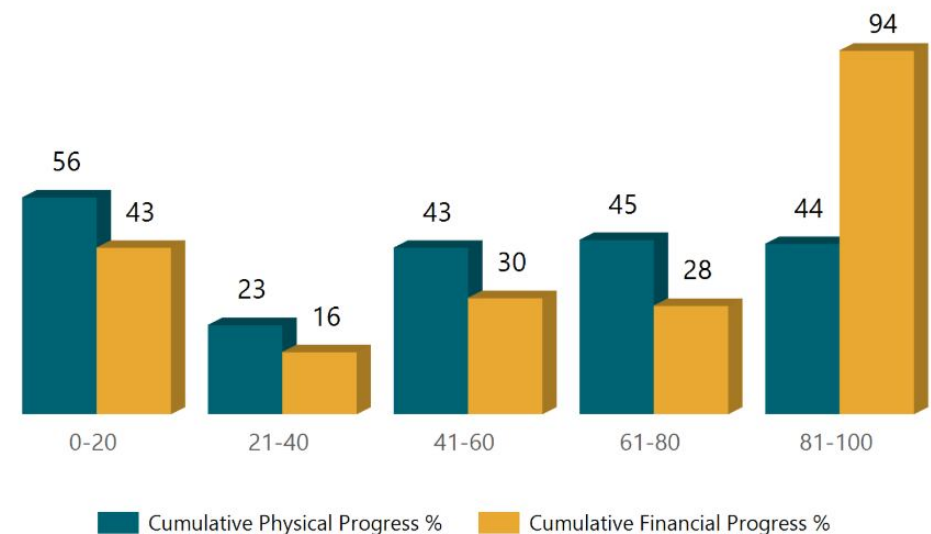

State Comparison : All States

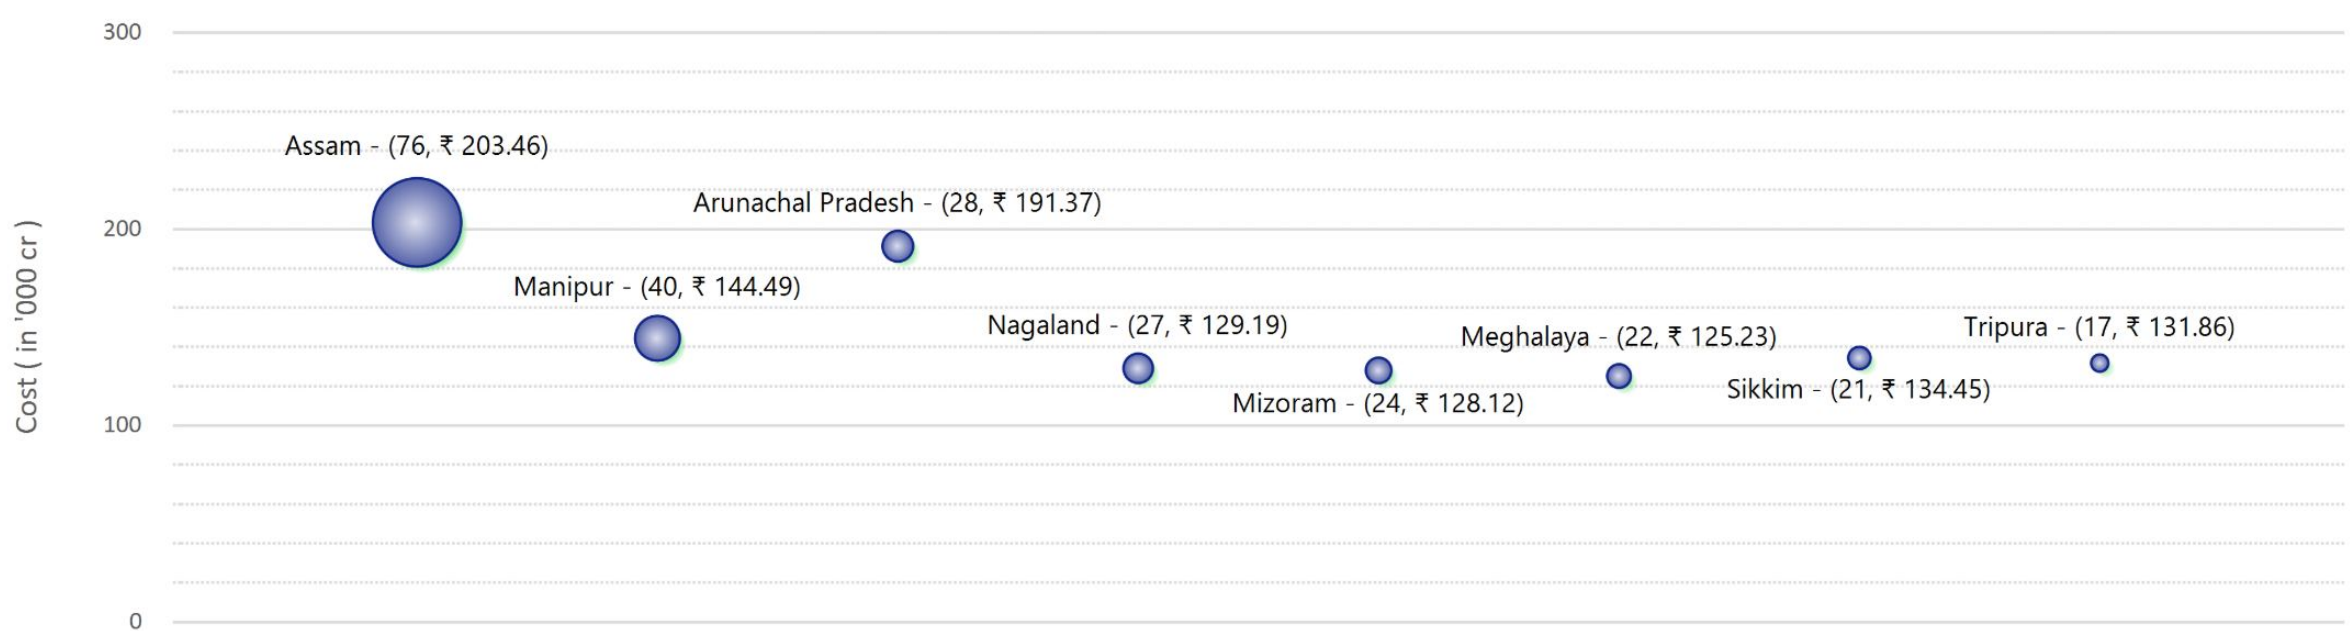

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022



HML Category 1 : Transport & Logistics

JULY 2026

1246
Ongoing Projects

₹ 17,70,500
Original Cost
(crores)


₹ 19,80,875
Revised Cost
(crores)

₹ 11,22,590
(56.67% of Revised Cost)
Cumulative Expenditure
(crores)


20
Commissioned during month

7
Newly Added during month

Cost Analytics : All Sectors

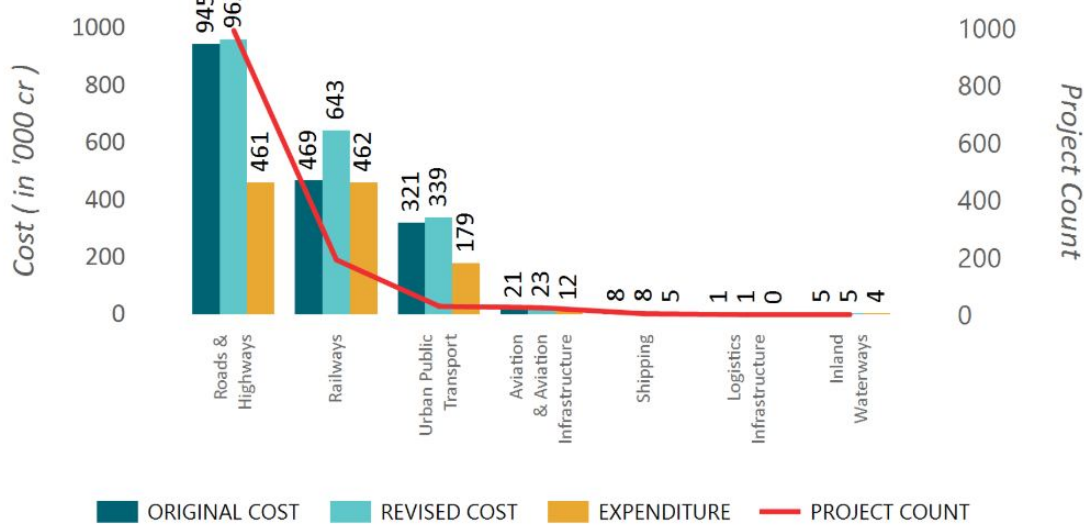

Cumulative Physical & Financial progress (%) : Project count

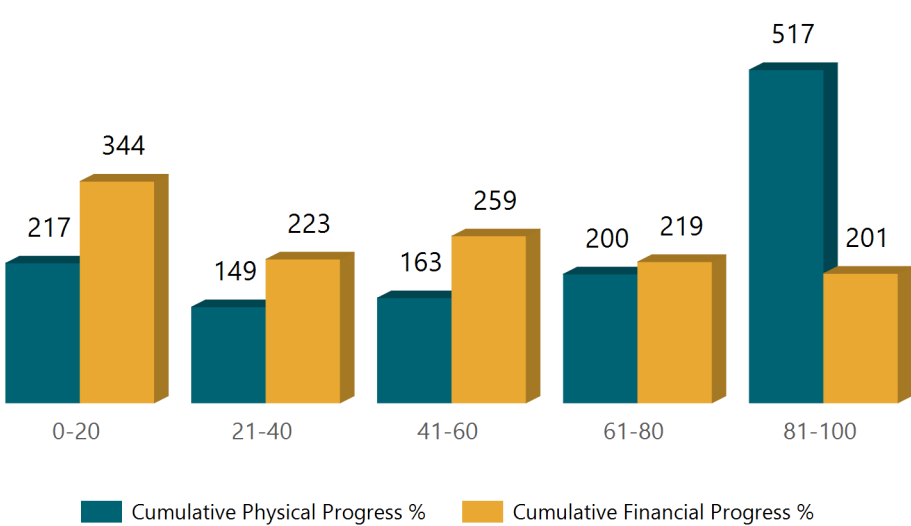

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Roads & Highways	993	945,371	961,717	460,545
2	Railways	192	469,207	643,473	461,968
3	Urban Public Transport	30	320,872	339,476	178,627
4	Aviation & Aviation Infrastructure	25	21,345	22,772	11,586
5	Shipping	4	7,573	7,613	5,246
6	Logistics Infrastructure	1	763	763	430
7	Inland Waterways	1	5,369	5,061	4,187

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	90,967	62.16
2	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		34,698	55.73
3	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
4	702635	CONSTRUCTION OF BANGALORE METRO RAIL PROJECT PHASE 2.	26,405	30,695	29,835	95.8
5	702632	DMRTS PHASE - IV [3 PRIORITY CORRIDORS]	24,949		21,421	83.46

HML Category 2 : Energy

JULY 2026

205
Ongoing Projects



₹ 9,74,151
Original Cost
(crores)

₹ 10,66,148
Revised Cost
(crores)

₹ 4,43,416
(41.59% of Revised Cost)
Cumulative Expenditure
(crores)

3
Commissioned during month

1
Newly Added during month

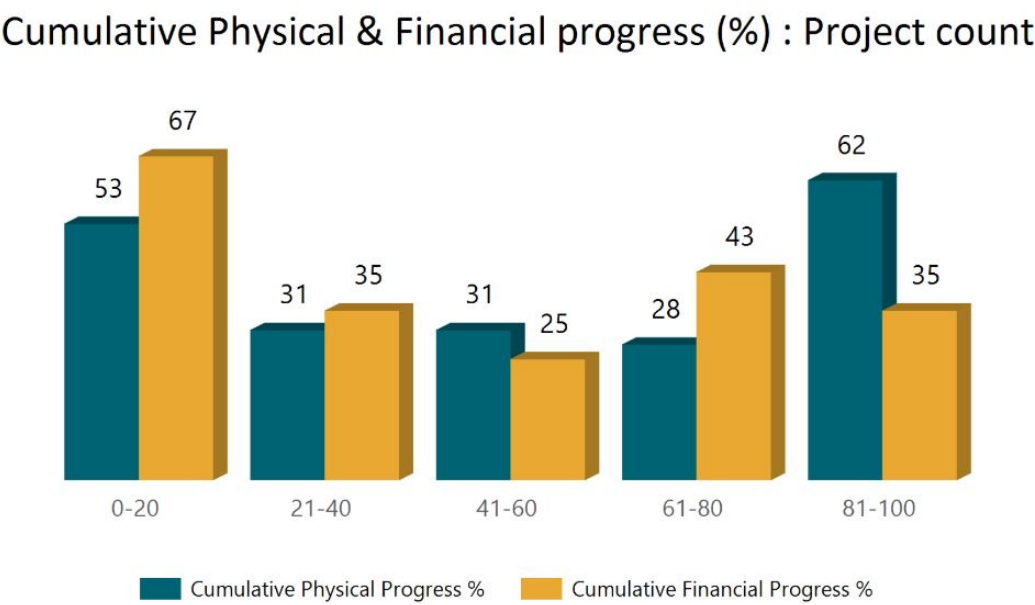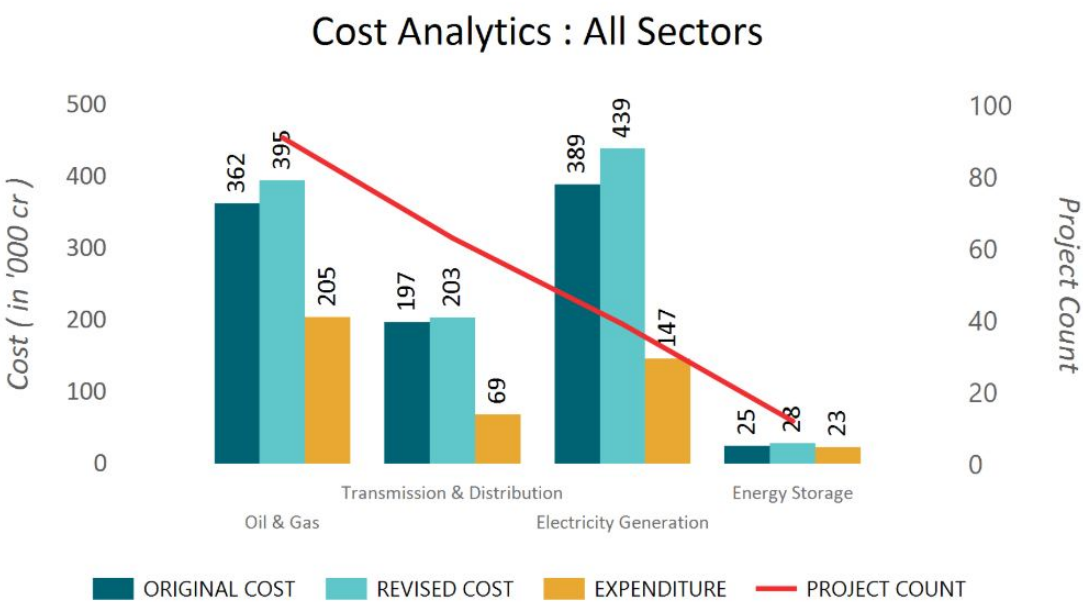

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	91	362,394	394,917	204,671
2	Transmission & Distribution	63	197,391	203,354	68,897
3	Electricity Generation	39	389,214	439,436	146,800
4	Energy Storage	12	25,152	28,441	23,049

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	6,104	33.5
2	298178	MEJA THERMAL POWER PROJECT, STAGE-II , (3X800 MW)	38,358		1,003	0.02
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	28,007	94.3
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,192	96.9
5	602182	DIBANG MULTIPURPOSE PROJECT	31,876		4,921	17.93



HML Category 3 : Water & Sanitation

JULY 2026

53

Ongoing Projects

₹ 1,04,277

Original Cost
(crores)

₹ 2,04,999

Revised Cost
(crores)

₹ 1,45,099

(70.78% of Revised Cost)
Cumulative Expenditure
(crores)


2

Commissioned during month


0

Newly Added during month

Cost Analytics : All Sectors

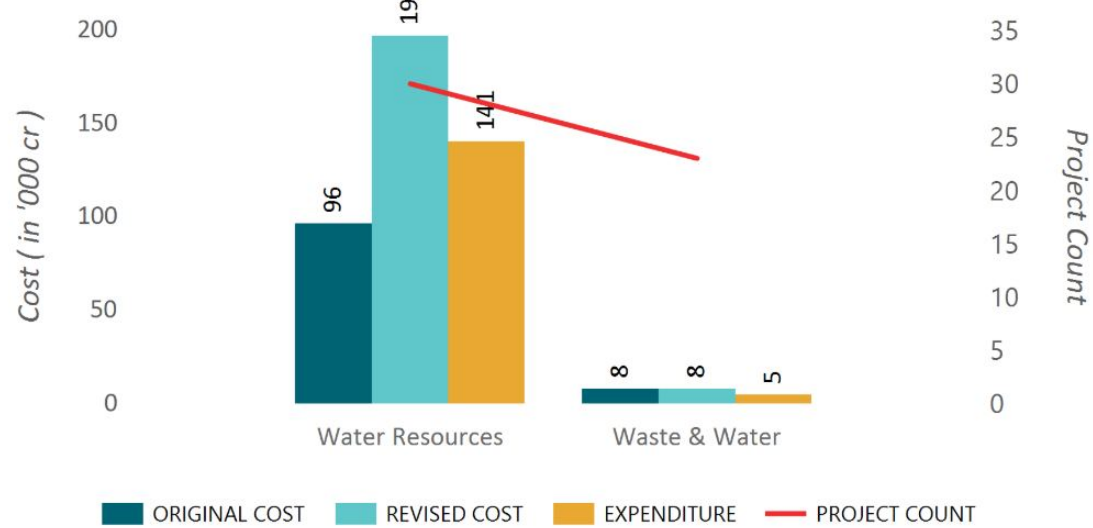

Cumulative Physical & Financial progress (%) : Project count

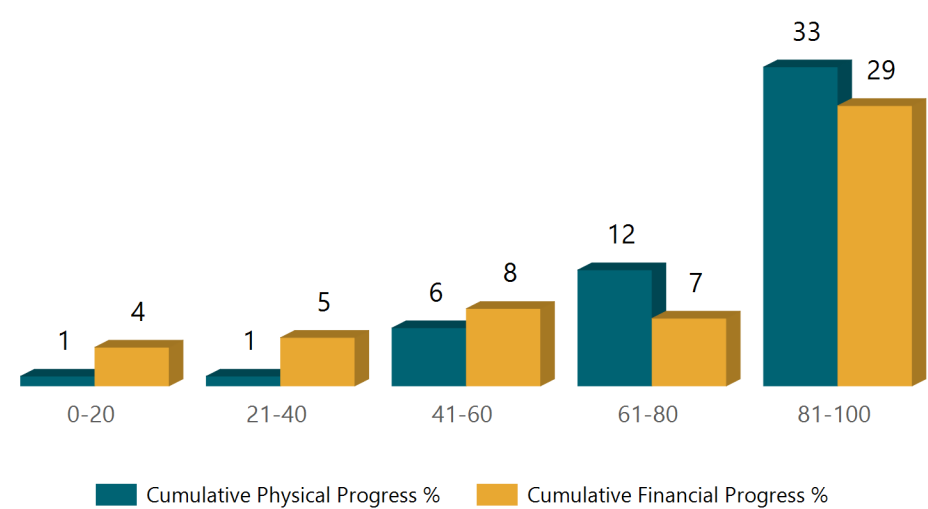

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	30	96,487	197,110	140,511
2	Waste & Water	23	7,790	7,889	4,588

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701530	KEN-BETWA LINKING DEVELOPMENT PROJECT	21,030		8,531	0
2	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,969	93.7
3	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	27,962	86.15
4	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,841	87.7
5	701386	GOSIKHURD PROJECT	7,196	12,770	14,439	72.65



HML Category 4 : Communication

JULY 2026

31
Ongoing Projects

₹ 2,07,195
Original Cost
(crores)


₹ 1,33,825
Revised Cost
(crores)

₹ 1,02,879
(76.88% of Revised Cost)
Cumulative Expenditure
(crores)


0
Commissioned during month

16
Newly Added during month

Cost Analytics : All Sectors

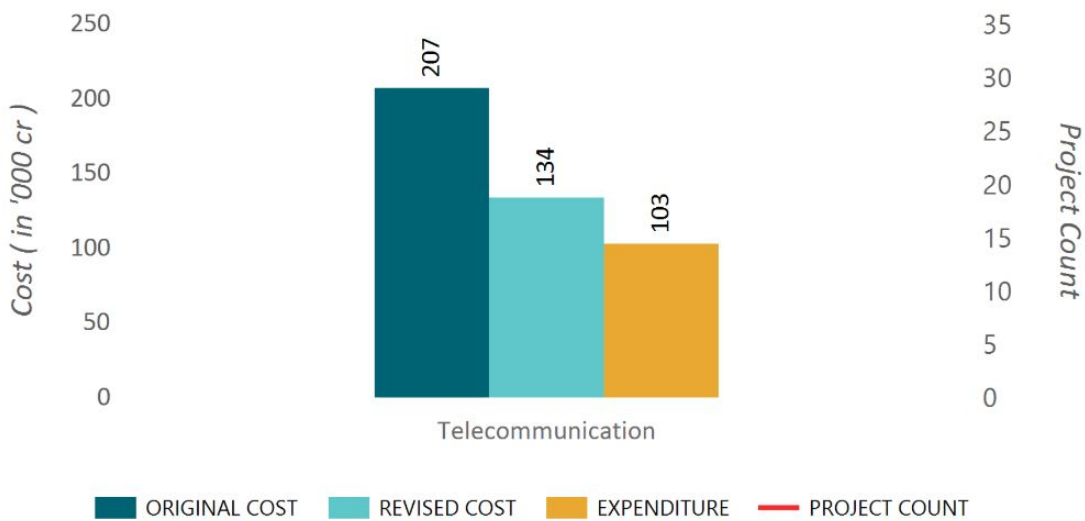

Cumulative Physical & Financial progress (%) : Project count

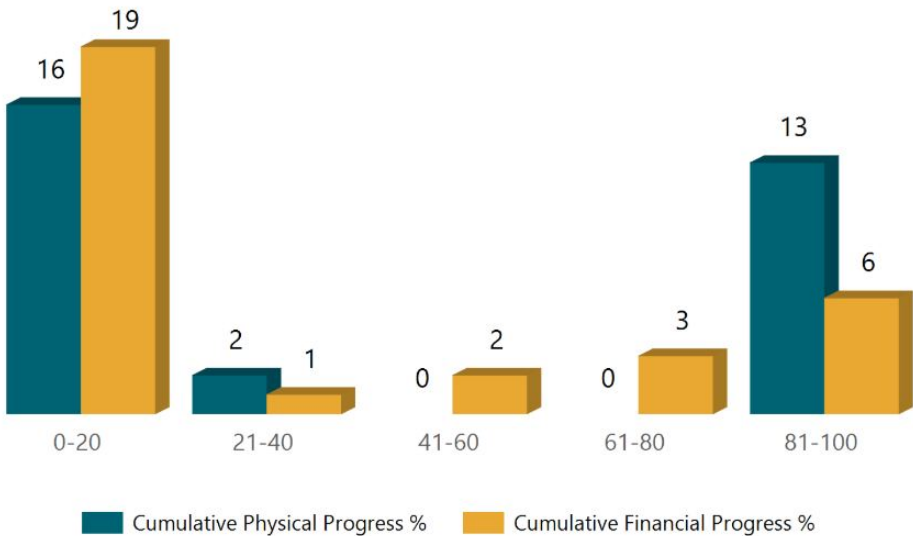

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	31	207,195	133,825	102,879

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	706775	BHARATNET	61,109	12,709	48,810	99.98
2	701593	4G SERVICES BY BSNL	28,466	19,592	9,165	98.56
3	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	15,393	8,723	87.7
4	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		9,166	98.56
5	547243	BHARATNET PHASE-II	22,175		20,692	93.33



HML Category 5 : Social & Commercial

JULY 2026

91

Ongoing Projects

₹ 94,225

Original Cost
(crores)

₹ 99,294

Revised Cost
(crores)

₹ 38,890

(39.17% of Revised Cost)

Cumulative Expenditure
(crores)


0

Commissioned during month


3

Newly Added during month

Cost Analytics : All Sectors

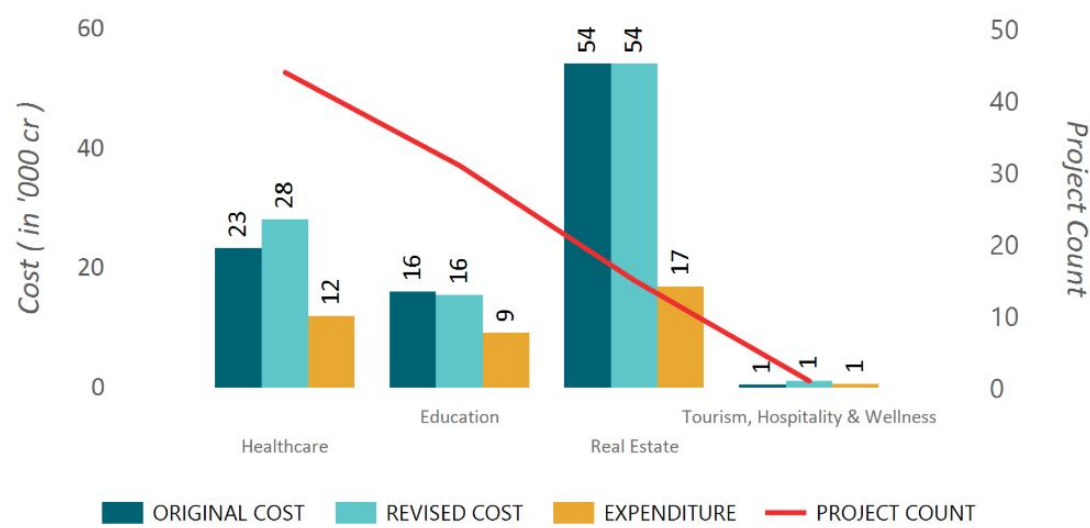

Cumulative Physical & Financial progress (%) : Project count

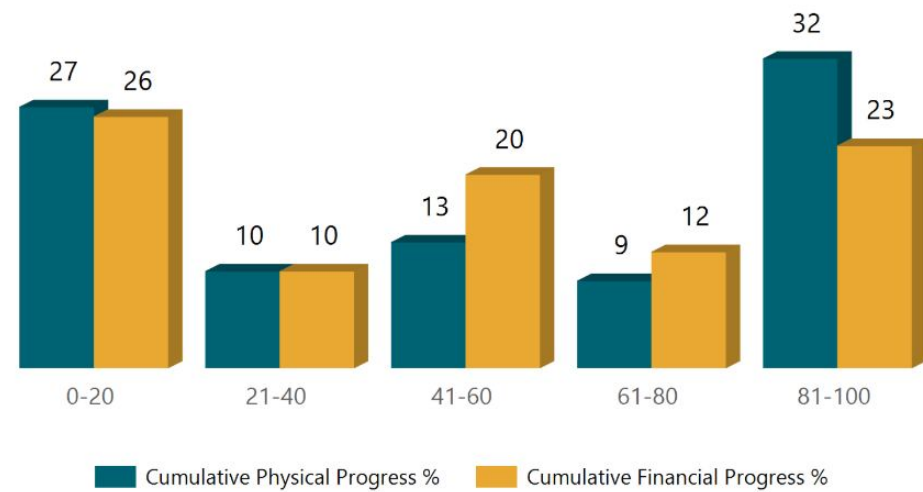

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Healthcare	44	23,350	28,175	12,039
2	Education	31	16,072	15,585	9,210
3	Real Estate	15	54,230	54,296	16,985
4	Tourism, Hospitality & Wellness	1	573	1,238	656

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850	32,841	14,370	46.7
2	617883	REDEVELOPMENT OF RESIDENTIAL COLONIES AT AYUR VIGYAN NAGAR AND WEST ANSARI NAGAR CAMPUSES OF AIIMS, NEW DELHI	4,441		44	57
3	701668	DEVELOPMENT OF PALAKKAD NODE UNDER EXTENSION OF CBIC TO KOCHI	3,805		58	5.3
4	617727	ORVAKAL INDUSTRIAL AREA	2,786		356	16.22
5	601812	DEVELOPMENT OF ZAHEERABAD NODE UNDER HYDERABAD NAGPUR INDUSTRIAL CORRIDOR	2,360		43	4.87

Other Sectors

JULY 2026

149
Ongoing Projects

₹ 2,19,791
Original Cost
(crores)


₹ 2,25,501
Revised Cost
(crores)

₹ 73,226
(32.47% of Revised Cost)
Cumulative Expenditure
(crores)

0
Commissioned during month

9
Newly Added during month

Cumulative Physical & Financial progress (%) : Project count

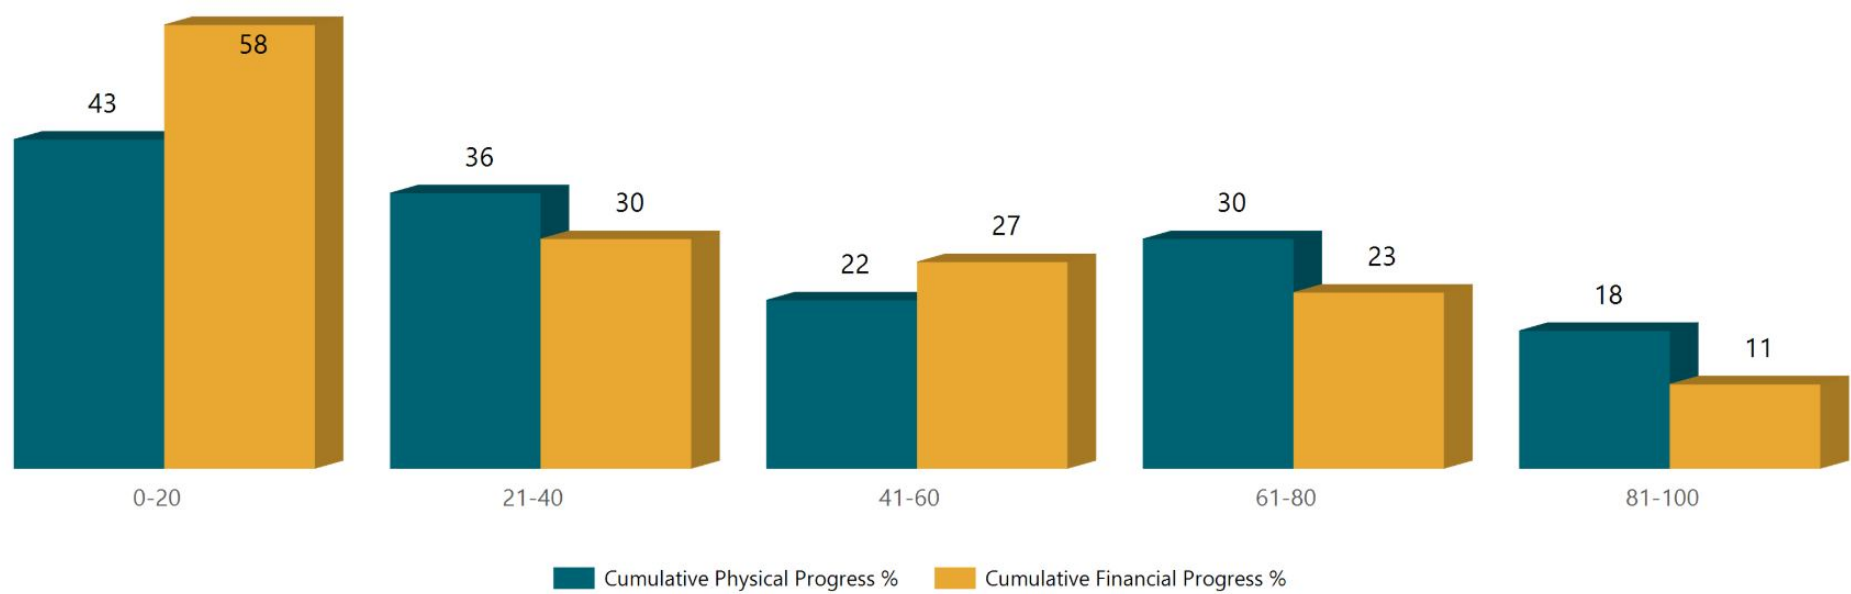

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	115	184,578	182,551	52,369
2	Steel	26	24,625	28,207	12,877
3	Metals & Mining	6	9,689	13,843	7,693
4	Construction	2	899	899	288

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	619032	JAYANT EXPN. [20 TO 38 MTPA]	25,560		333	2.1
2	400424	GEVRA OC [70 MTY]	11,816		7,825	78.48
3	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,778	35.8
4	400150	RPR MAGADH EXP OCP	6,964		2,300	39.42
5	617416	REVISED JHARIA MASTER PLAN FOR DEALING WITH FIRE, SUBSIDENCE & REHABILITATION OF AFFECTED FAMILIES IN JHARIA COALFIELD- REG.	5,940		521	34



Major Infrastructure Central Ministries & Departments





Ministry of Road Transport & Highways

JULY 2026

993

Ongoing Projects

₹ 9,45,371

Original Cost
(crores)

₹ 9,61,717

Revised Cost
(crores)

₹ 4,60,545

(47.89% of Revised Cost)
Cumulative Expenditure
(crores)

377 | ₹ 641,994

Mega Projects
Count | Original Cost (crores)

616 | ₹ 303,377

Major Projects
Count | Original Cost

20


Commissioned during month

6

Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

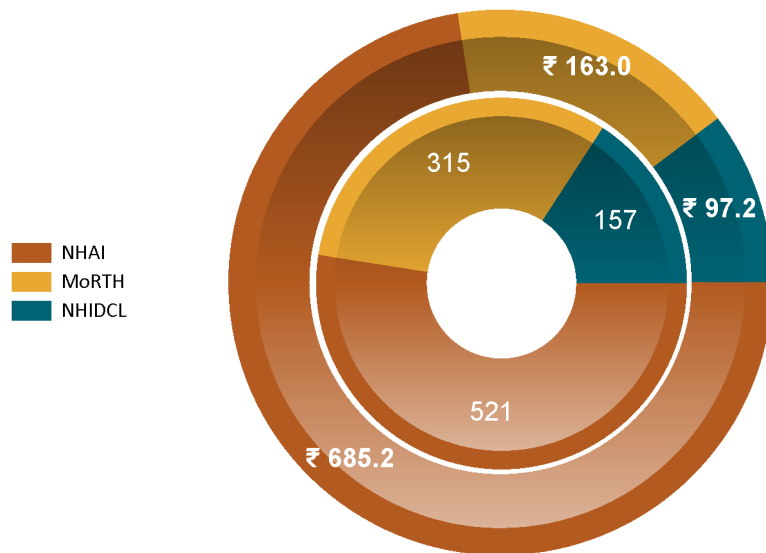


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Cumulative Physical & Financial progress (%) : Project count

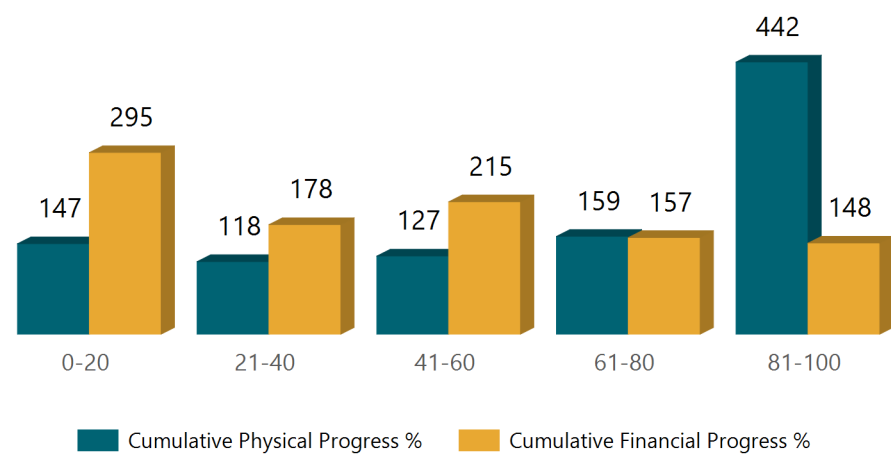

Cost Analytics : Major Sectors*

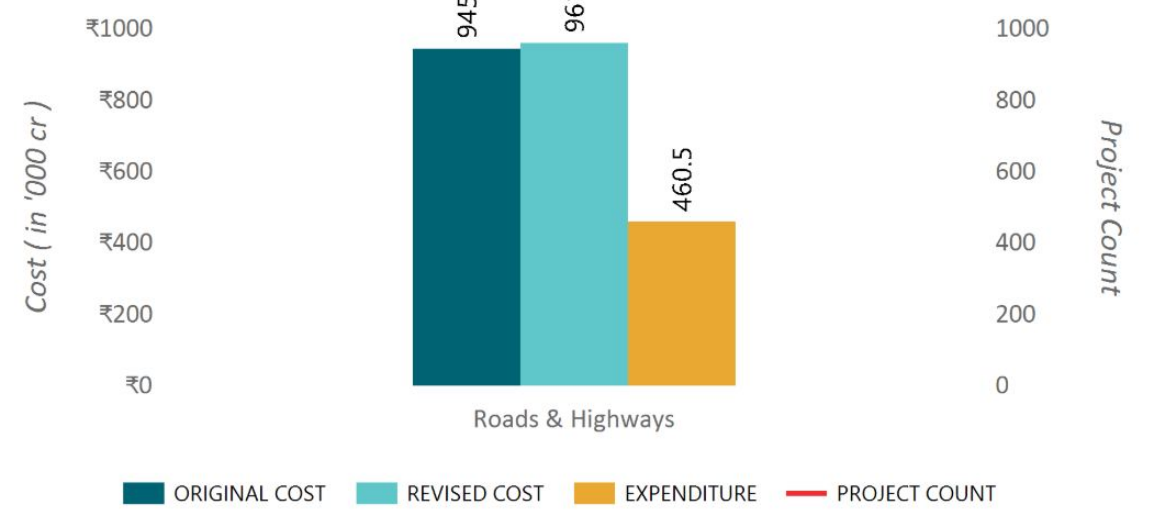

State Comparison : Major States*

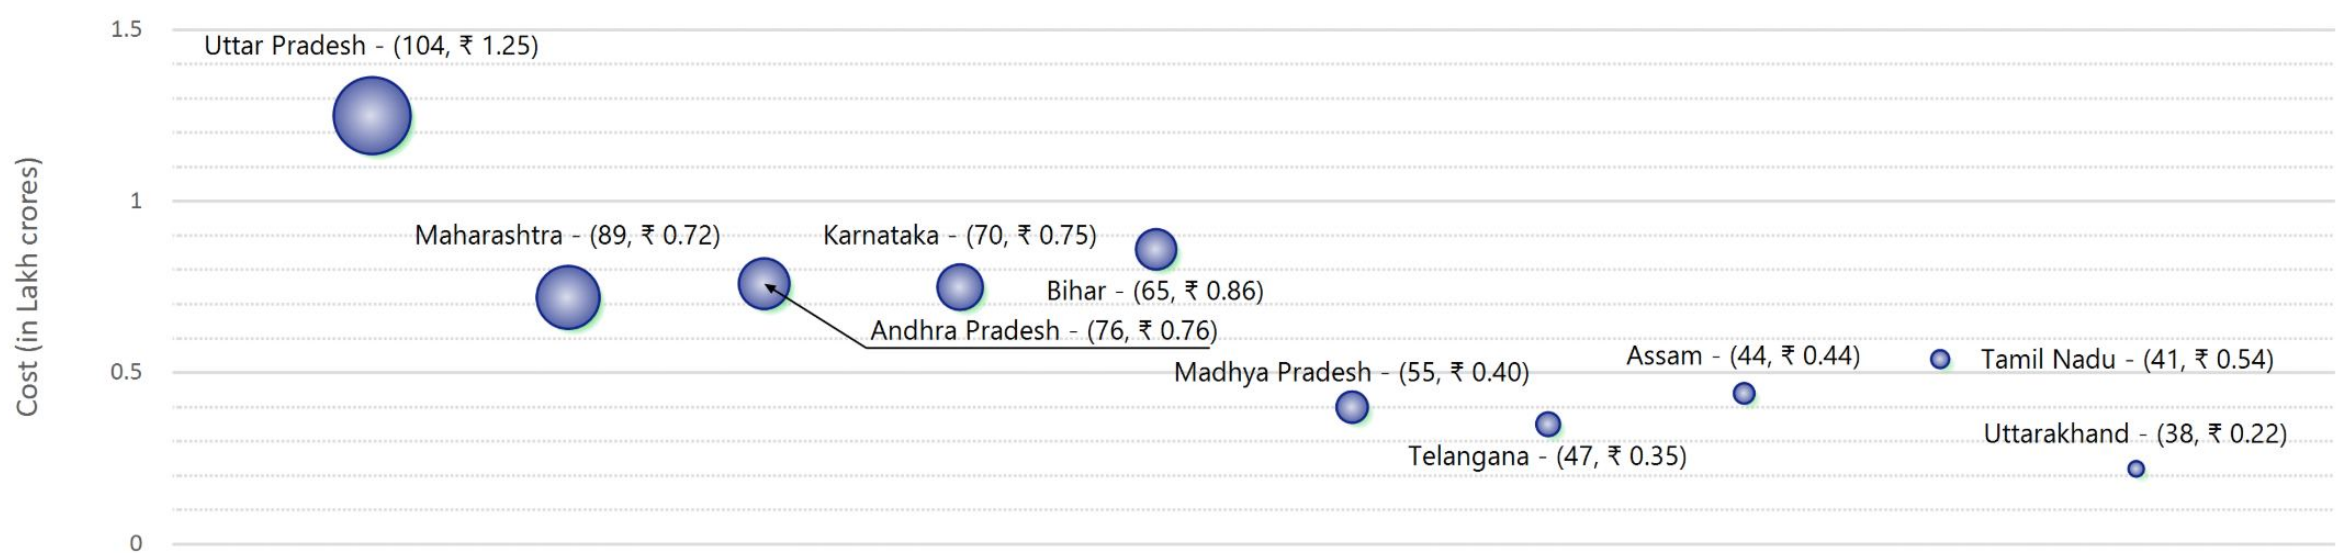

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count



Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	618412	CONSTRUCTION OF I CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL ROAD LENGTH 18.475KM AND II 14.150 KM LONG 2-L BI-DIRECTIONAL SINGLE TUBE ZOJI-LA TUNNEL ACROSS ZOJILA PASS ON SONAMARG - KARGIL SECTION FROM KM 82 TO KM 118 OF NH-01 UNDER PMDP	6,809	6,809	3,575	68.8
2	618738	6L BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD NH-131G STARTING FROM KM 8.480 NEAR SHERPUR TO KM 23.000 NEAR DIGHWARA	6,292	3,352	734	22.05
3	618934	GUWAHATI RING ROAD IN THE STATE OF ASSAM	5,729	5,729	328	0
4	618373	CONSTRUCTION OF 4-LANE BRIDGE INCLUDING APPROACHES OVER RIVER BRAHMAPUTRA BETWEEN DHUBRI ON NORTH BANK,ASSAM AND PHULBARI ON SOUTH BANK,MEGHALAYA ON NH-127B UNDER JICA ODA LOAN ASSISTANCE PHASE-III	4,997	4,997	3,081	77.14
5	618599	6L OF RAMANATUKKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66	4,919	4,919	3,765	100



Ministry of Railways

JULY 2026

190

Ongoing Projects

₹ 4,65,721

Original Cost
(crores)

₹ 6,38,470

Revised Cost
(crores)

₹ 4,59,391

(71.95% of Revised Cost)
Cumulative Expenditure
(crores)

94 | ₹ 418,076

Mega Projects
Count | Original Cost (crores)

96 | ₹ 47,645

Major Projects
Count | Original Cost

0


Commissioned during month

0

Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

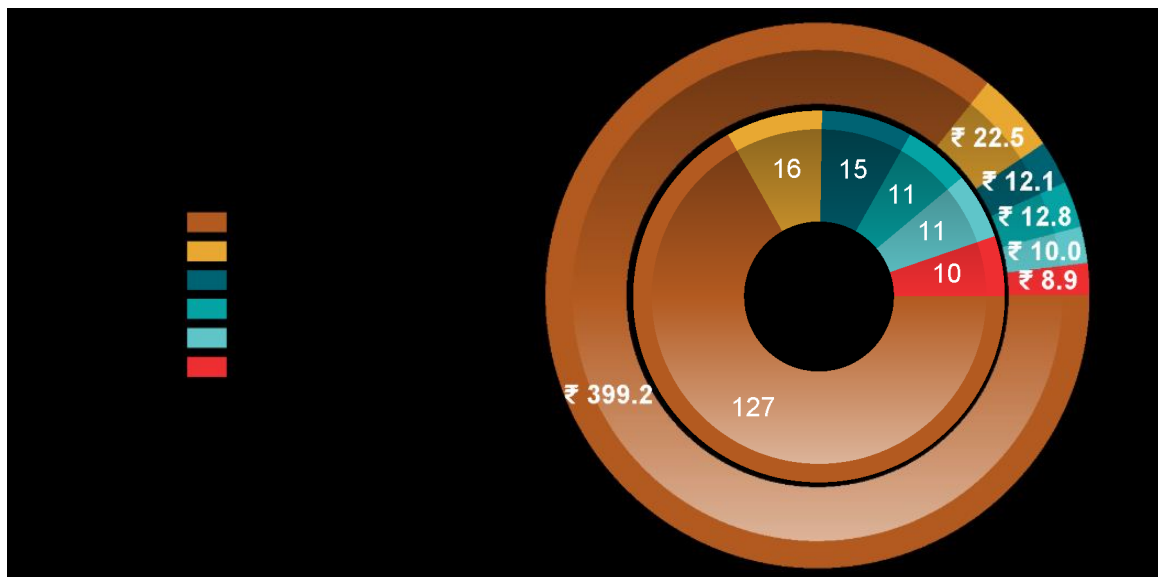


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Cumulative Physical & Financial progress (%) : Project count

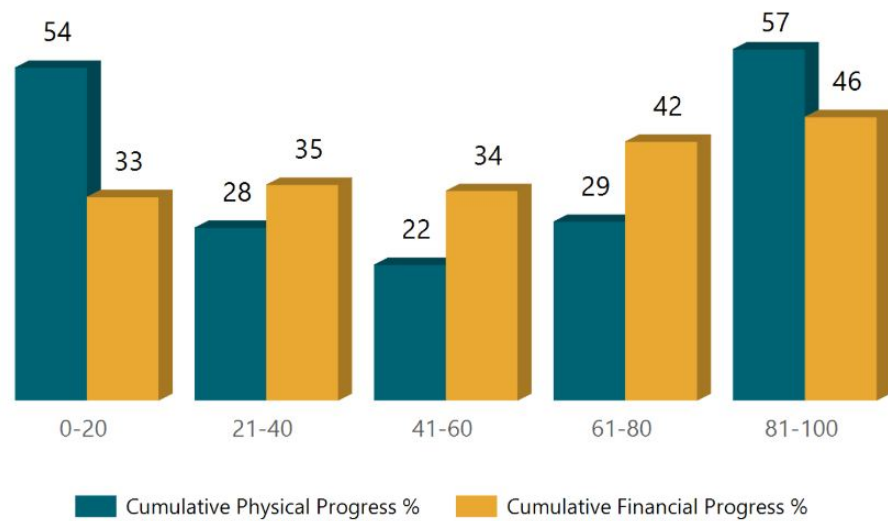

Cost Analytics : Major Sectors*



State Comparison : Major States*

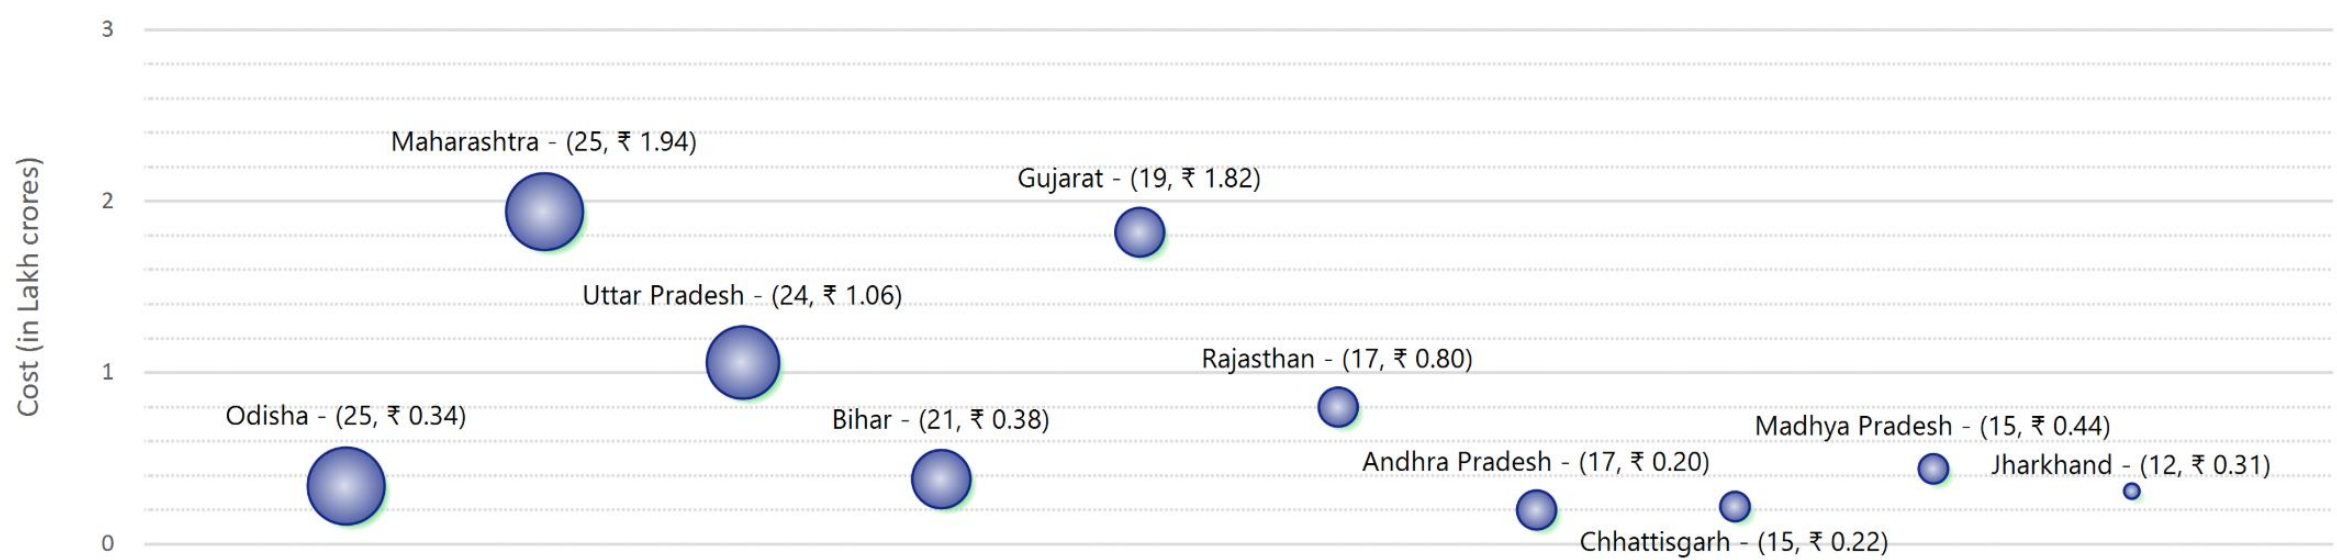

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	90,967	62.16
2	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
3	705941	BANGALORE SUBURBAN RAILWAY PROJECT	15,767	15,767	3,278	20.02
4	705391	JIRIBAM-IMPHAL 110 KM	14,323	21,886	16,932	78
5	616699	MULTI TRACKING OF SON NAGAR-ANDAL 374.53 RKM & 814.38 TKM PB34/ECOR/2023-24	12,334	12,334	1,153	3



Ministry of Coal

JULY 2026

121

Ongoing Projects

₹ 2,22,762

Original Cost
(crores)

₹ 2,21,971

Revised Cost
(crores)

₹ 60,237

(27.14% of Revised Cost)
Cumulative Expenditure
(crores)

41 | ₹ 183,146

Mega Projects
Count | Original Cost (crores)

80 | ₹ 39,616

Major Projects
Count | Original Cost

0


Commissioned during month

0

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

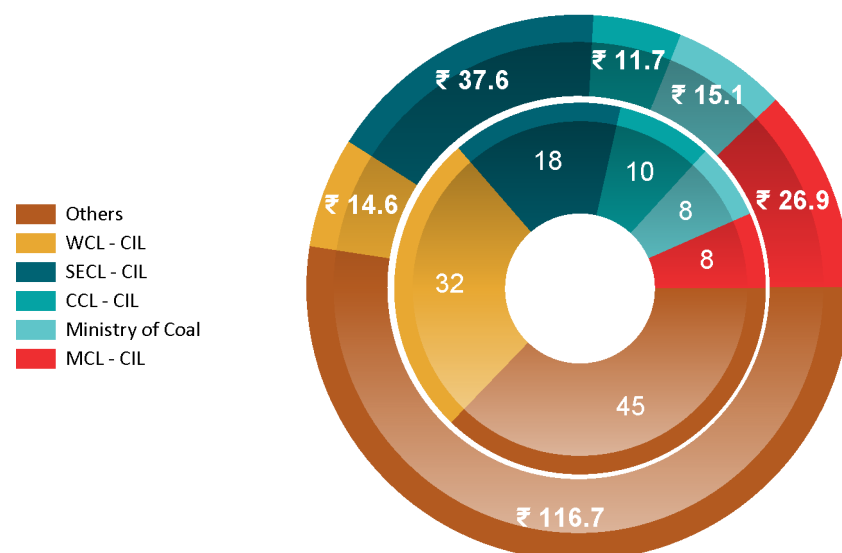


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

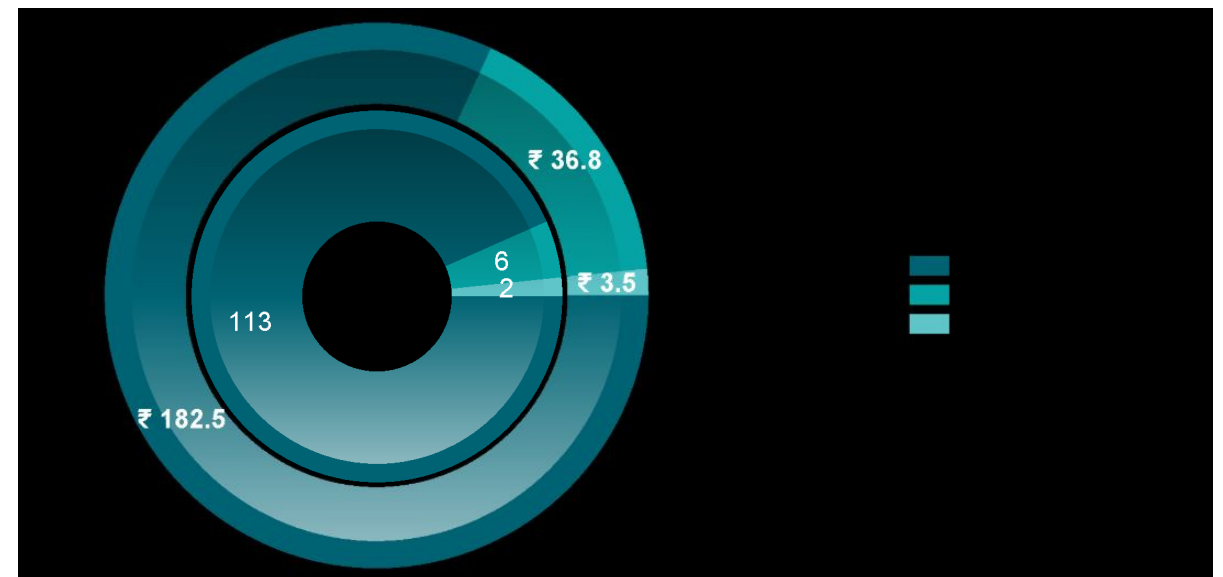


Cumulative Physical & Financial progress (%) : Project count

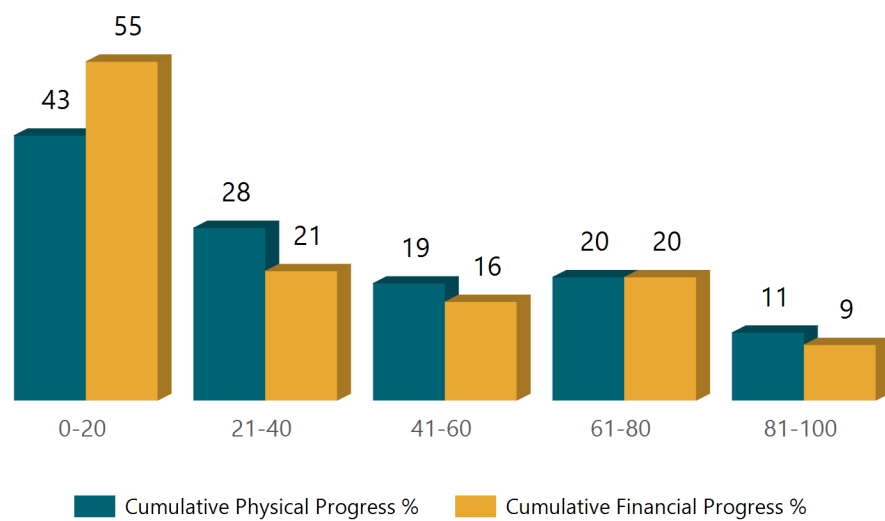

Cost Analytics : Major Sectors*

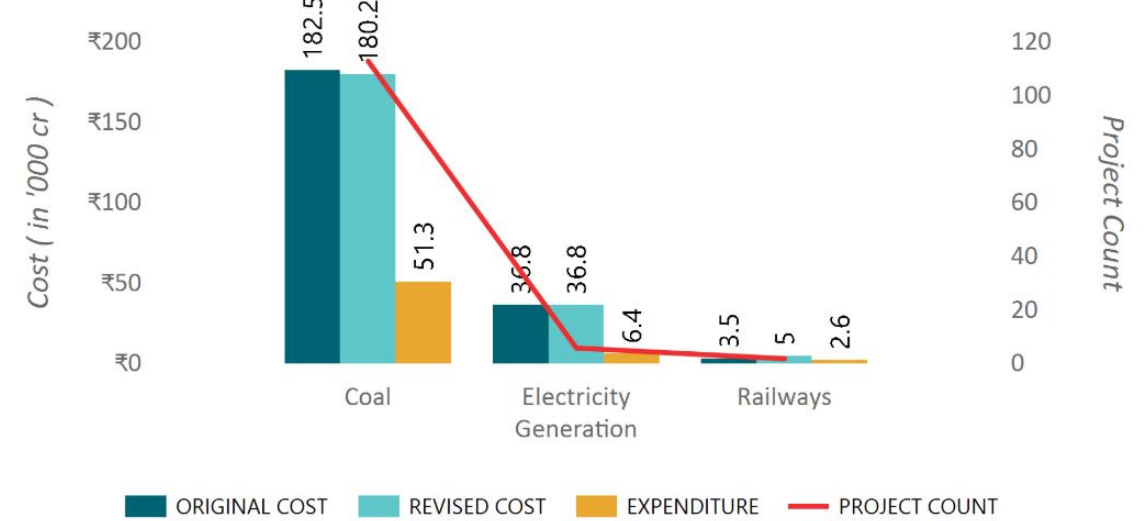

State Comparison : Major States*

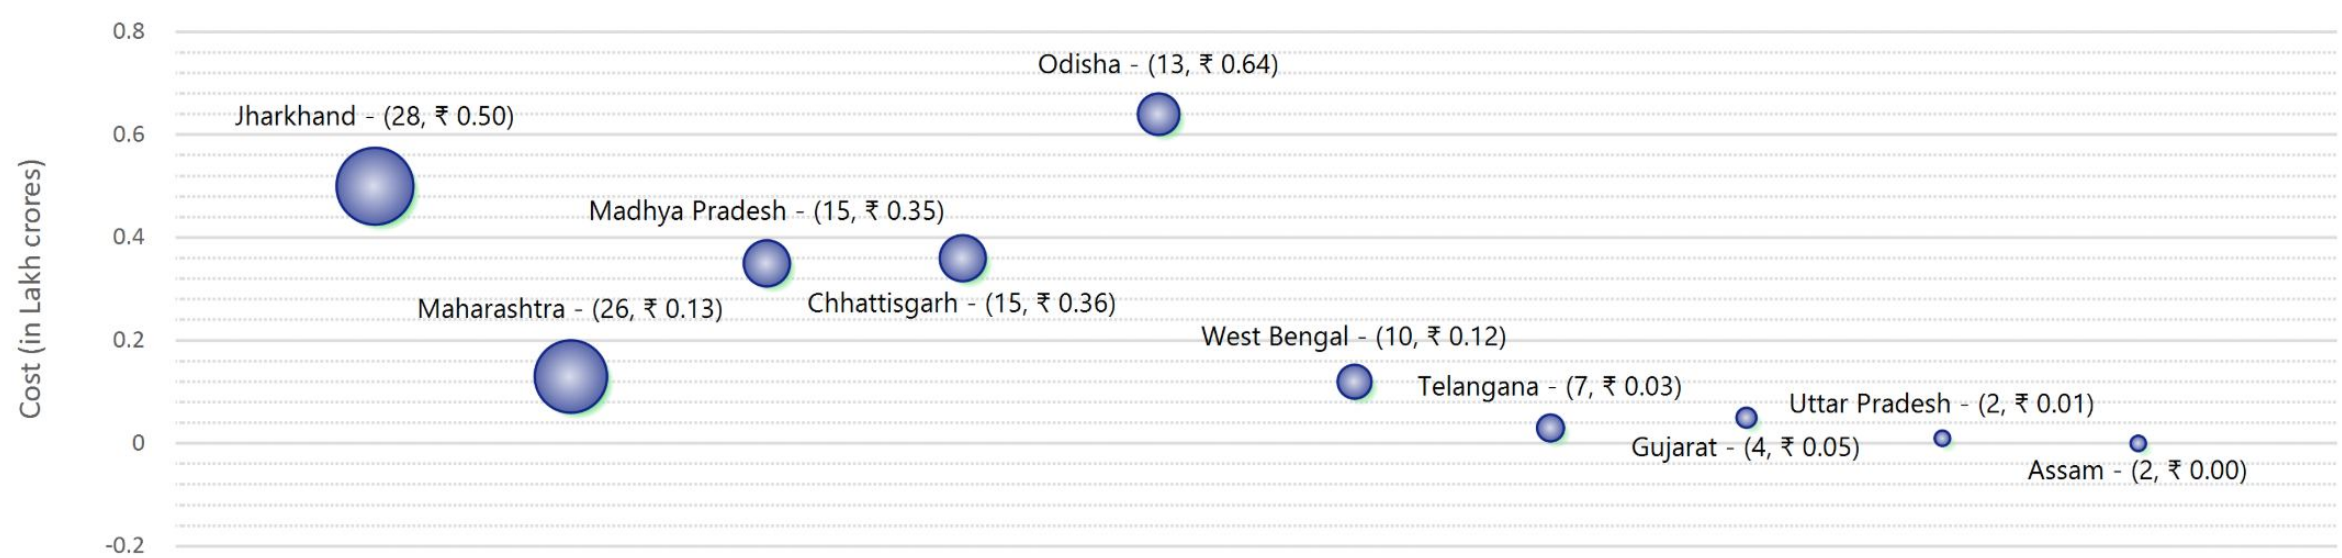

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	3,574	4.1
2	619032	JAYANT EXPN. [20 TO 38 MTPA]	25,560	25,560	333	2.1
3	400424	GEVRA OC [70 MTY]	11,816	11,816	7,825	78.48
4	400185	GOPALJI KANIHA OCP [10 TO 30 M]	8,416	6,108	1,778	35.8
5	400150	RPR MAGADH EXP OCP	6,964	6,964	2,300	39.42



Ministry of Petroleum & Natural Gas

JULY 2026

103

Ongoing Projects

₹ 3,87,546

Original Cost
(crores)

₹ 4,23,358

Revised Cost
(crores)

₹ 2,27,719

(53.79% of Revised Cost)

Cumulative Expenditure
(crores)

44 | ₹ 362,302

Mega Projects
Count | Original Cost (crores)

59 | ₹ 25,244

Major Projects
Count | Original Cost

2


Commissioned during month

0

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

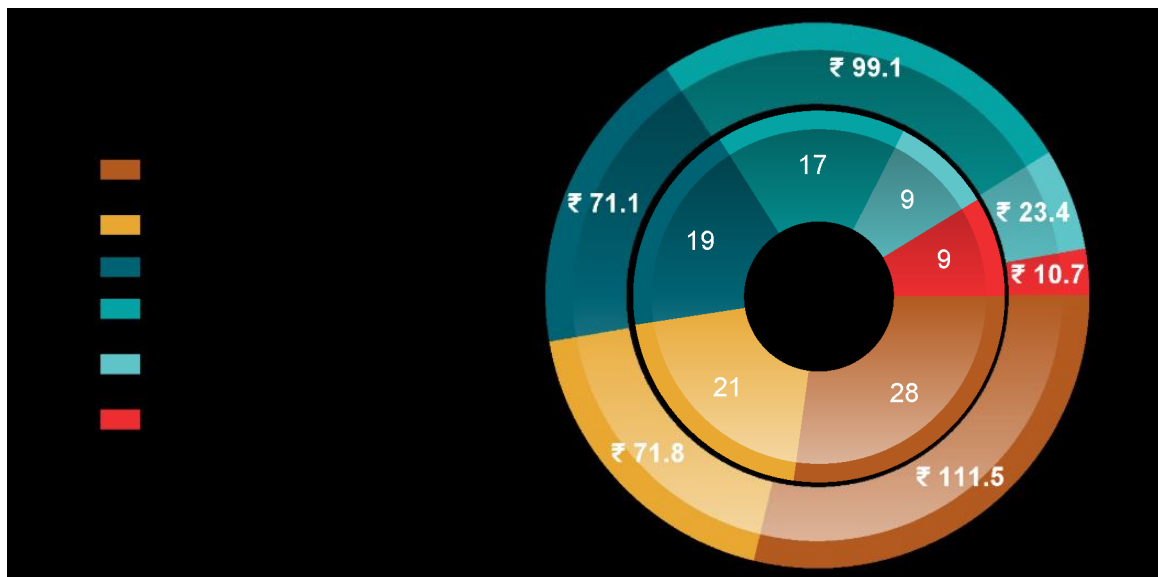


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

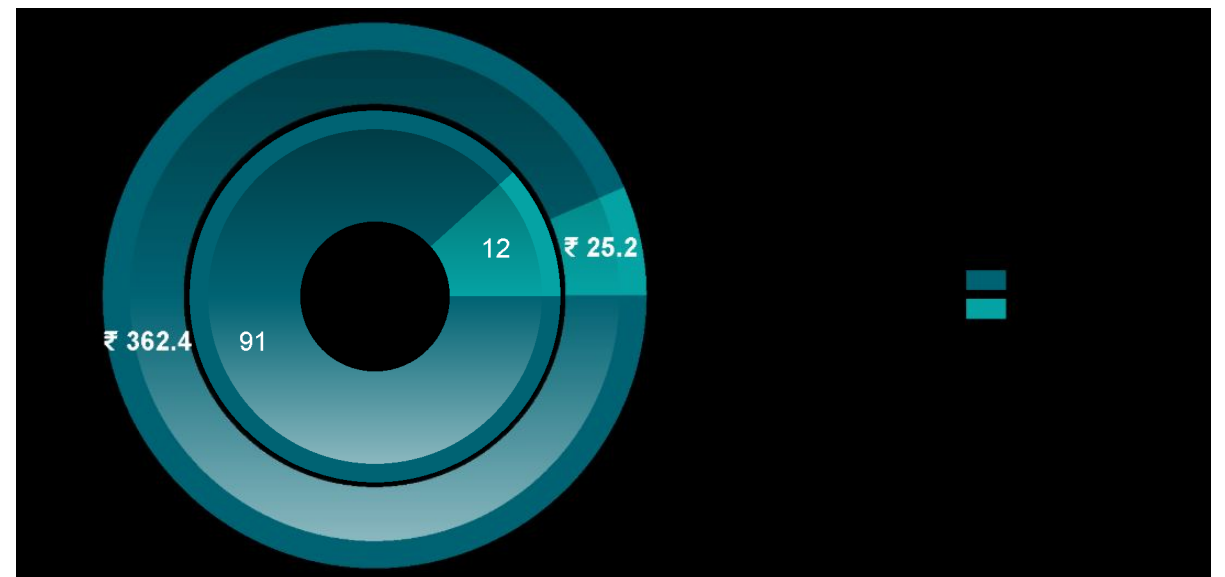


Cumulative Physical & Financial progress (%) : Project count

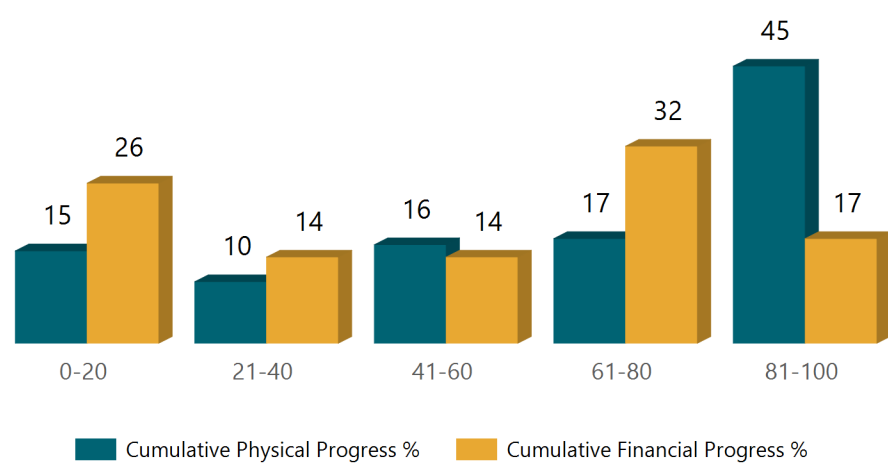

Cost Analytics : Major Sectors*

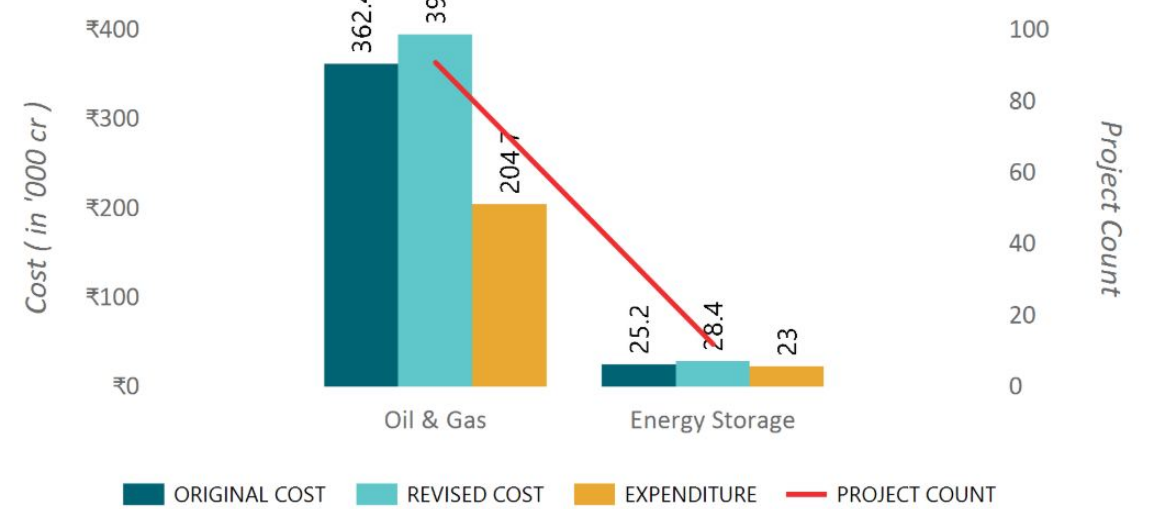

State Comparison : Major States*

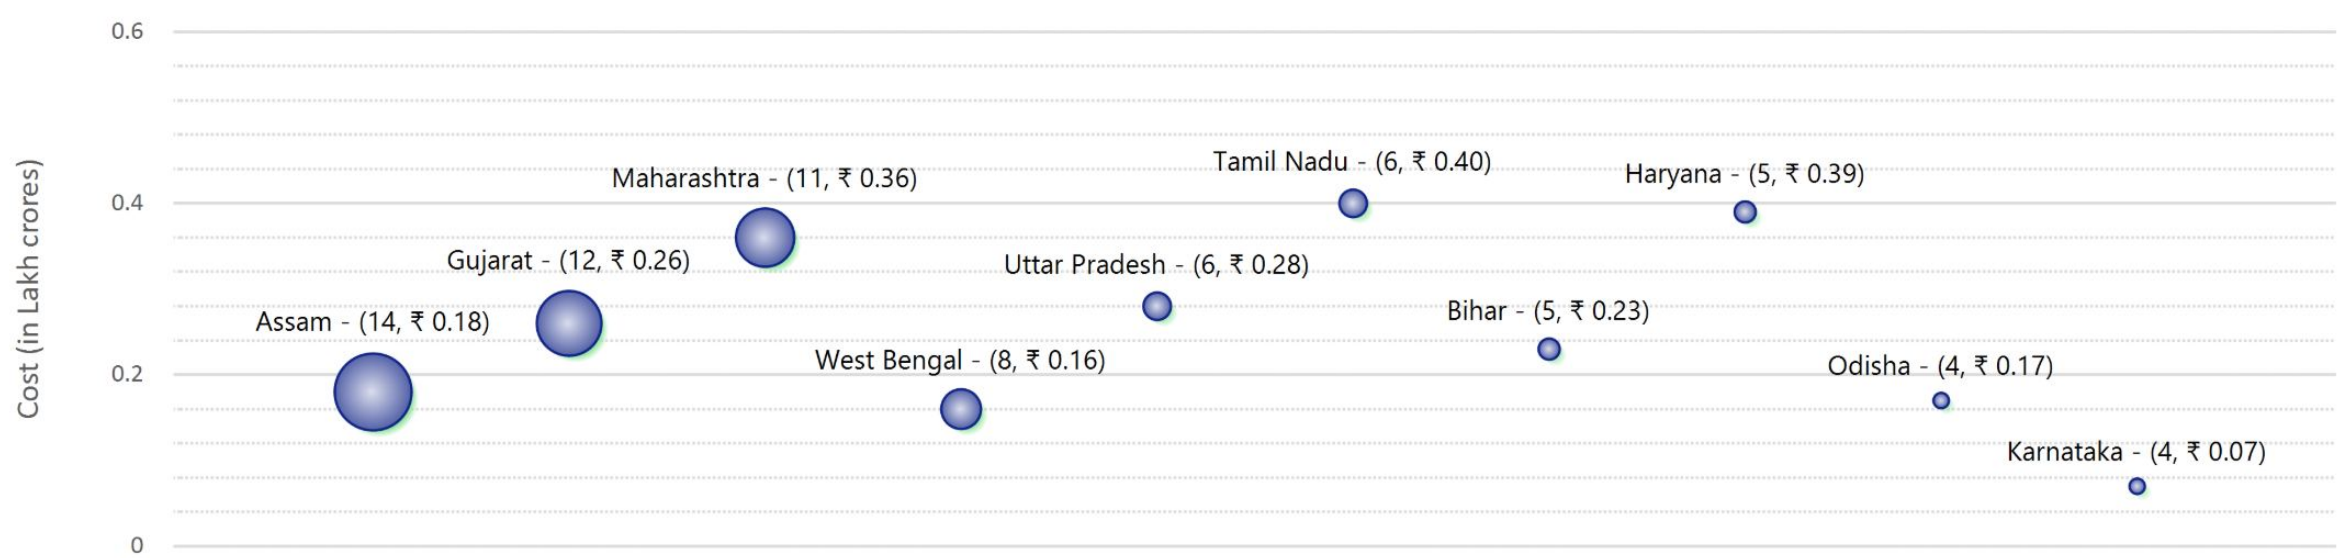

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	6,104	33.5
2	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	28,007	94.3
3	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,192	96.9
4	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,615	10.2
5	701329	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	18,936	17,825	13,901	89.6



Ministry of Power

JULY 2026

98

Ongoing Projects

₹ 5,51,906

Original Cost
(crores)

₹ 6,08,373

Revised Cost
(crores)

₹ 2,10,405

(34.58% of Revised Cost)
Cumulative Expenditure
(crores)

70 | ₹ 540,468

Mega Projects
Count | Original Cost (crores)

28 | ₹ 11,438

Major Projects
Count | Original Cost

1


Commissioned during month

1

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

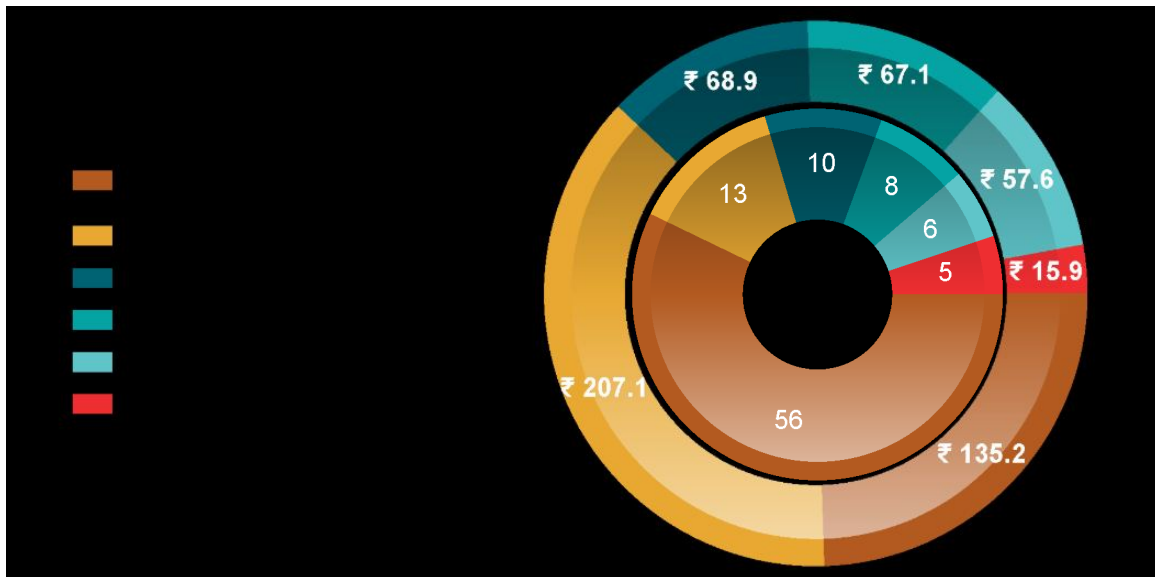


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

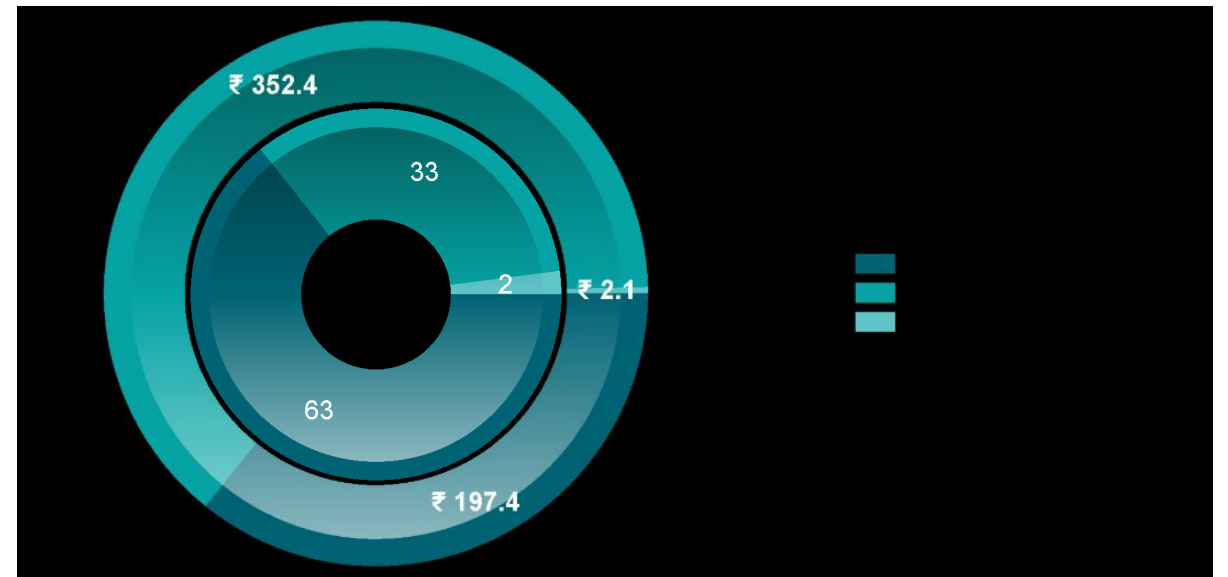


Cumulative Physical & Financial progress (%) : Project count

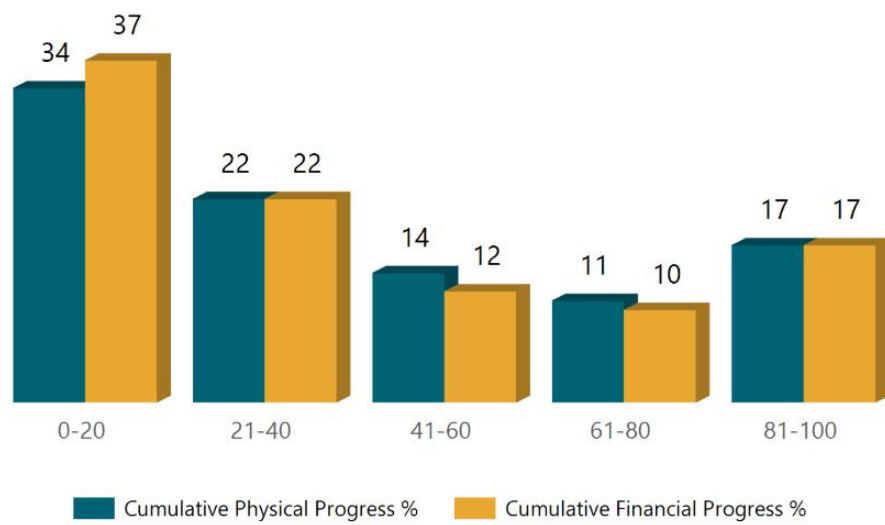

Cost Analytics : Major Sectors*

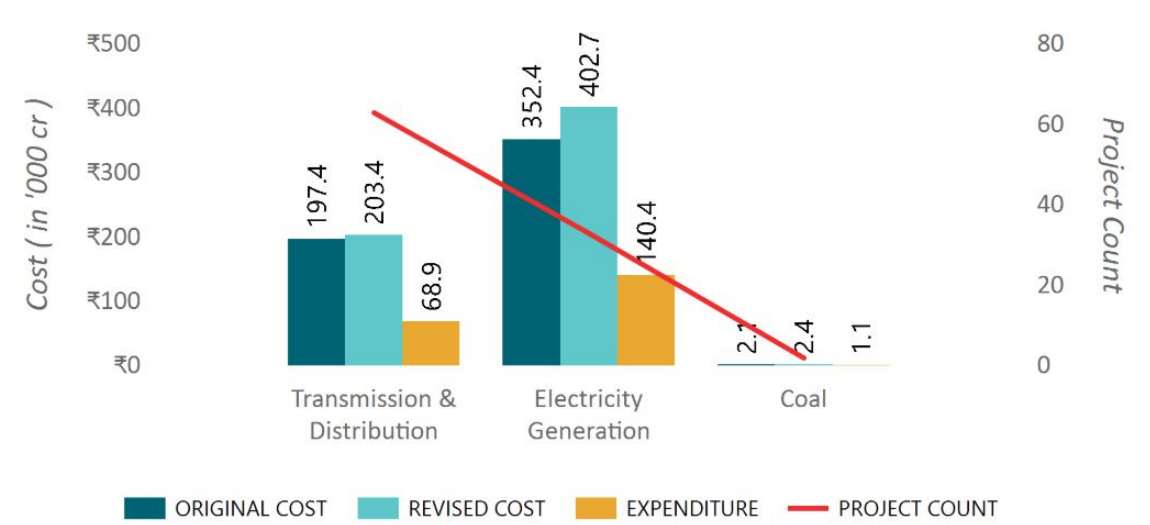


State Comparison : Major States*

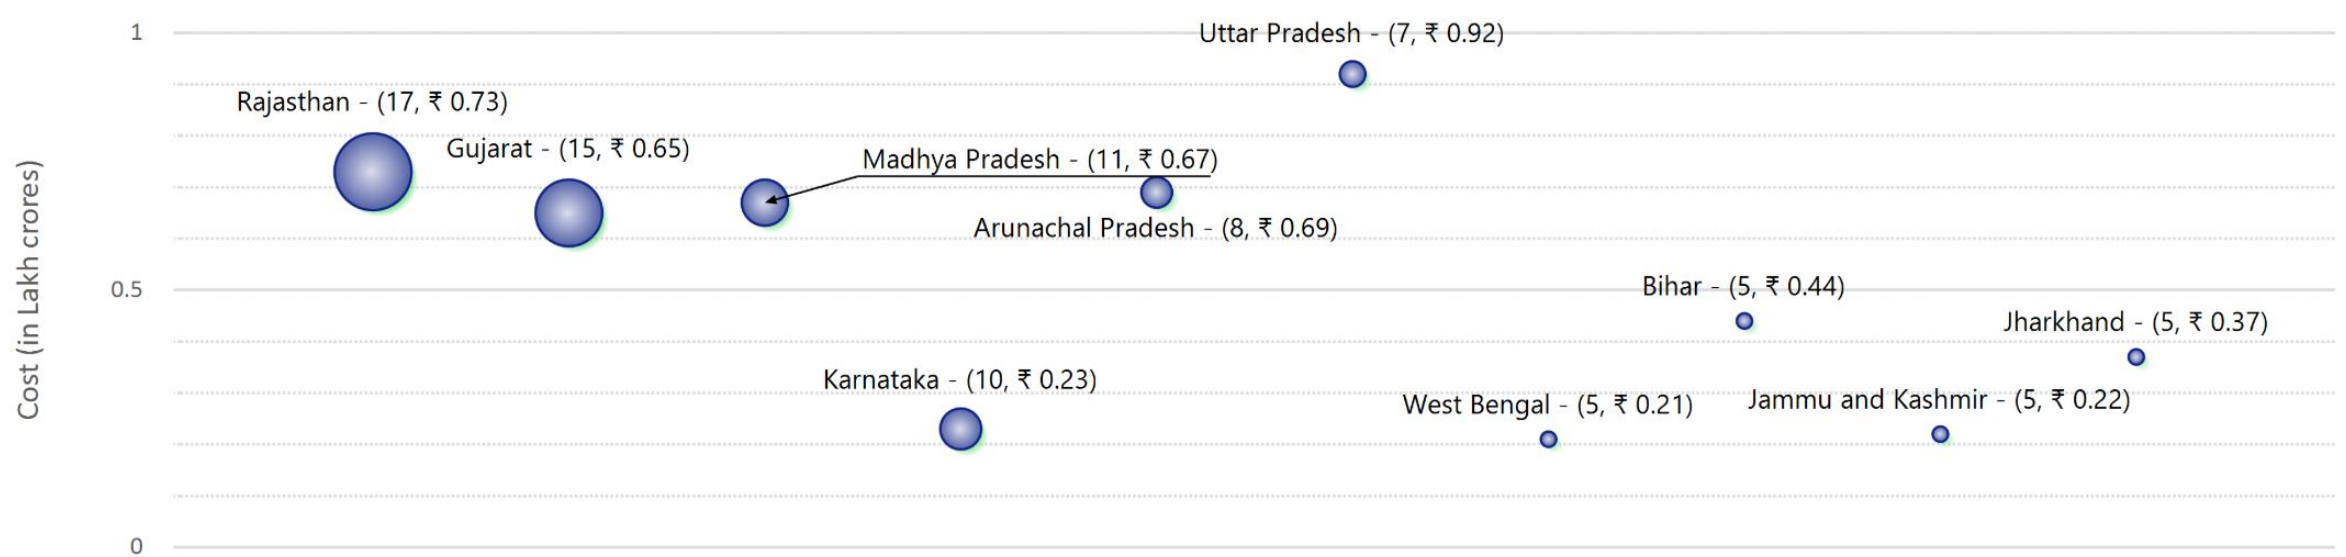

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	298178	MEJA THERMAL POWER PROJECT, STAGE-II , (3X800 MW)	38,358	38,358	1,003	0.02
2	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	4,921	17.93
3	619051	NABINAGAR SUPER THERMAL POWER PROJECT, STAGE-II [3X800 MW]	29,948	29,948	3,422	15
4	619341	TELANGANA SUPER THERMAL POWER PROJECT , STAGE-II [3 X 800 MW]	29,345	29,345	733	0.97
5	619025	RAJASTHAN PART I POWER TRANSMISSION LIMITED	25,000	25,000	735	10



List of Tables






Table 1: Ministry-wise Ongoing Projects





Ministry-wise Ongoing Projects

JULY 2026

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Logistics Infrastructure	1	763.00 (763.00)	430.00
		Real Estate	11	20480.02 (20480.02)	1893.94
		Total	12	21,243.02	2,323.94
2	Department of Higher Education	Education	30	15165.68 (14973.27)	8632.49
		Total	30	15,165.68	8,632.49
3	Department of Sports	Education	1	906.47 (611.74)	577.32
		Total	1	906.47	577.32
4	Department of Telecommunications	Telecommunication	31	207194.71 (133825.11)	102879.15
		Total	31	207,194.71	102,879.15
5	Department of Water Resources, River Development & GR	Waste & Water	8	4039.12 (4039.12)	1658.37
		Water Resources	30	96487.38 (197109.95)	140510.51
		Total	38	100,526.50	142,168.88
6	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	25	21345.07 (22771.55)	11586.47
		Total	25	21,345.07	11,586.47
7	Ministry of Coal	Coal	113	182494.77 (180186.43)	51305.23
		Electricity Generation	6	36781.81 (36781.81)	6354.71
		Railways	2	3485.86 (5002.87)	2577.50
		Total	121	222,762.44	60,237.44
8	Ministry of Health & Family Welfare	Healthcare	35	21050.26 (25678.42)	10844.00
		Total	35	21,050.26	10,844.00
9	Ministry of Housing & Urban Affairs	Construction	1	644.00 (644.00)	188.69
		Real Estate	4	33749.85 (33816.00)	15090.75
		Urban Public Transport	30	320872.37 (339476.05)	178627.24
		Waste & Water	15	3750.55 (3849.83)	2930.11
		Total	50	359,016.77	196,836.79
10	Ministry of Labour and Employment	Healthcare	9	2299.24 (2496.24)	1194.92
		Total	9	2,299.24	1,194.92
11	Ministry of Mines	Construction	1	255.37 (255.37)	98.94
		Metals & Mining	5	7989.36 (12087.17)	7400.84
		Total	6	8,244.73	7,499.78
12	Ministry of Petroleum & Natural Gas	Energy Storage	12	25151.96 (28440.82)	23048.58
		Oil & Gas	91	362394.10 (394917.26)	204670.66
		Total	103	387,546.06	227,719.24
13	Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 (5061.15)	4187.19
		Shipping	4	7572.50 (7613.11)	5245.77
		Tourism, Hospitality & Wellness	1	573.00 (1238.05)	656.38
		Total	6	13,514.68	10,089.34
14	Ministry of Power	Coal	2	2083.00 (2365.00)	1063.43
		Electricity Generation	33	352432.05 (402653.91)	140445.00
		Transmission & Distribution	63	197390.82 (203354.39)	68896.68
		Total	98	551,905.87	210,405.11
15	Ministry of Railways	Railways	190	465721.36 (638469.92)	459390.96
		Total	190	465,721.36	459,390.96
16	Ministry of Road Transport & Highways	Roads & Highways	993	945370.67 (961717.26)	460544.81
		Total	993	945,370.67	460,544.81
17	Ministry of Steel	Metals & Mining	1	1700.00 (1756.20)	292.01
		Steel	26	24624.69 (28206.53)	12876.92
		Total	27	26,324.69	13,168.93
Total			1775	3,370,138.22	1,926,099.57




Table 2: State-wise Ongoing Projects





Ongoing Projects State-Wise

JULY 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	7	26668.64 29330.8	18021.78
	PAN India	Department of Telecommunications	Telecommunication	2	53010.55 44136.6	18330.93
		Ministry of Railways	Railways	1	274.39 274.39	0.00
	Total			10	79953.58	36352.71
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 230	37.35
		Ministry of Road Transport & Highways	Roads & Highways	3	653.97 1081.48	275.78
	PAN India	Department of Telecommunications	Telecommunication	5	111918.69 52595.5	78855.54
	Total			9	112782.54	79168.67
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	3	7061.44 7061.44	1379.93
		Department of Higher Education	Education	1	305 305	67.73
		Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1977.02
		Department of Water Resources, River Development & GR	Water Resources	3	10901.5 57269.5	29465.48
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1224.86 1437.34	938.85
		Ministry of Housing & Urban Affairs	Waste & Water	1	172.22 172.22	88.86
		Ministry of Labour and Employment	Healthcare	1	384.27 384.27	286.38
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	34430.34 34490.3	33359.61
		Ministry of Power	Transmission & Distribution	4	15694.49 15694.5	4068.80
		Ministry of Railways	Railways	17	20027.63 27750.5	11318.79
		Ministry of Road Transport & Highways	Roads & Highways	76	75592.97 73188.2	34003.21
	PAN India	Department of Telecommunications	Telecommunication	4	110244.69 50921.5	78632.13
	Total			119	283186.58	195586.79
4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 592.61	551.30
		Department of Telecommunications	Telecommunication	1	1255.49 276.62	237.98
		Ministry of Power	Electricity Generation	6	64102.68 83892.9	31998.81
			Transmission & Distribution	2	4963.8 9338.7	8144.66
		Ministry of Railways	Railways	1	435 1334.45	1057.21
		Ministry of Road Transport & Highways	Roads & Highways	12	8612.04 8612.04	3130.05
	PAN India	Department of Telecommunications	Telecommunication	5	111412.69 52089.5	78755.41
Total			28	191374.31	123875.42	
5	Assam	Department of Higher Education	Education	1	153.71 153.71	266.14
		Department of Telecommunications	Telecommunication	1	1255.49 276.62	237.98
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 256.16	44.70
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1712 2520	2670.23
		Ministry of Coal	Coal	2	449.23 449.23	218.35
		Ministry of Petroleum & Natural Gas	Energy Storage	2	540.4 540.4	364.17
			Oil & Gas	12	17678.76 30687.9	23088.03
		Ministry of Power	Electricity Generation	1	6285.33 26075.5	26448.07
			Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Railways	Railways	5	14586.32 25184.5	13071.28
		Ministry of Road Transport & Highways	Roads & Highways	44	44354.69 45031.1	17101.93
	PAN India	Department of Telecommunications	Telecommunication	5	111076.69 51753.5	78715.29
Total			76	203460.11	167803.92	
6	Bihar	Department for Promotion of Industry & Internal Trade	Real Estate	1	1339.02 1339.02	0.00
		Department of Higher Education	Education	1	499.21 499.21	449.96
		Department of Telecommunications	Telecommunication	3	3883.82 2718.14	1021.96
		Department of Water Resources, River Development & GR	Waste & Water	5	2351.43 2351.43	1312.90

Ongoing Projects State-Wise

JULY 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Department of Water Resources, River Development & GR	Water Resources	1	1622.27 2430.76	345.94
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3541.56 3541.56	1645.23
		Ministry of Health & Family Welfare	Healthcare	8	3634.07 3884.07	970.34
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	13365.77 13365.8	5198.09
			Waste & Water	1	158.78 158.78	135.72
		Ministry of Petroleum & Natural Gas	Oil & Gas	5	23096.5 25031.5	14421.68
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	4187.19
		Ministry of Power	Electricity Generation	2	40387.09 43704.6	17154.02
			Transmission & Distribution	3	3119.63 3119.63	308.00
		Ministry of Railways	Railways	21	38022.35 45877.3	22991.15
		Ministry of Road Transport & Highways	Roads & Highways	65	85954.3 86653.9	38803.66
	PAN India	Department of Telecommunications	Telecommunication	5	111794.69 52471.5	78854.90
Total				126	338139.67	187800.74
7	PAN India	Department of Telecommunications	Telecommunication	3	88070.13 28747	57940.41
		Total		3	88070.13	57940.41
8	Chhattisgarh	Department of Higher Education	Education	1	1188.97 1188.97	1.92
		Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1977.02
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 1109.33	869.21
		Ministry of Coal	Coal	14	34428.39 34428.4	13757.56
			Railways	1	1686.22 2438.53	792.73
		Ministry of Health & Family Welfare	Healthcare	3	975 972.85	538.19
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	2769.04 2769.04	581.63
		Ministry of Power	Electricity Generation	2	25321 25897	7382.68
		Ministry of Railways	Railways	15	22210.9 26681.1	19202.92
		Ministry of Road Transport & Highways	Roads & Highways	22	21163.16 22402.5	9945.38
		Ministry of Steel	Metals & Mining	1	1700 1756.2	292.01
			Steel	7	7640.96 10504.5	6556.77
	PAN India	Department of Telecommunications	Telecommunication	4	110244.69 50921.5	78632.13
Total				77	237317.76	140530.15
9	Dadra & Nagar Haveli and Daman & Diu	Ministry of Railways	Railways	1	108000 108000	90966.89
		Ministry of Road Transport & Highways	Roads & Highways	2	2107.8 2891.81	1175.06
	PAN India	Department of Telecommunications	Telecommunication	4	93013.13 33690	58502.54
		Total		7	203120.93	150644.49
10	Delhi	Department of Higher Education	Education	2	706.49 709.42	367.95
		Department of Telecommunications	Telecommunication	1	248.2 248.2	237.43
		Ministry of Health & Family Welfare	Healthcare	2	4799.19 4799.19	98.17
		Ministry of Housing & Urban Affairs	Real Estate	1	32850 32841	14370.45
			Urban Public Transport	4	51594.36 51594.4	22669.45
		Ministry of Power	Transmission & Distribution	3	3038 3038	2555.05
		Ministry of Railways	Railways	2	7473.44 8797	9874.54
		Ministry of Road Transport & Highways	Roads & Highways	3	6302.28 8803.17	7728.61
	PAN India	Department of Telecommunications	Telecommunication	1	645.13 645.13	407.90
		Total		19	107657.09	58309.55
11	Goa	Ministry of Railways	Railways	1	1892 1892	0.00
		Ministry of Road Transport & Highways	Roads & Highways	5	2476.3 2252.18	278.80
	PAN India	Department of Telecommunications	Telecommunication	3	30703.13 19780	9566.03
		Total		9	35071.43	9844.83

Ongoing Projects State-Wise

JULY 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
12	Gujarat	Department of Higher Education	Education	1	490.63 490.63	342.26
		Department of Water Resources, River Development & GR	Water Resources	1	20718.17 33412.5	31969.40
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1668.1 1914.1	1075.00
		Ministry of Coal	Electricity Generation	4	5421.78 5421.78	2530.55
		Ministry of Health & Family Welfare	Healthcare	3	1845 2477.48	2209.46
		Ministry of Housing & Urban Affairs	Real Estate	1	539 539	623.44
			Urban Public Transport	1	12020.32 12020.3	9332.21
		Ministry of Labour and Employment	Healthcare	2	763.99 763.99	107.55
		Ministry of Petroleum & Natural Gas	Energy Storage	1	356.86 304.4	168.04
			Oil & Gas	11	25671.12 25649.5	19068.81
		Ministry of Ports, Shipping and Waterways	Shipping	2	4414.64 4455.25	2887.20
			Tourism, Hospitality & Wellness	1	573 1238.05	656.38
		Ministry of Power	Electricity Generation	1	339.35 339.35	370.00
			Transmission & Distribution	14	64870.45 64870.4	12799.93
		Ministry of Railways	Railways	19	181569.47 265806	238905.02
		Ministry of Road Transport & Highways	Roads & Highways	31	32109.82 32551.8	16914.51
	PAN India	Department of Telecommunications	Telecommunication	4	110244.69 50921.5	78632.13
Total				99	463616.39	418591.89
13	Haryana	Department for Promotion of Industry & Internal Trade	Logistics Infrastructure	1	763 763	430.00
		Ministry of Health & Family Welfare	Healthcare	1	1299 1646.43	747.62
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	11683.71 11683.7	993.80
			Waste & Water	1	278.01 278.01	228.49
		Ministry of Petroleum & Natural Gas	Oil & Gas	5	38892.07 42563.1	31735.55
		Ministry of Power	Transmission & Distribution	3	13749 13749	6119.95
		Ministry of Railways	Railways	3	53112 126418	126067.09
		Ministry of Road Transport & Highways	Roads & Highways	19	25551.69 28133.7	16582.15
	PAN India	Department of Telecommunications	Telecommunication	4	88907.13 29584	58024.09
Total				39	234235.61	240928.74
14	Himachal Pradesh	Department of Higher Education	Education	3	811.15 921.89	701.51
		Ministry of Power	Electricity Generation	3	5113.04 10664.1	4408.48
		Ministry of Railways	Railways	2	3558 6018.32	4036.00
		Ministry of Road Transport & Highways	Roads & Highways	24	22820.53 26827.4	14973.10
	PAN India	Department of Telecommunications	Telecommunication	5	111536.69 52213.5	78781.06
Total				37	143839.41	102900.15
15	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 500.91	484.52
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 861.37	370.44
		Ministry of Health & Family Welfare	Healthcare	3	2478 3220.19	1997.61
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	538 538	4.45
		Ministry of Power	Electricity Generation	4	22207.77 27945.1	16608.79
			Transmission & Distribution	1	218.6 218.6	3.72
		Ministry of Road Transport & Highways	Roads & Highways	36	33531.1 33631.9	15765.65
	PAN India	Department of Telecommunications	Telecommunication	5	111865.69 52542.5	78802.18
Total				52	172125.46	114037.36
16	Jharkhand	Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1977.02
		Department of Water Resources, River Development & GR	Water Resources	2	5430.04 12010.3	6386.21
		Ministry of Coal	Coal	27	48328.18 48328.2	11766.54



Ongoing Projects State-Wise

JULY 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	Jharkhand	Ministry of Coal	Railways	1	1799.64 2564.34	1784.77
		Ministry of Health & Family Welfare	Healthcare	2	500 958.9	336.00
		Ministry of Housing & Urban Affairs	Waste & Water	3	654.14 654.14	403.16
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	633.07 633.07	333.72
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	4187.19
		Ministry of Power	Coal	2	2083 2365	1063.43
			Electricity Generation	2	33026 34660	21965.03
			Transmission & Distribution	1	1842.25 1842.25	1648.05
		Ministry of Railways	Railways	12	30929.26 32081.4	12397.47
		Ministry of Road Transport & Highways	Roads & Highways	36	41182.86 41172.2	19081.03
		Ministry of Steel	Steel	5	2340.76 3059.05	1667.13
	PAN India	Department of Telecommunications	Telecommunication	4	110244.69 50921.5	78632.13
Total				103	291510.24	163628.88
17	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1701.81 1701.81	337.56
		Department of Water Resources, River Development & GR	Water Resources	1	770.16 1606.07	1515.60
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1143.4 1143.4	809.87
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	56804.24 61094.2	40713.45
			Waste & Water	1	162.73 162.73	79.50
		Ministry of Labour and Employment	Healthcare	2	428.92 428.92	111.57
		Ministry of Petroleum & Natural Gas	Oil & Gas	4	6747 6784.62	5172.33
		Ministry of Ports, Shipping and Waterways	Shipping	1	153.23 153.23	97.45
		Ministry of Power	Transmission & Distribution	10	23490.99 23491	9340.94
		Ministry of Railways	Railways	12	33849.7 32719.6	11303.68
		Ministry of Road Transport & Highways	Roads & Highways	70	75166.87 79380.3	48272.76
		Ministry of Steel	Steel	1	1043.63 1043.63	649.52
	PAN India	Department of Telecommunications	Telecommunication	4	91812.13 32489	58375.72
Total				113	293274.81	176779.95
18	Kerala	Department for Promotion of Industry & Internal Trade	Real Estate	1	3805 3805	57.93
		Department of Higher Education	Education	2	2533.45 2744.4	696.00
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	484.57 484.57	242.51
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1957.05 1957.05	816.80
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	5590 5980	1350.61
		Ministry of Power	Transmission & Distribution	1	173.14 173.14	2.08
		Ministry of Railways	Railways	3	2846 5784.41	3966.63
		Ministry of Road Transport & Highways	Roads & Highways	21	55625.3 61868.6	42535.43
	PAN India	Department of Telecommunications	Telecommunication	5	111009.69 51686.5	78727.08
Total				37	184024.2	128395.07
19	Ladakh	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480 640	512.55
		Ministry of Health & Family Welfare	Healthcare	1	325 325	127.00
		Ministry of Road Transport & Highways	Roads & Highways	3	1184.27 1184.27	1010.59
	PAN India	Department of Telecommunications	Telecommunication	4	50756.69 39833.5	29992.49
Total				9	52745.96	31642.63
20	PAN India	Department of Telecommunications	Telecommunication	2	22819.69 22819.7	21099.62
		Total		2	22819.69	21099.62
21	Madhya Pradesh	Department of Higher Education	Education	1	496.28 496.28	97.35
		Department of Telecommunications	Telecommunication	3	3883.82 2718.14	1021.96

Ongoing Projects State-Wise

JULY 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
21	Madhya Pradesh	Department of Water Resources, River Development & GR	Water Resources	3	23010.18 23323	11615.84
		Ministry of Coal	Coal	15	34550.26 34550.3	3976.50
		Ministry of Health & Family Welfare	Healthcare	2	650 650	268.91
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	14442.2 14442.2	9592.71
			Waste & Water	3	880.74 941.16	823.99
		Ministry of Mines	Metals & Mining	1	1856.36 3800	1018.09
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	45159 45159	6645.20
		Ministry of Power	Electricity Generation	1	20446 20446	2329.76
			Transmission & Distribution	10	46260.32 46260.3	9591.94
		Ministry of Railways	Railways	15	43653.55 70970.2	52665.45
		Ministry of Road Transport & Highways	Roads & Highways	55	39600.27 37330.9	14827.38
	PAN India	Department of Telecommunications	Telecommunication	5	115187.69 55864.5	79194.26
Total				118	390076.67	193669.34
22	Maharashtra	Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1977.02
		Department of Water Resources, River Development & GR	Water Resources	6	10857.15 20187.1	22101.43
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	399.77
		Ministry of Coal	Coal	26	12900.3 12900.3	3469.21
		Ministry of Health & Family Welfare	Healthcare	1	189 189	113.40
		Ministry of Housing & Urban Affairs	Urban Public Transport	9	60255.66 74569.4	39453.57
			Waste & Water	1	194.2 194.2	136.56
		Ministry of Labour and Employment	Healthcare	2	455.06 456.83	332.68
		Ministry of Petroleum & Natural Gas	Energy Storage	2	764.49 872.81	661.86
			Oil & Gas	9	35711.03 39788.3	13478.12
		Ministry of Power	Transmission & Distribution	4	29246 29246	3092.53
		Ministry of Railways	Railways	25	194304.74 292644	259927.70
		Ministry of Road Transport & Highways	Roads & Highways	89	72485.45 75034.9	30478.97
	PAN India	Department of Telecommunications	Telecommunication	4	110244.69 50921.5	78632.13
Total				182	535255.42	454254.95
23	Manipur	Department of Sports	Education	1	906.47 611.74	577.32
		Department of Water Resources, River Development & GR	Water Resources	1	1449.44 1822.24	1848.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499 499	212.17
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Railways	Railways	1	14323 21886	16931.50
		Ministry of Road Transport & Highways	Roads & Highways	30	10790.98 10791	7546.54
	PAN India	Department of Telecommunications	Telecommunication	5	111412.69 52089.5	78755.41
Total				40	144492.91	111448.86
24	Meghalaya	Department of Higher Education	Education	1	494.52 429.7	377.82
		Department of Telecommunications	Telecommunication	1	971.96 180.46	167.23
		Ministry of Health & Family Welfare	Healthcare	1	189 189	170.10
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Railways	Railways	1	1304.62 1432.14	1272.35
		Ministry of Road Transport & Highways	Roads & Highways	12	6148.96 5995.63	2161.18
	PAN India	Department of Telecommunications	Telecommunication	5	111012.69 51689.5	78632.13
Total				22	125233.08	88358.56
25	Mizoram	Department of Higher Education	Education	1	474.23 474.23	167.55
		Ministry of Petroleum & Natural Gas	Energy Storage	1	225.71 225.71	32.45



Ongoing Projects State-Wise

JULY 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
25	Mizoram	Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Road Transport & Highways	Roads & Highways	16	11295.22 11295.2	4230.35
	PAN India	Department of Telecommunications	Telecommunication	5	111012.69 51689.5	78632.13
	Total			24	128119.18	88640.23
26	Nagaland	Department of Higher Education	Education	1	275.63 275.63	263.25
		Ministry of Health & Family Welfare	Healthcare	1	325 325	155.00
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	227.62 227.62	28.03
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Railways	Railways	1	6663 15310.2	6719.53
		Ministry of Road Transport & Highways	Roads & Highways	17	5178.71 5732.76	2189.30
	PAN India	Department of Telecommunications	Telecommunication	5	111412.69 52089.5	78755.41
Total			27	129193.98	93688.27	
27	Odisha	Department of Higher Education	Education	3	1882.56 1496.33	1029.25
		Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1977.02
		Department of Water Resources, River Development & GR	Water Resources	3	4612.34 12314.5	13941.88
		Ministry of Coal	Coal	12	36569.58 34261.3	14209.97
			Electricity Generation	1	27212.96 27213	3574.21
		Ministry of Labour and Employment	Healthcare	1	164.6 164.6	16.44
		Ministry of Mines	Metals & Mining	3	5967 8121.17	6247.75
		Ministry of Petroleum & Natural Gas	Oil & Gas	4	16925.45 14903.5	9699.36
		Ministry of Ports, Shipping and Waterways	Shipping	1	3004.63 3004.63	2261.12
		Ministry of Power	Electricity Generation	2	22974.75 23674	7597.51
			Transmission & Distribution	2	3065.19 3065.19	334.50
		Ministry of Railways	Railways	25	33809.94 44008.9	27438.01
		Ministry of Road Transport & Highways	Roads & Highways	38	24703.36 27354	15008.66
		Ministry of Steel	Steel	5	5160.31 5160.31	1654.92
	PAN India	Department of Telecommunications	Telecommunication	5	111957.69 52634.5	78632.13
Total			108	305157.53	183622.73	
28	PAN India	Department of Telecommunications	Telecommunication	3	65496.13 17096.1	49652.90
	Puducherry	Department of Higher Education	Education	1	618.34 544.34	543.74
		Ministry of Railways	Railways	1	713 1748.55	1267.74
		Ministry of Road Transport & Highways	Roads & Highways	4	7027.6 7051.29	4116.96
	Total			9	73855.07	55581.34
29	PAN India	Department of Telecommunications	Telecommunication	5	111489.69 52166.5	78632.13
	Punjab	Department for Promotion of Industry & Internal Trade	Real Estate	1	1367.72 1367.72	0.00
		Department of Higher Education	Education	2	559.3 597.85	392.26
		Department of Water Resources, River Development & GR	Water Resources	2	3727.07 5177.86	4566.06
		Ministry of Health & Family Welfare	Healthcare	2	650 924.75	52.04
		Ministry of Housing & Urban Affairs	Waste & Water	2	545.53 553.64	374.66
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	2094.36 2094.36	1626.77
		Ministry of Power	Transmission & Distribution	1	5969 5969	1969.77
		Ministry of Railways	Railways	3	2490.42 4571.26	3104.15
		Ministry of Road Transport & Highways	Roads & Highways	32	41876.31 46755.2	27315.20
		Total			53	170769.4
30	PAN India	Department of Telecommunications	Telecommunication	5	113083.69 53760.5	78916.06
	Rajasthan	Department for Promotion of Industry & Internal Trade	Real Estate	1	921.66 921.66	0.00



Ongoing Projects State-Wise

JULY 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
30	Rajasthan	Department of Telecommunications	Telecommunication	1	421.65 228.94	152.96
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	2874 2874	1016.83
		Ministry of Coal	Electricity Generation	1	4147.07 4147.07	249.95
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	14222.55 14222.5	128.16
		Ministry of Petroleum & Natural Gas	Energy Storage	1	461.05 461.05	252.18
			Oil & Gas	3	10958 10958	6842.71
		Ministry of Power	Transmission & Distribution	17	72773 72773	25423.68
		Ministry of Railways	Railways	17	80486.99 157462	151325.18
		Ministry of Road Transport & Highways	Roads & Highways	22	16241.58 14357.5	7952.07
	Total			74	316591.24	272259.78
31	PAN India	Department of Telecommunications	Telecommunication	5	110404.69 51081.5	78632.13
	Sikkim	Department of Higher Education	Education	2	999.82 951.31	575.56
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 323.26	87.61
		Ministry of Health & Family Welfare	Healthcare	1	250 635.21	667.21
		Ministry of Power	Electricity Generation	2	6686.33 7576.15	6290.84
			Transmission & Distribution	1	4754.42 9129.32	8141.52
		Ministry of Railways	Railways	1	7877 11775	11090.47
		Ministry of Road Transport & Highways	Roads & Highways	8	3158.89 3287.17	2016.67
	Total			21	134454.41	107502.01
32	PAN India	Department of Telecommunications	Telecommunication	3	49135.69 38212.5	29822.44
	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1207 1207	331.85
		Ministry of Health & Family Welfare	Healthcare	1	1264 2021.51	540.92
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	63246 63246	34698.00
		Ministry of Mines	Metals & Mining	1	166 166	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	2	1507 2561	1588.83
			Oil & Gas	4	38385 46153	6918.16
		Ministry of Power	Transmission & Distribution	1	548 548	208.24
		Ministry of Railways	Railways	10	10489.69 16541	8194.52
		Ministry of Road Transport & Highways	Roads & Highways	41	54094.87 51067.6	24379.55
Total			65	220043.25	106817.51	
33	PAN India	Department of Telecommunications	Telecommunication	4	110244.69 50921.5	78632.13
	Telangana	Department for Promotion of Industry & Internal Trade	Real Estate	1	2360 2360	42.89
		Department of Higher Education	Education	1	262 262	223.65
		Department of Telecommunications	Telecommunication	2	3462.17 2489.2	869.00
		Department of Water Resources, River Development & GR	Water Resources	3	10268.14 21620	10303.64
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	399.77
		Ministry of Coal	Coal	7	2986.57 2986.57	1806.96
		Ministry of Health & Family Welfare	Healthcare	1	1028 1365.95	1028.94
		Ministry of Housing & Urban Affairs	Construction	1	644 644	188.69
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	215 215	46.87
		Ministry of Power	Electricity Generation	1	29344.85 29344.8	732.96
			Transmission & Distribution	1	1368 1368	1258.56
		Ministry of Railways	Railways	4	4811.31 4991.77	1680.40
		Ministry of Road Transport & Highways	Roads & Highways	47	35259.83 37868.8	14223.92
Total			75	202755.04	111438.38	



Ongoing Projects State-Wise

JULY 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
34	PAN India	Department of Telecommunications	Telecommunication	5	111012.69 51689.5	78632.13
	Tripura	Ministry of Petroleum & Natural Gas	Oil & Gas	2	9474.33 9396.51	7089.31
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Road Transport & Highways	Roads & Highways	9	6260.76 6260.76	2085.98
	Total			17	131859.11	93385.17
35	PAN India	Department of Telecommunications	Telecommunication	4	110244.69 50921.5	78632.13
	Uttar Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	658 658	75.63
		Department of Higher Education	Education	1	246 246	212.35
		Department of Telecommunications	Telecommunication	5	10808.82 9643.14	1523.96
		Department of Water Resources, River Development & GR	Waste & Water	2	1532.96 1532.96	243.43
			Water Resources	2	22090.67 25447.2	13106.60
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3949.13 3949.13	1371.28
		Ministry of Coal	Coal	2	1328.09 1328.09	1296.79
		Ministry of Housing & Urban Affairs	Urban Public Transport	4	27511.5 27511.5	15831.48
			Waste & Water	2	704.2 734.95	659.17
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11068.45 11068.5	8812.56
			Oil & Gas	4	17302.12 17302.1	1015.27
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	4187.19
		Ministry of Power	Electricity Generation	2	55553 55553	4843.21
			Transmission & Distribution	5	36697.81 36697.8	5590.77
		Ministry of Railways	Railways	24	106265.18 181398	156187.03
		Ministry of Road Transport & Highways	Roads & Highways	104	125106.38 119103	48682.48
	Total			168	536436.18	342271.33
36	PAN India	Department of Telecommunications	Telecommunication	5	112065.69 52742.5	78842.00
	Uttarakhand	Department for Promotion of Industry & Internal Trade	Real Estate	1	1265.37 1265.37	0.00
		Department of Higher Education	Education	1	650.85 650.85	401.56
		Department of Water Resources, River Development & GR	Water Resources	1	2584.1 2584.1	1307.15
		Ministry of Health & Family Welfare	Healthcare	2	650 1093.89	823.09
		Ministry of Housing & Urban Affairs	Real Estate	1	150.97 206	59.51
		Ministry of Labour and Employment	Healthcare	1	102.4 297.63	340.30
		Ministry of Power	Electricity Generation	2	6838.35 17312.4	13660.50
		Ministry of Road Transport & Highways	Roads & Highways	38	21871.56 20587.5	8267.01
	Total			52	146179.29	103701.12
37	PAN India	Department of Telecommunications	Telecommunication	5	111918.69 52595.5	78855.54
	West Bengal	Department of Higher Education	Education	1	500 442	418.86
		Department of Telecommunications	Telecommunication	2	3462.17 2489.2	869.00
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 154.73	102.04
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1877.3 1877.3	701.82
		Ministry of Coal	Coal	10	12282.26 12282.2	2100.14
		Ministry of Mines	Construction	1	255.37 255.37	98.94
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 12407	11168.49
			Oil & Gas	7	6157.65 7192	4817.76
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	4187.19
		Ministry of Power	Electricity Generation	3	20091.84 21644.6	5102.41
			Transmission & Distribution	2	751.63 751.63	150.06
		Ministry of Railways	Railways	12	36323.48 44617.8	22644.46

Ongoing Projects State-Wise

JULY 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
37	West Bengal	Ministry of Road Transport & Highways	Roads & Highways	22	14834.57 14244.7	8011.03
		Ministry of Steel	Steel	8	8439.03 8439.03	2348.58
		Total		78	232645.9	141576.32




Table 3: Completed Projects



Completed Projects During Month						JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
	Department of Water Resources, River Development & GR					
	Water Resources					
1	Rajiv Bhima Lift Irrigation Scheme (Irrigation and CAD-TG) 701406	Telangana	04/2007 (01/2008)	06/2026 (12/2019) (03/2026)	1402 (2509.66)	1839.76
	Total (1)				1402	1839.76
	Ministry of Housing & Urban Affairs					
	Waste & Water					
2	Pune Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) 702851	Maharashtra	03/2017 (07/2017)	07/2026 (03/2023) (08/2026)	235.95 (-)	220.77
	Total (1)				235.95	220.77
	Ministry of Petroleum & Natural Gas					
	Energy Storage					
3	Srikakulam Angul Gas Pipeline Project (Gas Authority of India Limited [GAIL]) 701343	Odisha	09/2019 (09/2019)	07/2026 (07/2026) (07/2026)	2658.34 (2810)	2315.2
4	New Mundra Panipat Crude Oil Pipeline (Indian Oil Corporation Limited [IOCL]) 400078	Rajasthan	12/2021 (12/2021)	07/2026 (12/2024) (07/2026)	9028 (9028)	7554.56
	Total (2)				11686.34	9869.76
	Ministry of Power					
	Transmission & Distribution					
5	Transmission System for Evacuation of power from Potential RE Zone in Khavda Area of Gujarat under phase IV 7GW-Part E4 (Power Grid Corporation of India Limited [POWERGRID]) 611966	Maharashtra	11/2023 (11/2023)	06/2026 (07/2025) (05/2026)	224.41 (-)	224.41
	Total (1)				224.41	224.41
	Ministry of Road Transport & Highways					
	Roads & Highways					
6	Tadipatri Bypass Km 0000 to Km 6285 of 4-Lane on NH-67 in Anantapuramu district of AP state under NHO on EPC Mode under Annual Plan 2022-23 (MoRTH) 617949	Andhra Pradesh	03/2023 (03/2024)	01/2026 (03/2026) (01/2026)	159.66 (-)	75.74
7	Rehabilitation and Upgrading of NH-707 OLD 72-B Package - 2 Hewna to Ashyari (MoRTH) 618051	Himachal Pradesh	04/2020 (03/2021)	12/2025 (03/2023) (12/2025)	242.8 (220.95)	145.49
8	Upgradation of Dindori-Sagartola-kabichabutra MP-CG border section of NH -45 from km 000Design to km 77.00 Design to Two lane with paved shoulder configration along with one time improvement in 04 nos. of bypaased built-up areas in a total length of 9.1 km in the state of Madhya Pradesh on EPC mode. (MoRTH) 617915	Madhya Pradesh	01/2022 (09/2023)	03/2026 (09/2025) (03/2026)	329.14 (319.09)	204.39
9	Upgradatiobn and Rehabilitation of Section of NH 361 F from Parli 00/000 to Gangakhed 30/400 to Two Lanes with paved shoulder / Four lane configurations on EPC mode in the State of Maharashtra. (MoRTH) 618136	Maharashtra	03/2021 (02/2022)	08/2025 (09/2023) (08/2025)	224.44 (-)	268.45
10	Rehabilitation and Upgradation of Satana to Mangrul Chandwad Section of NH752 G Design Ch Km 64.000 to Ch Km 101.140 two lane with paved shoulder/four lane configuration in the state of Maharashtra on EPC mode. (MoRTH) 618175	Maharashtra	03/2022 (05/2023)	02/2026 (05/2025) (02/2026)	428.8 (-)	184.63
11	Beawer Gomti 4LPS from km 58.245 to km 108.600 Pkg-I (MoRTH) 617887	Rajasthan	12/2020 (10/2021)	12/2025 (10/2023) (12/2025)	379.23 (-)	206.48
12	Widening to Two with Paved shoulders from Km 59.500 to Km 132.033 of Manneguda- Ravunapally section of NH-163 Erstwhile SH-4 in the State of Telangana on EPC mode under NH O Annual Plan 2016-17 (MoRTH) 617981	Telangana	03/2017 (05/2017)	10/2024 (05/2019) (10/2024)	359 (-)	724.23
13	Widening and strengthening of existing 2-lane to 2- lane with paved shoulders from km 159/0 to 165/4 and 186/0 to 215/0 of NH-163 on EPC mode int the state of Telangana (MoRTH) 617982	Telangana	01/2018 (06/2018)	11/2024 (11/2019) (11/2024)	230.03 (-)	383.3
14	Rehabilitation and upgradation of NH-167 from design km 157.707 to 187.723 design length 30.016 km to two lane with paved shoulders of Alinagar- Miryalaguda Sec on EPC mode in the state of Telangana (MoRTH) 617993	Telangana	02/2018 (05/2018)	12/2025 (11/2019) (12/2025)	220.28 (-)	223.79
15	Khammam-Devarapalle Pkg V [4L Access Controlled Greenfield from Gurvaygudem village to Devarapalle village Design Chainage 132664 to 162126 (NHAI) 618749	Andhra Pradesh	12/2020 (09/2022)	05/2026 (09/2024) (05/2026)	711.94 (926.48)	591.01
16	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-28 Ch.756052 to Ch.781282 (NHAI) 618460	Gujarat	09/2020 (11/2021)	04/2026 (11/2023) (04/2026)	1263.38 (1266.98)	935.5
17	Kodinar - Veraval Package VI from km. 221.610 to km. 263.00 of NH-8E & km. 120.900 to km. 121.150 of NH-8D (NHAI) 618833	Gujarat	02/2016 (02/2018)	05/2026 (07/2020) (05/2026)	894.01 (1127.42)	730.06
18	Kagvadar - Una Package-IV (NHAI) 619146	Gujarat	02/2016 (03/2017)	06/2026 (09/2019) (06/2026)	750.53 (955.78)	833.13
19	Dwarka Expressway Pkg-III Delhi/HR Border to Start of RoB Gurugram (NHAI) 618577	Multi-States (Delhi, Haryana)	01/2018 (11/2018)	05/2024 (11/2020) (05/2024)	2228.26 (2298.37)	1775.04

Completed Projects During Month

JULY 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
20	4L Poanta SahebMednipur from Km. 435.65 to km. 458.65 of NH-07Pkg-1 (NHAI) 619291	Multi-States (Uttarakhand, Himachal Pradesh)	03/2022 (05/2023)	03/2026 (05/2025) (03/2026)	524.54 (657.32)	321.15
21	4L of Padalur - Trichy section from km. 285.00 to km. 325.00 of NH - 45 Pkg VI-C (NHAI) 619113	Tamil Nadu	12/2005 (11/2006)	02/2026 (05/2009) (02/2026)	555.8 (235.8)	235.51
22	Aligarh-Kanpur Pkg I [Aligarh-Bhadwas] (NHAI) 618692	Uttar Pradesh	03/2018 (02/2019)	12/2024 (06/2022) (12/2024)	1226.64 (2069.6)	1359.15
23	Construction of Balance work of 2-Lane with PS of Joram-Koloriang Road NH-713 on EPC basis from Design Km 44.989 to Km 61.547 Existing Km 50.050 to Km 70.000 in the state of Arunachal Pradesh under SARDP-NE Pkg-3 (NHIDCL) 618432	Arunachal Pradesh	02/2017 (10/2020)	09/2024 (04/2022) (09/2024)	228.72 (-)	205.68
24	Rehabilitation and upgradation to 2 Lane with Paved shoulder of Economic corridor of NH-6 from Design chaiange Km 0.000 to Km 13.510 Package-1 in the state of Mizoram under Bharatmala Pariyojana on EPC mode (NHIDCL) 618342	Mizoram	03/2020 (07/2020)	06/2024 (06/2022) (06/2024)	206.9 (-)	214.51
25	Rehabilitation and Up gradation to 2-lane with paved shoulder of Keifang Section Economic Corridor of NH-06 from Existing Chainage Km 30050 Keifang to Km 50360 Keifang, Design Chainage Km 27400 to Km 45040 PkgIII in the State of Mizoram under Bharatmala Pariyojna on EPC Mode Seling-Dulte - III (NHIDCL) 618343	Mizoram	03/2020 (07/2020)	10/2024 (06/2022) (10/2024)	292.23 (-)	298.93
Total (20)					11456.33	9916.17

Note: Cumulative Expenditure is as per last reporting by Central Line Ministries/ Departments on the CRIP portal, this may not be the actual completion cost.




Table 4: Newly Added Projects



Newly Added Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
	Department for Promotion of Industry & Internal Trade				
	Real Estate				
1	Gaya Integrated Manufacturing Cluster IMC in Bihar (National Industrial Corridor Development Corporation) (707420)	Bihar	08/2024 (04/2026)	04/2029 (-)	1339.02 (-)
2	IMC Rajpura - Patiala Development Project (National Industrial Corridor Development Corporation) (701662)	Punjab	08/2024 (03/2026)	09/2028 (-)	1367.72 (-)
3	Development of IMC Khurpia Farms under AKIC Project (National Industrial Corridor Development Corporation) (701661)	Uttarakhand	08/2024 (03/2026)	09/2028 (-)	1265.37 (-)
	Total (3)				3972.11
	Department of Telecommunications				
	Telecommunication				
4	Amended BharatNet Program - J&K, LAD (Department of Telecommunications) (437130)	PAN India	08/2023 (06/2025)	06/2028 (-)	1621 (-)
5	Amended BharatNet Program - MGH, MZM, TRP (Department of Telecommunications) (462136)	PAN India	08/2023 (04/2025)	04/2029 (-)	768 (-)
6	Amended BharatNet Program - HP (Department of Telecommunications) (476006)	PAN India	08/2023 (02/2025)	02/2028 (-)	1292 (-)
7	Amended BharatNet Program - KL (Department of Telecommunications) (660056)	PAN India	08/2023 (06/2025)	06/2028 (-)	765 (-)
8	Amended BharatNet Program - UKD (Department of Telecommunications) (665021)	PAN India	08/2023 (05/2025)	05/2028 (-)	1821 (-)
9	Amended BharatNet Program - BR (Department of Telecommunications) (914467)	PAN India	08/2023 (03/2025)	03/2028 (-)	1550 (-)
10	Amended BharatNet Program - RJ (Department of Telecommunications) (938832)	PAN India	08/2023 (03/2026)	03/2029 (-)	2839 (-)
11	Amended BharatNet Program - SKM (Department of Telecommunications) (946208)	PAN India	08/2023 (06/2026)	06/2029 (-)	160 (-)
12	Amended BharatNet Program - ARP, NGL, MNP (Department of Telecommunications) (976009)	PAN India	08/2023 (06/2025)	06/2028 (-)	1168 (-)
13	Amended BharatNet Program - OD (Department of Telecommunications) (317725)	PAN India	08/2023 (07/2026)	07/2029 (-)	1713 (-)
14	Amended BharatNet Program - HR (Department of Telecommunications) (124199)	PAN India	08/2023 (03/2026)	03/2029 (-)	837 (-)
15	Amended BharatNet Program - PB (Department of Telecommunications) (171218)	PAN India	08/2023 (02/2025)	02/2028 (-)	1245 (-)
16	Amended BharatNet Program - MP, DD and DNH (Department of Telecommunications) (175860)	PAN India	06/2023 (05/2025)	05/2028 (-)	4943 (-)
17	Amended BharatNet Program - WB & ANI (Department of Telecommunications) (210914)	PAN India	08/2023 (02/2025)	02/2028 (-)	1674 (-)
18	Amended BharatNet Program - AS (Department of Telecommunications) (240484)	PAN India	08/2023 (03/2026)	03/2029 (-)	832 (-)
19	BharatNet Phase-II (Department of Telecommunications) (547243)	PAN India	07/2017 (11/2017)	05/2023 (-)	22174.56 (-)
	Total (16)				45402.56
	Ministry of Housing & Urban Affairs				
	Urban Public Transport				
20	Jaipur Metro Rail Project Phase 2 (Pralhadpura to Todi Mod) (Jaipur Metro Rail Corporation) (245986)	Rajasthan	04/2026 (04/2026)	10/2031 (-)	13037.66 (-)
	Total (1)				13037.66
	Ministry of Power				
	Electricity Generation				
21	Meja Thermal Power Project, Stage-II , (3x800 MW) (National Thermal Power Corporation [NTPC]) (298178)	Uttar Pradesh	06/2026 (06/2026)	12/2032 (-)	38358 (-)
	Total (1)				38358
	Ministry of Road Transport & Highways				
	Roads & Highways				
22	Upgradation of Existing Two Lane Carriageway to Two Lane Carriageway with Paved Shoulder from Ch. 665686 Existing Km. 665.686 in Khanpur Village in Vansda Taluka to Ch. 710470 Existing Km. 710.483 in Karvad Village in Vapi Taluka Length 44.784 Km Section of NH-56 in the State of Gujarat on EPC Mode (NHA) (619297)	Gujarat	02/2026 (07/2026)	07/2028 (01/2027)	647.2 (-)
23	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Chatra to junction with NH-100 in Deoria village from km 222.000 to km 253.000 Pkg -9 (NHA) (618731)	Jharkhand	03/2023 (07/2026)	07/2028 (07/2028)	1418.16 (-)

Newly Added Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
24	Capacity Augmentation in the stretch of DhulePimpalgaon section of NH60 Km. 261.720 to Km. 380.000 by Construction of Slip/Service Road on either side at various locations total length 30.30 Km LHSRHS and Flyover 2 x 30m at Sawadgaon Phata Km. 310.415 (NHAI) (619043)	Maharashtra	12/2025 (04/2026)	10/2026 (10/2027)	341.63 (-)
25	Widening and Strengthening of existing S/L, I/L, & D/L to 2 Lane with PS from Km 256/455 to 256/503, 256/820 to 256/960, 265/760 to 266/010, 266/010 to 266/800, 270/975 to 271/055, 276/460 to 276/560, 276/560 to 276/700, 276/700 to 277/480, 285/780 to 288/290, 288/290 to 291/050 and construction of 3 Nos. of Bypass from Km 266/800 to 267/300, 270/025 to 270/975, & 284/700 to 285/780 on NH-53 under NHO in Annual Plan 2022-23 for the State of Odisha. (MoRTH) (617918)	Odisha	03/2023 (06/2026)	12/2027 (-)	174.21 (-)
26	Rehabilitation & Upgradation of Thorrur to Nehru Nagar section to Two Lane with Paved shoulders from Km 109/420 to Km 178/500 of NH 930P in the state of Telangana on EPC mode under Annual Plan 2022-2023 (MoRTH) (619265)	Telangana	01/2025 (07/2026)	07/2028 (07/2028)	675.45 (-)
27	Realignment of Rudrapur-Kathgodam Section of NH-87 New NH-109 From Design Chainage 000 Existing Chainage Km.54050 To Design Chainage 7875 Existing Chainage Km.61550 Due To Proposed Expansion Of Pantnagar Airport in the state of Uttarakhand. (NHAI) (619221)	Uttarakhand	08/2025 (06/2026)	09/2027 (09/2027)	252.97 (-)
Total (6)					3509.62
Ministry of Steel					
Steel					
28	Super accelerated cooling system (Uniform Cooling) for high strength plates in Plate Mill at BSP (Steel Authority of India Limited (SAIL)) (944288)	Chhattisgarh	06/2025 (06/2025)	12/2026 (-)	192.21 (-)
29	Installation of 140 TPH Walking Beam type Reheating Furnace in Plate Mill at BSP (Steel Authority of India Limited (SAIL)) (505491)	Chhattisgarh	02/2026 (03/2026)	03/2028 (-)	268.36 (-)
30	Stamp Charge Battery No.7 Battery Proper at RSP (Steel Authority of India Limited (SAIL)) (738679)	Odisha	09/2024 (10/2024)	03/2028 (-)	2584.41 (-)
31	Stamp Charge Battery No.12 By-product Plant at RSP (Steel Authority of India Limited (SAIL)) (834015)	Odisha	09/2024 (10/2024)	03/2028 (-)	1140.07 (-)
32	Stamp Charge Battery No.7 Coke Dry Cooling Plant at RSP (Steel Authority of India Limited (SAIL)) (478482)	Odisha	02/2026 (02/2026)	08/2028 (-)	1064.55 (-)
33	New Product Testing Laboratory for NPM, SPP & NHSM at RSP (Steel Authority of India Limited (SAIL)) (635651)	Odisha	06/2025 (07/2025)	08/2027 (-)	155.26 (-)
34	Implementation of Treatment System-2 Under ZLD at RSP (Steel Authority of India Limited (SAIL)) (589703)	Odisha	02/2025 (03/2025)	09/2026 (-)	216.02 (-)
35	Stamp Charge Battery No.12 By-product Plant at IISCO Steel Plant (Steel Authority of India Limited (SAIL)) (364934)	West Bengal	01/2025 (02/2025)	07/2028 (-)	999.46 (-)
36	Stamp Charge Battery No.12 Coke Dry Cooling Plant at IISCO Steel Plant (Steel Authority of India Limited (SAIL)) (425828)	West Bengal	01/2025 (02/2025)	07/2028 (-)	706.51 (-)
Total (9)					7326.85




Table 5: Ongoing Projects North Eastern Region



Ongoing Projects of North-East Region

JULY 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (06/2026)	1712 (2520)	2670.23	99.5
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	212.17	53.14
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	06/2026 (06/2027)	323.26 (323.26)	87.61	36.14
	Total (3)				2534.26	2970.01	
	Ministry of Coal						
	Coal						
4	TIKAK EXTENSION OCP (INVALID CO.) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	112.69	89.73
5	TIRAP OCP (INVALID CO.) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.66	5
	Total (2)				449.23	218.35	
	Department of Higher Education						
	Education						
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (08/2024)	592.61 (592.61)	551.3	80
7	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 (153.71)	266.14	97.98
8	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (10/2026)	494.52 (429.7)	377.82	97.5
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (03/2022)	474.23 (474.23)	167.55	4
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	263.25	98
11	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	283.56	38
12	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (10/2026)	314.06 (340.55)	292	96.5
	Total (7)				2990.52	2201.62	
	Department of Sports						
	Education						
13	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081)	Manipur	06/2022 (01/2022)	08/2024 (08/2026)	906.47 (611.74)	577.32	97.5
	Total (1)				906.47	577.32	
	Ministry of Power						
	Electricity Generation						
14	Kalai-II Hydro Electric Project [1200 MW] (THDC India Limited) (619311)	Arunachal Pradesh	04/2026 (04/2026)	10/2032 (-)	14105.83 (14105.8)	189.68	0
15	700 MW Tato-II HE Project (North Eastern Electric Power Corporation Limited) (611716)	Arunachal Pradesh	09/2025 (09/2025)	09/2031 (-)	8146.21 (8146.21)	253.97	6.59
16	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	79.45	5.6
17	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	106.28	6.58
18	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	4921.36	17.93
19	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096)	Multi-States (Assam, Arunachal Pradesh)	09/2003 (01/2005)	09/2010 (03/2027)	6285.33 (26075.5)	26448.07	97.98
20	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (11/2026)	938.29 (1828.11)	1718.16	97.56
21	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (09/2029)	5748.04 (5748.04)	4572.68	73.78
	Total (8)				70789.01	38289.65	

Ongoing Projects of North-East Region							JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Transmission & Distribution							
22	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	3.14	3.89
23	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Nagaland, Mizoram, Manipur, Meghalaya, Tripura, Assam)	12/2014 (03/2016)	12/2018 (03/2027)	5111.33 (6700)	5577.75	99.2
24	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Sikkim, Arunachal Pradesh)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	8141.52	83.9
Total (3)					10075.13	13722.41	
Ministry of Petroleum & Natural Gas							
Energy Storage							
25	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (-)	156.36 (156.36)	114.1	83.8
26	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709755)	Assam	03/2023 (03/2023)	07/2027 (-)	384.04 (384.04)	250.07	87.5
27	LPG Bottling Plant at Mualkhang (Indian Oil Corporation Limited [IOCL]) (617829)	Mizoram	07/2024 (07/2024)	10/2028 (03/2028)	225.71 (225.71)	32.45	34
Total (3)					766.11	396.62	
Oil & Gas							
28	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (Numaligarh Refinery Limited) (709865)	Assam	04/2023 (04/2023)	12/2024 (12/2026)	293.5 (293.5)	81.84	99
29	DCU Revamp Project (Numaligarh Refinery Limited) (709864)	Assam	08/2021 (08/2021)	07/2024 (03/2027)	370 (370)	310.38	80.5
30	Borholla GGS Life Extension Project [BLEP] (Oil and Natural Gas Corporation Limited [ONGC]) (709850)	Assam	09/2023 (09/2023)	05/2026 (03/2027)	198.7 (198.7)	110.99	63.5
31	Pipeline Network Project Rudrasagar (Oil and Natural Gas Corporation Limited [ONGC]) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2027)	481.03 (481.03)	238.83	55.4
32	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Indian Oil Corporation Limited [IOCL]) (709779)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768 (740)	250.84	60.1
33	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Indian Oil Corporation Limited [IOCL]) (709776)	Assam	04/2022 (04/2022)	09/2026 (-)	277 (323.09)	236.16	84.3
34	Group Gathering Station, Lakwagaon (Oil India Limited) (619316)	Assam	10/2025 (10/2025)	10/2027 (-)	495.59 (495.59)	20.04	7.8
35	Coke Drum Structure Package (Numaligarh Refinery Limited) (617836)	Assam	12/2022 (12/2022)	12/2025 (-)	635.28 (635.28)	464.46	72
36	Pipeline Rehabilitation Project, Phase-II (Oil India Limited) (617827)	Assam	12/2024 (12/2024)	12/2029 (-)	680 (680)	13.53	29
37	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Oil India Limited) (616858)	Assam	12/2020 (12/2020)	03/2024 (11/2026)	430.76 (430.76)	348.65	95.9
38	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Oil India Limited) (604863)	Assam	01/2018 (01/2018)	02/2020 (12/2026)	682.9 (726.93)	601.12	94.4
39	Numaligarh Refinery Expansion Project (Numaligarh Refinery Limited) (604791)	Assam	07/2020 (07/2020)	07/2024 (03/2027)	12366 (25313)	20411.19	87
40	Augmentation/ Revamping of Dimapur Depot, Dimapur (Indian Oil Corporation Limited [IOCL]) (709786)	Nagaland	08/2023 (08/2023)	11/2027 (-)	227.62 (227.62)	28.03	43
41	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022 (03/2022)	05/2024 (10/2026)	209.33 (131.51)	81.31	71.3
42	North East Gas Grid (Indradhanush Gas Grid Limited) (701346)	Tripura	04/2020 (04/2020)	03/2024 (03/2028)	9265 (9265)	7008	88.2
Total (15)					27380.71	30205.37	
Ministry of Health & Family Welfare							
Healthcare							
43	Establishment of new GMC West Garo Hills [Tura] (Medical Education, Ministry of Health and Family Welfare) (706989)	Meghalaya	NA (01/1900)	01/1900 (-)	189 (189)	170.1	0
44	Establishment of new GMC Mon (Medical Education, Ministry of Health and Family Welfare) (707067)	Nagaland	NA (01/1900)	01/1900 (-)	325 (325)	155	0
45	Establishment of new GMC Gangtok (Medical Education, Ministry of Health and Family Welfare) (707039)	Sikkim	10/2018 (12/2018)	12/2026 (07/2026)	250 (635.21)	667.21	92
Total (3)					764	992.31	

Ongoing Projects of North-East Region

JULY 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Railways						
	Railways						
46	Lumding-Furkating section 140 km Umbrella work PB57/2019-20/NR (CAO/C-1/NFR NFR mor) (616701)	Assam	02/2024 (04/2025)	02/2028 (-)	2123.7 (2123.7)	200.23	1
47	New Bongaigaon - Goalpara - Guwahati Kamakhya 176 km (CAO/C-III/NFR NFR mor) (705572)	Assam	09/2016 (06/2017)	03/2026 (03/2026)	4060 (4983.94)	3821.96	91
48	Jiribam-Imphal 110 km (CAO/C-III/NFR NFR mor) (705391)	Manipur	10/2003 (04/2009)	12/2026 (06/2029)	14323 (21886)	16931.5	78
49	Murkongselek-Pasighat 26.15 km (CAO/C-II/NFR NFR mor) (705401)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (05/2023)	03/2025 (12/2026)	435 (1334.45)	1057.21	67
50	Dimapur-Kohima 88 km (CAO/C-1/NFR NFR mor) (705392)	Multi-States (Assam, Nagaland)	11/2006 (12/2015)	03/2025 (12/2029)	6663 (15310.2)	6719.53	45
51	Teteliya-Byrnihat 21.5 km (CAO/C-II/NFR NFR mor) (705394)	Multi-States (Meghalaya, Assam)	11/2006 (04/2011)	11/2011 (06/2027)	1304.62 (1432.14)	1272.35	87
52	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Sikkim	10/2009 (05/2010)	05/2015 (12/2027)	7877 (11775)	11090.47	80
	Total (7)				36786.32	41093.25	
	Ministry of Road Transport & Highways						
	Roads & Highways						
53	Construction of 2-lane road of Potin to Pangin section of NH-13 from Km 163.59 to Km 206.66 Package-5 on EPC Mode in the State of Arunachal Pradesh under Arunachal Pradesh Package of Roads and Highways of SARDP-NE [Job No SARDP-NE/P-P/Pkg-A/NH-13/Ar.Pr./PWD/2018-19/116] (MoRTH) (617892)	Arunachal Pradesh	03/2019 (11/2020)	11/2023 (10/2026)	450.65 (450.65)	345.01	96.61
54	Improvement and Widening to 2-lane with Paved Shoulder of NH-13 & 15 Old NH-52 from Existing Km 745.60 Design Km 0.000 to Existing km 770.600 Design Km 24.819 Brahmakund T-junction to Kamlang T-Junction, Existing Length 25.00 Km, Design Length 24.819 Km in the state of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (619248)	Arunachal Pradesh	12/2023 (06/2026)	06/2028 (06/2028)	441.41 (441.41)	25.88	14.69
55	Improvement and Widening to 2 lane with paved Shoulder of NH-15 old NH-52 from Existing Km 770.600 Design Km 24.819 to Existing km 805.750 Design Km 59.885 Kamlang T-Junction to Chowkham, Existing Length 35.150 Km, Design Length-35.066 Km in the state of Arunachal Pradesh on EPC mode Pkg-2 (NHIDCL) (619014)	Arunachal Pradesh	12/2023 (02/2026)	02/2028 (02/2028)	316.73 (316.73)	34.98	15.06
56	Construction of 2-Laning with hard shoulders of Demwe-Brahmakund section of NH-13 from Ch.0.00 km to 18.464 km on EPC under SARDP-NE NHO-NE - Balance Work (NHIDCL) (618445)	Arunachal Pradesh	08/2020 (06/2025)	12/2027 (12/2027)	353.9 (353.9)	26.82	19.57
57	Roing-Hunli Road Greenfield Alignment Project (NHIDCL) (618434)	Arunachal Pradesh	02/2017 (03/2018)	03/2022 (10/2026)	1718.59 (1718.59)	1123.4	82.45
58	Construction of Balance work of 2-Lane with PS of Joram Koloriang Road from existing Km122.600 to km138.00 [Design Km108.724 to Km123.714] in Arunachal Pradesh on EPC Mode under SARDP-NE Pkg-7 (NHIDCL) (618433)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (04/2026)	184.89 (184.89)	156.42	99.69
59	Construction of Intermediate Lane of Pango to Jorging Road from 0000 to Design Km Design Km 40000 Design Length 40.00 Km, Pkg-I, Greenfield Alignment in the State of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (618405)	Arunachal Pradesh	01/2024 (01/2025)	07/2027 (07/2027)	898.19 (898.19)	255.52	39.86
60	Construction of Intermediate Lane Road with hard shoulder from design chainage Km 0.000 to Km 53.040 Existing Length68.500 Km & Total Design length 53.04 km of Tato to Monigong section of NH-913 Frontier Highway on Nafra Bomdila to Vijaynagar along China border in state of Arunachal pradesh on EPC mode (NHIDCL) (618404)	Arunachal Pradesh	12/2023 (05/2025)	11/2027 (11/2027)	625.61 (625.61)	269.64	22.81
61	Construction of Intermediate Lane Road with hard shoulder from design Km 0.000 to Km 17.387 Total length 17.387 km of Hunli to Ithun Bridge section on NH-913 Frontier Highway in State of Arunachal Pradesh on EPC mode under NHO-NE (NHIDCL) (618403)	Arunachal Pradesh	02/2024 (01/2025)	01/2027 (01/2027)	275.5 (275.5)	163.15	56.18
62	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang from Design Km 0.000 to Km 53.000 Design Length 53.000 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Package-I (NHIDCL) (618402)	Arunachal Pradesh	02/2024 (03/2025)	02/2028 (03/2028)	1262.43 (1262.43)	255.45	19.13
63	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang Package-III from design Km 60.000 to Km 121.500 Design Length 61.500 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Pkg-3 (NHIDCL) (618401)	Arunachal Pradesh	02/2024 (07/2025)	07/2028 (07/2028)	1418.67 (1418.67)	93.19	1.7
64	Balance work of 4L of NarimbangloJatinga Junction- Harangajoroad section from Km 0.000 to Km 49.230 of NH-27 (NHAI) (619089)	Assam	03/2022 (01/2023)	01/2026 (08/2026)	1909.98 (2745.74)	1393.08	98

Ongoing Projects of North-East Region							JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
65	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 514.800 to Km 534.800 20.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (619060)	Assam	10/2014 (10/2024)	09/2025 (10/2026)	344.71 (619.7)	56.58	72
66	Construction of 4-Lane Badarpur Bypass from Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village to Design Chainage km 38600 on NH-37 Old NH-44 at Kandigram Chaita Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Pkg-3 (NHIDCL) (619057)	Assam	02/2023 (02/2024)	08/2026 (03/2027)	574.26 (574.26)	330.98	71.09
67	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 501.800 to Km 514.800 13.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-II Road Works (NHIDCL) (619013)	Assam	10/2014 (10/2024)	01/2026 (10/2026)	508.76 (542.87)	111.18	73.88
68	2L with ES of Yagyi - Kalewa section from Milepost 40/0 to Milepost 115/5 in Myanmar (NHAI) (618958)	Assam	12/2017 (05/2018)	06/2023 (07/2027)	1200.14 (1200.14)	0	52
69	Guwahati Ring Road in the State of Assam (NHAI) (618934)	Assam	08/2024 (01/2026)	01/2030 (01/2030)	5729.47 (5729.47)	328.42	0
70	Development of External Trunk Connectivity and Internal Infrastructure Works at Multi Model Logistics ParkMMLP at Jogighopa in the State of Assam on EPC Mode Package-I Road and Utility Works (NHIDCL) (618455)	Assam	02/2020 (09/2020)	04/2022 (09/2024)	693.97 (693.97)	308.85	100
71	Earthwork in Formation, Road Work, Construction of Bridges, Blanketing, P. Way Linking works including Supply of P. Way Fittings and Track Ballast in connection with Construction of Railway Siding from Jogighopa Railway Station to MMLP at Jogighopa from Ch. 00 to 3760 on Item Rate basis Package -3, Railway Siding from Jogighopa Railway Station to MMLP (NHIDCL) (618454)	Assam	02/2020 (12/2020)	06/2022 (09/2024)	693.97 (693.97)	40.17	93.23
72	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 477.000 to Km 490800 13.800 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (618442)	Assam	01/2024 (02/2024)	08/2024 (06/2026)	358.72 (358.72)	100.4	100
73	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 501.800 11.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618441)	Assam	01/2016 (10/2024)	09/2025 (10/2026)	467.79 (476.5)	97.88	87.33
74	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 534.800, under SARDP- NE on EPC Mode in the state of Assam Pkg- IV Structures & Toll Plaza (NHIDCL) (618440)	Assam	01/2016 (10/2024)	10/2025 (10/2026)	187.09 (100.22)	16.71	58.19
75	4-Laning of NH-37 Section between Demow to End of Moran Bypass From Km. 534.800 to Km. 561.700 including Emergency Landing Facility ELF under SARDP-NE, Phase 'A' in the State of Assam on EPC mode (NHIDCL) (618438)	Assam	01/2016 (01/2023)	07/2024 (08/2025)	385.57 (385.57)	680.44	100
76	Construction of Balance Work of 4-Laning of NH-37 Section between End of Moran Bypass to Bogibeel junction near Lapetketa Km. 561.700-Km. 580.875 under SARDP-NE, Phase 'A' in the State of Assam on EPC mode Pkg-I Road works & Toll Plaza (NHIDCL) (618437)	Assam	01/2016 (09/2024)	03/2025 (08/2025)	274.34 (274.34)	116.66	100
77	4-Laning of Jamugurihat to end of Biswanath Chariali By-Pass from Km 182.000 to Km 208.000 of NH-52 on EPC mode in state of Assam under SARDP-NE (NHIDCL) (618436)	Assam	03/2015 (12/2016)	06/2019 (07/2025)	599 (599)	432.62	100
78	Construction of 4-Lane Bridge including approaches over River Brahmaputra between Dhubri on North Bank,Assam and Phulbari on south Bank,Meghalaya on NH-127B under JICA ODA Loan assistance Phase-III (NHIDCL) (618373)	Assam	05/2019 (12/2020)	09/2028 (09/2028)	4997.04 (4997.04)	3081.08	77.14
79	Widening/Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Srirampur near Bhairiguri Village to Kachukhana Harichara Paglagaunj Package-I of Srirampur - Dhubri Section of NH-127B from existing Km 0.000 to Km 28.050 Design Km 0.000 to Km 27.650, Design Length27.650 Km under JICA ODA Loan assistance Phase-V -Balance work (NHIDCL) (618371)	Assam	03/2022 (11/2024)	11/2026 (11/2026)	613.89 (613.89)	384.6	89.5
80	Wideinig & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 96.870 near Jiri River to km 116.550 near Hangrum Package-7 on EPC mode Package7 (NHIDCL) (618354)	Assam	12/2023 (03/2024)	03/2026 (12/2026)	846.82 (846.82)	481.81	90.36
81	Widening & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 116.480 near Hangrum to km 136.500 near Hejaichak Package-8 on EPC mode under NHO-NE Package 8 (NHIDCL) (618353)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	904.04 (904.04)	563.52	85.2
82	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 136.500 near Hejaichak to km 156.489 near P. Leikul Package-9 on EPC mode under NHO-NE Package-9 (NHIDCL) (618352)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	860.37 (614.43)	559.51	87.5

Ongoing Projects of North-East Region							JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
83	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 156.489 near P. Leikul to km 176.410 near Borowapu on EPC mode under NHO-NE Assam portion Package-10 (NHIDCL) (618351)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	890.33 (693.15)	605.43	90.5
84	Widening/Improvement to 4-Lane with Paved Shoulder from km 626030 Nalani hulla Gaon to km 650450 Chotahapjan on existing Tinsukhia -Makum Bypass of NH-15 OLD NH-37 and Strengthening of existing NH-315 OLD NH-38 from Km 0000 Chotahapjan to Km 16900 Bogapani section 2-Lane PS in Assam on EPCMode under NHO-NE Package-3 (NHIDCL) (618340)	Assam	01/2023 (05/2023)	05/2025 (10/2026)	458.59 (458.59)	261.02	88.99
85	Improvement to 4-Lane with Paved Shoulder from existing km 260000 Design Ch.4560 km to existing km Ch.233000 D. Ch.24560 of Silchar near Nutan Dayapur village - Budha Nagar Section Length-20.00 Km of NH-37 under Package Silchar-Jiribam Pkg-1 in the state of Assam on HAM Mode (NHIDCL) (618331)	Assam	01/2024 (01/2025)	01/2028 (01/2028)	957.95 (957.95)	214.64	47.27
86	Widening/Improvement to 4-Lane with Paved Shoulder from KM 38500 to Km 51246 Design Chainage 38500 to 50959 with proposed Daboka Bypass of Daboka-Parokhaowa of NH 29 on EPC under NHO-NE Package-1 (NHIDCL) (618326)	Assam	01/2023 (11/2023)	11/2025 (06/2026)	516.88 (516.88)	322.98	99.7
87	Construction of 4-Lane Panchgram Bypass from Design Chainage km 15500 on NH-37 Old NH-53 at Kalinagar Pt.-I Village to Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Package-2 (NHIDCL) (618308)	Assam	03/2023 (08/2024)	02/2027 (03/2027)	676.18 (728.97)	339.78	57.17
88	Construction of Mangaldoi Bypass NH-15 starting at Ch 26400 and terminating at Ch 41505 under Rangia NH Division L 15.105 Km in the State of Assam. Job No. 15/AS/2021-22/234 (MoRTH) (617895)	Assam	03/2022 (04/2023)	04/2025 (12/2026)	535.03 (535.03)	209.27	76.32
89	Construction of 4 lane Gauripur Bypass Starting bfrom Km 852.56 of NH-31Dumardoha Pt-II and Terminating at Km 862.17 Baladmara via. Khudimari Pt.-II, Fulkumari, Charaldanga, Sajuakuti,Geramari Pt.-III and finally meeting at km 862.17 of NH-17New/ NH-31Old in the State of Assam under EPC Mode Job no. 31/AS/ 2023-24/265 (MoRTH) (617896)	Assam	03/2024 (04/2025)	10/2026 (10/2026)	421.15 (421.15)	0	34
90	Construction of 2 lane Barpeta Bypass from Km 77900Baradi to Km 86150 Deurikuchi Length8.25Km on NH-427 in the state of Assam under EPC ModeJob No.427/AS/2022-23/245 (MoRTH) (618034)	Assam	03/2023 (02/2025)	08/2026 (08/2026)	173.65 (173.65)	11.38	20
91	Widening/Improvement to 4-Laning and Greenfield alignment with Paved shoulder of Silchar-Badarpur Churaibari section of NH-37 & NH-8 from Design chainage 38.600 End point of proposed Badarpur Bypass to Km. 62.800 Start point of proposed Nilambazar/Cheragi Bypass in the state of Assam on HAM Mode Package-4 (NHIDCL) (618309)	Assam	02/2024 (08/2025)	08/2027 (08/2027)	1319.55 (1319.55)	185.17	23.07
92	Widening/Improvement to 4-L of Karimgani - sutarkandi section of NH 37 from design Ch 0020 Start of proposed Karimganj Bypass from NH -8 to design Chainage Km 14380 near Sutarkandi Spur Connectivity to Indo/Bangladesh Border on Silchar-Churaibari in the State of Assam on HAM Mode Package-7 (NHIDCL) (618310)	Assam	02/2024 (02/2025)	02/2027 (02/2027)	791.79 (791.79)	135.54	41.88
93	Widening/Improvement to 4-Lane with Paved shoulder for existing as well as Greenfield alignment of Badarpur Churaibari section of NH-8 from Design chainage 87.700 Chandkhira to Km. 106.500 Churaibari section Assam-Tripura border in the state of Assam on HAM Mode Package-6 (NHIDCL) (618311)	Assam	03/2024 (03/2025)	03/2027 (03/2027)	870 (870)	158.08	40.99
94	Widening/Improvement to 4-Lane with Paved Shoulder from existing road and Greenfield alignment form Design Ch. 62.800 start of proposed Nilambazar/Cheragi Bypass to Design Ch. 87.700 near Chandkhira Village of NH-8 on Silchar-Churaibari in the state of Assam on HAM Mode Package-5 (NHIDCL) (618312)	Assam	02/2024 (04/2025)	10/2027 (10/2027)	1258.13 (1258.13)	186.86	14.04
95	Widening/Improvement of Existing 2 lane to 4-Laning of Karimganj-Silchar section of NH-37 from Design Ch 0.000 near Silchar ISBT to Design Ch 15.970 near Kalinagar Pt I on NH-37 in Assam on HAM Mode Pkg-1 (NHIDCL) (618313)	Assam	03/2024 (09/2025)	09/2027 (09/2027)	1181.55 (1181.55)	178.62	41.26
96	Construction of new 2 Lane with paved shoulders of NH Standards from km 0.080 to km 11.690 L11.610 km in Majuli and from km 19.715 to km 27.484 L 7.769 km in Jorhat on the newly declared NH 715K and construction of 1.10 km flyover on NH-715 with its approaches and service roads L1.10 km, Total Length 20.479 km in the State of Assam Job No. 715K/AS/2023-24/256 (MoRTH) (618159)	Assam	02/2024 (09/2025)	03/2027 (03/2027)	382.1 (382.1)	28.96	6.7
97	Construction of 2 lane Major Bridge including approaches over Brahmaputra between Majuli on North Bank and Jorhat on South Bank from km. 11.690 to km. 19.715 length of bridge 6,812.5m Package - II on NH-715K in the state of Assam Job no. 715/AS/2020-21/213 (MoRTH) (618160)	Assam	03/2025 (12/2025)	12/2027 (12/2027)	1019.17 (1019.17)	0	3.25
98	4-L Bilasipara-Guwahati Package-10 (NHIDCL) (618282)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1264.9 (1264.9)	632.99	64.48
99	4-L Bilasipara-Guwahati Package-9 (NHIDCL) (618283)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1000.27 (1000.27)	505.47	59.78

Ongoing Projects of North-East Region							JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
100	Widening/Improvement to 4-Lane with paved shoulder from Km 99930 to Km 143680 Design Chainage 96000 to 139750 of Paikan to Dhupdhara Sahar of Bilasipura-Guwahati Road on NH-17 in the state of Assam on EPC mode under Bharatmala Pariyojana in Economic Corridors Project Length 43.750km under NHO-NE Package-8 (NHIDCL) (618284)	Assam	03/2023 (12/2023)	12/2026 (12/2026)	1457.59 (1457.59)	962.73	85.87
101	Construction of New 2-Lane Bridge with its approaches from km 0000 to Km 4385 across River Brahmaputra on NH-17 at Jogighopa in Assam on EPC mode (NHIDCL) (618286)	Assam	09/2021 (11/2021)	11/2024 (12/2026)	746.76 (746.76)	435.79	81.07
102	Widening/Improvement to 4-Lane with paved Shoulder from Ch. 25.633 Km to Ch. 52.470 Km Design Ch. 21.850 Km to Ch.48.670 Km for Package-2 of Bilasipura- Guwahati road NH-17 Section Near Mowatari, before Chapar Bypass to Tulungia junction with NH-17 in the state of Assam on HAM mode under NHO-NE Package-2 (NHIDCL) (618287)	Assam	11/2023 (12/2024)	06/2027 (06/2027)	1338.61 (1338.61)	199.15	12.45
103	Widening/Improvement to 4-Lane with Paved Shoulder from Ch.5.580 Km to Ch.25.633 Km Design Ch.0.000 Km to Ch.17.737km Km 901.100 to Km 921.145 of old NH-31 of Bilasipara- Guwahati road NH-17 Section Near Chirakuta to near Mowatari, before Chapar Bypass in the state of Assam on HAM mode Package-1 (NHIDCL) (618288)	Assam	02/2024 (02/2025)	08/2027 (08/2027)	1081.15 (1081.15)	163.12	35
104	Construction and up gradation to 4-Lane of existing two lane with paved shoulder from Hapachara to Tulungia road of NH-117 of existing Km 0.00 to km 14.050 and Design Km 0.000 to km 14.660 under BMP on EPC mode (NHIDCL) (618289)	Assam	03/2020 (06/2020)	12/2022 (03/2026)	224.85 (224.85)	209.95	97.76
105	4-Laning of Dhanehari Lailapur / Vairengte section from Existing Chainage km 12920 to km 43000 of NH 306 Design Chainage km 20000 to km 49360 on Silchar - Vairengte Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode. Project Length 29.360 km under NHO-NE Package-2 (NHIDCL) (618314)	Assam	03/2023 (02/2024)	08/2026 (03/2027)	1716.21 (1716.21)	1057.72	81.65
106	4-Laning of Silchar - Dhanehari section from Existing Chainage km 263800 of NH 37 to km 12920 of NH 306 Design Chainage km 0000 to km 20000 on Silchar - Vairengte - Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode Package-1 (NHIDCL) (618315)	Assam	02/2023 (01/2024)	07/2026 (03/2027)	1256.9 (1256.9)	632.2	59.65
107	Widening/Improvement to 2 lane with earthen shoulder of Choithar to Marrem Khullen section of NH-202 of Imphal Ukhrul Jessami Economic Corridor from Design Chainage km 53.110 to km 95.700 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-5 (NHIDCL) (618306)	Manipur	03/2023 (05/2025)	03/2027 (08/2027)	564.05 (564.05)	173.58	14.5
108	Improvement of existing road to 2 laning with Hard Shoulders of Maram -Peren section Package-1A, length- 22.340Km from Design Chainage 0.000 km to 22.340 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618416)	Manipur	02/2021 (06/2021)	12/2022 (03/2027)	226.32 (226.32)	190.19	75.08
109	Improvement of existing road to 2 laning with Hard Shoulders of Maram-Peren section Package-1B, length- 17.660 km from Design Chainage 22.340 km to 40.000 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618415)	Manipur	02/2021 (06/2021)	12/2022 (03/2026)	188.36 (188.36)	0	100
110	Widening/Improvement to 2 lane with earthen shoulder of Marrem Khullen to Jessami section of NH-202 of Imphal - Ukhrul - Jessami Economic Corridor from Design Chainage km 95.700 to km 140.180 in the State of Manipur on EPC mode under Bharatmala Pariyojana under NHO-NE Package-6 (NHIDCL) (618305)	Manipur	03/2023 (12/2024)	12/2026 (08/2027)	554.66 (554.66)	225.73	26.22
111	Widening/Improvement to 2 Lane with earthen shoulder of Jessami to Laynen bridge Nagaland border section of NH-29 of Imphal -Ukhrul - Jessami Economic Corridor from km 0.000 to km 11.009 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-7 (NHIDCL) (618304)	Manipur	03/2023 (12/2024)	06/2026 (02/2027)	164.89 (164.89)	128.92	28.12
112	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 0.000 to Km 16.900 of NH-202 in the state of Manipur on EPC mode Package-1 (NHIDCL) (618303)	Manipur	03/2020 (07/2020)	06/2022 (08/2026)	222.77 (222.77)	140.9	88.96
113	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 81.870 km to 105.825 km in the State of Manipur on EPC mode under NHO-TSP Package -4 (NHIDCL) (618389)	Manipur	09/2021 (08/2022)	02/2024 (08/2026)	310.76 (310.76)	287.73	97
114	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 50.850 km to 81.870 km in the State of Manipur on EPC mode under NHO-TSP Package -3 (NHIDCL) (618388)	Manipur	09/2021 (07/2023)	01/2025 (12/2026)	315.56 (315.56)	257.41	94.5
115	Construction of 2-laning with Hard shoulder of Ukhrul Tolloi - Tadubi section of NH-102A from Design Chainage km 9450 to km 50850 in the State of Manipur on EPC mode under NHO-NE Package-2 (NHIDCL) (618387)	Manipur	03/2023 (03/2024)	03/2026 (12/2026)	578.98 (578.98)	278.6	80.04
116	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 16.900 to Km 30.970 of NH-202 in the state of Manipur on EPC mode Package-2 (NHIDCL) (618302)	Manipur	03/2020 (07/2020)	06/2022 (08/2026)	256.04 (256.04)	195	98.12

Ongoing Projects of North-East Region							JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
117	Widening/Improvement of existing 2-lane to 4-Lane Divided Highway from Kuraopokpi to Sekmai section of Imphal-Kohima Road Design Ch. km 287.00 to 297.700 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5A (NHIDCL) (618301)	Manipur	09/2020 (02/2025)	08/2026 (12/2026)	228.97 (228.97)	143.26	48.35
118	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Taphukuki to Daili section of Imphal-Kohima road NH-02 Design Chainage from Km 262175 to Km 274610 in the state of Manipur on EPC mode Pkg-4A (NHIDCL) (618300)	Manipur	09/2020 (10/2020)	04/2022 (08/2026)	379.39 (379.39)	314.73	91.39
119	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Daili to Kuraopokpi section of Imphal-Kohima road NH-02 Design Chainage from Km 274610 to Km 287000 in the state of Manipur on EPC mode Pkg-4B (NHIDCL) (618299)	Manipur	09/2020 (12/2024)	06/2026 (01/2027)	268.98 (268.98)	206.28	76.63
120	Widening/Improvement of existing 2-Lane road to 4-Lane Divided Highway from Sekmai to Nilakuthi section of Imphal-Kohima Road Design Chainage from Km 297700 to Km 308729 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5B (NHIDCL) (618298)	Manipur	03/2021 (07/2021)	01/2023 (08/2026)	211.7 (211.7)	272.3	94.71
121	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 starting from km 80.630 near Mandeu to km 96.870 near Jiri River on EPC Mode Package-6 (NHIDCL) (618358)	Manipur	09/2021 (11/2021)	05/2023 (12/2025)	311.18 (311.18)	231.08	86.87
122	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 in Manipur starting from km 54.180 near Azuram to km 80.630 near Mandeu on EPC Mode Package 5 (NHIDCL) (618357)	Manipur	09/2021 (11/2021)	05/2023 (01/2026)	477.86 (477.86)	330.13	84.87
123	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur in the state of Manipur from km 31.430 at Old Tamenglong to km 43.480 ending near Phelong on EPC Mode Package-3 (NHIDCL) (618356)	Manipur	03/2021 (06/2021)	12/2022 (04/2026)	234.08 (234.08)	201.13	98.5
124	Construction of of 2 -Lane with paved shoulders road from Tamenglong-Tousem-Lisang-Mahur Road NH-137 starting near Dialong Village from km 10.000 at Dialong to km 31.430 near Old Tamenglong , near Barak River on EPC Mode Package-2 (NHIDCL) (618355)	Manipur	07/2021 (09/2021)	03/2023 (03/2026)	483.87 (483.87)	375.87	95.28
125	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from Design Chainage km 118850 to km 130000 Package-4A in the State of Manipur on EPC Mode (NHIDCL) (618349)	Manipur	04/2020 (08/2025)	08/2026 (08/2026)	204.12 (204.12)	112.41	25.93
126	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from km 130.000 to km 141.029 Package-4B in the State of Manipur on EPC Mode (NHIDCL) (618348)	Manipur	06/2020 (11/2025)	11/2026 (11/2026)	177.76 (177.76)	97.93	9.17
127	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 13.747 to km 32.835 in the State of Manipur on EPC mode under NHO Package-1B (NHIDCL) (618347)	Manipur	04/2020 (07/2020)	06/2022 (08/2026)	241.52 (241.52)	164.85	100
128	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 32.835 to km 48.587 in the State of Manipur on EPC mode under NHO Package-2A (NHIDCL) (618346)	Manipur	04/2020 (07/2020)	06/2022 (08/2026)	232.99 (232.99)	155.44	100
129	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section from Km 48.587 to Km 69.875 in the State of Manipur on EPC mode under NHO Package-2B (NHIDCL) (618345)	Manipur	06/2020 (08/2020)	08/2022 (08/2026)	365.53 (365.53)	198.28	88.2
130	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from Design Chainage 69.875 Km to 121.769 Km in the State of Manipur on EPC mode Package-3 (NHIDCL) (618344)	Manipur	03/2021 (08/2021)	08/2023 (12/2026)	673.27 (673.27)	563.39	85.84
131	Widening to 2-Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 15.940 km to 33.120 Km Existing Chainage Km 15.946 to Km 33.395 Total length17.180 Km in the State of Manipur on EPC mode PKG-2 - Balance Works & Rectification works (NHIDCL) (618338)	Manipur	03/2021 (03/2025)	03/2026 (10/2026)	195.14 (195.14)	162.71	93.1
132	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 33.000 km to 66.390 Km Existing Chainage from km 33.395 to km 67.496 on EPC Mode in Manipur PKG-3 (NHIDCL) (618337)	Manipur	03/2021 (09/2021)	03/2023 (03/2026)	467 (467)	593.79	86.33
133	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 66.110 km to 101.280 Km Existing Chainage km 67.496 to km 103.557 on EPC Mode in Manipur PKG-4 (NHIDCL) (618336)	Manipur	09/2021 (06/2022)	12/2023 (12/2026)	579.63 (579.63)	408.21	86.05
134	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from Km 101280 Near Khongsang Village to Km 131280 near Puiilon Kambiron Village on EPC Mode in Manipur PKG-5 (NHIDCL) (618335)	Manipur	12/2021 (11/2022)	05/2024 (12/2026)	410.68 (410.68)	382.67	91.02
135	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 131.280 to km 169.570 on EPC mode in Manipur under NHO-TSP PKG-6 (NHIDCL) (618334)	Manipur	12/2021 (02/2023)	02/2025 (12/2026)	504.76 (504.76)	325.89	95.2

Ongoing Projects of North-East Region							JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
136	Widening to 2 lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 169570 Near Nungkao village under Tamenglong District to km 205974 near Jiribam Bridge under Jiribam district under NHO-NE PKG-7 (NHIDCL) (618333)	Manipur	01/2023 (12/2023)	12/2025 (12/2026)	760.16 (760.16)	428.13	92.52
137	Improvement/Widening of New NH-217 Dainadubi-Darugiri section to Two lane with paved shoulder in Meghalaya from design Km 0000 to Km 40840 existing Km 8600 to Km 53000 of Old NH-62 under BMP Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618295)	Meghalaya	03/2023 (03/2025)	03/2027 (03/2027)	705.83 (705.83)	0	46.38
138	Improvement and Widening of National Highway No. 127B Darugiri - Songsak - Williamnagar Junction Section to two lane with paved shoulder from design Km 0000 to Km 36635 Design length 36.635 Km existing Km 112000 to Km 151060 of NH-1278 under Bharatmala Pariyojana Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618294)	Meghalaya	03/2023 (09/2025)	09/2027 (09/2027)	801.07 (801.07)	176.55	26.8
139	Improvement/Widening to 2-L with Paved Shoulder/ 4-Laning of NH-40 section from Km 151330 to Km 163400 design Km 63.530 to Km 71.520 including Dawki Bridge of length 368 m between Shillong-Dawki under JICA ODA Loan assistance Phase-II Pkg-5 -Balance work (NHIDCL) (618374)	Meghalaya	07/2020 (05/2024)	11/2026 (11/2026)	284.21 (284.21)	170.81	42.91
140	Improvement/Widening to 2-Lane with Paved Shoulder from design Km 45.760 to Km 63.530 between Shillong-Dawki under JICA ODA Loan assistance Phase-II - Balance work Pkg-4 (NHIDCL) (618375)	Meghalaya	07/2020 (04/2024)	04/2026 (10/2026)	445.51 (445.51)	42.39	53.43
141	Improvement/Widening to 2-Lane with Paved Shoulder between Shillong-Dawki road up to Bangladesh Border from design Km 10.670 to Km 37.550 under JICA ODA Loan assistance Phase-II -Balance Work-Pkg-2 (NHIDCL) (618376)	Meghalaya	07/2020 (02/2024)	08/2026 (12/2026)	525.67 (525.67)	0	53.21
142	Improvement/Widening to 2-L with Paved Shoulder/4-L from Km 81740 to Km 93490 design Km 0000 to Km 10670 of NH-40 New NH-106 & 206 section & 4-L from design Km 0.00 to Km 0.930 of NH-44 section between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance Work Pkg-1 (NHIDCL) (618377)	Meghalaya	07/2020 (10/2023)	10/2025 (06/2026)	351.12 (351.12)	243.15	100
143	Improvement and Widening two lannig with paved Shoulder of NH 127B from km 31.500 Goeragre to km 63.224 Package-II in state of Meghalaya (MoRTH) (618076)	Meghalaya	12/2023 (05/2025)	05/2027 (-)	504 (350.67)	0	4.5
144	Rehabilitation and up gradation of Nongstoin-Rambrai-Kyrshai road up to Meghalaya-Assam border from Km 0.335 to km 34.039 to 2-Lane under NHO - NE in the State of Meghalaya Package-1 (NHIDCL) (618418)	Meghalaya	09/2021 (05/2022)	05/2024 (12/2026)	359.86 (359.86)	310.07	83.05
145	Construction of 2-Lane with paved shoulders of Shillong Western Bypass starting from NH-06 near Ladumsaw existing Km 60.900 of old NH40 to NH106 old NH 44E Package-III, from km 24700 to km 38256 under SARDP-NE PHASE A in the state of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618419)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	562.48 (562.48)	340.17	52.28
146	Construction of 2 lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw existing km 60.900 of old NH-40 to NH-106 old NH-44E, Package-II km 12800 to km 24700 under SARDP-NE Phase A in the State of Meghalaya on EPC Mode (NHIDCL) (618420)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	686.03 (686.03)	357.32	50.48
147	Construction of 2-Lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw Existing km 60.900 of old NH-40 to NH106 old NH-44E, km 0000 to km 12800 Package-I under SARDP-NE PHASE A in the State of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618421)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	620.3 (620.3)	332.95	74.85
148	Rehabilitation and Up-gradation of Nongstoin Wakhaji section of Project Road Km 0000 to Km 43060 to Intermediate Lane with earthen shoulder under SARDP-NE Phase-A in the State of Meghalaya on EPC mode. Job No- SARDP-NE ong-Don-Maw/MG/2020-21/294 (MoRTH) (617885)	Meghalaya	08/2020 (02/2022)	08/2023 (08/2026)	302.88 (302.88)	187.77	99.62
149	Up-gradation to 2 lane with paved shoutders of Pawlrang - Rulchawm section- of NH-102B of Aizawl - Imphal Economic Corridor from Existing Chainage km 72.030 to km 104.129 including 2.459 km re-alignment section from Tuivai River to Rulchawm connecting km 48.150 of NH-6 [Design Chainage km 68.170 to km 98.579] in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-3 Keifang- Tuivai Pkg-3 (NHIDCL) (619010)	Mizoram	12/2021 (11/2023)	05/2025 (07/2026)	500.88 (500.88)	443.61	99.52
150	Balance work of widening to two laning/re-alignment and geometric improvement from Km. 11000 to Km. 114618 with rectification of damaged stretches and provision of protection works in vulnerable location of NH-44 in the State of Mizoram. (MoRTH) (619321)	Mizoram	10/2025 (05/2026)	05/2028 (-)	170.96 (170.96)	0	2
151	2-laning of Zorinpui - Longmasu section of NH-502A from km 0.000 to km 28.244 in the State of Mizoram on EPC mode under NHO-NE, stretch of IMBR (NHIDCL) (618452)	Mizoram	02/2023 (12/2024)	12/2026 (07/2027)	781.85 (781.85)	48.26	4.71
152	Construction of 2-lane Aizawl Bypass from km 15.200 to km 34.500 Package-3 on Sairang - Phaibawk section of NH-6 in the State of Mizoram under Bharatmala Pariyojna on EPC Mode under NHO-NE (NHIDCL) (618324)	Mizoram	02/2023 (10/2025)	11/2028 (-)	720.72 (720.72)	102.62	15.1

Ongoing Projects of North-East Region							JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
153	Construction of Twin Tube Uni-directional Aizawl Bypass Tunnel of 2.5 km and its approaches of 2.1 km from km 10.600 to km 15.200 on Sarrang - Phaibawk section of NH-6 in the State of Mizoram on EPC Mode under NHO-NE Package-2 (NHIDCL) (618323)	Mizoram	01/2024 (12/2025)	12/2028 (-)	1313.28 (1313.28)	0.11	0
154	Construction of 4-Laning of West Serawlg-Sairang section of NH-6 from Existing Chainage km 142000 to km 158900 Design Chainage km 123400 to km 136260 on Silchar - Vairengte - Sairang road in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-8 (NHIDCL) (618321)	Mizoram	02/2024 (11/2025)	11/2028 (-)	875.79 (875.79)	288.34	13.95
155	Construction of 4-Laning of N. Kawnpui N. Mualvum Mualkhang via Khamrang Village section Package-7 of NH-6 from Existing Chainage km 127200 to km 142000 Design Chainage km 111850 to km 123400 on Silchar - Vairengte - Sairang road in the State of Mizoram on EPC mode (NHIDCL) (618320)	Mizoram	02/2024 (10/2025)	10/2028 (-)	866.32 (866.32)	190.01	18.9
156	4-Laning of Sethawn - N. Kawnpui section Package-6 of NH-6 from Existing Chainage km 107850 to km 126315 Design Chainage km 95500 to km 111850 on Silchar-Vairengte- Sairang road, Vairengte - Sairang Pkg-6 (NHIDCL) (618319)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	595.65 (595.65)	189.39	6.72
157	4-Laning of Kolasib - Sethawn section Package-5 of NH-6 from Existing Chainage km 86000 to km 107850 Design Chainage km 77500 to km 95500 on silchar - vairengte - sairang road under Bharatmala Pariyojna on EPC mode under NHO-NE Vairengte - Sairang Pkg-5 (NHIDCL) (618318)	Mizoram	11/2021 (07/2025)	07/2027 (06/2027)	720.4 (720.4)	259.85	11.86
158	4-Laning of chhimluang-Kolasib from section pkg-4 of NH-306 & NH-6 existing chainage km 59700 to km 86000 design chainage km 61000 to km 77500 on Silchar-vairengte-sairang road in the state of Mizoram under Bharatmala Pariyojna on EPC mode Vairengte - Sairang Pkg-4 (NHIDCL) (618317)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	561.91 (561.91)	223.99	17.12
159	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 339.00 to km 380.00 Siaha on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-8 (NHIDCL) (618383)	Mizoram	09/2019 (03/2020)	09/2023 (06/2026)	637.06 (637.06)	547.01	99.82
160	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 125. 000 to Km 166 Package-3 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-3 (NHIDCL) (618380)	Mizoram	09/2019 (10/2019)	04/2023 (06/2026)	867.09 (867.09)	525.13	97.51
161	4-Laning of Vairengte - Chhimluang section Package-3 of NH-306 from Existing Chainage km 43000 to Km 59700 Design Chainage km 46000 to km 60850 on Silchar - Vairengte- Sairang road in the State of Mizoram under Bharatmala Pariyojna under NHO-NE. Package-1&2 in Assam state (NHIDCL) (618316)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	491.39 (491.39)	238.01	17.86
162	Construction of 2-laning with hard shoulder of Lunglei to Chhumkhum from Design Chainage Km 0.000 to Km 37.420 of NH-302 [Lunglei-Tlabung] Package-A (NHIDCL) (618362)	Mizoram	03/2021 (06/2021)	12/2022 (11/2026)	698.45 (698.45)	553.89	64.78
163	Construction of 2-laning with hard shoulder configuration of Chhumkhum to Tlabung from Design Chainage Km 37.420 to Km 74.950 of NH-302 in Mizoram under Bharatmala Pariyojana on EPC mode [Pkg-B] (NHIDCL) (618363)	Mizoram	06/2021 (07/2021)	01/2023 (12/2026)	740.58 (740.58)	494.49	61.34
164	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 208. 000 to Km 250.000 Package-5 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-5 (NHIDCL) (618379)	Mizoram	09/2019 (10/2019)	04/2023 (06/2026)	752.89 (752.89)	125.64	95.35
165	Widening/Improvement to 4-Lane with Paved Shoulder from km 55000 Nagabang Gamsuk to km 82514 Oyan in the State of Assam and Arunachal Pradesh on EPC mode under Bharatmala Pariyojna of Length 27.514 Km Package-3 (NHIDCL) (618359)	Multi-States (Arunachal Pradesh, Assam)	03/2023 (09/2024)	03/2027 (03/2027)	665.47 (665.47)	380.59	96.7
166	Widening of existing Single lane / Intermediate lane road to 2 lane from Km 101 to Km 125 of NH 61 (MoRTH) (617886)	Nagaland	06/2020 (06/2024)	06/2026 (04/2027)	252.2 (252.2)	0	44.46
167	4-Laning of Balance work of Dimapur-Kohima Road from design km 152.490 to km 166.700 Existing km 156.000 to km 172.900 Excluding Dimapur & Kohima Bypass under SARDP-NE Package-III (NHIDCL) (618328)	Nagaland	03/2016 (09/2023)	09/2025 (09/2026)	562.98 (794.75)	542.85	84.32
168	Widening to Existing single lane /intermediate lane to 2 lane from Km185.00 to Km 220.00 of NH-61 New NH-02 in the state of Nagaland. (MoRTH) (618072)	Nagaland	03/2021 (07/2022)	07/2024 (03/2026)	297.25 (297.25)	155.15	100
169	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-I Design Chainage 0000 Km to 34795 Km, in the State of Nagaland on EPC mode under NH O-NE (NHIDCL) (618364)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	430.24 (430.24)	0	87
170	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-III Design Chainage 69875 Km to 106816 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618365)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	497.18 (497.18)	0	85.67

Ongoing Projects of North-East Region							JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
171	Construction of 2-lane with Paved shoulder of Kohima- Bypass Road Connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29, NH-39New NH-02 from Design Km 32.00 to Design Km 43.454Design Length-11.454 Km in the State of Nagaland under SARDP-NE on EPC Mode Package-IV (NHIDCL) (618290)	Nagaland	07/2020 (10/2020)	04/2022 (12/2026)	202.36 (202.36)	102.32	46.77
172	Construction of 2-lane with Paved shoulder of Kohima-Bypass Road connecting NH- 39 New NH-02, NH150New NH-02, NH7-61 New NH-29 and NH-39 New NH-02 from Design km 21.000 to km 32.268 [Design length11.268 km] in the state of Nagaland Under SARDP-NE on EPC Mode Package- 3 (NHIDCL) (618291)	Nagaland	07/2020 (06/2023)	06/2025 (12/2026)	159.85 (342.29)	128.32	39.54
173	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting New NH-02 and New NH-29 from Design Km 10.500 to design Km 21.000 [Design Length- 10.500 km] including TUNNEL of 500m at Ch. 11.000 in the state of Nagaland Under SARDP-NE on EPC Mode Package-2 (NHIDCL) (618292)	Nagaland	07/2020 (10/2020)	10/2022 (10/2027)	277.44 (277.44)	201.99	69.76
174	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon Road on EPC Basis from existing road Km. 76.640 to Km 98.065 Design chainage Km. 63.800 to Km. 86.835 Design Length-23.035 Km in the state of Nagaland under SARDP-NE PKG-IV Balance work (NHIDCL) (619059)	Nagaland	03/2018 (09/2023)	09/2025 (12/2026)	323.98 (323.98)	147.37	79.03
175	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29 and NH-39New NH-02 from design Km 0.00 to Km 10.500 in the State of Nagaland under SARDP-NE on EPC Mode Package-1 -Balance work (NHIDCL) (618293)	Nagaland	07/2020 (11/2023)	11/2026 (11/2026)	232.29 (350.88)	120.92	27.24
176	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-II Design Chainage 34795 Km to 69875 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618366)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	442.54 (442.54)	0	58.5
177	Balance work of Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 old NH-150 from existing km 98.380 near Chizami vill. to km120.367 Nagaland/Manipur Border [Design km 95.700 to design km 117.200] [Design Length 21.500 km] in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode Package-V under NHO (NHIDCL) (618296)	Nagaland	03/2020 (11/2023)	11/2025 (07/2026)	330.8 (330.8)	268.18	98.39
178	Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 Old NH-150 from existing Km 30.474 Near Kidwema road Chakahabama to existing Km 53.220 Near Kikruma Village Design Km 29.60 to Km 51.50 Design length-21.90 Km in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode under NHO Package-II -Balance work (NHIDCL) (618297)	Nagaland	03/2020 (01/2024)	01/2026 (12/2026)	355.79 (355.79)	0	43.13
179	Construction of 2 laning with Hard shoulder of Peren-Dimapur section on NH 129A from Design Km 146.208 to Km 163.592 Length- 17.384 km in the state of Nagaland on EPC mode under NHO-TSP Package-III (NHIDCL) (618413)	Nagaland	02/2021 (06/2023)	06/2025 (08/2026)	177.77 (199.02)	111.71	95.62
180	Construction of Balance work for 2-lane with hard shoulder of Peren- Dimapur section on NH-129A from Design Km 126.775 to Km 146.208 Length 19.433 Km in the state of Nagaland on EPC mode under NHO-TSP Package-II (NHIDCL) (618414)	Nagaland	01/2021 (09/2023)	09/2025 (09/2025)	258.52 (258.52)	136.09	96.53
181	Construction of 2-lane with hard shoulders of Merangkong-Tamlu-Mon road Wakching Twon portion on EPC basis from existing Chainage Km 59000 to Km 73640 [Design Km. 59000 to Km, 72450] Design length - 13.450 Km under SARDP-NE package-V Balance work (NHIDCL) (618422)	Nagaland	03/2021 (09/2023)	09/2025 (07/2026)	161.73 (161.73)	101.28	99.75
182	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon MTM Road from existing Km 20.456 to Km 41.065 Design Km. 20 to Km. 40.0 Design Length-20.000 Km in the State of Nagaland under SARDP-NE Phase-A Pkg-2 Balance work (NHIDCL) (618423)	Nagaland	03/2018 (08/2023)	08/2025 (03/2026)	215.79 (215.79)	173.12	100
183	Rehabilitation & Upgradation of existing road to 2-lane with paved shoulder including geometric improvement of section from start of Rabangla km33.600 to km58.840 under SARDP-NE Phase A Pkg- IV (NHIDCL) (618450)	Sikkim	07/2020 (10/2020)	05/2022 (12/2026)	292.8 (292.8)	253.63	65.15
184	Construction & Upgradation of existing road to 2-lane with paved shoulder from km27.200 End of Rongli bypass to km37.600New Rolep Bridge of Rhenok-Menla spur NH-717B on EPC Mode under SARDP-NE Phase-A in Sikkim Pkg-II B (NHIDCL) (618449)	Sikkim	07/2020 (10/2020)	04/2023 (09/2026)	230.45 (244.91)	249.71	86.19
185	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Chochenpheri at Km 52000 to Helipad near Menla at Km 82000 of Rhenock-Menla Spur NH-717B Package-IIIA on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618448)	Sikkim	10/2020 (12/2020)	12/2023 (05/2027)	816.79 (786.6)	474.96	64.31
186	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Helipad near Menla at Km 82000 to Menla at Km 94030 of Rhenock-Menla Spur NH-717B Package-IIIB on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618447)	Sikkim	01/2021 (02/2021)	02/2024 (05/2027)	410.6 (379.3)	241.77	82.64
187	Construction & Upgradation of existing road to 2-lane with paved shoulder from New Rolep Bridge at km 37.600 to Chochenpheri at km 52.00 in the section of Rongli to Chochenpheri of NH 717B Pkg-II C (NHIDCL) (618446)	Sikkim	10/2020 (05/2021)	05/2024 (09/2026)	493.42 (478.79)	395.19	79.13

Ongoing Projects of North-East Region							JULY 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
188	Construction of two lane with paved shoulder Gangtok Bypass Road from Ranipool to Burtuk Ch 0.00 Km to 23.316 L23.316 Km in the State of Sikkim (MoRTH) (618071)	Sikkim	10/2021 (05/2022)	05/2024 (12/2026)	385.15 (342.89)	203.36	92
189	Realignment of NH-717A from Design Ch.0.00 Km 77.800 of NH-10 to Design Ch.2.00 Km 3.100 of NH-717A with two lane paved shoulder including Major Bridge of 680 m in the State of Sikkim on EPC Mode-COS work (NHIDCL) (618428)	Sikkim	01/2021 (04/2021)	04/2023 (05/2026)	264.84 (380.94)	70.71	100
190	Construction/Up gradation of Existing road to 2 Lane with Paved Shoulder including Geometric Improvement from Ranipool to Pakyong Balance work from Km 2.000 to 16.167 of NH-717-A on EPC basis under SARDP-NE Phase A in the State of Sikkim (NHIDCL) (618426)	Sikkim	03/2018 (01/2023)	07/2024 (12/2026)	264.84 (380.94)	127.34	87.03
191	Improvement and Widening to 2-lane with paved shoulder of road from design Km 72.000 Pati Chhari to design Km 107.654 Harina Total length 35.654 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-4 (NHIDCL) (618367)	Tripura	01/2024 (12/2024)	12/2026 (06/2027)	726.9 (726.9)	100.25	9.5
192	Improvement and Widening to 2-lane with paved shoulder of road from design Km 36.000 Rangamati to design Km 72.000 Pati Chhari Total length 36.000 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-3 (NHIDCL) (618368)	Tripura	01/2024 (09/2024)	09/2026 (05/2027)	670.9 (670.9)	183.24	14.7
193	Improvement and Widening to 2-lane with paved shoulder of road from existing Km 438.170 Khowai Chowmuhani to existing Km 439.410 South Pulinpur of NH-08 and from design Km 0.000 South Pulinpur to design Km 36.00 near Rangamati of NH 208 on Khowai Teliamura- Harina section Total length 37.24 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-2 (NHIDCL) (618369)	Tripura	01/2024 (09/2024)	09/2026 (03/2027)	657.21 (657.21)	301.86	60.7
194	Improvement and Widening to 2-lane with paved shoulder of road from Km 101.300 to km 127.319 Total Length 26.019 Km i.e. the Khowai Teliamura-Amarpur-Harina-Sabroom section of NH 208 in the state of Tripura on EPC under JICA ODA Loan Phase VI Package-1 (NHIDCL) (618370)	Tripura	01/2024 (07/2024)	07/2026 (04/2027)	431.78 (431.78)	265.36	63.15
195	Rehabilitation and up-gradation of road from design km 25.250 to km 36.460 Total lenth 11.210 km of Kailashahar-Kurti Bridge section on NH-208A to 2-lane with paved shoulder on EPC basis under NHO Package-III- Balance Work (NHIDCL) (618385)	Tripura	02/2020 (09/2024)	03/2026 (03/2026)	174.43 (174.43)	67.1	53.14
196	Melaghar-Srimantapur section on NH-08 Spur from Km 23 to Km 34.500 11.5 Km and overlay from Km 20.30 to Km 22.00 1.7 Km Total Length 13.2 Km (NHIDCL) (618411)	Tripura	01/2023 (05/2023)	11/2024 (10/2026)	195.95 (195.95)	95.54	72.48
197	Improvement & widening of existing NH-08 to 4-lane with Paved Shoulder from Champak Nagar to Khayerpur section design Km 242500 to Km 261610 in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618350)	Tripura	12/2023 (09/2024)	09/2026 (03/2027)	920.66 (920.66)	404.6	48.3
198	Construction of 4-Lane with paved shoulder Agartala bypass Western side, length 25.402 km connecting NH-8 near Amtali to NH-108B near Lembuchhera in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618417)	Tripura	03/2023 (03/2024)	03/2027 (03/2027)	2026.05 (2026.05)	462.34	9.2
199	Rehabilitation and up-gradation of road from km 16.077 to km 43.935 total length 27.858 km of Lalchara-Kanchanpur section via Shivbari on NH-44A to 2 lane with paved shoulder in the state of Tripura on EPC Mode Pkg-2 under BharatMala Pariyojana Manu-Simlung -2 (NHIDCL) (618307)	Tripura	02/2022 (01/2023)	01/2025 (01/2026)	456.88 (456.88)	205.69	54.56
	Total (147)				95134.78	40081.41	
	Department of Telecommunications						
	Telecommunication						
200	Amended BharatNet Program - AS (Department of Telecommunications) (240484)	Assam	08/2023 (03/2026)	03/2029 (-)	832 (832)	83.16	0
201	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (06/2026)	971.96 (180.46)	167.23	99.84
202	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (09/2026)	1255.49 (276.62)	237.98	99.84
203	Amended BharatNet Program - ARP, NGL, MNP (Department of Telecommunications) (976009)	Multi-States (Arunachal Pradesh, Manipur, Nagaland)	08/2023 (06/2025)	06/2028 (-)	1168 (1168)	123.28	0.61
204	Saturation 4G mobile coverage of Uncovered Villages through USOF (Department of Telecommunications [DoT]) (400013)	Multi-States (Arunachal Pradesh, Meghalaya, Sikkim, Mizoram, Assam, Nagaland, Manipur, Tripura)	07/2022 (07/2022)	06/2024 (03/2027)	26316 (15392.8)	8722.82	87.7
205	BharatNet Phase-II (Department of Telecommunications) (547243)	Multi-States (Manipur, Meghalaya, Arunachal Pradesh, Nagaland, Sikkim, Assam, Mizoram, Tripura)	07/2017 (11/2017)	05/2023 (-)	22174.56 (22174.6)	20691.72	93.33

Ongoing Projects of North-East Region

JULY 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
206	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT <i>(BSNL)</i> (709856)	Multi-States (Meghalaya, Manipur, Assam, Mizoram, Nagaland, Sikkim, Arunachal Pradesh, Tripura)	05/2023 (05/2023)	08/2024 (08/2026)	645.13 (645.13)	407.9	92.1
207	BharatNet <i>(Department of Telecommunications [DoT])</i> (706775)	Multi-States (Nagaland, Mizoram, Tripura, Sikkim, Manipur, Meghalaya, Arunachal Pradesh, Assam)	07/2017 (10/2011)	08/2023 (03/2019)	61109 (12709)	48809.69	99.98
208	Amended BharatNet Program - MGH, MZM, TRP <i>(Department of Telecommunications)</i> (462136)	Multi-States (Tripura, Mizoram, Meghalaya)	08/2023 (04/2025)	04/2029 (-)	768 (768)	0	0
209	Amended BharatNet Program - SKM <i>(Department of Telecommunications)</i> (946208)	Sikkim	08/2023 (06/2026)	06/2029 (-)	160 (160)	0	0
	Total (10)				115400.14	79243.78	
	Department of Water Resources, River Development & GR						
	Water Resources						
210	Borolia Irrigation Project <i>(Department of Water Resources, River Development & GR)</i> (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55.44
211	Thoubal Multipurpose Project <i>(Water Resources Department-MN)</i> (701400)	Manipur	04/1997 (04/1997)	12/2019 (12/2026)	1449.44 (1822.24)	1848.17	99
	Total (2)				1705.6	1892.87	




Table 6: All Ongoing Projects



All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport (Airport Authority of India [AAI]) (612786) (-) (-)	Andhra Pradesh	03/2023 (01/2024)	01/2026 (09/2026)	265.91 (265.91)	176.38	80
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. (Airport Authority of India [AAI]) (701107) (-) (-)	Andhra Pradesh	06/2020 (09/2020)	09/2022 (11/2026)	611.80 (824.28)	572.99	89.7
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. (Airport Authority of India [AAI]) (701121) (-) (-)	Andhra Pradesh	12/2022 (08/2023)	08/2025 (08/2026)	347.15 (347.15)	189.48	96
4	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724) (-) (-)	Assam	12/2016 (03/2018)	03/2025 (06/2026)	1712.00 (2520.00)	2670.23	99.5
5	Development of New Civil Enclave at Bihta (Airport Authority of India [AAI]) (612183) (-) (-)	Bihar	08/2024 (04/2025)	03/2027 (-)	1413.00 (1413.00)	15.53	4.15
6	Development of New Civil Enclave and associated works at Darbhanga Airport (Airport Authority of India [AAI]) (612194) (-) (-)	Bihar	07/2024 (07/2024)	07/2026 (11/2026)	911.66 (911.66)	426.22	71.1
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna (Airport Authority of India [AAI]) (701101) (-) (-)	Bihar	10/2018 (10/2018)	05/2026 (08/2026)	1216.90 (1216.90)	1203.48	99.26
8	Development of Keshod Airport. (Airport Authority of India [AAI]) (619054) (-) (-)	Gujarat	01/2024 (07/2025)	01/2027 (-)	363.10 (363.10)	108.64	46.69
9	Development of Dholera International Greenfield Airport , Gujarat (Airport Authority of India [AAI]) (701126) (-) (-)	Gujarat	06/2022 (07/2022)	06/2026 (09/2026)	1305.00 (1551.00)	966.36	88
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. (Airport Authority of India [AAI]) (611047) (-) (-)	Jammu and Kashmir	10/2023 (12/2023)	06/2026 (11/2026)	861.37 (861.37)	370.44	58.35
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport (Airport Authority of India [AAI]) (612787) (-) (-)	Karnataka	06/2023 (01/2024)	01/2026 (09/2026)	320.47 (320.47)	169.11	88.5
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. (Airport Authority of India [AAI]) (612788) (-) (-)	Karnataka	06/2023 (02/2024)	02/2026 (08/2026)	322.45 (322.45)	240.99	97
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 (Airport Authority of India [AAI]) (612789) (-) (-)	Kerala	06/2023 (02/2024)	09/2025 (12/2026)	484.57 (484.57)	242.51	65.8
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh (Airport Authority of India [AAI]) (400010) (-) (-)	Ladakh	07/2018 (09/2018)	09/2021 (07/2026)	480.00 (640.00)	512.55	88
15	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718) (-) (-)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499.00 (499.00)	212.17	53.14
16	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, Jewar [earlier MOPA, without ASMGCS], HIAL & BIAL (Airport Authority of India [AAI]) (611570) (-) (-)	Multi-States (Karnataka, Maharashtra, Telangana, Uttar Pradesh)	12/2020 (10/2022)	09/2025 (08/2026)	500.48 (500.48)	399.77	80
17	Development of New Greenfield Airport at Bundi, Kota Rajasthan. (Airport Authority of India [AAI]) (618977) (-) (-)	Rajasthan	08/2025 (10/2025)	10/2027 (11/2027)	1507.00 (1507.00)	81.41	13.6
18	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. (Airport Authority of India [AAI]) (701127) (-) (-)	Rajasthan	06/2022 (05/2023)	03/2026 (06/2026)	480.00 (480.00)	348.2	100
19	Construction of New Integrated Passenger Terminal Building at Udaipur Airport (Airport Authority of India [AAI]) (701128) (-) (-)	Rajasthan	06/2023 (11/2023)	03/2026 (09/2026)	887.00 (887.00)	587.22	78.71

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
20	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793) (-) (-)	Sikkim	11/2023 (12/2023)	06/2026 (06/2027)	323.26 (323.26)	87.61	36.14
21	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAI]) (611602) (-) (-)	Tamil Nadu	05/2018 (06/2023)	07/2025 (12/2026)	1207.00 (1207.00)	331.85	46
22	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAI]) (701113) (-) (-)	Uttar Pradesh	07/2024 (07/2024)	07/2027 (07/2027)	2869.65 (2869.65)	746.93	33
23	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAI]) (701122) (-) (-)	Uttar Pradesh	06/2024 (07/2024)	07/2026 (11/2026)	579.00 (579.00)	224.58	44.94
24	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAI]) (611495) (-) (-)	West Bengal	08/2024 (09/2024)	03/2027 (03/2027)	1549.00 (1549.00)	548.3	27.9
25	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCB Airport Kolkata. (Airport Authority of India [AAI]) (612791) (-) (-)	West Bengal	03/2023 (12/2023)	10/2025 (08/2026)	328.30 (328.30)	153.52	73.5
	Total (25)				21345.07	11586.47	
	Ministry of Coal						
	Coal						
26	TIKAK EXTENSION OCP (INVALID CO.) (615820) (-) (-)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	112.69	89.73
27	TIRAP OCP (INVALID CO.) (615821) (-) (-)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.66	5
28	PORDA CHIMTAPANI OCP [10 MTY] (SECL - CIL) (400144) (-) (-)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	2310.12 (2310.12)	118.97	11.81
29	BAROUD OC EXPANSION [3.0-10.0M] (SECL - CIL) (400149) (-) (-)	Chhattisgarh	08/2020 (08/2020)	03/2029 (-)	2309.80 (2309.80)	1039.65	55.95
30	DIPKA EXPANSION OCP [40 MTY] (SECL - CIL) (400354) (-) (-)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	5241.40 (5241.40)	2941.23	39.34
31	GEVRA OC [70 MTY] (SECL - CIL) (400424) (-) (-)	Chhattisgarh	03/2016 (03/2016)	03/2023 (03/2027)	11816.40 (11816.40)	7825.46	78.48
32	AMERA OC RCE [1.0 MTY] (SECL - CIL) (613798) (-) (-)	Chhattisgarh	02/2015 (02/2015)	03/2026 (-)	335.97 (335.97)	91.91	42.47
33	AMGAON OC RCE [1.0 MTY] (SECL - CIL) (613799) (-) (-)	Chhattisgarh	07/2015 (07/2015)	03/2026 (-)	316.11 (316.11)	193	78.86
34	JAGANNATHPUR OC RCE PROJECT (SECL - CIL) (613800) (-) (-)	Chhattisgarh	07/2016 (07/2016)	03/2025 (03/2027)	459.49 (459.49)	290.4	96.15
35	MAHAMAYA OCP [1.50 MTY] (SECL - CIL) (613801) (-) (-)	Chhattisgarh	05/2018 (05/2018)	03/2026 (03/2028)	410.26 (410.26)	188.72	54.6
36	KATKONA RO UG MINE (SECL - CIL) (615191) (-) (-)	Chhattisgarh	01/2023 (01/2023)	03/2029 (-)	329.21 (329.21)	62.01	2.01
37	PELMA OC MDO (SECL - CIL) (616234) (-) (-)	Chhattisgarh	10/2022 (10/2022)	03/2033 (-)	1725.04 (1725.04)	16.71	23.75
38	KUSMUNDA OC EXPANSION PROJECT (SECL - CIL) (617287) (-) (-)	Chhattisgarh	11/2024 (11/2024)	03/2030 (-)	4516.88 (4516.88)	847.19	23.75
39	MANIKPUR OC EXPANSION PROJECT (SECL - CIL) (617288) (-) (-)	Chhattisgarh	01/2025 (01/2025)	03/2029 (-)	382.61 (382.61)	138.87	21.29
40	RPR FOR DURGAPUR OCP 10 MTY (SECL - CIL) (619171) (-) (-)	Chhattisgarh	09/2025 (09/2025)	03/2032 (-)	2415.91 (2415.91)	2.99	0.01

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
41	MADANNAGAR OCP 12 MTY - MDO (SECL - CIL) (619172) (-) (-)	Chhattisgarh	12/2024 (12/2024)	03/2033 (-)	1859.19 (1859.19)	0.45	0
42	HURA C OCP (Eastern Coal Fields Limited [ECL]) (400018) (-) (-)	Jharkhand	08/2022 (08/2022)	03/2029 (-)	859.41 (859.41)	455.95	63.3
43	KONAR EXPANSION OCP (CCL - CIL) (400073) (-) (-)	Jharkhand	01/2022 (01/2022)	03/2032 (-)	674.65 (674.65)	175.59	50.78
44	KARO EXPANSION OCP (CCL - CIL) (400074) (-) (-)	Jharkhand	01/2022 (01/2022)	03/2029 (-)	849.31 (849.31)	237.61	23.28
45	SANGHMITRA OC (CCL - CIL) (400136) (-) (-)	Jharkhand	03/2024 (03/2024)	03/2032 (-)	2660.00 (2660.00)	17.03	16.77
46	CHANDRAGUPT OCP (CCL - CIL) (400138) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	973.50 (973.50)	772.12	25.11
47	KOTRE BASANTPUR PACHMO OCP (Ministry of Coal) (400139) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	625.40 (625.40)	456.48	45.78
48	Pachwara South Coal Block (NLC India Limited) (400142) (-) (-)	Jharkhand	03/2016 (11/2019)	09/2028 (-)	2242.90 (2242.90)	1432.45	87
49	RPR MAGADH EXP OCP (Ministry of Coal) (400150) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2028 (-)	6964.33 (6964.33)	2299.77	39.42
50	NORTH URIMARI EXPANSION OCP (Ministry of Coal) (400151) (-) (-)	Jharkhand	07/2021 (07/2021)	03/2029 (-)	634.30 (634.30)	598.34	68.9
51	EPR ROHINI - KARKETTA OCP (Ministry of Coal) (400153) (-) (-)	Jharkhand	01/2021 (01/2021)	03/2028 (-)	995.57 (995.57)	85.34	24.02
52	EPR PUNDI OCP (Ministry of Coal) (400154) (-) (-)	Jharkhand	11/2020 (11/2020)	03/2027 (-)	639.60 (639.60)	14.78	11.24
53	EPR ASHOK OC (Ministry of Coal) (400155) (-) (-)	Jharkhand	05/2021 (05/2021)	03/2031 (-)	2821.07 (2821.07)	186.02	27.74
54	EPR AMRAPALI OCP (CCL - CIL) (400156) (-) (-)	Jharkhand	02/2020 (02/2020)	03/2028 (-)	4983.57 (4983.57)	1838.82	43.69
55	RAJRAPPA RCE OCP (CCL - CIL) (400160) (-) (-)	Jharkhand	12/2009 (12/2009)	03/2016 (03/2027)	510.85 (510.85)	488.71	75.61
56	CHITRA EAST OC (ECL - CIL) (400172) (-) (-)	Jharkhand	08/2018 (08/2018)	03/2026 (03/2028)	513.99 (513.99)	276	53.03
57	JHARKHAND-LAIYO OCP (Ministry of Coal) (400352) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2031 (-)	654.87 (654.87)	1.97	32.45
58	MOONIDIH XV SEAM UG (BCCL - CIL) (400425) (-) (-)	Jharkhand	08/2011 (08/2011)	03/2019 (09/2026)	1230.27 (1230.27)	800.25	84.02
59	AMALAGAMATED NTST KUJAMA OCP 8.5MTY (Bharat Coking Coal Limited (BCCL)) (611864) (-) (-)	Jharkhand	01/2023 (01/2023)	03/2030 (-)	4011.85 (4011.85)	414.97	31.16
60	MURAI DIH UG PROJECT (BCCL - CIL) (613808) (-) (-)	Jharkhand	02/2011 (02/2011)	04/2014 (12/2026)	339.87 (339.87)	191.14	70.47
61	TAPIN SOUTH EXPN (CCL - CIL) (615349) (-) (-)	Jharkhand	11/2020 (11/2020)	03/2028 (-)	230.41 (230.41)	22.02	23.67
62	SIRKA OC (CCL - CIL) (615822) (-) (-)	Jharkhand	05/2020 (05/2020)	03/2028 (-)	183.18 (183.18)	89.92	56.47
63	TETARIAKHAR OC (CCL - CIL) (615843) (-) (-)	Jharkhand	11/2019 (11/2019)	03/2025 (03/2027)	232.64 (232.64)	50.82	30.06

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
64	CHUPERBHITA SIMLONG OCP MDO 6 (ECL - CIL) (616225) (-) (-)	Jharkhand	12/2023 (12/2023)	03/2037 (-)	979.08 (979.08)	0	0.05
65	JARANGDIH EXPN. OCP 1.5 MTY (CCL - CIL) (616236) (-) (-)	Jharkhand	02/2020 (02/2020)	03/2029 (-)	372.06 (372.06)	85.6	32.99
66	BLOCK E OCP (BCCL - CIL) (616253) (-) (-)	Jharkhand	03/2024 (03/2024)	03/2029 (-)	5850.83 (5850.83)	20.32	4.18
67	Revised Jharia Master Plan for Dealing with Fire, Subsidence & Rehabilitation of affected families in Jharia Coalfield- Reg. (Bharat Coking Coal Limited [BCCL]) (617416) (-) (-)	Jharkhand	06/2025 (07/2025)	12/2028 (-)	5940.47 (5940.47)	520.75	34
68	North Dhadu Western Part OCP (NLC India Limited [NLCIL]) (617764) (-) (-)	Jharkhand	10/2023 (12/2023)	03/2029 (-)	1354.20 (1354.20)	233.77	40
69	AMADAND OCP[4.0MTY] (SECL - CIL) (400148) (-) (-)	Madhya Pradesh	03/2016 (03/2016)	03/2021 (03/2027)	869.44 (869.44)	325.09	75.15
70	BLOCK B EXPANSION [3.5 TO 8.0 (NCL - CIL) (400162) (-) (-)	Madhya Pradesh	07/2019 (07/2019)	03/2023 (03/2027)	998.71 (998.71)	545.34	51.31
71	NIGAH I EXPANSION [15 TO 25 MTP (NCL - CIL) (400321) (-) (-)	Madhya Pradesh	11/2020 (11/2020)	03/2025 (03/2028)	1729.68 (1729.68)	985.35	53.73
72	KANCHAN OC EXP (SECL - CIL) (613802) (-) (-)	Madhya Pradesh	12/2014 (12/2014)	03/2026 (03/2028)	371.04 (371.04)	157.9	58.2
73	JHIRIA WEST OCP [1.5 MTY] (SECL - CIL) (613803) (-) (-)	Madhya Pradesh	01/2024 (01/2024)	03/2029 (-)	366.94 (366.94)	37.19	41.29
74	RPR TAWA-III UG 0.84 MTY (WCL - CIL) (613804) (-) (-)	Madhya Pradesh	12/2021 (12/2021)	03/2027 (-)	314.09 (314.09)	17.9	17.78
75	AMALGAMATED DHANKASA & JAMUNIA (WCL - CIL) (615185) (-) (-)	Madhya Pradesh	09/2022 (09/2022)	03/2027 (-)	399.20 (399.20)	117.2	67.13
76	RPR OF VISHNUPURI UG TO OC (WCL - CIL) (615187) (-) (-)	Madhya Pradesh	11/2022 (11/2022)	03/2029 (-)	220.62 (220.62)	0	11.2
77	URDHAN EXPANSION OC COST PLUS (WCL - CIL) (615194) (-) (-)	Madhya Pradesh	07/2022 (01/2023)	03/2031 (-)	206.88 (206.88)	50.69	2.02
78	SHARDA UG MINE (WCL - CIL) (615195) (-) (-)	Madhya Pradesh	07/2022 (09/2023)	03/2028 (-)	166.25 (166.25)	5.93	9.39
79	GANDHIGRAM UG MINE (WCL - CIL) (615206) (-) (-)	Madhya Pradesh	08/2019 (08/2019)	03/2026 (03/2027)	414.15 (414.15)	28.54	56.88
80	JAYANT EXPN. [20 TO 38 MTPA] (NCL - CIL) (619032) (-) (-)	Madhya Pradesh	02/2025 (02/2025)	03/2032 (-)	25560.48 (25560.48)	333.3	2.1
81	RPR FOR RAMPUR BATURA OCP (SECL - CIL) (619053) (-) (-)	Madhya Pradesh	05/2025 (05/2025)	03/2030 (-)	1604.69 (1604.69)	75.28	0.3
82	BHATADI EXPANSION OC (WCL - CIL) (400033) (-) (-)	Maharashtra	02/2020 (05/2022)	03/2028 (-)	580.61 (580.61)	112.17	34.25
83	AMALGAMATED YEKONA I & YEKONA (WCL - CIL) (400177) (-) (-)	Maharashtra	08/2015 (08/2015)	03/2025 (03/2027)	727.28 (727.28)	564.25	80.77
84	DINESH[MAKARDHOKRA-III] OC (WCL - CIL) (400178) (-) (-)	Maharashtra	02/2020 (02/2020)	03/2027 (-)	822.88 (822.88)	792	40.63
85	DHUPTALA OC [SASTI UG TO OC] (WCL - CIL) (400353) (-) (-)	Maharashtra	02/2019 (10/2021)	03/2028 (-)	711.01 (711.01)	174.66	19.02

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
86	SAONER UG MINE -1 EXPANSION 1. (WCL - CIL) (615184) (-) (-)	Maharashtra	01/2022 (01/2022)	03/2028 (-)	228.64 (228.64)	157.01	69.33
87	SASTI EXPANSION OPENCAST (WCL - CIL) (615186) (-) (-)	Maharashtra	08/2020 (08/2020)	03/2026 (03/2027)	319.04 (319.04)	155.37	32.21
88	NEW MAJRI UG TO OC 3 MTY COST (WCL - CIL) (615188) (-) (-)	Maharashtra	05/2019 (09/2022)	03/2027 (-)	402.27 (402.27)	67.81	24.17
89	MAKARDHOKRA EXPN OC 4.9 MTY (WCL - CIL) (615189) (-) (-)	Maharashtra	06/2022 (06/2022)	03/2026 (03/2027)	361.87 (361.87)	104.17	12.2
90	SINGHORI DEEP OC MIN 2.0 MTY (WCL - CIL) (615190) (-) (-)	Maharashtra	05/2022 (05/2022)	03/2029 (-)	335.75 (335.75)	53.94	9.64
91	GOKUL EXTENSION OC MINE (WCL - CIL) (615192) (-) (-)	Maharashtra	04/2021 (04/2021)	03/2026 (03/2027)	309.58 (309.58)	62.31	8.44
92	KOLGAON EXPANSION DEEP OC MINE (WCL - CIL) (615199) (-) (-)	Maharashtra	01/2023 (09/2023)	03/2027 (-)	198.71 (198.71)	25.08	3.93
93	BALLARPUR NORTH WEST OC MINE (WCL - CIL) (615330) (-) (-)	Maharashtra	12/2022 (12/2022)	03/2029 (-)	360.81 (360.81)	26.97	5.35
94	GADEGAON OC 3 MTY (WCL - CIL) (615331) (-) (-)	Maharashtra	10/2023 (10/2023)	03/2030 (-)	497.41 (497.41)	95.69	2.19
95	GHONSA EXPANSION DEEP OC MINE (WCL - CIL) (615914) (-) (-)	Maharashtra	03/2021 (04/2021)	03/2029 (-)	184.71 (184.71)	15.72	12.98
96	AMLG GAURI PAUNI EXPANSION OC (WCL - CIL) (615916) (-) (-)	Maharashtra	04/2024 (04/2024)	03/2030 (-)	1225.21 (1225.21)	92.02	4.21
97	GAURIDEEP/GAURI CENTRAL OCP 7. (WCL - CIL) (615917) (-) (-)	Maharashtra	08/2023 (06/2024)	03/2030 (-)	973.07 (973.07)	1.55	2.31
98	RPR OF BHANEGAON OC (WCL - CIL) (615918) (-) (-)	Maharashtra	02/2017 (09/2022)	03/2028 (-)	405.20 (405.20)	43.16	16.06
99	N. EXTN. MUNGOLI NIRGUDA D OCP (WCL - CIL) (615919) (-) (-)	Maharashtra	06/2024 (06/2024)	03/2029 (-)	1024.91 (1024.91)	218.26	27.92
100	NILJAI EXPANSION DEEP OCP (WCL - CIL) (615982) (-) (-)	Maharashtra	08/2016 (08/2016)	03/2022 (03/2027)	319.75 (319.75)	196.82	79.83
101	UKNI DEEP OC MINE -COST PLUS (WCL - CIL) (616044) (-) (-)	Maharashtra	11/2018 (01/2019)	03/2021 (03/2027)	237.06 (237.06)	168.91	94.57
102	AMALGAMATED INDER-KAMPTEE DEEP (WCL - CIL) (616050) (-) (-)	Maharashtra	09/2018 (09/2018)	03/2024 (03/2027)	235.90 (235.90)	128.49	98.97
103	ADASA UG TO OC MINE (WCL - CIL) (616223) (-) (-)	Maharashtra	11/2018 (11/2018)	03/2024 (03/2027)	316.00 (316.00)	209.29	86.49
104	AMAL GONDEGAON GHATROHANA EXPN (WCL - CIL) (616229) (-) (-)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	668.54 (668.54)	2.95	2.55
105	WAGHODA UG MINE [1.02 MTY] (WCL - CIL) (617233) (-) (-)	Maharashtra	01/2024 (01/2025)	03/2030 (-)	379.30 (379.30)	0	0.11
106	KOLARPIMPRI EXPANSION OC [2.5 (WCL - CIL) (617278) (-) (-)	Maharashtra	06/2024 (02/2025)	03/2030 (-)	630.37 (630.37)	0.61	0.4
107	SAONER-III EXPN UG MINE 1.54 (WCL - CIL) (619055) (-) (-)	Maharashtra	08/2025 (08/2025)	03/2032 (-)	444.42 (444.42)	0	0
108	BINA KAKRI AMALGAMATION EXPANS (WCL - CIL) (400369) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020 (08/2020)	03/2024 (03/2027)	836.42 (836.42)	917.1	92.05



All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
109	KHADIA EXPANSION [10 TO 16 MTP (NCL - CIL) (615183) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021 (06/2021)	03/2025 (03/2027)	491.67 (491.67)	379.69	57.12
110	SUBHADRA OCP (MCL - CIL) (400165) (-) (-)	Odisha	05/2021 (05/2021)	04/2032 (-)	1693.81 (1693.81)	1332.87	46.57
111	SIARMAL OCP (Mahanadi Coalfields Limited [MCL]) (400166) (-) (-)	Odisha	02/2021 (02/2021)	03/2029 (-)	5194.95 (5194.95)	3543.45	61.04
112	BALARAM EXPANSION OCP (Mahanadi Coalfields Limited [MCL]) (400183) (-) (-)	Odisha	08/2020 (08/2020)	03/2029 (-)	3504.21 (3504.21)	963.81	62.06
113	GOPALJI KANIHA OCP [10 TO 30 M (MCL - CIL) (400185) (-) (-)	Odisha	04/2022 (04/2022)	03/2030 (-)	8416.19 (6107.87)	1777.54	35.8
114	INTEGRATED LAKHANPUR-BELPAHAR- (MCL - CIL) (400187) (-) (-)	Odisha	05/2018 (05/2018)	03/2027 (-)	2434.75 (2434.75)	2133.7	82.9
115	BHARATPUR RE-ORGANIZATION OCP (MCL - CIL) (400392) (-) (-)	Odisha	11/2018 (11/2018)	03/2029 (-)	2838.86 (2838.86)	1716.58	53.54
116	Naini Coal Mine (Singareni Collieries Company Limited [SCCL]) (615857) (-) (-)	Odisha	03/2020 (03/2020)	03/2026 (-)	494.30 (494.30)	491.33	80
117	INTEGRATED KULDA GARJANBAHAL O (MCL - CIL) (616226) (-) (-)	Odisha	04/2023 (04/2023)	03/2033 (-)	3563.50 (3563.50)	692.76	10.43
118	BHUBANESWARI EXPN OCP 50 MTY (MCL - CIL) (616231) (-) (-)	Odisha	03/2024 (03/2024)	03/2033 (-)	5366.27 (5366.27)	477.73	34.03
119	HINGULA II OC EXPN PH III 15 M (MCL - CIL) (616232) (-) (-)	Odisha	11/2022 (11/2022)	03/2029 (-)	1561.85 (1561.85)	284.22	33.55
120	BALABHADRA OCP (MCL - CIL) (616233) (-) (-)	Odisha	04/2023 (04/2023)	03/2030 (-)	978.44 (978.44)	461.54	18.93
121	Talabira II & III OCP - FMC (NLC India Limited [NLCIL]) (618982) (-) (-)	Odisha	10/2022 (05/2023)	06/2026 (12/2026)	522.45 (522.45)	334.44	74.8
122	Jawahar Khani Open Cast Mine (Singareni Collieries Company Limited [SCCL]) (615818) (-) (-)	Telangana	12/2021 (12/2021)	03/2025 (03/2027)	297.88 (297.88)	50.39	20
123	Kalyanikhani Opencast Project (Singareni Collieries Company Limited [SCCL]) (615858) (-) (-)	Telangana	03/2016 (05/2017)	03/2026 (-)	384.32 (384.32)	304.39	77
124	Godavarikhani Coal Mine - 5 (Singareni Collieries Company Limited [SCCL]) (615860) (-) (-)	Telangana	07/2019 (05/2019)	03/2025 (03/2026)	607.04 (607.04)	201	71
125	Indaram Opencast Project (Singareni Collieries Company Limited [SCCL]) (615861) (-) (-)	Telangana	08/2017 (12/2022)	03/2025 (03/2026)	424.81 (424.81)	408.69	81
126	Goleti Opencast Mine (Singareni Collieries Company Limited [SCCL]) (615862) (-) (-)	Telangana	07/2021 (08/2021)	03/2026 (-)	345.60 (345.60)	111.94	33
127	Venkatesh Khani Coal Mine (Singareni Collieries Company Limited [SCCL]) (615863) (-) (-)	Telangana	10/2020 (06/2020)	03/2026 (-)	484.50 (484.50)	477.14	97
128	Kakatiyakhani OC - 2 Project (Singareni Collieries Company Limited [SCCL]) (615865) (-) (-)	Telangana	08/2017 (09/2017)	03/2025 (03/2026)	442.42 (442.42)	253.41	64
129	MOHANPUR EXPANSION OC -PHASE I (Eastern Coal Fields Limited [ECL]) (400173) (-) (-)	West Bengal	11/2020 (11/2020)	03/2026 (03/2030)	888.99 (888.99)	153.96	31.52
130	BONJEMEhari EXPANSION OCP (Eastern Coal Fields Limited [ECL]) (400180) (-) (-)	West Bengal	08/2021 (08/2021)	03/2026 (03/2030)	570.11 (570.11)	98.58	17.13
131	NAKRAKONDA KUMARDIH- B OCP (ECL - CIL) (400181) (-) (-)	West Bengal	08/2018 (08/2018)	03/2029 (-)	502.68 (502.67)	88.9	28.58

All Ongoing Projects							JULY 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
132	TILABONI UG (ECL - CIL) (400186) (-) (-)	West Bengal	01/2023 (01/2023)	03/2029 (-)	749.08 (749.07)	53.97	12.14
133	JHANJRA EXPANSION UG (Eastern Coal Fields Limited [ECL]) (400312) (-) (-)	West Bengal	04/2020 (04/2020)	03/2029 (-)	1210.12 (1210.12)	633.57	52.04
134	SONEPUR BAZARI EXPANSION OCP [(Eastern Coal Fields Limited [ECL]) (400315) (-) (-)	West Bengal	07/2021 (07/2021)	03/2029 (-)	5365.88 (5365.88)	697.64	18.5
135	ITAPARA OCP (Eastern Coal Fields Limited [ECL]) (612816) (-) (-)	West Bengal	12/2023 (12/2023)	03/2030 (-)	929.10 (929.10)	132.43	8.41
136	SHYAMSUNDARPUR UG INCLUDING SA (ECL - CIL) (613793) (-) (-)	West Bengal	04/2020 (04/2020)	03/2026 (03/2028)	483.65 (483.65)	96.8	16.79
137	PARASEA-BELBAID UG PROJECT (ECL - CIL) (613794) (-) (-)	West Bengal	01/2023 (01/2023)	03/2028 (-)	389.10 (389.10)	132.48	22.26
138	PARASCOLE JAMBAD OCP (ECL - CIL) (616230) (-) (-)	West Bengal	11/2024 (11/2024)	03/2037 (-)	1193.55 (1193.55)	11.81	0.23
Total (113)					182494.77	51305.23	
Electricity Generation							
139	50 MW Wind Power Project (NLC India Limited) (617299) (-) (-)	Gujarat	07/2022 (01/2024)	06/2025 (12/2026)	383.84 (383.84)	333.34	52
140	600 MW Khavda Solar Power Project (NLC India Limited [NLCIL]) (617730) (-) (-)	Gujarat	08/2023 (06/2024)	06/2026 (12/2026)	3335.85 (3335.85)	2122.95	62
141	200 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (618991) (-) (-)	Gujarat	07/2022 (03/2024)	12/2026 (-)	1221.41 (1221.41)	71.51	0
142	100 MW SPP part of SECI 150 MW Hybrid (NLC India Limited [NLCIL]) (618992) (-) (-)	Gujarat	07/2022 (04/2024)	12/2026 (-)	480.68 (480.68)	2.75	1.2
143	NLC Talabira Thermal Power Project (NLC India Limited) (400231) (-) (-)	Odisha	01/2017 (01/2024)	03/2030 (-)	27212.96 (27212.96)	3574.21	4.1
144	810 MW Solar Power Project - Rajasthan (NLC India Limited [NLCIL]) (618981) (-) (-)	Rajasthan	10/2024 (09/2025)	03/2028 (-)	4147.07 (4147.07)	249.95	0
Total (6)					36781.81	6354.71	
Railways							
145	Dharamjaigarh-Korba (Railway) (400203) (-) (-)	Chhattisgarh	05/2018 (03/2017)	12/2026 (08/2026)	1686.22 (2438.53)	792.73	43.7
146	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] (Ministry of Coal) (400416) (-) (-)	Jharkhand	02/2018 (05/2022)	06/2025 (06/2027)	1799.64 (2564.34)	1784.77	72
Total (2)					3485.86	2577.5	
Ministry of Power							
Coal							
147	Tubed Coal Mine (Damodar Valley Corporation) (400192) (-) (-)	Jharkhand	07/2016 (10/2016)	05/2026 (12/2026)	1581.00 (1581.00)	624.86	37
148	Badam Coal Mining project of NTPC (National Thermal Power Corporation [NTPC]) (603293) (-) (-)	Jharkhand	02/2019 (09/2019)	12/2056 (04/2027)	502.00 (784.00)	438.57	67.86
Total (2)					2083.00	1063.43	
Electricity Generation							
149	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182) (-) (-)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.39)	4921.36	17.93
150	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698) (-) (-)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	106.28	6.58

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
151	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699) (-) (-)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	79.45	5.6
152	700 MW Tato-II HE Project (North Eastern Electric Power Corporation Limited) (611716) (-) (-)	Arunachal Pradesh	09/2025 (09/2025)	09/2031 (-)	8146.21 (8146.21)	253.97	6.59
153	Kalai-II Hydro Electric Project [1200 MW] (THDC India Limited) (619311) (-) (-)	Arunachal Pradesh	04/2026 (04/2026)	10/2032 (-)	14105.83 (14105.83)	189.68	0
154	Buxar Thermal Power Project [1320 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602579) (-) (-)	Bihar	03/2019 (06/2019)	01/2024 (05/2026)	10439.09 (13756.56)	13731.77	95.01
155	Nabinagar Super Thermal Power Project, Stage-II [3x800 MW] (National Thermal Power Corporation [NTPC]) (619051) (-) (-)	Bihar	11/2024 (03/2025)	07/2030 (07/2030)	29948.00 (29948.00)	3422.25	15
156	Lara Super Thermal Power Project Stage-II [2 x 800 MW] (National Thermal Power Corporation [NTPC]) (611930) (-) (-)	Chhattisgarh	08/2023 (08/2023)	06/2028 (11/2028)	15530.00 (16106.00)	5472.13	33.5
157	Sipat Super Thermal Power Project, Stage-III [1x800 MW] (National Thermal Power Corporation [NTPC]) (617188) (-) (-)	Chhattisgarh	09/2024 (09/2024)	09/2029 (11/2029)	9791.00 (9791.00)	1910.55	22.31
158	Bagodara Solar Power Project (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709747) (-) (-)	Gujarat	03/2021 (05/2021)	12/2025 (12/2025)	339.35 (339.35)	370	51.86
159	Dhaultasidh Hydro Electric Project [66 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602582) (-) (-)	Himachal Pradesh	10/2020 (05/2021)	11/2025 (03/2027)	687.97 (1763.31)	1275.68	80.69
160	Luhri Stage-I Hydro Electric Project [210 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602593) (-) (-)	Himachal Pradesh	11/2020 (11/2020)	01/2026 (05/2030)	1810.56 (4345.31)	1980.59	52.13
161	Sunni Dam Hydro Electric Project [382 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (611586) (-) (-)	Himachal Pradesh	01/2023 (01/2023)	04/2028 (12/2029)	2614.51 (4555.49)	1152.21	34.66
162	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW (National Hydroelectric Power Corporation Limited [NHPC]) (602525) (-) (-)	Jammu and Kashmir	10/2014 (02/2018)	04/2020 (12/2026)	8112.12 (12728.00)	9313.54	82.05
163	Kiru HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (602532) (-) (-)	Jammu and Kashmir	03/2019 (02/2020)	09/2023 (12/2026)	4287.59 (5409.00)	3948.67	87
164	Rattle HE Project - 850 MW, Rattle Hydroelectric Power Corporation Limited. (National Hydroelectric Power Corporation Limited [NHPC]) (602535) (-) (-)	Jammu and Kashmir	02/2021 (01/2022)	02/2026 (11/2028)	5281.94 (5281.94)	1645.11	31.53
165	Kwar HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (605155) (-) (-)	Jammu and Kashmir	05/2022 (11/2022)	11/2026 (03/2028)	4526.12 (4526.12)	1701.47	36.52
166	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] (National Thermal Power Corporation [NTPC]) (400261) (-) (-)	Jharkhand	11/2017 (11/2017)	03/2023 (04/2027)	18668.00 (20302.00)	19735.72	92
167	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand (Damodar Valley Corporation) (611509) (-) (-)	Jharkhand	04/2023 (11/2024)	07/2029 (-)	14358.00 (14358.00)	2229.31	14.3
168	Gadarwara Super Thermal Power Project, Stage-II [2x800 MW] (National Thermal Power Corporation [NTPC]) (618976) (-) (-)	Madhya Pradesh	11/2024 (05/2025)	03/2030 (03/2030)	20446.00 (20446.00)	2329.76	11.5
169	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (03/2027)	6285.33 (26075.54)	26448.07	97.98
170	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion (National Thermal Power Corporation [NTPC]) (602961) (-) (-)	Odisha	08/2022 (09/2022)	05/2027 (05/2028)	11843.75 (12543.00)	7031.31	55
171	Darlipali Super Thermal Power Project, Stage-II [1x800 MW] (National Thermal Power Corporation [NTPC]) (619056) (-) (-)	Odisha	11/2025 (11/2025)	01/2031 (05/2031)	11131.00 (11131.00)	566.2	2.7
172	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181) (-) (-)	Sikkim	03/2019 (03/2020)	03/2024 (09/2029)	5748.04 (5748.04)	4572.68	73.78

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
173	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156) (-) (-)	Sikkim	03/2021 (08/2021)	05/2024 (11/2026)	938.29 (1828.11)	1718.16	97.56
174	Telangana Super Thermal Power Project , Stage-II [3 x 800 MW] (National Thermal Power Corporation [NTPC]) (619341) (-) (-)	Telangana	03/2026 (03/2026)	01/2032 (-)	29344.85 (29344.85)	732.96	0.97
175	Meja Thermal Power Project, Stage-II , (3x800 MW) (National Thermal Power Corporation [NTPC]) (298178) (-) (-)	Uttar Pradesh	06/2026 (06/2026)	12/2032 (-)	38358.00 (38358.00)	1002.73	0.02
176	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] (National Thermal Power Corporation [NTPC]) (612142) (-) (-)	Uttar Pradesh	03/2024 (03/2024)	02/2030 (04/2030)	17195.00 (17195.00)	3840.48	25
177	Tapovan-Vishnugad HEP [4x130 MW] (National Thermal Power Corporation [NTPC]) (602185) (-) (-)	Uttarakhand	11/2006 (11/2006)	03/2013 (07/2029)	2978.00 (10907.30)	7827.81	76.07
178	Vishnugad Pipalkoti Hydro Electric Project [444 MW] (THDC India Limited) (602195) (-) (-)	Uttarakhand	08/2008 (01/2014)	12/2022 (06/2028)	3860.35 (6405.08)	5832.69	81.5
179	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal (Damodar Valley Corporation) (400062) (-) (-)	West Bengal	01/2023 (02/2025)	08/2029 (-)	17673.00 (17673.00)	2268.62	13
180	Rammam-III HEPP [3x40 MW] (National Thermal Power Corporation [NTPC]) (602184) (-) (-)	West Bengal	09/2014 (09/2014)	09/2019 (09/2029)	1381.84 (2865.56)	1690.73	57.86
181	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 (Damodar Valley Corporation) (602538) (-) (-)	West Bengal	06/2019 (02/2021)	01/2024 (09/2026)	1037.00 (1106.00)	1143.06	97
Total (33)					352432.05	140445	
Transmission & Distribution							
182	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617183) (-) (-)	Andhra Pradesh	03/2025 (03/2025)	12/2027 (-)	2886.00 (2886.00)	894.66	43.89
183	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375) (-) (-)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	3.14	3.89
184	Transmission system for evacuation of Power from REZ in Rajasthan [20 GW] under phase-III Part-D Phase-II (Power Grid Corporation of India Limited [POWERGRID]) (615336) (-) (-)	Delhi	11/2023 (10/2024)	02/2026 (12/2026)	284.00 (284.00)	90.88	45.94
185	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (612139) (-) (-)	Gujarat	12/2023 (12/2023)	12/2025 (12/2026)	4231.00 (4231.00)	3175.79	72.12
186	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (612855) (-) (-)	Gujarat	05/2024 (05/2024)	05/2026 (09/2026)	697.00 (697.00)	592.45	82
187	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615342) (-) (-)	Gujarat	10/2024 (10/2024)	07/2026 (04/2027)	329.00 (329.00)	72.38	33
188	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] (Power Grid Corporation of India Limited [POWERGRID]) (615343) (-) (-)	Gujarat	11/2024 (11/2024)	11/2026 (-)	501.00 (501.00)	26.45	8.67
189	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345) (-) (-)	Gujarat	10/2024 (10/2024)	10/2026 (10/2027)	4766.00 (4766.00)	2144.7	38.26
190	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069) (-) (-)	Gujarat	02/2025 (02/2025)	02/2027 (-)	466.00 (466.00)	154.9	37
191	Augmentation of Banaskantha [Raghanesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182) (-) (-)	Gujarat	03/2025 (03/2025)	03/2027 (-)	172.00 (172.00)	61.92	42

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
192	Augmentation of Transformation Capacity at Bhuj-II PS [GIS] (Power Grid Corporation of India Limited [POWERGRID]) (617391) (-) (-)	Gujarat	02/2025 (02/2025)	11/2026 (06/2027)	488.29 (488.29)	14.64	7.2
193	Jamnagar Transmission Limited (Adani Transmission Limited) (617405) (-) (-)	Gujarat	10/2024 (10/2024)	10/2026 (09/2027)	4000.00 (4000.00)	698	24
194	Provision of ICT Augmentation & Bus Reactor at Bhuj-II PS (Power Grid Corporation of India Limited [POWERGRID]) (617801) (-) (-)	Gujarat	03/2025 (03/2025)	12/2026 (06/2027)	581.74 (581.74)	17.45	7.2
195	KPSIII HVDC Transmission Limited (Adani Transmission Limited) (619026) (-) (-)	Gujarat	12/2025 (12/2025)	12/2029 (-)	19000.00 (19000.00)	20	1
196	Transmission System for Reliable Power Supply to Dholera (Power Grid Corporation of India Limited [POWERGRID]) (619029) (-) (-)	Gujarat	09/2024 (09/2024)	03/2026 (12/2026)	319.42 (319.42)	70.27	35.2
197	Khavda IVA Power Transmission Limited (Adani Transmission Limited) (619049) (-) (-)	Gujarat	08/2024 (08/2024)	08/2026 (03/2027)	4500.00 (4500.00)	2772.7	70
198	Transmission Scheme for evacuation of Power from Ratle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179) (-) (-)	Jammu and Kashmir	07/2024 (07/2024)	07/2026 (06/2027)	218.60 (218.60)	3.72	1.7
199	Implementation of Transmission Systems in the State of Jharkhand consisting of 400/220/132/33 kV transmission lines and substations under Jharkhand Consultancy Project (Power Grid Corporation of India Limited [POWERGRID]) (617326) (-) (-)	Jharkhand	02/2012 (02/2012)	03/2026 (06/2027)	1842.25 (1842.25)	1648.05	96.4
200	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140) (-) (-)	Karnataka	12/2023 (12/2023)	12/2025 (09/2026)	4445.00 (4445.00)	4089.4	95.95
201	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672) (-) (-)	Karnataka	01/2025 (01/2025)	06/2027 (-)	1354.00 (1354.00)	338.5	38.07
202	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068) (-) (-)	Karnataka	02/2025 (02/2025)	06/2027 (-)	288.00 (288.00)	28.8	18.75
203	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184) (-) (-)	Karnataka	03/2025 (03/2025)	09/2027 (-)	3453.00 (3453.00)	552.48	23.01
204	Transmission System Strengthening at Davanagere for Integration of RE Generation [SPV Name - POWERGRID Davanagere Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617803) (-) (-)	Karnataka	09/2025 (09/2025)	09/2027 (-)	379.00 (379.00)	17.06	2.5
205	Transmission System Strengthening for integration of additional RE Potential at Davanagere [0.25 GW] and Bellary [2.75 GW] (Power Grid Corporation of India Limited [POWERGRID]) (619228) (-) (-)	Karnataka	02/2026 (02/2026)	02/2028 (-)	1111.00 (1111.00)	22.22	1
206	Augmentation of 1x500 MVA 400/220kV ICT [3rd] at Thrissur VSC HVDC Station in Kerala (Power Grid Corporation of India Limited [POWERGRID]) (619028) (-) (-)	Kerala	08/2025 (08/2025)	08/2027 (12/2027)	173.14 (173.14)	2.08	1.5
207	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344) (-) (-)	Madhya Pradesh	10/2024 (10/2024)	10/2026 (06/2027)	3674.00 (3674.00)	1673.14	47.9
208	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346) (-) (-)	Madhya Pradesh	08/2024 (08/2024)	08/2026 (02/2027)	2708.00 (2708.00)	1624.8	72.39
209	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272) (-) (-)	Madhya Pradesh	06/2024 (06/2024)	12/2026 (-)	370.00 (370.00)	148	55.26

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
210	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279) (-) (-)	Madhya Pradesh	06/2025 (06/2025)	12/2027 (-)	558.00 (558.00)	180.9	18.47
211	Augmentation of Transformation Capacity and Implementation of Line Bays at Mandsaur S/S for RE Interconnection [SPV Name- POWERGRID Mandsaur I RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617802) (-) (-)	Madhya Pradesh	10/2025 (10/2025)	03/2028 (-)	319.00 (319.00)	17.23	4.8
212	Mahan Transmission Limited (Adani Transmission Limited) (619024) (-) (-)	Madhya Pradesh	03/2025 (03/2025)	04/2027 (-)	3125.32 (3125.32)	542.79	30
213	WRNES Talegaon Power Transmission Limited (Adani Transmission Limited) (619027) (-) (-)	Maharashtra	05/2025 (05/2025)	01/2028 (-)	2000.00 (2000.00)	25	5
214	Network Expansion Scheme in Maharashtra for removal of Transmission constraints in Pune Region-I [765/400kV AIS Pune East] (Power Grid Corporation of India Limited [POWERGRID]) (619227) (-) (-)	Maharashtra	03/2026 (03/2026)	03/2028 (-)	1420.00 (1420.00)	38.9	3.92
215	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	03/2025 (03/2025)	03/2027 (09/2027)	5550.00 (5550.00)	1776	28.77
216	Transmission System for Integration of Ananthapur 2 REZ Phase 1 for 4.5 GW. SPV Name Anantapuram 2 REZ Transmission Ltd (Sterlite Power) (617806) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	08/2024 (03/2025)	03/2027 (-)	4535.99 (4535.99)	1207.57	64
217	Inter-Regional Strengthening between SR Grid and ER Grid (Power Grid Corporation of India Limited [POWERGRID]) (619030) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	02/2026 (02/2026)	08/2028 (-)	2722.50 (2722.50)	190.57	3
218	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223) (-) (-)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	8141.52	83.9
219	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709) (-) (-)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (03/2027)	5111.33 (6700.00)	5577.75	99.2
220	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271) (-) (-)	Multi-States (Bihar, Odisha, West Bengal)	09/2024 (09/2024)	03/2026 (09/2026)	342.69 (342.69)	143.93	29.75
221	Inter-regional [NR-WR] Transmission System strengthening to relieve the loading of 765 kV Vindhyachal-Varanasi D/c line (Power Grid Corporation of India Limited [POWERGRID]) (617807) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	10/2025 (10/2025)	10/2027 (-)	2368.00 (2368.00)	157.94	6.38
222	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270) (-) (-)	Multi-States (Bihar, West Bengal)	11/2024 (11/2024)	05/2026 (09/2027)	408.94 (408.94)	6.13	1.5
223	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D Phase I [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132) (-) (-)	Multi-States (Delhi, Haryana, Rajasthan)	02/2024 (02/2024)	08/2025 (03/2027)	2423.00 (2423.00)	2229.16	92.47
224	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735) (-) (-)	Multi-States (Delhi, Rajasthan)	12/2022 (12/2022)	03/2025 (12/2026)	331.00 (331.00)	235.01	68.9
225	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAYDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347) (-) (-)	Multi-States (Gujarat, Maharashtra)	11/2024 (11/2024)	05/2029 (-)	24819.00 (24819.00)	2978.28	18.56
226	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339) (-) (-)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024 (11/2024)	11/2026 (04/2027)	5969.00 (5969.00)	1969.77	33.3
227	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Siwani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340) (-) (-)	Multi-States (Haryana, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5357.00 (5357.00)	1921.02	36.53
228	Inter-Regional Strengthening between SR Grid and WR Grid (Power Grid Corporation of India Limited [POWERGRID]) (617808) (-) (-)	Multi-States (Karnataka, Maharashtra)	10/2025 (10/2025)	10/2027 (-)	1007.00 (1007.00)	50.35	3

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
229	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138) (-) (-)	Multi-States (Karnataka, Telangana)	02/2024 (02/2024)	02/2026 (08/2026)	1368.00 (1368.00)	1258.56	96.84
230	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (12/2026)	2227.00 (2227.00)	1113.5	49.31
231	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (04/2027)	3251.00 (3251.00)	2048.13	46.87
232	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [Rajasthan V Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025 (03/2025)	03/2027 (06/2027)	5028.00 (5028.00)	1508.4	34.03
233	RAJASTHAN PART I POWER TRANSMISSION LIMITED (Adani Transmission Limited) (619025) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	01/2025 (01/2025)	07/2029 (-)	25000.00 (25000.00)	735.05	10
234	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133) (-) (-)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023 (12/2023)	12/2025 (04/2027)	3271.00 (3271.00)	2731.29	73.45
235	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670) (-) (-)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024 (12/2024)	12/2026 (06/2027)	5846.00 (5846.00)	1953.73	40.71
236	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949) (-) (-)	Rajasthan	10/2023 (10/2023)	04/2025 (08/2026)	1160.00 (1160.00)	1148.4	99.87
237	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134) (-) (-)	Rajasthan	12/2023 (12/2023)	12/2025 (04/2027)	4741.00 (4741.00)	3887.62	79.39
238	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332) (-) (-)	Rajasthan	08/2024 (08/2024)	08/2026 (03/2027)	3279.00 (3279.00)	1901.82	56.15
239	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615335) (-) (-)	Rajasthan	08/2024 (08/2024)	08/2026 (03/2027)	1382.00 (1382.00)	628.81	57.31
240	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615337) (-) (-)	Rajasthan	08/2024 (08/2024)	02/2026 (09/2026)	369.00 (369.00)	258.3	87.1
241	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615338) (-) (-)	Rajasthan	11/2024 (11/2024)	11/2026 (06/2027)	2735.00 (2735.00)	1121.35	47.28
242	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617181) (-) (-)	Rajasthan	03/2025 (03/2025)	12/2026 (06/2027)	404.00 (404.00)	32.32	17.2
243	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Tarnsmision Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616671) (-) (-)	Tamil Nadu	01/2025 (01/2025)	12/2026 (03/2027)	548.00 (548.00)	208.24	23.78
244	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex (Power Grid Corporation of India Limited [POWERGRID]) (617269) (-) (-)	Uttar Pradesh	12/2024 (12/2024)	06/2026 (12/2026)	212.81 (212.81)	12.76	12.07
	Total (63)				197390.82	68896.68	

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Housing & Urban Affairs							
Construction							
245	Construction of One Tower of Office Complex and another Tower of Residential quarters i/c internal water supply, sanitary installation and all development and bulk services, Horticulture works on EPC Mode-I basis i/c comprehensive operation and maintenance of Civil, E&M services for 7 years after completion of original construction work for Ranga Reddy, Secunderabad, Medchal, Audit-I, Audit-II Commissionerates of Central Tax at Khajaguda, Serilingampally, Hyderabad. (Central Public Works Department - CPWD) (617412) (-) (-)	Telangana	03/2024 (11/2024)	09/2027 (-)	644.00 (644.00)	188.69	26
Total (1)					644.00	188.69	
Real Estate							
246	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System (ministry of housing and urban affairs) (707229) (-) (-)	Andaman & Nicobar	07/2021 (11/2021)	05/2023 (10/2025)	209.88 (230.00)	37.35	97
247	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi (National Buildings Construction Corporation [NBCC]) (400188) (-) (-)	Delhi	07/2016 (05/2018)	12/2025 (12/2025)	32850.00 (32841.00)	14370.45	46.7
248	Rehabilitation in Junavadaj Area Smart City Project (ministry of housing and urban affairs) (701719) (-) (-)	Gujarat	02/2016 (06/2016)	07/2022 (07/2026)	539.00 (539.00)	623.44	98.5
249	Green Building Development Project (ministry of housing and urban affairs) (701766) (-) (-)	Uttarakhand	11/2019 (08/2019)	11/2023 (12/2026)	150.97 (206.00)	59.51	40.3
Total (4)					33749.85	15090.75	
Urban Public Transport							
250	Patna Metro Rail Project (Patna Metro Rail Corporation Ltd. [PMRCL]) (702627) (-) (-)	Bihar	02/2019 (02/2019)	02/2024 (06/2027)	13365.77 (13365.77)	5198.09	50.05
251	Delhi Metro Rail Phase-IV [2 Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (617207) (-) (-)	Delhi	03/2024 (03/2024)	03/2029 (-)	8399.81 (8399.81)	183.23	4.31
252	Delhi Metro Rail Phase V A (Delhi Metro Rail Corporation Limited [DMRC]) (619031) (-) (-)	Delhi	01/2026 (01/2026)	12/2028 (-)	12014.91 (12014.91)	264.98	5.65
253	DMRTS Phase - IV [3 Priority Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (702632) (-) (-)	Delhi	07/2019 (07/2019)	03/2025 (12/2026)	24948.65 (24948.65)	21420.76	83.46
254	Surat Metro Rail Project (Gujarat Metro Rail Corporation Limited [GMRCL]) (702630) (-) (-)	Gujarat	03/2019 (03/2019)	03/2024 (03/2027)	12020.32 (12020.32)	9332.21	81.9
255	Metro connectivity from Millennium City Centre to Cyber City with Spur to Dwarka Expressway, Gurugram. (Gurugram Metro Rail Limited [GMRL]) (619022) (-) (-)	Haryana	07/2023 (08/2024)	07/2027 (-)	5452.72 (5452.72)	193.32	10.05
256	Bangalore Metro Rail Project - PHASE-3 (Bengaluru Metro Rail) (612878) (-) (-)	Karnataka	09/2024 (06/2026)	05/2031 (-)	15611.00 (15611.00)	0	3.8
257	Construction of Bangalore Metro Rail Project Phase 2. (Bengaluru Metro Rail) (702635) (-) (-)	Karnataka	02/2014 (02/2016)	03/2021 (09/2026)	26405.14 (30695.12)	29834.97	95.8
258	Construction Bangalore Metro Rail Project Phase-2A & 2B (Bengaluru Metro Rail) (702665) (-) (-)	Karnataka	06/2021 (01/2019)	06/2026 (06/2026)	14788.10 (14788.10)	10878.48	67.5
259	Kochi Metro Rail Phase 2 Development Project (CSPCC Projects) (702664) (-) (-)	Kerala	11/2022 (11/2022)	11/2026 (11/2026)	1957.05 (1957.05)	816.8	41.2
260	Bhopal Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702625) (-) (-)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (06/2028)	6941.40 (6941.40)	4498.76	62.7
261	Indore Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702626) (-) (-)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (12/2028)	7500.80 (7500.80)	5093.95	65.48
262	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617225) (-) (-)	Maharashtra	10/2023 (10/2023)	01/2027 (-)	910.18 (960.18)	322.59	49.12
263	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617226) (-) (-)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	2954.53 (2954.53)	190.07	9.04

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
264	Thane Integral Ring Metro Rail Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617327) (-) (-)	Maharashtra	09/2024 (09/2024)	09/2029 (-)	12200.10 (12200.10)	101.17	10.04
265	Pune Metro Rail Project Phase-2 Corridor 2A Vanaz to Chandani Chowk and Corridor 2B Ramwadi to Wagholi/Vitthalwadi (Maharashtra Metro Rail Corporation Limited [MMRCL]) (618971) (-) (-)	Maharashtra	07/2025 (07/2025)	07/2029 (-)	3626.24 (3626.24)	16.17	2.4
266	Pune Metro Rail Project Phase-2 Line-4 Kharadi to Khadakwasla with Spur Line 4A Nal Stop - Warje - Manikbaug (Maharashtra Metro Rail Corporation Limited [MMRCL]) (618985) (-) (-)	Maharashtra	12/2025 (12/2025)	12/2030 (-)	9857.85 (9857.85)	8.62	1.51
267	New Suburba Station Development Project (ministry of housing and urban affairs) (701745) (-) (-)	Maharashtra	04/2018 (03/2019)	07/2022 (-)	262.76 (262.76)	163.21	48
268	Kalyan Station Precinct Imporvement Project (ministry of housing and urban affairs) (701991) (-) (-)	Maharashtra	04/2018 (07/2020)	07/2023 (06/2026)	600.00 (723.70)	530.04	85
269	Mumbai Metro Line 3 (Mumbai Metro Rail Corporation Limited [MMRC]) (702637) (-) (-)	Maharashtra	07/2013 (06/2016)	03/2023 (08/2025)	23136.00 (37276.00)	35959.97	99.21
270	Nagpur Metro Rail Phase II Development Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (702658) (-) (-)	Maharashtra	12/2022 (12/2022)	12/2027 (-)	6708.00 (6708.00)	2161.73	42.11
271	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] (Delhi Metro Rail Corporation Limited [DMRC]) (617206) (-) (-)	Multi-States (Delhi, Haryana)	01/2025 (01/2025)	01/2029 (-)	6230.99 (6230.99)	800.48	5.36
272	Jaipur Metro Rail Project Phase 2 (Pralhadpura to Todi Mod) (Jaipur Metro Rail Corporation) (245986) (-) (-)	Rajasthan	04/2026 (04/2026)	10/2031 (-)	13037.66 (13037.66)	1.79	1.79
273	Rajasthan Metro Rail Project Phase 1C from Badi Chaupar to Transport Nagar via Galta Gate (Jaipur Metro Rail Corporation) (612066) (-) (-)	Rajasthan	10/2025 (09/2023)	04/2027 (-)	980.08 (980.08)	103.03	0
274	Jaipur Metro Phase 1D Project from Mansarovar to Ajmer Road Chauraha (Jaipur Metro Rail Corporation) (612068) (-) (-)	Rajasthan	05/2026 (12/2023)	03/2026 (-)	204.81 (204.81)	23.34	12.48
275	Chennai Metro Rail Phase-II Development Project (Chennai Metro Rail Limited [CMRL]) (702668) (-) (-)	Tamil Nadu	10/2024 (11/2020)	08/2029 (-)	63246.00 (63246.00)	34698	55.73
276	Extension of Aqua Line Metro Corridor from Noida Sector-142 station to Botanical Garden, Noida of Noida Metro Rail Corporation (Noida Metro Rail Corporation Ltd. [NMRCL]) (616221) (-) (-)	Uttar Pradesh	03/2026 (03/2026)	03/2030 (-)	2254.35 (2254.35)	0	0
277	LUCKNOW METRO RAIL PROJECT PHASE-1B EAST WEST CORRIDOR (Uttar Pradesh metro rail corporation [UPMRC]) (619052) (-) (-)	Uttar Pradesh	09/2025 (05/2026)	04/2031 (-)	5801.05 (5801.05)	0.05	2
278	Kanpur Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702628) (-) (-)	Uttar Pradesh	05/2019 (11/2019)	05/2024 (03/2027)	11076.48 (11076.48)	9463.15	83
279	Agra Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702629) (-) (-)	Uttar Pradesh	05/2019 (12/2020)	05/2024 (06/2027)	8379.62 (8379.62)	6368.28	73
	Total (30)				320872.37	178627.24	
	Waste & Water						
280	ESR - 8 nos., distribution system - 216 Km, new house service connections - 38760 nos. upgrading of feeder mains, pumping station etc. - Phase II (Ministry of Housing & Urban Affairs) (702674) (-) (-)	Andhra Pradesh	02/2017 (07/2018)	03/2023 (08/2026)	172.22 (172.22)	88.86	82
281	Muzaffarpur Storm Water Drainage Phase-I Project (Ministry of Housing & Urban Affairs) (702699) (-) (-)	Bihar	11/2016 (02/2019)	10/2023 (06/2026)	158.78 (158.78)	135.72	85
282	Sewerage Management Scheme Part-3 Implementation (Ministry of Housing & Urban Affairs) (702734) (-) (-)	Haryana	03/2017 (11/2017)	09/2023 (09/2026)	278.01 (278.01)	228.49	88
283	Dhanbad Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702741) (-) (-)	Jharkhand	02/2017 (12/2018)	03/2023 (06/2026)	216.55 (216.55)	129.16	76
284	SAAP-3 Water Supply Infrastructure SAAP-3 Project (Ministry of Housing & Urban Affairs) (702742) (-) (-)	Jharkhand	02/2017 (12/2018)	10/2023 (06/2026)	159.31 (159.31)	87.5	67



All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
285	Augmentation and Strengthening of Urban Water Supply Phase 1 - SAAP 3 (Ministry of Housing & Urban Affairs) (702746) (-) (-)	Jharkhand	02/2017 (12/2018)	03/2023 (06/2026)	278.28 (278.28)	186.5	81
286	Belgavi Improvement in Sewerage System Project (Ministry of Housing & Urban Affairs) (702760) (-) (-)	Karnataka	12/2015 (10/2016)	07/2023 (06/2026)	162.73 (162.73)	79.5	80
287	Indore Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702793) (-) (-)	Madhya Pradesh	12/2016 (11/2017)	03/2023 (06/2026)	287.17 (287.17)	252.5	99
288	Satna Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702808) (-) (-)	Madhya Pradesh	11/2015 (12/2016)	03/2024 (08/2026)	191.56 (215.89)	200.32	96
289	Singrauli Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702810) (-) (-)	Madhya Pradesh	05/2016 (11/2017)	03/2023 (06/2026)	402.01 (438.10)	371.17	90
290	Kalyan-Dombivali Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702833) (-) (-)	Maharashtra	07/2016 (09/2019)	10/2023 (08/2026)	194.20 (194.20)	136.56	75
291	Jalandhar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (703021) (-) (-)	Punjab	11/2016 (08/2020)	08/2023 (08/2026)	258.53 (266.64)	161.02	90
292	Patiala Water Supply Infrastructure Part-2 Project (Ministry of Housing & Urban Affairs) (703057) (-) (-)	Punjab	11/2016 (08/2020)	10/2023 (08/2026)	287.00 (287.00)	213.64	99
293	Jhansi Water Supply Infrastructure Phase-II Project (Ministry of Housing & Urban Affairs) (702949) (-) (-)	Uttar Pradesh	03/2017 (06/2019)	07/2023 (08/2026)	561.74 (561.74)	506.52	95
294	Lucknow Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702958) (-) (-)	Uttar Pradesh	09/2016 (05/2019)	03/2023 (08/2026)	142.46 (173.21)	152.65	95
Total (15)					3750.55	2930.11	
Ministry of Mines							
Construction							
295	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata (Central Public Works Department [CPWD]) (617280) (-) (-)	West Bengal	04/2019 (02/2020)	08/2026 (-)	255.37 (255.37)	98.94	64
Total (1)					255.37	98.94	
Metals & Mining							
296	Expansion of Malanjkhand Copper Project (Hindustan Copper Limited [HCL]) (400426) (-) (-)	Madhya Pradesh	09/2011 (04/2015)	04/2020 (03/2029)	1856.36 (3800.00)	1018.09	28
297	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonne Per Annum (National Aluminium Company Limited [NALCO]) (400141) (-) (-)	Odisha	04/2017 (04/2017)	12/2022 (06/2026)	4103.00 (5677.40)	5023.49	95.64
298	Pottangi Bauxite Mines Project (National Aluminium Company Limited [NALCO]) (400299) (-) (-)	Odisha	05/2018 (05/2018)	03/2025 (11/2026)	1381.00 (1960.77)	770.37	52.4
299	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (National Aluminium Company Limited [NALCO]) (709831) (-) (-)	Odisha	11/2017 (11/2019)	05/2025 (06/2026)	483.00 (483.00)	453.89	93.18
300	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (National Aluminium Company Limited [NALCO]) (709832) (-) (-)	Tamil Nadu	09/2017 (12/2017)	03/2025 (03/2026)	166.00 (166.00)	135	70
Total (5)					7989.36	7400.84	
Department of Higher Education							
Education							
301	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008) (-) (-)	Andhra Pradesh	09/2019 (12/2023)	06/2027 (-)	305.00 (305.00)	67.73	44.5
302	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898) (-) (-)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (08/2024)	592.61 (592.61)	551.3	80
303	Tezpur University Projects (Tezpur University) (606112) (-) (-)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 (153.71)	266.14	97.98

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
304	Additional Campus of NITPatna (NIT Patna) (606013) (-) (-)	Bihar	07/2022 (08/2022)	07/2024 (01/2026)	499.21 (499.21)	449.96	98.6
305	Phase B Construction of Permanent Campus of IIT Bhilai (Indian Institute of Technology, Bhilai) (617877) (-) (-)	Chhattisgarh	05/2025 (01/2026)	10/2028 (-)	1188.97 (1188.97)	1.92	0
306	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis (National Institute of Technology Delhi) (612851) (-) (-)	Delhi	09/2009 (11/2022)	09/2025 (01/2026)	333.49 (336.42)	336.42	100
307	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886) (-) (-)	Delhi	09/2024 (03/2025)	10/2026 (-)	373.00 (373.00)	31.53	14
308	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Central University of Gujarat) (612916) (-) (-)	Gujarat	12/2020 (02/2021)	03/2025 (03/2026)	490.63 (490.63)	342.26	86
309	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099) (-) (-)	Himachal Pradesh	09/2018 (08/2020)	10/2023 (08/2026)	392.51 (454.78)	339.65	98.6
310	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128) (-) (-)	Himachal Pradesh	03/2023 (03/2024)	03/2026 (09/2026)	166.66 (166.66)	138.26	93
311	Construction of Permanent Campus of Central University of Himachal Pradesh at Dehra, District - Kangra, [H.P.] on Engineering. Procurement and Construction [EPC Mode 1] Basis. (Central University, Himachal Pradesh) (612894) (-) (-)	Himachal Pradesh	03/2021 (08/2022)	11/2024 (03/2026)	251.98 (300.45)	223.6	86
312	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098) (-) (-)	Jammu and Kashmir	03/2019 (10/2020)	06/2023 (11/2025)	424.93 (500.91)	484.52	96
313	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431) (-) (-)	Kerala	07/2017 (03/2020)	06/2022 (06/2026)	1006.45 (1217.40)	686.2	86.5
314	Phase B of Construction of Permanent Campus of IIT Palakkad (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (617878) (-) (-)	Kerala	05/2025 (01/2026)	10/2028 (-)	1527.00 (1527.00)	9.8	0
315	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] (Indian Institute of Technology, Indore) (611957) (-) (-)	Madhya Pradesh	12/2023 (04/2024)	02/2027 (-)	496.28 (496.28)	97.35	67.5
316	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885) (-) (-)	Meghalaya	09/2009 (09/2014)	03/2022 (10/2026)	494.52 (429.70)	377.82	97.5
317	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876) (-) (-)	Mizoram	09/2009 (06/2014)	12/2029 (03/2022)	474.23 (474.23)	167.55	4
318	Establishment of NIT Nagaland (NIT Nagaland) (613013) (-) (-)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	263.25	98
319	IISER BERHAMPUR (Indian Institutes of Science Education and Research, Behrampur) (610315) (-) (-)	Odisha	10/2018 (09/2019)	03/2021 (06/2026)	1229.32 (843.09)	874.09	98.5
320	Construction of IIT Bhubaneswar -Phase III (Indian Institute of Technology, Bhubaneshwar) (611961) (-) (-)	Odisha	02/2024 (05/2024)	11/2026 (-)	454.27 (454.27)	102.15	10.45
321	1000 seater Boys hostel, 500 seater Girls hostel, 1.5 MLD Sewage Treatment Plant and Faculty Residence - 72 nos. Flats (NIT Rourkela) (619033) (-) (-)	Odisha	09/2023 (01/2024)	06/2026 (08/2027)	198.97 (198.97)	53.01	50
322	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] (National Institute of Technology, Puducherry) (612877) (-) (-)	Puducherry	09/2009 (07/2013)	12/2024 (05/2026)	618.34 (544.34)	543.74	99.5
323	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I (Indian intitue of Management, Amritsar) (605292) (-) (-)	Punjab	10/2019 (07/2020)	06/2023 (11/2026)	348.31 (386.86)	293.24	91.7

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
324	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment (Central University of Punjab) (617221) (-) (-)	Punjab	08/2024 (04/2025)	10/2027 (-)	210.99 (210.99)	99.02	58
325	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736) (-) (-)	Sikkim	08/2020 (01/2022)	01/2025 (10/2026)	314.06 (340.55)	292	96.5
326	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883) (-) (-)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	283.56	38
327	Construction of Precast housing and hostels at IIT Hyderabad (Indian Institute of Technology, Hyderabad) (609996) (-) (-)	Telangana	09/2022 (11/2022)	10/2024 (01/2026)	262.00 (262.00)	223.65	90.39
328	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] (Banaras Hindu University) (606479) (-) (-)	Uttar Pradesh	06/2020 (06/2020)	09/2022 (07/2027)	246.00 (246.00)	212.35	99.1
329	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal (National Institute of Technology Uttarakhand) (611963) (-) (-)	Uttarakhand	06/2020 (04/2024)	09/2027 (-)	650.85 (650.85)	401.56	63
330	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur (Indian Institute of Technology, Kharagpur) (609019) (-) (-)	West Bengal	06/2018 (04/2019)	03/2023 (12/2026)	500.00 (442.00)	418.86	97
	Total (30)				15165.68	8632.49	
	Department of Sports						
	Education						
331	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081) (-) (-)	Manipur	06/2022 (01/2022)	08/2024 (08/2026)	906.47 (611.74)	577.32	97.5
	Total (1)				906.47	577.32	
	Ministry of Petroleum & Natural Gas						
	Energy Storage						
332	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754) (-) (-)	Assam	03/2023 (03/2023)	07/2027 (-)	156.36 (156.36)	114.1	83.8
333	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709755) (-) (-)	Assam	03/2023 (03/2023)	07/2027 (-)	384.04 (384.04)	250.07	87.5
334	Capacity Augmentation of Kandla LPG Import Terminal [KLIT] from 0.6 MMTPA to 2.5 MMTPA (Indian Oil Corporation Limited [IOCL]) (617839) (-) (-)	Gujarat	05/2023 (05/2023)	07/2026 (-)	356.86 (304.40)	168.04	68
335	Andheri Residential Towers, Mumbai (Indian Oil Corporation Limited [IOCL]) (604833) (-) (-)	Maharashtra	06/2017 (06/2017)	05/2025 (06/2027)	281.35 (389.67)	281.24	86
336	Setting up of 50 MW [plus/minus 5 percent] Wind Power Plant for Captive Consumption at MR (Bharat Petroleum Corporation Limited [BPCL]) (619313) (-) (-)	Maharashtra	05/2023 (05/2023)	04/2027 (-)	483.14 (483.14)	380.62	77.9
337	LPG Bottling Plant at Mualkhang (Indian Oil Corporation Limited [IOCL]) (617829) (-) (-)	Mizoram	07/2024 (07/2024)	10/2028 (03/2028)	225.71 (225.71)	32.45	34
338	Petrochemical evacuation marketing terminal at Barmer, Rajasthan (Hindustan Petroleum Corporation Limited) (709759) (-) (-)	Rajasthan	12/2023 (12/2023)	12/2026 (-)	461.05 (461.05)	252.18	97.5
339	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] (Ministry of Petroleum Natural Gas) (400043) (-) (-)	Tamil Nadu	01/2022 (01/2022)	05/2026 (03/2027)	829.00 (829.00)	382.47	81
340	Multi Product Pipeline from Irugur to Devangonchi (Ministry of Petroleum Natural Gas) (400301) (-) (-)	Tamil Nadu	11/2012 (11/2012)	02/2017 (09/2026)	678.00 (1732.00)	1206.36	86.4
341	Kandla Gorakhpur LPG Pipeline (Indian Oil Corporation Limited [IOCL]) (400012) (-) (-)	Uttar Pradesh	12/2018 (12/2018)	12/2021 (10/2026)	10088.00 (10088.00)	8504.21	96
342	Grass-root Terminal at Mirzapur, Uttar Pradesh (Indian Oil Corporation Limited [IOCL]) (604852) (-) (-)	Uttar Pradesh	09/2022 (09/2022)	11/2026 (-)	980.45 (980.45)	308.35	77.2

All Ongoing Projects							JULY 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
343	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (<i>Numaligarh Refinery Limited</i>) (701349) (-) (-)	West Bengal	01/2019 (01/2019)	07/2024 (10/2026)	10228.00 (12407.00)	11168.49	93.2
	Total (12)				25151.96	23048.58	
	Oil & Gas						
344	KG-DWN-98/2 Cluster - II Development Project - NELP Block (<i>Oil and Natural Gas Corporation Limited [ONGC]</i>) (400120) (-) (-)	Andhra Pradesh	03/2016 (03/2016)	06/2020 (09/2026)	34012.00 (34012.00)	33192	96.9
345	Provision of four bitumen tanks with capacity of 5 TMT each at Visakh Refinery (<i>Hindustan Petroleum Corporation Limited</i>) (619226) (-) (-)	Andhra Pradesh	09/2025 (09/2025)	03/2028 (-)	258.34 (258.34)	8.67	20.2
346	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery (<i>Hindustan Petroleum Corporation Limited</i>) (709752) (-) (-)	Andhra Pradesh	09/2021 (09/2021)	06/2024 (02/2027)	160.00 (220.00)	158.94	94
347	Numaligarh Refinery Expansion Project (<i>Numaligarh Refinery Limited</i>) (604791) (-) (-)	Assam	07/2020 (07/2020)	07/2024 (03/2027)	12366.00 (25313.00)	20411.19	87
348	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (<i>Oil India Limited</i>) (604863) (-) (-)	Assam	01/2018 (01/2018)	02/2020 (12/2026)	682.90 (726.93)	601.12	94.4
349	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (<i>Oil India Limited</i>) (616858) (-) (-)	Assam	12/2020 (12/2020)	03/2024 (11/2026)	430.76 (430.76)	348.65	95.9
350	Pipeline Rehabilitation Project, Phase-II (<i>Oil India Limited</i>) (617827) (-) (-)	Assam	12/2024 (12/2024)	12/2029 (-)	680.00 (680.00)	13.53	29
351	Coke Drum Structure Package (<i>Numaligarh Refinery Limited</i>) (617836) (-) (-)	Assam	12/2022 (12/2022)	12/2025 (-)	635.28 (635.28)	464.46	72
352	Group Gathering Station, Lakwagaon (<i>Oil India Limited</i>) (619316) (-) (-)	Assam	10/2025 (10/2025)	10/2027 (-)	495.59 (495.59)	20.04	7.8
353	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (<i>Indian Oil Corporation Limited [IOCL]</i>) (709776) (-) (-)	Assam	04/2022 (04/2022)	09/2026 (-)	277.00 (323.09)	236.16	84.3
354	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (<i>Indian Oil Corporation Limited [IOCL]</i>) (709779) (-) (-)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768.00 (740.00)	250.84	60.1
355	Pipeline Network Project Rudrasagar (<i>Oil and Natural Gas Corporation Limited [ONGC]</i>) (709847) (-) (-)	Assam	01/2023 (01/2023)	04/2026 (04/2027)	481.03 (481.03)	238.83	55.4
356	Borholla GGS Life Extension Project [BLEP] (<i>Oil and Natural Gas Corporation Limited [ONGC]</i>) (709850) (-) (-)	Assam	09/2023 (09/2023)	05/2026 (03/2027)	198.70 (198.70)	110.99	63.5
357	DCU Revamp Project (<i>Numaligarh Refinery Limited</i>) (709864) (-) (-)	Assam	08/2021 (08/2021)	07/2024 (03/2027)	370.00 (370.00)	310.38	80.5
358	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (<i>Numaligarh Refinery Limited</i>) (709865) (-) (-)	Assam	04/2023 (04/2023)	12/2024 (12/2026)	293.50 (293.50)	81.84	99
359	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar (<i>Bharat Petroleum Corporation Limited [BPCL]</i>) (617304) (-) (-)	Bihar	10/2023 (10/2023)	03/2027 (-)	340.15 (340.15)	186.21	56
360	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA (<i>Indian Oil Corporation Limited [IOCL]</i>) (701324) (-) (-)	Bihar	01/2020 (01/2020)	04/2023 (12/2026)	14810.00 (16724.00)	13089.84	91.8
361	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery (<i>Indian Oil Corporation Limited [IOCL]</i>) (709777) (-) (-)	Bihar	01/2022 (01/2022)	04/2025 (06/2027)	389.35 (410.30)	124.57	66.3
362	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts (<i>Bharat Petroleum Corporation Limited [BPCL]</i>) (709792) (-) (-)	Bihar	12/2022 (12/2022)	03/2030 (-)	3638.00 (3638.00)	493.91	33.6

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
363	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts (Bharat Petroleum Corporation Limited [BPCL]) (709793) (-) (-)	Bihar	12/2022 (12/2022)	06/2030 (-)	3919.00 (3919.00)	527.15	30.3
364	City Gas Distribution [CGD] Project in Kondagaon, Bastar, Sukma, Narayanpur, Bijapur & Dantewada GA (GAIL Gas) (617819) (-) (-)	Chhattisgarh	06/2022 (06/2022)	06/2030 (-)	557.04 (557.04)	11.63	2.2
365	Redevelopment of Sobhasan Complex (Oil and Natural Gas Corporation Limited [ONGC]) (400087) (-) (-)	Gujarat	08/2021 (08/2021)	03/2027 (-)	885.63 (1347.61)	1062.32	95.6
366	Redevelopment of Santhal Field [Onshore-Mehsana Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (400167) (-) (-)	Gujarat	02/2017 (02/2017)	03/2026 (12/2026)	1162.56 (1162.56)	1127.73	96.8
367	Redevelopment of Linch Field (Oil and Natural Gas Corporation Limited [ONGC]) (400169) (-) (-)	Gujarat	04/2021 (04/2021)	03/2025 (10/2026)	631.03 (845.42)	622.24	93.7
368	Petrochemical and Lube Integration Project at Gujarat Refinery (Indian Oil Corporation Limited [IOCL]) (701329) (-) (-)	Gujarat	09/2020 (09/2020)	08/2024 (11/2026)	18936.00 (17825.00)	13901.13	89.6
369	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery (Indian Oil Corporation Limited [IOCL]) (709778) (-) (-)	Gujarat	01/2022 (01/2022)	08/2025 (12/2026)	328.29 (344.36)	218.17	87.7
370	Commercial Polymer Flooding Project in Bechraji field (Oil and Natural Gas Corporation Limited [ONGC]) (709838) (-) (-)	Gujarat	01/2022 (01/2022)	11/2024 (05/2027)	621.40 (739.02)	280.45	50
371	Restoration of Gas Terminal, Phase-I [Part-A], Hazira (Oil and Natural Gas Corporation Limited [ONGC]) (709840) (-) (-)	Gujarat	05/2022 (05/2022)	02/2025 (-)	249.43 (249.43)	219.56	97.6
372	Old Pipe Line Replacement [OPRP] Group-A (Oil and Natural Gas Corporation Limited [ONGC]) (709841) (-) (-)	Gujarat	07/2021 (07/2021)	07/2025 (11/2026)	173.03 (169.84)	168.22	94.6
373	Kalol Redevelopment Project, Ahmedabad Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709842) (-) (-)	Gujarat	08/2022 (08/2022)	03/2027 (-)	1487.41 (1487.41)	946.45	66
374	Revamping of SV Stations, Gas Terminal & Kribhco Terminal (Oil and Natural Gas Corporation Limited [ONGC]) (709845) (-) (-)	Gujarat	11/2022 (11/2022)	08/2026 (-)	837.34 (1119.86)	469.99	70.9
375	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad (Indian Oil Corporation Limited [IOCL]) (604853) (-) (-)	Haryana	06/2019 (06/2019)	12/2022 (07/2027)	2281.94 (3200.00)	1922.03	65.4
376	Poly Butadiene Rubber plant at Panipat (Indian Oil Corporation Limited [IOCL]) (611917) (-) (-)	Haryana	03/2022 (03/2022)	03/2025 (12/2026)	1459.00 (2531.44)	1560.24	90.1
377	Capacity Expansion of Panipat Refinery from 15 to 25 MMTPA (Indian Oil Corporation Limited [IOCL]) (701289) (-) (-)	Haryana	02/2021 (02/2021)	09/2024 (12/2026)	34627.00 (36225.00)	28007.35	94.3
378	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. (Indian Oil Corporation Limited [IOCL]) (709783) (-) (-)	Haryana	12/2020 (12/2020)	06/2023 (10/2026)	165.13 (247.69)	193.38	92.5
379	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts (Indian Oil Corporation Limited [IOCL]) (709773) (-) (-)	Jammu and Kashmir	03/2022 (03/2022)	09/2034 (-)	538.00 (538.00)	4.45	0.6
380	Development of Jharia CBM Block [Phase-1] (Oil and Natural Gas Corporation Limited [ONGC]) (610984) (-) (-)	Jharkhand	11/2019 (11/2019)	01/2024 (09/2026)	431.00 (431.00)	267.74	66.2
381	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] (Indian Oil Corporation Limited [IOCL]) (709785) (-) (-)	Jharkhand	02/2023 (02/2023)	02/2026 (03/2027)	202.07 (202.07)	65.98	58.4
382	Power System Upgradation Project (Mangalore Refinery and Petrochemicals Limited) (612790) (-) (-)	Karnataka	10/2023 (10/2023)	11/2025 (09/2026)	385.00 (385.00)	271.36	90.4
383	Demo Bio-ATF Project (Mangalore Refinery and Petrochemicals Limited) (616879) (-) (-)	Karnataka	03/2024 (03/2024)	01/2027 (-)	364.00 (364.00)	91.39	54.8
384	City Gas Distribution Maharashtra Natural Gas Limited (Gas Authority of India Limited [GAIL]) (701338) (-) (-)	Karnataka	01/2006 (01/2006)	06/2031 (-)	5535.00 (5535.00)	4481.93	47

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
385	Revamping/ Augmentation of facilities at existing port terminal at Mangalore (Indian Oil Corporation Limited [IOCL]) (709774) (-) (-)	Karnataka	01/2022 (01/2022)	12/2025 (06/2027)	463.00 (500.62)	327.65	85.6
386	Augmentation of CCKPL and IDPL Pipelines capacity along with setting up of Palakkad TOP (Bharat Petroleum Corporation Limited [BPCL]) (617838) (-) (-)	Kerala	09/2024 (09/2024)	08/2028 (-)	1130.00 (1130.00)	324.61	48.8
387	Setting up Polypropylene Unit at Kochi Refinery (Bharat Petroleum Corporation Limited [BPCL]) (709799) (-) (-)	Kerala	12/2023 (12/2023)	10/2027 (-)	4460.00 (4850.00)	1026	45.2
388	C2/C3 Vijaipur Pata Pipeline (Gas Authority of India Limited [GAIL]) (617830) (-) (-)	Madhya Pradesh	05/2024 (05/2024)	01/2027 (-)	1792.00 (1792.00)	541.2	73
389	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery (Bharat Petroleum Corporation Limited [BPCL]) (709798) (-) (-)	Madhya Pradesh	05/2023 (05/2023)	05/2028 (-)	43367.00 (43367.00)	6104	33.5
390	500 KTA PDHPP Project, Usar (Gas Authority of India Limited [GAIL]) (400168) (-) (-)	Maharashtra	04/2021 (04/2021)	04/2025 (06/2027)	8797.00 (11256.00)	8861.88	91.9
391	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery (Hindustan Petroleum Corporation Limited) (616933) (-) (-)	Maharashtra	12/2024 (12/2024)	03/2028 (08/2029)	4679.00 (6008.00)	314.9	14.1
392	Petro Resid Fluidized Catalytic Cracking [PRFCC] Unit and its associated facilities at Mumbai Refinery (Bharat Petroleum Corporation Limited [BPCL]) (619223) (-) (-)	Maharashtra	05/2025 (05/2025)	09/2029 (-)	13626.00 (13626.00)	93.6	7.2
393	Augmentation of DUPL-DPPL Pipeline (Gas Authority of India Limited [GAIL]) (619224) (-) (-)	Maharashtra	06/2025 (06/2025)	03/2028 (-)	844.00 (844.00)	1.2	8.2
394	Installation of Compression facility at GAIL Usar (Gas Authority of India Limited [GAIL]) (619225) (-) (-)	Maharashtra	04/2025 (04/2025)	04/2027 (-)	260.20 (260.20)	0	0
395	ONGC-BP Redevelopment Phase-1 Scheme of Mumbai High Field (Oil and Natural Gas Corporation Limited [ONGC]) (619328) (-) (-)	Maharashtra	11/2025 (11/2025)	03/2027 (-)	3713.40 (3908.00)	2304.68	56.3
396	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts (Indian Oil Corporation Limited [IOCL]) (709771) (-) (-)	Maharashtra	03/2022 (03/2022)	09/2031 (-)	865.00 (865.00)	89.23	3.4
397	Construction of Additional Tankages and Allied Facilities at JNPT Terminal (Indian Oil Corporation Limited [IOCL]) (709780) (-) (-)	Maharashtra	04/2022 (04/2022)	08/2026 (-)	341.43 (436.14)	305.01	72.9
398	POL & LOBS Installations with Receipt Pipelines at Rasayani (Bharat Petroleum Corporation Limited [BPCL]) (709797) (-) (-)	Maharashtra	05/2023 (05/2023)	05/2026 (-)	2585.00 (2585.00)	1507.62	87.3
399	Visakh Raipur Pipeline Project (Hindustan Petroleum Corporation Limited) (616254) (-) (-)	Multi-States (Chhattisgarh, Odisha)	09/2024 (09/2024)	09/2027 (-)	2212.00 (2212.00)	570	38.4
400	Change of service of existing Mundra-Panipat Pipeline [Panipat - Churwa section] from Crude oil to Product (Indian Oil Corporation Limited [IOCL]) (619196) (-) (-)	Multi-States (Gujarat, Haryana, Rajasthan)	05/2025 (05/2025)	04/2027 (-)	359.00 (359.00)	52.55	43.3
401	Augmentation/ Revamping of Dimapur Depot, Dimapur (Indian Oil Corporation Limited [IOCL]) (709786) (-) (-)	Nagaland	08/2023 (08/2023)	11/2027 (-)	227.62 (227.62)	28.03	43
402	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (Indian Oil Corporation Limited [IOCL]) (604859) (-) (-)	Odisha	07/2020 (07/2020)	01/2024 (08/2026)	13805.00 (11783.00)	8870.29	94.9
403	City Gas Distribution [CGD] Project in Gajapati, Kandhamal, Boudh, & Sonepur GA (GAIL Gas) (617818) (-) (-)	Odisha	02/2022 (02/2022)	12/2031 (-)	514.91 (514.91)	25.77	5.8
404	CUF POL Depot at Sadashibpur [Meramundali], Odisha (Bharat Petroleum Corporation Limited [BPCL]) (709800) (-) (-)	Odisha	04/2021 (04/2021)	03/2026 (09/2026)	393.54 (393.54)	233.3	86
405	Life Extension of 48 well platforms of Mumbai High & Heera Fields (Oil and Natural Gas Corporation Limited [ONGC]) (400119) (-) (-)	Offshore	12/2015 (12/2015)	04/2018 (10/2026)	3190.69 (3375.90)	3123.2	90
406	PRP-VIII [Group-A] (Oil and Natural Gas Corporation Limited [ONGC]) (616950) (-) (-)	Offshore	09/2024 (09/2024)	02/2026 (-)	1589.40 (1486.40)	629.46	60.2

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
407	Pipeline Replacement Project- PRP-IX (Oil and Natural Gas Corporation Limited [ONGC]) (619314) (-) (-)	Offshore	08/2025 (08/2025)	05/2027 (-)	6684.00 (6175.00)	979.47	23.5
408	Daman Upside Development Project (Oil and Natural Gas Corporation Limited [ONGC]) (709839) (-) (-)	Offshore	06/2022 (06/2022)	10/2025 (12/2026)	4144.41 (6406.90)	6302.5	92.9
409	MHN TCPP PGC BGC Project [MTPBP] (Oil and Natural Gas Corporation Limited [ONGC]) (709848) (-) (-)	Offshore	06/2022 (06/2022)	05/2026 (12/2026)	2329.45 (2354.23)	1930.25	95.6
410	PRP-VIII Group B [NH & BS Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (709849) (-) (-)	Offshore	06/2024 (06/2024)	02/2026 (12/2026)	2546.90 (3348.60)	3003.9	98.7
411	Integrated Development of 4 Contract Areas under DSF-II (Oil and Natural Gas Corporation Limited [ONGC]) (709851) (-) (-)	Offshore	05/2023 (05/2023)	04/2027 (-)	6183.79 (6183.79)	2053	47.4
412	2G Ethanol Biorefinery at Bathinda (Hindustan Petroleum Corporation Limited) (400171) (-) (-)	Punjab	05/2020 (05/2020)	02/2023 (12/2026)	1421.46 (1421.46)	1291.35	95.9
413	Gurdaspur Jammu Pipeline (Gas Authority of India Limited [GAIL]) (612853) (-) (-)	Punjab	07/2023 (07/2023)	07/2026 (-)	521.90 (521.90)	326.4	91.1
414	City Gas Distribution Project at Pathankot District (Indian Oil Corporation Limited [IOCL]) (709770) (-) (-)	Punjab	03/2022 (03/2022)	09/2033 (-)	151.00 (151.00)	9.02	2
415	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (Indian Oil Corporation Limited [IOCL]) (701330) (-) (-)	Rajasthan	07/2011 (07/2011)	06/2024 (-)	7392.00 (7392.00)	6360.86	90.2
416	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (Bharat Petroleum Corporation Limited [BPCL]) (709794) (-) (-)	Rajasthan	12/2022 (12/2022)	06/2030 (-)	3207.00 (3207.00)	429.3	31.1
417	CBR 9 MMTPA Project (Chennai Petroleum Corporation Limited [CPCL]) (604795) (-) (-)	Tamil Nadu	09/2021 (09/2021)	06/2025 (-)	31580.00 (36354.00)	1615.38	10.2
418	Kochi - Kootanad - Bangalore - Mangalore Pipeline Phase-II (Gas Authority of India Limited [GAIL]) (701228) (-) (-)	Tamil Nadu	06/2009 (06/2009)	12/2012 (09/2026)	2915.00 (5909.00)	4881.8	97.4
419	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore (Chennai Petroleum Corporation Limited [CPCL]) (709750) (-) (-)	Tamil Nadu	01/2024 (01/2024)	09/2025 (12/2026)	205.00 (205.00)	117.88	76.9
420	City Gas Distribution Projects at the Nilgiris and Erode districts (Bharat Petroleum Corporation Limited [BPCL]) (709796) (-) (-)	Tamil Nadu	12/2022 (12/2022)	03/2030 (-)	3685.00 (3685.00)	303.1	25.5
421	ATF Pipeline from BPCLs Malkapur POL Installation to Hyderabad International airport (Bharat Petroleum Corporation Limited [BPCL]) (617822) (-) (-)	Telangana	03/2025 (03/2025)	09/2027 (-)	215.00 (215.00)	46.87	29.1
422	North East Gas Grid (Indradhanush Gas Grid Limited) (701346) (-) (-)	Tripura	04/2020 (04/2020)	03/2024 (03/2028)	9265.00 (9265.00)	7008	88.2
423	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837) (-) (-)	Tripura	03/2022 (03/2022)	05/2024 (10/2026)	209.33 (131.51)	81.31	71.3
424	Kanpur LPG Bottling Plant (Bharat Petroleum Corporation Limited [BPCL]) (619191) (-) (-)	Uttar Pradesh	09/2025 (09/2025)	09/2027 (-)	202.00 (202.00)	132.75	62.5
425	Bulk Loading Hub- Kanpur (Bharat Petroleum Corporation Limited [BPCL]) (619312) (-) (-)	Uttar Pradesh	09/2025 (09/2025)	09/2027 (-)	186.00 (186.00)	104.24	62.5
426	Revamping / Augmentation of Facilities at Mathura Bitumen Plant (Indian Oil Corporation Limited [IOCL]) (709781) (-) (-)	Uttar Pradesh	04/2022 (04/2022)	06/2027 (12/2026)	260.12 (260.12)	23.58	57.3
427	City Gas Distribution Projects at Lakhimpur Kheri , Sitapur, Bahraich, Shravasti,Balrampur, Siddharth Nagar & Maharajganj districts (Bharat Petroleum Corporation Limited [BPCL]) (709795) (-) (-)	Uttar Pradesh	12/2022 (12/2022)	06/2030 (-)	16654.00 (16654.00)	754.7	19.8
428	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] (Gas Authority of India Limited [GAIL]) (617302) (-) (-)	West Bengal	03/2017 (03/2017)	12/2020 (09/2026)	1740.00 (2583.00)	2380.8	95.7

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
429	Siliguri-Jhapa Pipeline Project (Indian Oil Corporation Limited [IOCL]) (617828) (-) (-)	West Bengal	09/2024 (09/2024)	08/2029 (08/2029)	267.00 (267.00)	3.19	16.5
430	Siliguri Marketing Terminal [SMT] Capacity Augmentation Project (Numaligarh Refinery Limited) (617837) (-) (-)	West Bengal	11/2021 (11/2021)	12/2025 (10/2026)	484.00 (484.00)	319.32	89
431	Dhamra Haldia Pipeline Project (Gas Authority of India Limited [GAIL]) (701344) (-) (-)	West Bengal	03/2020 (03/2020)	11/2022 (09/2026)	1030.65 (1125.00)	927.4	94.4
432	Haldia Panagarh Pipeline Project (Hindustan Petroleum Corporation Limited) (709753) (-) (-)	West Bengal	11/2022 (11/2022)	11/2025 (08/2026)	1010.00 (1107.00)	884.2	98.3
433	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts (Indian Oil Corporation Limited [IOCL]) (709772) (-) (-)	West Bengal	03/2022 (03/2022)	06/2031 (-)	609.00 (609.00)	64.44	3
434	City Gas Distribution Projects at Alipurduar and Cooch Behar (Bharat Petroleum Corporation Limited [BPCL]) (709791) (-) (-)	West Bengal	12/2022 (12/2022)	03/2030 (-)	1017.00 (1017.00)	238.41	43.8
	Total (91)				362394.10	204670.66	
	Ministry of Health & Family Welfare						
	Healthcare						
435	AIIMS Darbhanga (PMSSY AND Institute of NATIONAL Importance) (701172) (-) (-)	Bihar	09/2020 (09/2020)	07/2029 (-)	2006.07 (2006.07)	40.33	1.12
436	Establishment of new GMC Saran [Chhapara] (Medical Education, Ministry of Health and Family Welfare) (706965) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	189.00 (189.00)	113.4	0
437	Establishment of new GMC Samastipur (Medical Education, Ministry of Health and Family Welfare) (706966) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	189.00 (189.00)	113.4	0
438	Establishment of new GMC Sitamarhi (Medical Education, Ministry of Health and Family Welfare) (707016) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	250.00 (250.00)	150	0
439	Establishment of new GMC Jhanjharpur (Medical Education, Ministry of Health and Family Welfare) (707017) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	250.00 (250.00)	150	0
440	Establishment of new GMC Siwan (Medical Education, Ministry of Health and Family Welfare) (707018) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	250.00 (250.00)	150	0
441	Establishment of new GMC Buxar (Medical Education, Ministry of Health and Family Welfare) (707019) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	250.00 (250.00)	150	0
442	Establishment of new GMC Jamui (Medical Education, Ministry of Health and Family Welfare) (707020) (-) (-)	Bihar	03/2019 (10/2022)	10/2025 (-)	250.00 (500.00)	103.21	50
443	Establishment of new GMC Korba (Medical Education, Ministry of Health and Family Welfare) (707044) (-) (-)	Chhattisgarh	02/2023 (10/2023)	12/2026 (-)	325.00 (322.85)	179.49	55
444	Establishment of new GMC Mahasamund (Medical Education, Ministry of Health and Family Welfare) (707045) (-) (-)	Chhattisgarh	10/2023 (10/2023)	05/2026 (-)	325.00 (325.00)	321.7	84
445	Establishment of new GMC Kanker (Medical Education, Ministry of Health and Family Welfare) (707046) (-) (-)	Chhattisgarh	02/2020 (09/2024)	03/2027 (-)	325.00 (325.00)	37	45
446	Setting up IT Infrastructure including Network Security and Hosting at AIIMS, New Delhi (PMSSY AND Institute of NATIONAL Importance) (617882) (-) (-)	Delhi	09/2025 (09/2025)	09/2026 (-)	358.19 (358.19)	53.73	40
447	Redevelopment of Residential colonies at Ayur Vigyan Nagar and West Ansari Nagar campuses of AIIMS, New Delhi (PMSSY AND Institute of NATIONAL Importance) (617883) (-) (-)	Delhi	10/2016 (06/2022)	06/2027 (-)	4441.00 (4441.00)	44.44	57
448	AIIMS Rajkot (PMSSY AND Institute of NATIONAL Importance) (701170) (-) (-)	Gujarat	01/2019 (01/2019)	03/2026 (12/2026)	1195.00 (1195.00)	805.48	94
449	Establishment of new GMC Panchmahal (Medical Education, Ministry of Health and Family Welfare) (707049) (-) (-)	Gujarat	09/2022 (09/2022)	03/2026 (-)	325.00 (663.50)	467.34	88

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
450	Establishment of new GMC Porbandar (Medical Education, Ministry of Health and Family Welfare) (707050) (-) (-)	Gujarat	04/2022 (10/2022)	09/2024 (-)	325.00 (618.98)	936.64	81
451	AIIMS Majra Rewari Haryana (Ministry of Health and Family Welfare) (701173) (-) (-)	Haryana	02/2019 (02/2019)	12/2026 (12/2026)	1299.00 (1646.43)	747.62	67.45
452	AIIMS Kashmir at Awantipora Jammu & Kashmir (PMSSY AND Institute of NATIONAL Importance) (701167) (-) (-)	Jammu and Kashmir	01/2019 (03/2019)	12/2025 (12/2026)	1828.00 (2570.19)	1602.61	79
453	Establishment of new GMC Udhampur (Medical Education, Ministry of Health and Family Welfare) (707051) (-) (-)	Jammu and Kashmir	09/2019 (01/2022)	03/2027 (-)	325.00 (325.00)	222	75
454	Establishment of new GMC Handwara [Distt. Kupwara] (Medical Education, Ministry of Health and Family Welfare) (707052) (-) (-)	Jammu and Kashmir	NA (01/1900)	01/1900 (-)	325.00 (325.00)	173	0
455	Establishment of new GMC Koderma (Medical Education, Ministry of Health and Family Welfare) (707021) (-) (-)	Jharkhand	09/2023 (02/2024)	08/2026 (-)	250.00 (504.80)	271	40
456	Establishment of new GMC Chaibasa [Singbhum] (Medical Education, Ministry of Health and Family Welfare) (707022) (-) (-)	Jharkhand	06/2018 (03/2023)	09/2025 (-)	250.00 (454.10)	65	57
457	Establishment of new GMC Leh (Medical Education, Ministry of Health and Family Welfare) (707057) (-) (-)	Ladakh	10/2019 (01/1900)	01/1900 (-)	325.00 (325.00)	127	0
458	Establishment of new GMC Rajgarh (Medical Education, Ministry of Health and Family Welfare) (707058) (-) (-)	Madhya Pradesh	12/2021 (11/2022)	04/2024 (-)	325.00 (325.00)	179.5	86
459	Establishment of new GMC Mandla (Medical Education, Ministry of Health and Family Welfare) (707059) (-) (-)	Madhya Pradesh	08/2023 (10/2023)	04/2026 (-)	325.00 (325.00)	89.41	45
460	Establishment of new GMC Gondia (Medical Education, Ministry of Health and Family Welfare) (706988) (-) (-)	Maharashtra	07/2021 (01/1900)	01/1900 (-)	189.00 (189.00)	113.4	40.14
461	Establishment of new GMC West Garo Hills [Tura] (Medical Education, Ministry of Health and Family Welfare) (706989) (-) (-)	Meghalaya	NA (01/1900)	01/1900 (-)	189.00 (189.00)	170.1	0
462	Establishment of new GMC Mon (Medical Education, Ministry of Health and Family Welfare) (707067) (-) (-)	Nagaland	NA (01/1900)	01/1900 (-)	325.00 (325.00)	155	0
463	Establishment of new GMC Kapurthala (Medical Education, Ministry of Health and Family Welfare) (707069) (-) (-)	Punjab	11/2019 (07/2027)	12/2028 (-)	325.00 (550.00)	50	0
464	Establishment of new GMC Hoshiarpur (Medical Education, Ministry of Health and Family Welfare) (707070) (-) (-)	Punjab	01/2020 (03/2026)	12/2028 (-)	325.00 (374.75)	2.04	5
465	Establishment of new GMC Gangtok (Medical Education, Ministry of Health and Family Welfare) (707039) (-) (-)	Sikkim	10/2018 (12/2018)	12/2026 (07/2026)	250.00 (635.21)	667.21	92
466	ALL India Institute of Medical Sciences-AIIMS Madurai (PMSSY AND Institute of NATIONAL Importance) (701168) (-) (-)	Tamil Nadu	12/2018 (12/2018)	08/2022 (10/2026)	1264.00 (2021.51)	540.92	54
467	AIIMS Bibinagar (PMSSY AND Institute of NATIONAL Importance) (701171) (-) (-)	Telangana	12/2018 (07/2022)	06/2026 (12/2026)	1028.00 (1365.95)	1028.94	87.58
468	Establishment of new GMC Rudrapur (Medical Education, Ministry of Health and Family Welfare) (707086) (-) (-)	Uttarakhand	10/2022 (02/2024)	12/2026 (-)	325.00 (325.00)	353.01	95
469	Establishment of new GMC Pithoragarh (Medical Education, Ministry of Health and Family Welfare) (707087) (-) (-)	Uttarakhand	08/2021 (04/2023)	12/2026 (-)	325.00 (768.89)	470.08	78
Total (35)					21050.26	10844	
Ministry of Labour and Employment							
Healthcare							
470	Construction of 350 beds + 50 Super Specialty beds ESIC Hospital Sheelanagar, Visakhapatnam, Andhra Pradesh (Employee's State Insurance Company [ESIC]) (612167) (-) (-)	Andhra Pradesh	02/2021 (04/2023)	10/2025 (08/2026)	384.27 (384.27)	286.38	95

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
471	350 Bedded [Upgradable to 500 beds] ESI Hospital at Sanand (Employee's State Insurance Company [ESIC]) (612186) (-) (-)	Gujarat	06/2022 (04/2023)	03/2026 (05/2027)	558.12 (558.12)	55.81	28
472	Demolition, Construction and upgradation of ESI Hospital, Kalol, Gujarat from 50 beds to 150 beds. (Employee's State Insurance Company [ESIC]) (612211) (-) (-)	Gujarat	08/2022 (10/2023)	10/2025 (11/2026)	205.87 (205.87)	51.74	58
473	Construction of 200 bed ESI Hospital at Bommasandra, Karnataka (Employee's State Insurance Company [ESIC]) (612745) (-) (-)	Karnataka	02/2015 (10/2024)	01/2027 (05/2027)	278.00 (278.00)	80.52	35
474	Construction of 100 bed ESI Hospital and Staff Quarters [32 Nos.] at Harohalli, Karnataka (Employee's State Insurance Company [ESIC]) (612748) (-) (-)	Karnataka	07/2019 (03/2025)	02/2027 (-)	150.92 (150.92)	31.05	28.1
475	Construction of 200 Bedded ESIC Hospital at Butibori, Nagpur, Maharashtra. (Employee's State Insurance Company [ESIC]) (612213) (-) (-)	Maharashtra	10/2013 (08/2022)	08/2025 (09/2026)	194.93 (196.70)	116.22	67
476	Upgradation & Extension of ESIC Hospital and Construction of PG Hostel / Staff Housing for ESIC Hospital at Andheri, Mumbai (Employee's State Insurance Company [ESIC]) (616691) (-) (-)	Maharashtra	12/2008 (06/2009)	08/2025 (09/2026)	260.13 (260.13)	216.46	89
477	Construction of 100 Bedded ESI Hospital at Duburi, Odisha. (Employee's State Insurance Company [ESIC]) (612513) (-) (-)	Odisha	12/2010 (02/2025)	06/2027 (-)	164.60 (164.60)	16.44	7.2
478	CONSTRUCTION OF 300 BEDDED HOSPITAL AT HARIDWAR (Employee's State Insurance Company [ESIC]) (612259) (-) (-)	Uttarakhand	02/2021 (12/2021)	10/2024 (07/2026)	102.40 (297.63)	340.3	90.5
Total (9)					2299.24	1194.92	
Ministry of Ports, Shipping and Waterways							
Inland Waterways							
479	Jal Marg Vikas Project (Inland Waterways Authority of India [IWAI]) (701565) (-) (-)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	01/2018 (02/2018)	12/2023 (10/2026)	5369.18 (5061.15)	4187.19	85.1
Total (1)					5369.18	4187.19	
Shipping							
480	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust) (609424) (-) (-)	Gujarat	10/2022 (03/2024)	03/2027 (09/2027)	4243.64 (4243.64)	2737.7	60
481	Replacement and revamping of pipeline projects in oil jetty area, Kandla (Deendayal Port Trust [DPT]) (701570) (-) (-)	Gujarat	09/2021 (09/2021)	09/2023 (03/2025)	171.00 (211.61)	149.5	92
482	Mechanization of Berth No.14 for handling Containers and other cargo on DBFOT basis - Phase II (New Mangalore Port Authority) (617804) (-) (-)	Karnataka	12/2023 (06/2024)	03/2027 (-)	153.23 (153.23)	97.45	95
483	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574) (-) (-)	Odisha	05/2022 (01/2023)	12/2027 (10/2028)	3004.63 (3004.63)	2261.12	76
Total (4)					7572.50	5245.77	
Tourism, Hospitality & Wellness							
484	National Maritime Heritage Complex [NMHC] Phase-I (Indian Port Rail & Ropeway Corporation Ltd. [IPRCL]) (707215) (-) (-)	Gujarat	02/2019 (01/2022)	11/2026 (03/2026)	573.00 (1238.05)	656.38	79.87
Total (1)					573.00	656.38	
Department for Promotion of Industry & Internal Trade							
Logistics Infrastructure							
485	Integrated Multi Modal Logistics Hub at Nangal Chaudhary in Haryana - Other Trunk Infrastructure Development Phase 1 (NICDC) (707410) (-) (-)	Haryana	05/2018 (12/2021)	12/2023 (05/2028)	763.00 (763.00)	430	60
Total (1)					763.00	430	
Real Estate							
486	Orvakal Industrial Area (NICDC) (617727) (-) (-)	Andhra Pradesh	08/2024 (10/2025)	10/2028 (-)	2786.00 (2786.00)	356.05	16.22
487	Kopparthy Industrial Area (NICDC) (617729) (-) (-)	Andhra Pradesh	08/2024 (10/2025)	10/2028 (-)	2136.00 (2136.00)	39.75	5.39

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
488	Krishnapatnam Node - Phase 1 - Roads and Services Development (National Industrial Corridor Development Corporation) (701658) (-) (-)	Andhra Pradesh	12/2020 (02/2024)	02/2027 (-)	2139.44 (2139.44)	984.13	47.77
489	Gaya Integrated Manufacturing Cluster IMC in Bihar (National Industrial Corridor Development Corporation) (707420) (-) (-)	Bihar	08/2024 (04/2026)	04/2029 (-)	1339.02 (1339.02)	0	5
490	Tumakuru Node - Phase 1 - Roads and Services Development (NICDC) (701657) (-) (-)	Karnataka	12/2020 (02/2023)	09/2026 (09/2027)	1701.81 (1701.81)	337.56	27.12
491	Development of Palakkad Node under extension of CBIC to Kochi (National Industrial Corridor Development Corporation) (701668) (-) (-)	Kerala	08/2024 (10/2025)	04/2029 (-)	3805.00 (3805.00)	57.93	5.3
492	IMC Rajpura - Patiala Development Project (National Industrial Corridor Development Corporation) (701662) (-) (-)	Punjab	08/2024 (03/2026)	09/2028 (-)	1367.72 (1367.72)	0	3.4
493	Development of Jodhpur Pali Marwar Industrial Area JPMIA in Rajasthan (National Industrial Corridor Development Corporation) (603210) (-) (-)	Rajasthan	08/2024 (01/2026)	07/2028 (-)	921.66 (921.66)	0	6.32
494	Development of Zaheerabad Node under Hyderabad Nagpur Industrial Corridor (National Industrial Corridor Development Corporation) (601812) (-) (-)	Telangana	08/2024 (02/2026)	02/2029 (-)	2360.00 (2360.00)	42.89	4.87
495	IMC at Prayagraj (National Industrial Corridor Development Corporation) (707419) (-) (-)	Uttar Pradesh	08/2024 (04/2026)	06/2027 (-)	658.00 (658.00)	75.63	27.79
496	Development of IMC Khurpia Farms under AKIC Project (National Industrial Corridor Development Corporation) (701661) (-) (-)	Uttarakhand	08/2024 (03/2026)	09/2028 (-)	1265.37 (1265.37)	0	3.23
	Total (11)				20480.02	1893.94	
	Ministry of Steel						
	Metals & Mining						
497	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul (National Mineral Development Corporation Limited [NMDC]) (615202) (-) (-)	Chhattisgarh	08/2021 (07/2022)	12/2028 (03/2028)	1700.00 (1756.20)	292.01	23.09
	Total (1)				1700.00	292.01	
	Steel						
498	Installation of 140 TPH Walking Beam type Reheating Furnace in Plate Mill at BSP (Steel Authority of India Limited [SAIL]) (505491) (-) (-)	Chhattisgarh	02/2026 (03/2026)	03/2028 (-)	268.36 (268.36)	0	0
499	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617243) (-) (-)	Chhattisgarh	07/2024 (08/2024)	07/2026 (-)	198.62 (198.62)	129.25	82.79
500	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617255) (-) (-)	Chhattisgarh	10/2023 (12/2023)	06/2026 (09/2026)	471.83 (471.83)	266.11	74.3
501	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617256) (-) (-)	Chhattisgarh	11/2023 (01/2024)	10/2025 (09/2026)	884.10 (884.10)	693.83	94.73
502	NMDC Slurry Pipeline Project Phase-1 (National Mineral Development Corporation Limited [NMDC]) (706811) (-) (-)	Chhattisgarh	11/2015 (09/2020)	06/2023 (08/2026)	2907.00 (5427.00)	3649.08	95.8
503	SCREENING PLANT-III AT KIRANDUL (National Mineral Development Corporation Limited [NMDC]) (709826) (-) (-)	Chhattisgarh	01/2009 (10/2021)	01/2026 (07/2027)	2718.84 (3062.39)	1754.7	83.42
504	Super accelerated cooling system (Uniform Cooling) for high strength plates in Plate Mill at BSP (Steel Authority of India Limited [SAIL]) (944288) (-) (-)	Chhattisgarh	06/2025 (06/2025)	12/2026 (-)	192.21 (192.21)	63.8	48.01
505	New Sinter Plant at BSL, SAIL (Steel Authority of India Limited [SAIL]) (400174) (-) (-)	Jharkhand	03/2015 (10/2015)	10/2027 (06/2027)	1034.01 (1752.30)	1028.11	64.26
506	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617249) (-) (-)	Jharkhand	01/2025 (02/2025)	01/2027 (-)	211.94 (211.94)	60.6	62.05
507	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617250) (-) (-)	Jharkhand	01/2025 (02/2025)	10/2026 (04/2027)	207.13 (207.13)	103.47	55.91

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
508	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617254) (-) (-)	Jharkhand	03/2024 (04/2024)	06/2026 (04/2027)	260.37 (260.37)	127.53	53.15
509	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617257) (-) (-)	Jharkhand	11/2023 (12/2023)	11/2026 (11/2027)	627.31 (627.31)	347.42	68.07
510	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. (National Mineral Development Corporation Limited [NMDC]) (400121) (-) (-)	Karnataka	11/2014 (06/2024)	08/2026 (-)	1043.63 (1043.63)	649.52	70.33
511	Stamp Charge Battery No.7 Coke Dry Cooling Plant at RSP (Steel Authority of India Limited [SAIL]) (478482) (-) (-)	Odisha	02/2026 (02/2026)	08/2028 (-)	1064.55 (1064.55)	73.91	0
512	Implementation of Treatment System-2 Under ZLD at RSP (Steel Authority of India Limited [SAIL]) (589703) (-) (-)	Odisha	02/2025 (03/2025)	09/2026 (-)	216.02 (216.02)	134.29	89.83
513	New Product Testing Laboratory for NPM, SPP & NHSM at RSP (Steel Authority of India Limited [SAIL]) (635651) (-) (-)	Odisha	06/2025 (07/2025)	08/2027 (-)	155.26 (155.26)	56.24	71.75
514	Stamp Charge Battery No.7 Battery Proper at RSP (Steel Authority of India Limited [SAIL]) (738679) (-) (-)	Odisha	09/2024 (10/2024)	03/2028 (-)	2584.41 (2584.41)	1182.92	54.16
515	Stamp Charge Battery No.12 By-product Plant at RSP (Steel Authority of India Limited [SAIL]) (834015) (-) (-)	Odisha	09/2024 (10/2024)	03/2028 (-)	1140.07 (1140.07)	207.56	22.59
516	Stamp Charge Battery No.12 By-product Plant at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (364934) (-) (-)	West Bengal	01/2025 (02/2025)	07/2028 (-)	999.46 (999.46)	70.37	18.72
517	Stamp Charge Battery No.12 Coke Dry Cooling Plant at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (425828) (-) (-)	West Bengal	01/2025 (02/2025)	07/2028 (-)	706.51 (706.51)	132.26	11.87
518	Rebuilding of COB 4 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (612781) (-) (-)	West Bengal	09/2023 (09/2023)	09/2027 (09/2027)	916.78 (916.78)	244.78	37.19
519	Installation of New Bar Mill at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617242) (-) (-)	West Bengal	07/2024 (08/2024)	06/2027 (-)	2115.44 (2115.44)	935.57	67.5
520	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617246) (-) (-)	West Bengal	09/2024 (10/2024)	10/2027 (10/2027)	758.09 (758.09)	316.01	62.17
521	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617248) (-) (-)	West Bengal	11/2024 (12/2024)	07/2026 (11/2026)	227.96 (227.96)	111.44	74.55
522	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617251) (-) (-)	West Bengal	07/2024 (12/2024)	05/2026 (12/2026)	196.40 (196.40)	65.74	34.58
523	Stamp Charge Battery No.12 Battery Proper at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617338) (-) (-)	West Bengal	01/2025 (02/2025)	07/2028 (-)	2518.39 (2518.39)	472.41	27.66
Total (26)					24624.69	12876.92	
Ministry of Railways							
Railways							
524	Nadikude-Srikalahasti 308.7 km (CAO/C/SCoR SCoR mor) (400298) (-) (-)	Andhra Pradesh	03/2012 (08/2015)	05/2027 (03/2028)	2312.00 (5906.03)	2535.68	2
525	Doubling between Gooty-Pendakallu 29.225 km PB73/2023-24/NR (CAO/C/SCoR SCoR mor) (611752) (-) (-)	Andhra Pradesh	03/2023 (11/2024)	03/2027 (03/2027)	351.83 (351.83)	149.34	0
526	South Central Railway - Rail road over double line between Guntakal West-Mallapa Gate 9.64 km PB34/CR/2023-24 (CAO/C/SCoR SCoR mor) (611754) (-) (-)	Andhra Pradesh	07/2023 (01/2025)	07/2026 (-)	293.30 (293.30)	91.42	0
527	Kurnool - Setting up facilities for coach midlife rehabilitation workshop (WPO/Patna) (611927) (-) (-)	Andhra Pradesh	01/2014 (10/2017)	12/2023 (-)	560.72 (560.72)	276.66	65
528	Flyover between Pendurthi-Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB73/2023-24/NR (CAO/C/SCoR SCoR mor) (612827) (-) (-)	Andhra Pradesh	04/2023 (06/2024)	04/2027 (-)	183.65 (183.65)	25.44	21

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
529	3rd & 4 th line Vadlapudi-Gate Jn. incl. tie line between Gangavaram Port-Visakhapatnam Steel Plant12.04 km PB73/2023-24/NR (CAO/C/SCoR SCoR mor) (616697) (-) (-)	Andhra Pradesh	04/2023 (03/2024)	06/2026 (-)	154.28 (154.28)	89.67	87
530	South Central Railway- 3rd line between Gudur-Renigunta stations 83.17 km PB34/CR/2023-24 (CAO/C/SCoR SCoR mor) (617216) (-) (-)	Andhra Pradesh	10/2024 (10/2024)	03/2027 (-)	877.34 (877.34)	53.46	0
531	Kurnool Coach Midlife Rehabilitation Project (South Central Railway [SCR] - II) (705253) (-) (-)	Andhra Pradesh	05/2016 (07/2014)	12/2020 (12/2026)	563.00 (560.72)	959.27	75.01
532	Lumding-Furkating section 140 km Umbrella work PB57/2019-20/NR (CAO/C-1/NFR NFR mor) (616701) (-) (-)	Assam	02/2024 (04/2025)	02/2028 (-)	2123.70 (2123.70)	200.23	1
533	New Bongaigaon - Goalpara - Guwahati Kamakhya 176 km (CAO/C-III/NFR NFR mor) (705572) (-) (-)	Assam	09/2016 (06/2017)	03/2026 (03/2026)	4060.00 (4983.94)	3821.96	91
534	Sakri-Hasanpur 79 km (CAO/Con/North/MHX ECR mor) (400254) (-) (-)	Bihar	12/2023 (04/2019)	12/2024 (03/2027)	735.20 (802.45)	615.69	80
535	East Central Railway - Construction of Bulb line at Nabinagar Ankorah 17.49Km PB45/ECOR/2024-25. (CAO/Con/South/MHX ECR mor) (617231) (-) (-)	Bihar	06/2024 (07/2026)	06/2028 (-)	611.74 (611.74)	0	0
536	Narkatiaganj-Raxaul-Sitamarhi-Darbhanga & Sitamarhi-Muzaffarpur Sections doubling 256 km Umbrella work PB57/2019-20/NR (CAO/Con/North/MHX ECR mor) (617239) (-) (-)	Bihar	11/2024 (05/2026)	11/2029 (03/2030)	4079.95 (4079.96)	18.9	0
537	Hajipur-Sagauli via Vaishali 148.3 km (CAO/Con/North/MHX ECR mor) (705366) (-) (-)	Bihar	10/2007 (12/2008)	03/2020 (06/2027)	2067.00 (3991.33)	2843.39	74
538	Araria-Supaul 92 km (CAO/Con/North/MHX ECR mor) (705368) (-) (-)	Bihar	08/2009 (09/2020)	03/2024 (01/2027)	1605.00 (2621.05)	2140.8	40
539	Fatuah-Islampur incl. material modification for extension of new line from Neora to Daniawan Daniawan to Biharsharif Biharsharif to Barbigha Barbigha to Sheikhpura (CAO/Con/South/MHX ECR mor) (705373) (-) (-)	Bihar	08/2002 (02/2000)	03/2023 (08/2025)	1473.00 (3259.35)	3041.78	95
540	Jogbani-Biratnagar New Rail Line project (Indian Railway Construction International Limited [IRCON]) (705450) (-) (-)	Bihar	06/2010 (01/2011)	03/2022 (12/2026)	402.00 (486.00)	369.48	86.5
541	Samastipur-Darbhanga 38 km (CAO/Con/North/MHX ECR mor) (705526) (-) (-)	Bihar	11/2015 (02/2017)	03/2025 (10/2025)	519.00 (973.56)	746.81	92
542	Sagauli - Valmikinagar 109.7 km (CAO/Con/North/MHX ECR mor) (705527) (-) (-)	Bihar	03/2018 (02/2018)	12/2025 (12/2025)	1216.00 (1558.77)	1460.42	91
543	Muzaffarpur - Sagauli 100.6 km (CAO/Con/North/MHX ECR mor) (705528) (-) (-)	Bihar	03/2018 (03/2019)	06/2024 (06/2026)	1586.00 (1744.84)	1554.88	99
544	Rampur Dumra-Tal-Rajendrapul - Addl bridge and doubling 14 km (CGM/CIVIL ECR mor) (706759) (-) (-)	Bihar	03/2016 (04/2017)	12/2024 (12/2025)	2373.64 (2535.13)	2028.18	95
545	Barauni-Bachwara 16 km - 3rd & 4th line incl Barauni yard remodelling 32 km Umbrella work PB57/2019-20/NR (CAO/Con/North/MHX ECR mor) (706860) (-) (-)	Bihar	10/2022 (02/2025)	08/2025 (10/2026)	645.00 (485.58)	228.43	38
546	Jhajha - Batia 20 km Umbrella work PB23/2018-19/NR (CAO/Con/South/MHX ECR mor) (900874) (-) (-)	Bihar	02/2019 (04/2026)	03/2028 (01/2030)	588.18 (588.18)	26.52	0
547	Kharsia-Dharamjaygarh with Spur line [East Corridor-Phase 1] (Indian Railway Construction International Limited [IRCON]) (400220) (-) (-)	Chhattisgarh	03/2016 (01/2014)	09/2018 (12/2026)	3055.00 (3798.06)	2790.19	95.15
548	Kirandul-Jagdalpur 150 km (CAO/C/ECOR ECoR mor) (400291) (-) (-)	Chhattisgarh	02/2013 (04/2013)	03/2020 (04/2027)	1589.00 (1798.00)	1369.01	89
549	Gauge Conversion of Kendri-Dhamtari including Abhanpur - Rajim Branch line 67.20 Kms - 2nd Material Modification to Raipur Titlagarh doubling. (SECR) (602792) (-) (-)	Chhattisgarh	07/2011 (05/2021)	02/2025 (06/2026)	1171.00 (1171.00)	448.77	100

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
550	Nipania-Bhatapra 14.4 km 4th line PB72/NR/2022-23 (CAOC/SECR SECR mor) (612815) (-) (-)	Chhattisgarh	12/2022 (03/2023)	03/2027 (-)	170.49 (170.49)	12.12	3
551	Dallirajhra- Rowghat New Railway Line - Phase I [95 km] (Rail Vikas Nigam Limited) (705433) (-) (-)	Chhattisgarh	07/2009 (12/2009)	09/2025 (12/2025)	1628.00 (1628.00)	1440.85	82
552	Gevra Road-Pendra Road New Railway Line [135 km] (Indian Railway Construction International Limited [IRCON]) (705444) (-) (-)	Chhattisgarh	04/2014 (04/2014)	03/2022 (12/2026)	4970.00 (7448.52)	5327.55	83.36
553	Boridand-Ambikapur 118.81 km Umbrella work PB57/2019-20/NR (CAOC/SECR SECR mor) (706854) (-) (-)	Chhattisgarh	06/2022 (03/2024)	06/2030 (06/2030)	1376.00 (1576.72)	499.37	38
554	4th line - Rajnandgaon-Dongarhgarh 31.2 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709818) (-) (-)	Chhattisgarh	09/2022 (10/2024)	01/2027 (01/2027)	328.34 (328.34)	98.21	5
555	3rd & 4th line - Saragbundia & Madwarani 12.2 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709819) (-) (-)	Chhattisgarh	09/2022 (03/2023)	12/2026 (12/2026)	167.64 (167.64)	28.44	10
556	Anand Vihar-Tilak Bridge - 3rd & 4th line 9.77 km (CAOC/NR NR mor) (705583) (-) (-)	Delhi	06/2012 (04/2014)	03/2023 (12/2027)	667.00 (701.88)	393.68	23
557	Chandorgaon-Cansaulim rail flyover 16 km Umbrella work PB57/2019-20/NR (CAOC/SWR SWR mor) (706865) (-) (-)	Goa	NA (01/2022)	03/2031 (-)	1892.00 (1892.00)	0	0
558	Kosamba- Umarpada 69.70 Km PB32/WR/2023-24 (CAOCWR WR mor) (611918) (-) (-)	Gujarat	07/2023 (01/2024)	03/2027 (-)	468.00 (468.00)	146.38	31
559	New BG line between Naliya - Jakhau Port 24.88 Km (CAOCWR WR mor) (611943) (-) (-)	Gujarat	02/2023 (11/2025)	01/2028 (02/2028)	410.26 (410.26)	11.86	5
560	Petlad-Bhadran 22.5 km (CAOCWR WR mor) (611945) (-) (-)	Gujarat	05/2022 (05/2024)	05/2030 (05/2030)	307.11 (307.12)	114.73	32
561	Samlaya-Timba Road 53.53 km (CAOCWR WR mor) (611970) (-) (-)	Gujarat	02/2023 (05/2024)	03/2030 (03/2030)	670.17 (670.17)	195.1	25
562	Samni-Jambusar 24.08 km (CAOCWR WR mor) (611971) (-) (-)	Gujarat	05/2022 (04/2024)	03/2030 (03/2030)	350.00 (349.93)	188.23	40
563	Western Railway- Samakhiali-Gandhidham Quadrupiling 53 km PB34/CR/2023-24 (CAOCWR WR mor) (611974) (-) (-)	Gujarat	08/2023 (04/2024)	12/2026 (12/2027)	1430.00 (1430.00)	748.46	50
564	Barejadi Nandej Geratpur - Sanand - 4th line 38.20 km (CAOCWR WR mor) (612072) (-) (-)	Gujarat	02/2023 (03/2024)	03/2027 (07/2028)	961.67 (961.67)	548.14	23
565	Kosamba Umarpada GC PROJECT (Ministry of Railways-) (616983) (-) (-)	Gujarat	07/2023 (07/2023)	06/2027 (-)	467.58 (467.58)	70.54	16
566	Miyagam-Karjan-Dabhoi-Samlaya 96.46 km- Gauge conversion with electrification (CAOCWR WR mor) (705458) (-) (-)	Gujarat	01/2017 (06/2026)	12/2026 (12/2026)	483.88 (1015.07)	816.25	34
567	Rajkot-Kanalus 111.20 km (CAOCWR WR mor) (706763) (-) (-)	Gujarat	10/2021 (08/2022)	10/2026 (06/2026)	1080.58 (1205.18)	1107.75	90
568	Nadiad-Petlad 37.26 km (CAOCWR WR mor) (709812) (-) (-)	Gujarat	05/2022 (05/2024)	06/2030 (06/2030)	461.91 (461.91)	142.21	30
569	New BG line intersection 5 nos between Geratpur-Sanand & Botad-Ahmedabad 16.51 km PB29/NR/2022-23 (CAOCWR WR mor) (709813) (-) (-)	Gujarat	10/2022 (03/2025)	10/2027 (10/2027)	437.21 (463.95)	463.96	22
570	Doubling between Bhiwani - Dobh Bahali PB73/2023-24/NR (CAOC/NWR NWR mor) (611884) (-) (-)	Haryana	02/2023 (04/2023)	06/2027 (02/2028)	471.00 (471.00)	342.36	77
571	Pradhankhuntha Jn-Patherdih Bazar-Bhojudih 17.1 km Umbrella work PB57/2019-20/NR (CAO/Con/South/MHX ECR mor) (617372) (-) (-)	Jharkhand	11/2022 (09/2025)	11/2027 (03/2026)	349.22 (349.22)	162.92	60

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
572	Koderma-Barkakana Arigada 133 Km (CAO/Con/South/MHX ECR mor) (617832) (-) (-)	Jharkhand	06/2025 (07/2026)	12/2029 (-)	2887.11 (2887.11)	0.85	0
573	Gomoh - Flyover for down trains 20 km (CAO/Con/South/MHX ECR mor) (705765) (-) (-)	Jharkhand	01/2018 (04/2022)	03/2026 (03/2026)	686.00 (686.03)	531.63	65
574	Lodhma-Piska - Link line bypassing Hatia / Ranchi with Y connection 17.2 km (CAO/C/SER SER mor) (705785) (-) (-)	Jharkhand	08/2021 (11/2025)	06/2026 (05/2027)	473.00 (472.50)	344.5	14
575	Pradhan Kuntha Jn Line Doubling Project (East Central Railway [ECR] - I) (706837) (-) (-)	Jharkhand	11/2022 (11/2022)	11/2027 (11/2027)	349.22 (349.22)	145.57	72
576	Construction of New BG line between Hassan to Belur [27 Km] (South Western Railway [SWR] - II) (400023) (-) (-)	Karnataka	03/2019 (12/2025)	04/2028 (03/2030)	749.00 (749.00)	3.43	0.5
577	Gadag - Wadi 252 km (CAOC/SWR SWR mor) (705490) (-) (-)	Karnataka	04/2013 (08/2017)	03/2027 (12/2027)	2842.00 (3668.17)	2252.04	35
578	Kadur-Chickmagalur-Sakleshpur 93 km (CAOC/SWR SWR mor) (705492) (-) (-)	Karnataka	01/2014 (06/2023)	06/2025 (12/2025)	825.00 (1043.15)	790.72	83
579	Hubli-Ankola 167 km (CAOC/SWR SWR mor) (705493) (-) (-)	Karnataka	01/1999 (08/2023)	03/2005 (03/2030)	5174.00 (533.32)	186.31	10
580	Bagalkot-Kudachi 142 km (CAOC/SWR SWR mor) (705495) (-) (-)	Karnataka	02/2010 (02/2025)	03/2027 (01/2027)	1378.00 (1710.44)	797.37	35
581	Tumkur-Chitradurg-Davangere 199.7 km (CAOC/SWR SWR mor) (705496) (-) (-)	Karnataka	03/2011 (11/2017)	03/2019 (12/2027)	1876.00 (1801.01)	676.71	22
582	Bangalore-Whitefield-Bangalore City-Krishnarajapuram 23.08 km - Quadrupling (CPM/GS/SBC SWR mor) (705663) (-) (-)	Karnataka	03/2018 (05/2022)	02/2026 (02/2026)	493.00 (717.54)	459.94	70
583	Shimoga-Shikaripura-Ranebennur 103 km umbrella work PB23/2018-19/NR (CAOC/SWR SWR mor) (705761) (-) (-)	Karnataka	09/2019 (12/2023)	12/2027 (06/2028)	1454.00 (455.86)	106.18	14
584	Bangalore Suburban Railway Project (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (705941) (-) (-)	Karnataka	10/2020 (10/2020)	12/2026 (03/2030)	15767.00 (15767.00)	3277.99	20.02
585	Kumbalam-Turavur - Patch doubling 15.59 km (CAO/CN/ERS SR mor) (705638) (-) (-)	Kerala	04/2023 (10/2024)	03/2027 (03/2027)	813.00 (1171.46)	395.03	30
586	Ernakulam-Kumbalam - Patch doubling 7.71 km (CAO/CN/ERS SR mor) (705639) (-) (-)	Kerala	04/2023 (10/2024)	03/2028 (02/2027)	601.00 (827.50)	312.63	25
587	Gwalior-Sheorpurkalan with extension to Kota 284 km (CAO/C/NCR NCR mor) (705419) (-) (-)	Madhya Pradesh	02/2010 (04/2018)	03/2025 (02/2026)	2913.00 (3947.00)	3068.75	91
588	Satna - Rewa 50 km (CE/C-4/WCR WCR mor) (705659) (-) (-)	Madhya Pradesh	11/2015 (08/2016)	03/2026 (03/2026)	500.00 (646.10)	618.19	88
589	Katni - Grade separator / bypass 21.50 km (GM IRCON KATNI WCR mor) (705661) (-) (-)	Madhya Pradesh	08/2016 (09/2017)	09/2024 (09/2026)	1248.00 (2300.00)	1839.46	84
590	Nimach-Ratlam 133 km (CAOCWR WR mor) (705933) (-) (-)	Madhya Pradesh	10/2021 (08/2022)	10/2027 (10/2027)	1095.88 (1770.58)	1488.18	100
591	Aurangabad-Ankai 98.25 km (CAOCON/SCR SCR mor) (611751) (-) (-)	Maharashtra	05/2023 (06/2024)	12/2025 (-)	960.64 (960.64)	381.13	0
592	Pachora-Jamner with extension upto Malkapur-Narrow gauge to broad gauge 84 km (CAOC/CR CR mor) (612845) (-) (-)	Maharashtra	08/2022 (01/2026)	08/2027 (-)	955.39 (2093.82)	294.53	10
593	Redevelopment of Chhatrapati Shivaji Maharaj Terminus [CSMT] and construction of associated infrastructure (Rail Land Development Authority) (613015) (-) (-)	Maharashtra	04/2023 (07/2023)	03/2027 (-)	1813.00 (1813.00)	873.99	25

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
594	Doubling between Parbhani-Parli Vajinath stations 64.71 km PB34/CR/2023-24 (CAOCON/SCR SCR mor) (617215) (-) (-)	Maharashtra	12/2023 (05/2025)	03/2028 (-)	769.93 (769.93)	174.3	1
595	Central Railway - Double chord line between Nilaje and Kopar 4.495 km PB34/CR/2023-24 (CAOC/CR CR mor) (617364) (-) (-)	Maharashtra	07/2023 (12/2024)	07/2028 (-)	338.33 (205.00)	57.54	15
596	Ahmednagar - Beed - Parli - Vajinath New Broad Gauge Line Railway Project [261.3 km] (CAOC/CR CR mor) (705356) (-) (-)	Maharashtra	02/1997 (04/2013)	12/2026 (03/2026)	2538.67 (5942.48)	5054.69	93
597	Baramati - Lonand 54 km (CAOC/CR CR mor) (705357) (-) (-)	Maharashtra	02/1999 (12/2003)	03/2027 (03/2027)	138.48 (1790.50)	1132.25	60
598	Wadsa-Gadchiroli 49.5 km (CAOC/SECR SECR mor) (705479) (-) (-)	Maharashtra	05/2017 (11/2023)	03/2027 (03/2027)	1886.00 (1880.61)	1015.46	69
599	Wardha - Yavatmal Nanded Railway Line Project (Central Railways) (705497) (-) (-)	Maharashtra	02/2008 (04/2013)	12/2026 (-)	3445.34 (4030.69)	4053.03	47
600	Kalyan-Kasara - 3rd line 67.62 km (CAOC/CR CR mor) (705498) (-) (-)	Maharashtra	09/2015 (09/2015)	12/2026 (12/2026)	792.89 (1395.50)	1159.82	73
601	Wardha Sevagram-Nagpur - 3rd line 76.3 km (CAOC/CR CR mor) (705500) (-) (-)	Maharashtra	09/2015 (10/2015)	12/2025 (10/2026)	540.02 (899.52)	836.27	88
602	Wardha-Balharshah - 3rd line 132 km (CAOC/CR CR mor) (705502) (-) (-)	Maharashtra	03/2016 (05/2016)	12/2025 (02/2026)	1384.72 (2603.11)	1894.7	86
603	Daund - Manmad 247.50 km (CAOC/CR CR mor) (705504) (-) (-)	Maharashtra	10/2017 (11/2018)	12/2025 (03/2026)	2081.27 (3554.74)	3191.56	95
604	Wardha-Nagpur - 4th line 78.70 km (CAOC/CR CR mor) (705505) (-) (-)	Maharashtra	04/2017 (06/2017)	12/2025 (10/2026)	637.95 (1194.59)	1090.49	88
605	3rd Line Manmad - Jalgaon [160 Kilometres] (Central Railway [CR] - II) (705506) (-) (-)	Maharashtra	05/2017 (04/2018)	12/2024 (11/2025)	1035.16 (1870.00)	1843.54	100
606	Solapur-Osmanabad - New line via Tuljapur 84.44 km umbrella work PB23/2018-19/NR (CAOC/CR CR mor) (705735) (-) (-)	Maharashtra	01/2019 (09/2024)	03/2027 (03/2028)	904.92 (1647.87)	1202.73	22
607	Jiribam-Imphal 110 km (CAO/C-III/NFR NFR mor) (705391) (-) (-)	Manipur	10/2003 (04/2009)	12/2026 (06/2029)	14323.00 (21886.00)	16931.5	78
608	Marikuppam-Kuppam 23.7 km (CAOC/SWR SWR mor) (705491) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	10/2011 (06/2015)	06/2026 (06/2026)	297.00 (502.13)	145.72	20
609	Rayadurg-Tumkur via Kalyandurg 213 km (CAOC/SWR SWR mor) (705494) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	02/2007 (02/2011)	09/2015 (02/2028)	2496.00 (4612.00)	1906.63	65
610	Kottavalasa-Koraput 189.278 km (CAO/C/ECOR ECoR mor) (705512) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	12/2015 (01/2016)	03/2022 (03/2028)	2500.00 (3580.41)	2300.04	74
611	Tindivanam-Nagari 179.2 km (CAOC/SR SR mor) (400275) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	07/2008 (05/2009)	09/2016 (03/2028)	3631.00 (3631.34)	1175.82	16
612	Tirupati-Pakala-Katpadi Doubling 104.39 Km Item83/NR/2024-25 (CAO/C/SCoR SCoR mor) (617210) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	04/2025 (04/2025)	04/2029 (-)	1215.56 (1215.56)	0	0
613	Renigunta 9.60 km, Wadi 7.60 km & Gooty 3.8 km - Bypass (CAO/C/SCoR SCoR mor) (705610) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	04/2016 (08/2016)	12/2025 (03/2026)	302.00 (850.74)	421.36	50
614	Doubling between Motumari Vishnupuram 88.81 km and Rail over Rail RoR at Motumari 10.877 Km (CAO/C/SCoR SCoR mor) (616857) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	02/2024 (07/2025)	03/2029 (-)	1595.55 (1595.55)	327.62	22
615	South Central Railway- Rail connectivity to Amaravati, Capital of Andhra Pradesh Errupalem- Amaravati- Namburu New line 57 km PB7/WR/2023-24 (CAO/C/SCoR SCoR mor) (617214) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	11/2024 (06/2026)	03/2027 (-)	2047.40 (2047.40)	155	0

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
616	Vijayawada19.50 km & Kazipet10.65 km -Bypass line (CAO/C/SCoR SCoR mor) (705632) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	04/2016 (01/2021)	01/2025 (12/2025)	647.00 (827.46)	705.66	90
617	Murkongselek-Pasighat 26.15 km (CAO/C-II/NFR NFR mor) (705401) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (05/2023)	03/2025 (12/2026)	435.00 (1334.45)	1057.21	67
618	Teteliya-Byrnihat 21.5 km (CAO/C-II/NFR NFR mor) (705394) (-) (-)	Multi-States (Assam, Meghalaya)	11/2006 (04/2011)	11/2011 (06/2027)	1304.62 (1432.14)	1272.35	87
619	Dimapur-Kohima 88 km (CAO/C-1/NFR NFR mor) (705392) (-) (-)	Multi-States (Assam, Nagaland)	11/2006 (12/2015)	03/2025 (12/2029)	6663.00 (15310.23)	6719.53	45
620	Koderma-Tilaiya 68 km (CAO/Con/South/MHX ECR mor) (705375) (-) (-)	Multi-States (Bihar, Jharkhand)	11/2004 (05/2017)	02/2025 (02/2026)	1626.00 (2433.13)	2269.03	90
621	Pirpainti - Jasidih 97 km (CAOC/ER ER mor) (705385) (-) (-)	Multi-States (Bihar, Jharkhand)	03/2014 (04/2026)	03/2028 (03/2028)	2555.00 (2700.43)	1775.66	40
622	Multi tracking of Son Nagar-Andal 374.53 rkm & 814.38 tkm PB34/ECOR/2023-24 (CAO/Con/South/MHX ECR mor) (616699) (-) (-)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	08/2023 (09/2025)	03/2028 (-)	12333.57 (12333.57)	1152.79	3
623	NER Provision of Automatic Block Signalling on Gorakhpur Cantt[Excl] Chhapra Gramin & Burhwal Jn [Excl] Sitapur Jn section of high density routes (North Eastern Railway [NER]) (611669) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	05/2022 (06/2023)	03/2027 (03/2028)	380.47 (380.47)	258.65	25
624	Gorakhpur-Valmikinagar Doubling project (NER) (617224) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	08/2023 (03/2024)	12/2027 (-)	1120.00 (1120.00)	442.7	32
625	Construction of surface traingle between Bhadaura and new crossing station Karma Dildarnagar-Taraghat line 11.1 km PB72/NR/2022-23 (CAO/Con/South/MHX ECR mor) (617333) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	10/2022 (06/2024)	02/2027 (-)	199.96 (199.96)	64.04	0
626	Chhapra-Ballia - Patch doubling 65 km (CAOC/NER NER mor) (705562) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	03/2013 (12/2015)	02/2025 (05/2026)	963.00 (1010.84)	1000.05	95
627	Katihar-Kumedpur & Katihar-Mukuria 64.5 km Umbrella work PB57/2019-20/NR (CAO/C-II/NFR NFR mor) (617245) (-) (-)	Multi-States (Bihar, West Bengal)	08/2022 (10/2023)	08/2027 (02/2027)	942.64 (1961.00)	952.95	65
628	Rajnandgaon-Nagpur - 3rd line 228 km (CAOC/SECR SECR mor) (705617) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	09/2016 (12/2016)	12/2024 (06/2026)	3545.00 (3544.92)	3143.54	95
629	4th line - Bhatapara-Hathband 8.8 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709815) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	09/2022 (03/2023)	01/2027 (12/2027)	177.03 (177.03)	21.08	3
630	4th line - Bhilai-Bhilai nagar 8.8 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709816) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	09/2022 (03/2023)	02/2027 (02/2027)	177.34 (177.34)	35.21	3
631	4th line - Dadhapara-Belha 9.2 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709817) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	09/2022 (03/2023)	11/2026 (11/2026)	169.06 (169.06)	65.43	10
632	Jagdulpur-Koraput 110.22 km (CAO/C/ECOR ECoR mor) (705511) (-) (-)	Multi-States (Chhattisgarh, Odisha)	12/2015 (10/2021)	03/2024 (12/2026)	1547.00 (1547.38)	1382.17	90
633	Jharsuguda - Bilaspur - 4th line 206 km (CAOC/SECR SECR mor) (705616) (-) (-)	Multi-States (Chhattisgarh, Odisha)	09/2016 (03/2016)	10/2024 (03/2026)	2140.00 (2978.55)	2540.98	88
634	Mumbai-Ahmedabad High Speed Rail Project- 508 km (National High Speed Rail Corporation [NHSRC]) (705728) (-) (-)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	03/2015 (09/2017)	08/2027 (12/2029)	108000.00 (108000.00)	90966.89	62.16
635	Raising of speed to 160 kmph/200 kmph on existing New Delhi-Mumbai route incl. Vadodara-Ahmedabad (PCE/WR) (705793) (-) (-)	Multi-States (Delhi, Gujarat, Madhya Pradesh, Maharashtra, Rajasthan)	09/2019 (09/2019)	03/2024 (03/2026)	6806.44 (8095.12)	9480.86	66.32
636	Western Dedicated Freight Corridor (DFCCIL) (705237) (-) (-)	Multi-States (Gujarat, Haryana, Maharashtra, Rajasthan, Uttar Pradesh)	02/2008 (01/2012)	03/2022 (12/2025)	51101.00 (124005.00)	124623	96

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
637	Dahod-Indore via Sardarpur, Jhabua & Dhar 200.97 km incl. material modification for change in alignment via Amjhera 4.82 km (CAOCWR WR mor) (705453) (-) (-)	Multi-States (Gujarat, Madhya Pradesh)	06/2012 (12/2008)	02/2027 (02/2027)	456.07 (9217.23)	4509.3	57
638	Chhota Udepur-Dhar 157 km (CAOCWR WR mor) (705454) (-) (-)	Multi-States (Gujarat, Madhya Pradesh)	02/2007 (08/2008)	12/2025 (12/2025)	1794.00 (1993.65)	1855.01	58
639	Taranga Hill-Abu Road via Ambaji 116.65 km (CAOC/NWR NWR mor) (400022) (-) (-)	Multi-States (Gujarat, Rajasthan)	07/2022 (05/2023)	07/2030 (07/2030)	2798.00 (3198.16)	1953.58	48
640	LUNI- SAMDARI- BHILDI DOUBLING (North Western Railway [NWR]) (616842) (-) (-)	Multi-States (Gujarat, Rajasthan)	02/2024 (02/2024)	07/2027 (-)	3085.59 (3085.59)	962.77	36
641	Chandigarh-Baddi 33.23 km (CAOC/NR NR mor) (705424) (-) (-)	Multi-States (Haryana, Himachal Pradesh)	02/2018 (07/2022)	12/2026 (12/2026)	1540.00 (1942.17)	1101.73	47
642	Nangal Dam-Talwara 83.74 km - New broad gauge line & taking over siding Mukerian-Talwara 29.16 km (CAOC/NR NR mor) (705410) (-) (-)	Multi-States (Himachal Pradesh, Punjab)	03/1983 (04/1983)	12/2025 (12/2027)	2018.00 (4076.15)	2934.27	84
643	Bondamunda - Ranchi 158.50 km (CAO/C/SER SER mor) (705628) (-) (-)	Multi-States (Jharkhand, Odisha)	03/2016 (02/2017)	06/2025 (06/2026)	3029.00 (3029.04)	2696.32	95
644	Buramara - Chakulia 59.96 km PB9/SECR/2023-24 (CAO/C/SER SER mor) (616588) (-) (-)	Multi-States (Jharkhand, Odisha, West Bengal)	08/2024 (08/2024)	12/2029 (-)	1459.13 (1459.13)	11.7	2
645	3rd line between Chandil - Anara- Damodar section 121.26 km (CAO/C/SER SER mor) (616227) (-) (-)	Multi-States (Jharkhand, West Bengal)	09/2024 (09/2024)	09/2029 (-)	1932.01 (1932.01)	9.07	0
646	Kharagpur-Adityapur - 3rd line 132 km (CMD / RVNL RVNL mor) (705668) (-) (-)	Multi-States (Jharkhand, West Bengal)	09/2016 (11/2016)	03/2025 (06/2026)	3250.00 (3450.00)	3297.43	98
647	Baiyyappanahalli-Hosur 48 km (M.D/KRIDE SWR mor) (703586) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	04/2019 (07/2020)	12/2024 (01/2026)	498.70 (1160.00)	700.64	85
648	Trivandrum- Kanyakumari (CAO/CN/ERS SR mor) (705635) (-) (-)	Multi-States (Kerala, Tamil Nadu)	08/2017 (08/2019)	03/2025 (06/2028)	1432.00 (3785.45)	3258.97	59
649	Ratlam-Mhow-Khandwa-Akola 472.64 km including material modification for Fatehabad-Chandrawati Ganj-Ujjain 22.96 km and Rau-DADN doubling 9.40 km (CAOCWR WR mor) (705457) (-) (-)	Multi-States (Madhya Pradesh, Maharashtra)	01/2008 (09/2011)	03/2027 (09/2028)	1656.25 (13314.47)	5045.54	75
650	Itarsi-Nagpur bal. 280 km (CAOC/CR CR mor) (705507) (-) (-)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016 (12/2016)	03/2027 (12/2027)	2449.91 (2509.24)	2290.12	55
651	Ramganj Mandi-Bhopal 262 km (CPM/Kota WCR mor) (705481) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	02/2000 (08/2001)	12/2025 (12/2027)	3032.00 (5074.76)	4498.51	86
652	Nimach-Badi Sadri NL Project 48 km (CAOC/NWR NWR mor) (705764) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	10/2018 (01/2022)	03/2026 (06/2026)	495.00 (895.67)	577.16	60
653	Mathura-Jhansi - 3rd line 273.80 km (CMD / RVNL RVNL mor) (705667) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	09/2016 (02/2017)	12/2023 (12/2026)	5961.00 (5960.76)	5725.22	94
654	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho 541 km (CE/C-4/WCR WCR mor) (705480) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	01/2007 (02/1999)	03/2027 (12/2027)	8914.00 (8913.94)	6622.82	73
655	Jhansi-Bina - 3rd line 152.57 km (CAO/C/NCR NCR mor) (705598) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	09/2016 (03/2020)	03/2022 (03/2026)	2002.00 (2001.63)	1943.61	98
656	Jhansi-Khairar-Manikpur & Khirar-Bhimsen (North Central Railway) (705608) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2018 (04/2019)	03/2026 (03/2026)	4330.00 (4330.00)	3102.72	73
657	Bangriposi - Gorumahisani 85.60 km PB9/SECR/2023-24 (CAO/C/SER SER mor) (616586) (-) (-)	Multi-States (Odisha, West Bengal)	08/2024 (08/2024)	12/2029 (-)	2269.49 (2269.49)	7.31	2
658	Narayangarh - Bhadrak - 3rd line 155 km (CAO/C/SER SER mor) (705629) (-) (-)	Multi-States (Odisha, West Bengal)	03/2019 (02/2020)	12/2025 (01/2027)	2400.00 (3425.32)	2886.02	84

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
659	Tiruchchirappalli-Nagore-Karaikal with extension of Nagapattinam-Velankani-Tiruthirapundi incl. new material modification of Karaikal - Peralam 23 km new line (CAOC/SR SR mor) (400223) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	11/1995 (02/2014)	03/2025 (03/2028)	713.00 (1748.55)	1267.74	80
660	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432) (-) (-)	Multi-States (Sikkim, West Bengal)	10/2009 (05/2010)	05/2015 (12/2027)	7877.00 (11775.05)	11090.47	80
661	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass 35 km (CAOC/ER ER mor) (602797) (-) (-)	Multi-States (Uttar Pradesh, West Bengal)	08/2017 (06/2024)	03/2027 (03/2027)	461.64 (797.94)	185.23	15
662	Jharsuguda-Barpali-Sardega Ph II Works- Rail Connectivity for Coal Loading Bulb at Barpali. (South Eastern Railway [SER] - I) (400006) (-) (-)	Odisha	10/2021 (10/2021)	10/2025 (12/2026)	808.99 (808.99)	743.46	44
663	Proposed 6 nos Road Over Bridge [ROB] at different locations under MCL Talcher Under Deposit Scheme. (East Coast Railway [ECoR] - II) (400045) (-) (-)	Odisha	08/2022 (07/2022)	03/2025 (01/2025)	168.32 (168.32)	69.85	82
664	Doubling of Lingaraj SILO connectivity of NTPC line and augmentation of NTPC exchange yard and NTPC Block Cabin. (East Coast Railway [ECoR] - II) (400047) (-) (-)	Odisha	08/2022 (06/2022)	12/2024 (12/2026)	210.00 (210.00)	41.17	53
665	Doubling of lines connecting the loading spurs in Talcher Yard. (East Coast Railway [ECoR] - II) (400048) (-) (-)	Odisha	09/2022 (06/2022)	12/2024 (06/2027)	186.21 (186.21)	105.07	88
666	Brundamal - Jharsuguda - Fly-over connection for joining down line 6.6 km (CAO/C/ECOR ECoR mor) (400232) (-) (-)	Odisha	01/2014 (02/2024)	12/2026 (12/2026)	297.00 (296.51)	46.39	55
667	3rd & 4th line between Sarla - Sason 8 km PB73/2023-24/NR (CAO/C/ECOR ECoR mor) (612834) (-) (-)	Odisha	04/2023 (01/2024)	12/2025 (-)	252.00 (252.00)	169.6	88
668	Rourkela-Bondamunda A-Cabin 5th line 10 km Umbrella work PB57/2019-20/NR (CAO/C/SER SER mor) (615915) (-) (-)	Odisha	09/2022 (12/2023)	09/2024 (11/2026)	244.99 (244.99)	155.23	45
669	Flyover between Siju & Paradeep coaching yard 7 km PB73/2023-24/NR (CAO/C/ECOR ECoR mor) (616694) (-) (-)	Odisha	04/2023 (10/2023)	07/2028 (-)	200.77 (200.77)	55.91	0
670	Construction of Paradeep- Badabandha 3rd & 4th line 18.51 km PB34/ECOR/2023-24 (CAO/C/ECOR ECoR mor) (616695) (-) (-)	Odisha	08/2023 (11/2025)	11/2028 (-)	300.15 (300.15)	21.5	7
671	Gunupur - Therubali new line 73.62 km (CAO/C/ECOR ECoR mor) (616839) (-) (-)	Odisha	08/2024 (05/2026)	12/2029 (-)	1165.89 (1165.73)	1.95	0
672	Khurda Road-Bolangir 301 km (CAO/C/ECOR ECoR mor) (705358) (-) (-)	Odisha	03/1994 (03/2001)	12/2026 (12/2026)	3792.00 (6221.98)	4825.28	93
673	Talcher-Bimlagarh 154 km (CAO/C/ECOR ECoR mor) (705359) (-) (-)	Odisha	03/2004 (07/2008)	03/2025 (03/2029)	1928.00 (4546.84)	2164.01	56
674	Bhadrak-Nergundi - 3rd line 80 km (CAO/C/ECOR ECoR mor) (705510) (-) (-)	Odisha	03/2012 (09/2016)	11/2024 (01/2026)	1284.00 (1600.00)	1395.78	87
675	Koraput-Singapur Road 164.56 km (CAO/C/ECOR ECoR mor) (705513) (-) (-)	Odisha	12/2015 (01/2016)	12/2027 (03/2028)	2362.00 (2462.17)	2093.47	56
676	Jarapaada-Budhapank with flyover at Talcher Road - 3rd & 4th line 47 44 km (CAO/C/ECOR ECoR mor) (705514) (-) (-)	Odisha	11/2015 (05/2016)	11/2018 (03/2028)	1000.00 (928.54)	758.57	25
677	Budhapank-Salegaon via Rajatgarh - 3rd & 4th line 85 85 km (CAO/C/ECOR ECoR mor) (705515) (-) (-)	Odisha	12/2015 (04/2016)	03/2026 (03/2026)	1173.00 (3034.80)	2213.72	86
678	Jeypore - Navarangpur 38 km (CAO/C/ECOR ECoR mor) (705741) (-) (-)	Odisha	07/2017 (09/2022)	07/2028 (12/2029)	748.00 (747.91)	15.93	1
679	Jeypore - Malkangiri 130 km (CAO/C/ECOR ECoR mor) (705742) (-) (-)	Odisha	02/2018 (04/2026)	07/2033 (07/2033)	2344.00 (2343.64)	736.58	6
680	North Region Video Surveillance Project (RCIL) (705298) (-) (-)	PAN India	06/2020 (04/2023)	03/2024 (-)	274.39 (274.39)	0	48

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
681	Ludhiana Mullanpur 21Km Doubling Railway project (CAOC/CNR) (607653) (-) (-)	Punjab	NA (10/2022)	06/2024 (02/2027)	234.78 (234.78)	61.39	99
682	Ludhiana-Kila Raipur 19 km with freight line at Gill station (CAOC/NR NR mor) (705783) (-) (-)	Punjab	03/2019 (12/2022)	03/2025 (02/2027)	237.64 (260.33)	108.49	70
683	Nathdwara Mavli - Devgarh Madariya 82.542 km (CAOC/NWR NWR mor) (611855) (-) (-)	Rajasthan	01/2023 (08/2023)	06/2028 (-)	968.92 (1100.00)	816.16	75
684	Maintenance cum workshop depot for Vande Bharat Sleeper Trains as per conditions under WTA 527 (WPO/Patna) (611929) (-) (-)	Rajasthan	09/2022 (06/2023)	12/2024 (-)	166.86 (166.86)	0	0
685	Pushkar - Merta Katyasani 51.346 km (CAOC/NWR NWR mor) (616841) (-) (-)	Rajasthan	02/2024 (08/2024)	12/2026 (12/2028)	799.64 (799.64)	242.08	7
686	Ajmer-Chanderiya section 178.28 km Umbrella work PB57/2019-20/NR (CAOC/NWR NWR mor) (616843) (-) (-)	Rajasthan	02/2024 (09/2024)	06/2027 (03/2028)	1634.79 (1634.79)	560.17	23
687	SADULPUR - CHURU DOUBLING PROJECT (North Western Railway [NWR]) (617403) (-) (-)	Rajasthan	01/2024 (01/2024)	06/2026 (-)	468.64 (468.64)	197.84	95
688	North Western Railway - New line between Ramdevra and Pokhran via Bhairav Gufa - Kailash Tekri 13.38 Km PB30/NR/2025-26 (CAOC/NWR NWR mor) (617404) (-) (-)	Rajasthan	04/2025 (05/2026)	03/2028 (-)	189.21 (189.21)	57.31	3
689	Gudha-Thathana Mithri - Construction of dedicated test track for testing and trial of rolling stocks and infrastructure components umbrella work PB23/2018-19/NR (CAOC/NWR NWR mor) (705752) (-) (-)	Rajasthan	04/2019 (11/2019)	11/2026 (11/2026)	819.48 (540.00)	326.2	95
690	Agra Fort-Bandikui Doubling Line Project (CAO/C/NCR) (705919) (-) (-)	Rajasthan	06/2022 (02/2021)	06/2027 (06/2027)	1390.00 (1390.00)	529.92	56
691	Dedicatedtest track for RDSO Phase-2 34 km Umbrella work PB22/2019-20/NR (CAOC/NWR NWR mor) (706836) (-) (-)	Rajasthan	11/2021 (11/2021)	11/2026 (-)	466.42 (619.19)	586.33	98
692	Sawaimadhopur - Bypass line 6.98 km Umbrella work PB57/2019-20/NR (CAOC/NWR NWR mor) (706866) (-) (-)	Rajasthan	12/2022 (04/2024)	03/2026 (05/2027)	304.00 (239.00)	188.07	72
693	Phase II extension of MRTS from Velachery to St Thomas Mount (Ministry of Railways) (400280) (-) (-)	Tamil Nadu	11/2007 (11/2008)	07/2025 (09/2025)	734.00 (734.01)	486.53	99.9
694	Redevelopment of Chennai Egmore Station (Ministry of Railways) (613002) (-) (-)	Tamil Nadu	05/2022 (10/2022)	03/2026 (-)	842.00 (842.00)	340	0
695	Coach Production Factory Upgradation Project (CPM/ICF) (705244) (-) (-)	Tamil Nadu	12/2017 (07/2018)	12/2021 (-)	520.00 (520.00)	192.25	0
696	Madurai-Tuticorin via Aruppukkottai 143.5 km (CAOC/SR SR mor) (705489) (-) (-)	Tamil Nadu	04/2011 (06/2016)	07/2021 (01/2031)	601.43 (2053.39)	351.21	14
697	Railway Manufacturing Unit (RVNL - II) (617409) (-) (-)	Telangana	07/2016 (02/2023)	12/2026 (03/2026)	521.36 (521.36)	492.12	91
698	Bahraich - Khalilabad via Bhinga, Shravasti, Balrampur, Utraula, Domriyaganj, Mehdawal, Bansi 240.26 km (CAOC/NER NER mor) (400204) (-) (-)	Uttar Pradesh	10/2018 (01/2024)	10/2030 (10/2030)	4939.78 (4939.78)	1671.24	15
699	Sahjanwa - Dohrighat 81.17 km (CAOC/NER NER mor) (400205) (-) (-)	Uttar Pradesh	08/2019 (04/2025)	03/2029 (03/2029)	1319.75 (1319.75)	728.08	1
700	Varanasi- Pt. Deen Dayal Upadhyaya - Multitracking 15 km, including construction of a new Rail- cum- Road Bridge across Ganga River (CAOC/C-II/NR NR mor) (617213) (-) (-)	Uttar Pradesh	10/2024 (08/2025)	10/2029 (-)	2464.46 (2464.46)	109.93	5
701	Anand Nagar - Ghughuli via Maharajganj 53.37 km (CAOC/NER NER mor) (617252) (-) (-)	Uttar Pradesh	08/2023 (01/2026)	03/2028 (-)	958.27 (1501.10)	888.5	12
702	Doubling between Jaunpur Jn - Zaffarabad 6.28 km PB73/2023-24/NR (CAOC/NR NR mor) (617370) (-) (-)	Uttar Pradesh	03/2023 (04/2025)	01/2027 (-)	180.66 (237.38)	78.47	22

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
703	Burhwal - Gonda - 3rd line 61.72 km (CAOC/NER NER mor) (705567) (-) (-)	Uttar Pradesh	11/2017 (04/2020)	03/2025 (05/2026)	1016.00 (1307.62)	777.21	100
704	Janghai - Pratapgarh - Amethi 87 km (CAO/C-II/NR NR mor) (705588) (-) (-)	Uttar Pradesh	11/2017 (03/2019)	03/2025 (03/2026)	722.00 (1528.83)	1216.52	80
705	Lalitpur - Birari with flyover at Lalitpur 15.80 km (CAO/C/NCR NCR mor) (705766) (-) (-)	Uttar Pradesh	03/2017 (03/2023)	12/2024 (01/2026)	304.44 (356.10)	287.11	85
706	Mughalsarai - Allahabad - 3rd line 150 km (CAO/C/NCR NCR mor) (705772) (-) (-)	Uttar Pradesh	08/2019 (12/2020)	12/2026 (03/2027)	2649.00 (2649.44)	2027.64	77
707	Aligarh-Daud Khan - 3rd line 6.9 km & construction of flyover at Daud Khan (CAO/C/NCR NCR mor) (705774) (-) (-)	Uttar Pradesh	04/2019 (02/2021)	01/2025 (03/2027)	758.00 (779.49)	395.24	87
708	Bhandai - Flyover for Etawah bound down trains 10 km (CAO/C/NCR NCR mor) (705777) (-) (-)	Uttar Pradesh	04/2019 (12/2025)	02/2026 (02/2027)	250.18 (250.18)	146.85	11
709	Bhatni - Aunrihar with electrification 125 km excl Indara - Mau 116.95 km (CMD / RVNL RVNL mor) (705780) (-) (-)	Uttar Pradesh	03/2018 (11/2019)	03/2024 (06/2026)	2529.00 (2529.46)	2295.3	94
710	Barabanki-Malhaur - 3rd & 4th Line 32.84 km (CAO/C-II/NR NR mor) (705782) (-) (-)	Uttar Pradesh	01/2019 (08/2022)	03/2025 (08/2026)	407.00 (480.13)	444.11	77
711	Kalinarayanpur-Krishnanagar with Krishnanagar-Shantipur-Nabadwipghat - GC, Krishnanagar-Chartala, MM for Krishnanagar-Chapra-NL, Naihati-Ranaghat-3rd line, Nabadwipghat-Nabadwipdham upto BB loop 9.58 km, Ranaghat-Lalgola-strengthening bridge No.2 (CAOC/ER ER mor) (400247) (-) (-)	West Bengal	07/2015 (12/2005)	02/2027 (03/2028)	1000.00 (2153.91)	925.7	49
712	Tarakeswar-Bishnupur with extension upto Dhaniakhali, Arambagh-Irphala, Irphala-Ghatal 11.2 km, Arambagh-Champadanga 23.3 km & Bishnupur-Uparsol 31.8 km and new material modification for Mynapur-Kamarpukur via Birsha 19 km (CAOC/ER ER mor) (400273) (-) (-)	West Bengal	03/2001 (03/2005)	03/2019 (02/2026)	1189.00 (1878.82)	1607.64	75
713	Construction of Balurghat-Hilli new BG Line (Northeast Frontier Railway [NFR]) (612096) (-) (-)	West Bengal	12/2010 (12/2010)	03/2027 (03/2027)	1209.00 (1181.57)	518.15	18
Total (190)					465721.36	459390.96	
Ministry of Road Transport & Highways							
Roads & Highways							
714	Rehabilitation and up-gradation and completion of balance works of the section from Km 107.760 km to 129.445 km After Middle strait to Humphrey, Km 130.600 to 138.300 After Humphrey to Kadamtala of NH-4 Intermediate/2-Lane with hard shoulder in the Union Territory of Andaman & Nicobar Islands on EPC basis Package- IIIA (NHIDCL) (619184) (-) (-)	Andaman & Nicobar	02/2018 (03/2024)	09/2025 (12/2026)	207.45 (376.48)	0	81.95
715	Rehabilitation and up-gradation and completion of balance work of section from Km 155.00 to Km 181.00 End of Jarwa to Rangat of NH -4 Total length 26 Km to Intermediate Lane/2-lane with hard shoulders in the UT of A&N Islands on EPC basis - Package-III.B Balance work (NHIDCL) (619185) (-) (-)	Andaman & Nicobar	02/2018 (05/2024)	10/2025 (03/2027)	183.56 (333.12)	163.63	50.15
716	Construction of Balance works of Major Bridge over Middle Strait Creek between Km.106.590 to km108.553 of NH-04 connecting South Andaman & Baratang Island in the Union Territory of Andaman & Nicobar Islands on EPC basis (NHIDCL) (619186) (-) (-)	Andaman & Nicobar	03/2015 (05/2024)	02/2026 (12/2026)	262.96 (371.88)	112.15	12.98
717	Gudivada Town 2 RoB, and Road improvement NH-165 (MoRTH) (617984) (-) (-)	Andhra Pradesh	03/2022 (05/2023)	05/2025 (03/2027)	317.22 (317.22)	158.64	75.2
718	Widening to two lane with paved shoulders from Km 0/0 to 64/020 Pamarru to Akiveedu (MoRTH) (617985) (-) (-)	Andhra Pradesh	03/2020 (11/2021)	11/2023 (05/2027)	529.54 (588.65)	248.31	74.41
719	Kurnool/Kadapa Border-Jammalamadugu section of NH-167K i.e. Design Ch. Km 248010 to km 269900 to 2 (MoRTH) (617986) (-) (-)	Andhra Pradesh	03/2023 (12/2024)	12/2026 (12/2026)	292.63 (292.63)	0	95.77
720	Nandyala-Kurnool/Kadapa Border section of NH-167K i.e. Km 186/000 to Km 250/000Design Ch.186000 to 248010 to 2LPS (MoRTH) (617987) (-) (-)	Andhra Pradesh	10/2024 (09/2025)	09/2027 (09/2027)	691.81 (691.81)	0	49.71

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
721	Sangameswaram - Atmakuru section from Km 96 to Km 124 & Velegodu- Nandyal section including Nandyal Bypass from Km 143/6 to 185/9 NH-167K (MoRTH) (617988) (-) (-)	Andhra Pradesh	10/2024 (07/2025)	07/2027 (07/2027)	776.17 (644.14)	0	41.98
722	Rehabilitation and up-gradation of NH-167 from Km 14/900 to Km70/000 Design Ch. 14/900 to 69/700 Chintakunta to Adoni section to two lane with paved shoulders in the State of Andhra Pradesh under Corridor Approach through Engineering, Procurement (MoRTH) (617991) (-) (-)	Andhra Pradesh	11/2016 (05/2017)	05/2019 (12/2026)	290.15 (290.15)	141.83	91.9
723	4-laning of Puttaparthi-Koduru Section of NH-342 (MoRTH) (618013) (-) (-)	Andhra Pradesh	10/2022 (11/2023)	11/2025 (08/2026)	1318.59 (909.19)	464.06	90.19
724	Rehabilitation and Up-gradation of existin of road from 2-lane to 2-lane with paved shoulders from km. 0.00 to km 53.590 total length-53.590 km of Raychoti to Vempalli section of NH-440 in the State of Andhra Pradesh on EPC mode. (MoRTH) (618037) (-) (-)	Andhra Pradesh	12/2021 (05/2022)	05/2024 (09/2026)	439.82 (359.52)	213.12	90.2
725	Gorantla - Hindupur section from Km 120/300 to 165/000 of NH716G in the State of Andhra Pradesh (MoRTH) (618052) (-) (-)	Andhra Pradesh	10/2024 (08/2025)	08/2027 (08/2027)	808.70 (808.70)	0	37.7
726	Muddanur to B. Kothapalli section of NH-716G from Km. 0/000 to Km. 56/500 56.500 Km in the State of Andhra Pradesh on EPC mode Job no. 741 (MoRTH) (618053) (-) (-)	Andhra Pradesh	10/2024 (08/2025)	08/2027 (08/2027)	1019.97 (1019.97)	0	33.55
727	Kondamodu to Perecherla Section Design Ch. Km 000 to Km 49917 of NH-167AG to to 4LPS (MoRTH) (618101) (-) (-)	Andhra Pradesh	10/2024 (04/2025)	04/2027 (04/2027)	881.61 (881.61)	0	37.95
728	Rehabilitation and upgradation from Km 22300 to 58635 of MudireddyPalle to Kadapa/Nellore Border via porumamilla Section of NH 167 Two Lane with paved Shoulder in (MoRTH) (618103) (-) (-)	Andhra Pradesh	03/2022 (10/2024)	04/2026 (07/2026)	279.29 (279.29)	168.7	90.33
729	Rehabilitation and upgradation of NH 326A from km 0/0 to 41/979 excluding km 2/255 to 3/372 and km 36/820 to 38/275 Odisha border to Narasamapeta to two lane with paved Shoulders in the State of Andhra Pradesh under NHO on EPC Mode (MoRTH) (618125) (-) (-)	Andhra Pradesh	03/2018 (09/2018)	03/2020 (10/2025)	228.32 (228.32)	44.94	100
730	Widening of Existing Road to Two Lane with Paved Shoulder Configuration from Km 0.00 to 26.000 & Km 45.200 To 59.622 Of NH 365BB in the State of Andhra Pradesh Under Annual Plan 2023-24 through EPC Mode (MoRTH) (618193) (-) (-)	Andhra Pradesh	01/2024 (04/2025)	12/2026 (12/2026)	368.63 (368.63)	76.12	45.62
731	Rehabilitation and upgradation of New NH 544DD from design Chainage Km. 56/000 to 102/20 of Kalyandrg - Molakalmuru Section (MoRTH) (618194) (-) (-)	Andhra Pradesh	03/2018 (08/2018)	02/2020 (09/2025)	294.13 (285.29)	312.4	98.52
732	Rehabilitation and Up-gradation of Dhindi - Digamarru section from Km 126/510 to Km 135/740 of NH -214 New NH -216 and digamarru -Losari section from Km 0/000 tp Km 34/230 of NH-214 A New Nh-216 to two lane with paved shoulder in the state of AP-NH (MoRTH) (618236) (-) (-)	Andhra Pradesh	02/2016 (05/2016)	05/2018 (11/2023)	316.06 (288.76)	222.43	100
733	Rehabilitation and Up-gradation of Thimmapuram to Gurajanapalli section from Km 26/150 to Km 41/161 of NH - 214 New NH - 216 to two lane with paved shoulder in the state of Andhra Pradesh under NHDP-IV (MoRTH) (618238) (-) (-)	Andhra Pradesh	08/2016 (01/2017)	07/2018 (09/2026)	350.61 (432.91)	233.93	98.2
734	Rehabilitation & Upgradation of NH214 New NH-216 from Km 34/230 to Km 84/550 Losari to Machavaram Section to two lane with paved shoulder in the state of Andhrapradesh under NHDP-IV through Engineering, Procurement& Construction EPC mode. (MoRTH) (618239) (-) (-)	Andhra Pradesh	03/2016 (09/2016)	09/2018 (07/2025)	445.22 (459.37)	512.79	98.6
735	Construction of Paderu bypass Km 0000 to Km 13000 of 2- lane with paved shoulder on NH-516E (MoRTH) (618254) (-) (-)	Andhra Pradesh	03/2023 (01/2025)	07/2026 (12/2026)	244.43 (244.43)	21.96	13
736	Two laning with paved shoulders of Lambasingi to Paderusection of NH 516E (MoRTH) (618255) (-) (-)	Andhra Pradesh	04/2020 (11/2023)	11/2025 (03/2027)	361.24 (358.05)	145.94	56.69
737	Rehabilitation and Upgradation to 2-lane with paved should ers Sir, configuration of Chaprathipalem to Lambasingi section Km 165500 to Km 205000 of NH-516E in the State of Andhra Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode (MoRTH) (618256) (-) (-)	Andhra Pradesh	08/2020 (10/2022)	10/2024 (07/2026)	311.22 (311.22)	211.05	93.01

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
738	Rehabilitation and Upgradation to 2-lane with paved shoulders configuration of Koyyuru to Chaprathipalem section Km 120000 to Km 165500 of NH-516E in the State of Andhra Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode (MoRTH) (618257) (-) (-)	Andhra Pradesh	08/2020 (07/2022)	07/2024 (07/2026)	349.29 (349.29)	264.86	98.09
739	Construction of i Connecting Road from Z-Morh Tunnel to Zojila Tunnel Road Length 18.475km and ii 14.150 Km long 2-L Bi-directional single tube Zoji-la Tunnel across Zojila Pass on Sonamarg - Kargil section from Km 82 to Km 118 of NH-01 under PMDP (NHIDCL) (618412) (-) (-)	Andhra Pradesh	01/2018 (10/2020)	09/2026 (02/2028)	6808.69 (6808.69)	3574.5	68.8
740	Bangalore Chennai Expressway Phase-II Pkg-II from km.96.000 to Km 127.000 Baireddypalle to Bangarupalem section (NHAI) (618475) (-) (-)	Andhra Pradesh	02/2021 (06/2023)	06/2025 (10/2026)	2548.04 (2548.04)	1332.41	94.24
741	Bangalore Chennai Expressway Phase-II Pkg-III from km.127.000 to Km 156.000 Bangarupalem to Gudipala section (NHAI) (618476) (-) (-)	Andhra Pradesh	11/2020 (10/2022)	10/2024 (08/2026)	1407.33 (1407.33)	868.62	99.46
742	Construction of 6 lane elevated corridor including its approaches from Km. 629880 to Km. 634470 Design Chainage of NH-16 in Ranasthalam Town portion in the state of Andhra Pradesh on EPC Mode under NHO. (NHAI) (618524) (-) (-)	Andhra Pradesh	07/2024 (03/2025)	03/2027 (08/2027)	257.98 (192.85)	55.83	39.1
743	Construction of flyover at Gammon Junction at Km.903.265 on NH16 including vent at Diwancheruvu junction at Km.902.308 Blackspot ID No.AP03299 in Andhra Pradesh on EPC mode under NHO (NHAI) (618525) (-) (-)	Andhra Pradesh	03/2025 (10/2025)	10/2027 (10/2027)	326.61 (223.29)	43.82	18.9
744	6L of Gundugolanu Design km 1023.280 to Kalaparru Design km 1050.680 of NH-5 New NH-16 (NHAI) (618526) (-) (-)	Andhra Pradesh	10/2018 (01/2020)	07/2021 (08/2026)	665.59 (665.59)	643.95	95.73
745	6L of Anandapuram Pendurthi Anakapalli Section from km. 681.000 to km. 731.780 of NH-16 (NHAI) (618579) (-) (-)	Andhra Pradesh	01/2018 (01/2019)	07/2021 (08/2026)	2527.00 (2957.25)	2376.11	100
746	Nandigama Bypass and Kanchikacherla bypass (NHAI) (618629) (-) (-)	Andhra Pradesh	11/2017 (03/2018)	06/2019 (09/2026)	416.07 (444.58)	387.77	98.47
747	4L of Kadapa China Orampadu section of NH-716 Package I of Kadapa-Renigunta section (NHAI) (618633) (-) (-)	Andhra Pradesh	12/2022 (03/2026)	03/2028 (03/2028)	1732.66 (1732.66)	106.39	5.01
748	6L Korlam-Kantakapalle Section of NH-130CD Road from Km 421.100 to Km 445.100 Pkg-3 (NHAI) (618682) (-) (-)	Andhra Pradesh	02/2021 (02/2022)	02/2024 (08/2026)	1112.70 (1127.63)	849.98	99.5
749	Renigunta - Poyya - Naidupeta km 124.60 to km 183.4 of NH 71 (NHAI) (618700) (-) (-)	Andhra Pradesh	03/2020 (01/2022)	01/2024 (09/2026)	1863.09 (2510.14)	1677.19	98.6
750	6L Access Controlled Greenfield Highway from Kodur Ch. 0000 to Vanavolu Ch. 24300 of [NH-544G] Package-1 (NHAI) (618712) (-) (-)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (03/2027)	912.94 (798.25)	357.89	87.65
751	6L Access Controlled Greenfield Highway from Yerragudipadu Ch. 129000 to Audireddipalle Ch. 160000 of [NH 544G] Package-6 (NHAI) (618713) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (11/2027)	1200.42 (1019.69)	282.16	47.2
752	6L Access Controlled Greenfield Highway from Nallacheruvu palli Ch. 96300 to Yerragudipadu Ch. 129000 of [NH-544G] Package-5 (NHAI) (618714) (-) (-)	Andhra Pradesh	02/2022 (02/2024)	02/2026 (06/2027)	1253.26 (1095.78)	389.19	67.05
753	6L Access Controlled Greenfield Highway from Odulapalle Ch. 72000 to Nallacheruvu-palli Ch. 96300 of [NH-544G]Package-4 (NHAI) (618715) (-) (-)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (04/2027)	1058.90 (946.10)	403.17	76.97
754	6L Access Controlled Greenfield Highway from Vankarakunta Ch. 45700 to Odulapalle Ch. 72000 of [NH-544G]Package-3 (NHAI) (618716) (-) (-)	Andhra Pradesh	12/2022 (03/2024)	03/2026 (03/2027)	992.91 (888.07)	351.23	77.21
755	6L Access Controlled Greenfield Highway from Vanavolu Ch. 24300 to Vankarakunta Ch. 45700 of [NH-544G] Package-2 (NHAI) (618717) (-) (-)	Andhra Pradesh	01/2023 (03/2024)	03/2026 (02/2027)	750.81 (626.91)	261.4	87.24

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
756	6L Access Controlled Greenfield Highway from Kavulakuntla Ch. 196000 to Narayanmpet Ch. 203500Package-09 (NHAI) (618718) (-) (-)	Andhra Pradesh	02/2023 (02/2025)	02/2027 (12/2027)	1092.18 (956.40)	242.13	54.56
757	6L Access Controlled Greenfield Highway from Mallapalle Ch. 176000 to Kavulakuntla Ch. 196000 Package-08 (NHAI) (618719) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (07/2027)	909.02 (751.81)	290.04	65.92
758	6L Access Controlled Greenfield Highway from Audireddipalle Ch. 160000 to Mallapalle Ch. 176000Package-07 (NHAI) (618720) (-) (-)	Andhra Pradesh	02/2023 (03/2024)	03/2026 (04/2027)	987.10 (848.06)	338.45	73.78
759	6L Access Controlled Greenfield Highway from Chandrasekharapuram Ch. 228000 to Polavaram Ch. 260000of [NH-544G] Package-11 (NHAI) (618721) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (08/2027)	1292.65 (1110.33)	358.41	64.2
760	4L PS Mydukur - Badvel from Km 585.820 to Km 630.960 of NH-67 (NHAI) (618759) (-) (-)	Andhra Pradesh	05/2022 (09/2023)	09/2025 (10/2026)	1063.57 (1103.87)	585.79	90.4
761	4L of Pileru to Kalur Section from Km 55.900 to Km 92.800 & Km 94.500 to Km 95.717 of NH-71Package-II (NHAI) (618777) (-) (-)	Andhra Pradesh	03/2022 (10/2023)	11/2025 (08/2026)	1877.47 (592.85)	246.42	98.84
762	4L of Madanapalle to Pileru Section from Km 0.000 to Km 55.900 of NH-71Package-I (NHAI) (618778) (-) (-)	Andhra Pradesh	02/2022 (01/2023)	01/2025 (08/2026)	1877.47 (1994.10)	1182.65	94.9
763	Development of 4L Road from Samarlakota to Achampeta Junction as part of Kakinada Port Connectivity to NH-16 Rajanagaram Junction in East Godavari District (NHAI) (618803) (-) (-)	Andhra Pradesh	09/2022 (08/2023)	08/2025 (12/2026)	645.63 (750.20)	680.09	93
764	Dedicated Port road to Krishnapatnam Port Package-I from Km. 0.000 to Km. 18.000 (NHAI) (618804) (-) (-)	Andhra Pradesh	03/2018 (12/2018)	12/2020 (03/2027)	348.72 (341.36)	310.54	80.19
765	6L Connectivity to Port Road from Sabbavaram Sheelanagar-NH516C (NHAI) (618805) (-) (-)	Andhra Pradesh	12/2024 (02/2026)	02/2028 (02/2028)	977.33 (977.33)	155.51	7.2
766	Improvement of 4L road to 6L road and 4L dedicated Port Roads for the Port connectivity road from Convent junction to Sheelanagar Junction (NHAI) (618806) (-) (-)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (12/2026)	685.99 (680.21)	493.92	79
767	4L Greenfield Road connecting North and South industrial cluster of Khandaleru Creek near Krishnapatnam port at Thamminapatnam to Mollur from Km 0.0 to Km 16.046, Part I & 6L extension of dedicated port road of NH-67 Km 18.0 to Km 19.3, Part II (NHAI) (618807) (-) (-)	Andhra Pradesh	08/2022 (09/2023)	09/2025 (01/2027)	609.43 (559.98)	579.22	84.03
768	4 Laning of NH-544D from Km 0.000 to km 37.000 of Anantapur- Muchukota section Pkg-1 (NHAI) (618826) (-) (-)	Andhra Pradesh	10/2022 (07/2023)	07/2025 (08/2026)	907.76 (905.98)	468.12	92.34
769	4 Laning of NH-544D from Km 37.000 to km 69.000 of Muchukota- Bugga section Pkg-2 (NHAI) (618827) (-) (-)	Andhra Pradesh	10/2022 (08/2023)	08/2025 (12/2026)	1097.57 (1055.23)	466.9	84.92
770	Access Controlled Highway of 4 Lane with Paved Shoulders from TN/AP Border Design Chainage Km 6151 to Puttur Design Chainage Km 81540 of NH-716 & 6 Lane with Paved Shoulders from Mallavaram to Renigunta (NHAI) (618920) (-) (-)	Andhra Pradesh	03/2024 (12/2024)	12/2026 (03/2027)	1346.82 (1260.37)	188.68	42.48
771	Six Laning of Vijayawada Bypass from Chinna Avutapalli to Gollapudi in Vijayawada - Gundugolanu Section from km. 0.00 to km. 30.00 Pkg-III (NHAI) (619076) (-) (-)	Andhra Pradesh	01/2020 (02/2021)	02/2023 (09/2026)	1581.24 (1883.71)	1024.51	98.2
772	4 L of China Orampadu-Renigunta section of NH-716 Package-II of Kadapa-Renigunta section (NHAI) (619102) (-) (-)	Andhra Pradesh	12/2022 (03/2026)	03/2028 (03/2028)	1500.11 (1500.11)	121.06	2.25
773	6L Jakkuva Korlam Section of NH-130CD Road from km 396.800 to km 421.100 Pkg 2 (NHAI) (619111) (-) (-)	Andhra Pradesh	02/2021 (03/2022)	03/2024 (08/2026)	840.51 (840.51)	573.9	99.83
774	6L Kantakapalle Sabbavaram Section of NH-130CD Road from Km 445.100 to Km 464.662 Pkg-4 (NHAI) (619112) (-) (-)	Andhra Pradesh	02/2021 (10/2022)	10/2024 (12/2026)	1012.57 (1012.57)	702.4	84.6

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
775	6L Access Controlled Greenfield Highway from Narayanmpet Ch. 203500 to Chandrasekharapuram Ch. 228000Package-10 (NHAI) (619123) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (07/2027)	813.66 (678.21)	223.35	66.12
776	6L Access Controlled Greenfield Highway from Polavaram Ch. 260000 to Marripudi Ch. 285500 of [NH-544G]Package-12 (NHAI) (619124) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (05/2027)	747.29 (626.83)	250.93	70.2
777	6L Access Controlled Greenfield Highway from Somavarappadu Ch.314.600 to Muppavaram Ch.343240 of [NH-544G] Package-14 (NHAI) (619125) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (10/2027)	1103.90 (943.66)	267.61	44.56
778	6L Access Controlled Greenfield Highway from Marripudi Ch. 285500 to Somavarappadu Ch. 314600 of [NH-544G] Package-13 (NHAI) (619126) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (04/2027)	976.41 (798.71)	370.82	73
779	6L of Naidupeta Junction - Turpukanupur Section from km 57.046 to km 91.927 (NHAI) (619140) (-) (-)	Andhra Pradesh	08/2022 (10/2023)	10/2025 (10/2027)	1398.84 (965.58)	388.87	53.7
780	Construction of four lane access controlled highway from Chillakuru cross road to Turpu KanupurPart 1 of Package - II km 0.000 131.500 of NH - 16 to km 23.770 on New NH-516W including six lane flyover and approaches on NH-16 length km 1.050 and six lane access controlled from Turpu Kanupur to Port South Gate Part 2 of Package - II km 23.770 to km 35.015 on New NH-516W in the state of Andhra Pradesh on HAM Mode under Bharatmala Pariyojana Phase I (NHAI) (619141) (-) (-)	Andhra Pradesh	08/2022 (12/2023)	12/2025 (03/2026)	864.20 (844.39)	358.97	55.53
781	Balance works in AP Portion and punch list items in TN & AP portion of NH-205 (NHAI) (619160) (-) (-)	Andhra Pradesh	10/2022 (07/2023)	01/2025 (01/2026)	166.52 (113.46)	98.52	100
782	Construction of 2-lane road of Potin to Pangin section of NH-13 from Km 163.59 to Km 206.66 Package-5 on EPC Mode in the State of Arunachal Pradesh under Arunachal Pradesh Package of Roads and Highways of SARDP-NE [Job No SARDP-NE/P-P/Pkg-A/NH-13/Ar.Pr./PWD/2018-19/116] (MoRTH) (617892) (-) (-)	Arunachal Pradesh	03/2019 (11/2020)	11/2023 (10/2026)	450.65 (450.65)	345.01	96.61
783	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang Package-III from design Km 60.000 to Km 121.500 Design Length 61.500 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Pkg-3 (NHIDCL) (618401) (-) (-)	Arunachal Pradesh	02/2024 (07/2025)	07/2028 (07/2028)	1418.67 (1418.67)	93.19	1.7
784	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang from Design Km 0.000 to Km 53.000 Design Length 53.000 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Package-I (NHIDCL) (618402) (-) (-)	Arunachal Pradesh	02/2024 (03/2025)	02/2028 (03/2028)	1262.43 (1262.43)	255.45	19.13
785	Construction of Intermediate Lane Road with hard shoulder from design Km 0.000 to Km 17.387 Total length 17.387 km of Hunli to Ithun Bridge section on NH-913 Frontier Highway in State of Arunachal Pradesh on EPC mode under NHO-NE (NHIDCL) (618403) (-) (-)	Arunachal Pradesh	02/2024 (01/2025)	01/2027 (01/2027)	275.50 (275.50)	163.15	56.18
786	Construction of Intermediate Lane Road with hard shoulder from design chainage Km 0.000 to Km 53.040 Existing Length68.500 Km & Total Design length 53.04 km of Tato to Monigong section of NH-913 Frontier Highway on Nafra Bomdila to Vijaynagar along China border in state of Arunachal pradesh on EPC mode (NHIDCL) (618404) (-) (-)	Arunachal Pradesh	12/2023 (05/2025)	11/2027 (11/2027)	625.61 (625.61)	269.64	22.81
787	Construction of Intermediate Lane of Pango to Jorging Road from 0000 to Design Km Design Km 40000 Design Length 40.00 Km, Pkg-I, Greenfield Alignment in the State of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (618405) (-) (-)	Arunachal Pradesh	01/2024 (01/2025)	07/2027 (07/2027)	898.19 (898.19)	255.52	39.86
788	Construction of Balance work of 2-Lane with PS of Joram Koloriang Road from existing Km122.600 to km138.00 [Design Km108.724 to Km123.714] in Arunachal Pradesh on EPC Mode under SARDP-NE Pkg-7 (NHIDCL) (618433) (-) (-)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (04/2026)	184.89 (184.89)	156.42	99.69
789	Roing-Hunli Road Greenfield Alignment Project (NHIDCL) (618434) (-) (-)	Arunachal Pradesh	02/2017 (03/2018)	03/2022 (10/2026)	1718.59 (1718.59)	1123.4	82.45
790	Construction of 2-Laning with hard shoulders of Demwe-Brahmakund section of NH-13 from Ch.0.00 km to 18.464 km on EPC under SARDP-NE NHO-NE -Balance Work (NHIDCL) (618445) (-) (-)	Arunachal Pradesh	08/2020 (06/2025)	12/2027 (12/2027)	353.90 (353.90)	26.82	19.57

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
791	Improvement and Widening to 2 lane with paved Shoulder of NH-15 old NH-52 from Existing Km 770.600 Design Km 24.819 to Existing km 805.750 Design Km 59.885 Kamlang T-Junction to Chowkham, Existing Length 35.150 Km, Design Length-35.066 Km in the state of Arunachal Pradesh on EPC mode Pkg-2 (NHIDCL) (619014) (-) (-)	Arunachal Pradesh	12/2023 (02/2026)	02/2028 (02/2028)	316.73 (316.73)	34.98	15.06
792	Improvement and Widening to 2-lane with Paved Shoulder of NH-13 & 15 Old NH-52 from Existing Km 745.60 Design Km 0.000 to Existing km 770.600 Design Km 24.819 Brahmakund T-junction to Kamlang T-Junction, Existing Length 25.00 Km, Design Length 24.819 Km in the state of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (619248) (-) (-)	Arunachal Pradesh	12/2023 (06/2026)	06/2028 (06/2028)	441.41 (441.41)	25.88	14.69
793	Construction of Mangaldoi Bypass NH-15 starting at Ch 26400 and terminating at Ch 41505 under Rangia NH Division L 15.105 Km in the State of Assam. Job No. 15/AS/2021-22/234 (MoRTH) (617895) (-) (-)	Assam	03/2022 (04/2023)	04/2025 (12/2026)	535.03 (535.03)	209.27	76.32
794	Construction of 4 lane Gauripur Bypass Starting bfrom Km 852.56 of NH-31Dumardoha Pt-II and Terminating at Km 862.17 Baladmara via. Khudimari Pt.- II, Fulkumari, Charaldanga, Sajuakuti,Geramari Pt.-III and finally meeting at km 862.17 of NH-17New/ NH-31Old in the State of Assam under EPC Mode Job no. 31/AS/ 2023-24/265 (MoRTH) (617896) (-) (-)	Assam	03/2024 (04/2025)	10/2026 (10/2026)	421.15 (421.15)	0	34
795	Construction of 2 lane Barpeta Bypass from Km 77900Baradi to Km 86150 Deurikuchi Length8.25Km on NH-427 in the state of Assam under EPC ModeJob No.427/AS/2022-23/245 (MoRTH) (618034) (-) (-)	Assam	03/2023 (02/2025)	08/2026 (08/2026)	173.65 (173.65)	11.38	20
796	Construction of new 2 Lane with paved shoulders of NH Standards from km 0.080 to km 11.690 L11.610 km in Majuli and from km 19.715 to km 27.484 L 7.769 km in Jorhat on the newly declared NH 715K and construction of 1.10 km flyover on NH-715 with its approaches and service roads L1.10 km, Total Length 20.479 km in the State of Assam Job No. 715K/AS/2023-24/256 (MoRTH) (618159) (-) (-)	Assam	02/2024 (09/2025)	03/2027 (03/2027)	382.10 (382.10)	28.96	6.7
797	Construction of 2 lane Major Bridge including approaches over Brahmaputra between Majuli on North Bank and Jorhat on South Bank from km. 11.690 to km. 19.715 length of bridge 6,812.5m Package - II on NH-715K in the state of Assam Job no. 715/AS/2020-21/213 (MoRTH) (618160) (-) (-)	Assam	03/2025 (12/2025)	12/2027 (12/2027)	1019.17 (1019.17)	0	3.25
798	4-L Bilasipara-Guwahati Package-10 (NHIDCL) (618282) (-) (-)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1264.90 (1264.90)	632.99	64.48
799	4-L Bilasipara-Guwahati Package-9 (NHIDCL) (618283) (-) (-)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1000.27 (1000.27)	505.47	59.78
800	Widening/Improvement to 4-Lane with paved shoulder from Km 99930 to Km 143680 Design Chainage 96000 to 139750 of Paikan to Dhupdhara Sahar of Bilasipura-Guwahati Road on NH-17 in the state of Assam on EPC mode under Bharatmala Pariyojana in Economic Corridors Project Length 43.750km under NHO-NE Package-8 (NHIDCL) (618284) (-) (-)	Assam	03/2023 (12/2023)	12/2026 (12/2026)	1457.59 (1457.59)	962.73	85.87
801	Construction of New 2-Lane Bridge with its approaches from km 0000 to Km 4385 across River Brahmaputra on NH-17 at Jogighopa in Assam on EPC mode (NHIDCL) (618286) (-) (-)	Assam	09/2021 (11/2021)	11/2024 (12/2026)	746.76 (746.76)	435.79	81.07
802	Widening/Improvement to 4-Lane with paved Shoulder from Ch. 25.633 Km to Ch. 52.470 Km Design Ch. 21.850 Km to Ch.48.670 Km for Package-2 of Bilasipura-Guwahati road NH-17 Section Near Mowatari, before Chapar Bypass to Tulungia junction with NH-17 in the state of Assam on HAM mode under NHO-NE Package-2 (NHIDCL) (618287) (-) (-)	Assam	11/2023 (12/2024)	06/2027 (06/2027)	1338.61 (1338.61)	199.15	12.45
803	Widening/Improvement to 4-Lane with Paved Shoulder from Ch.5.580 Km to Ch.25.633 Km Design Ch.0.000 Km to Ch.17.737km Km 901.100 to Km 921.145 of old NH-31 of Bilasipara- Guwahati road NH-17 Section Near Chirakuta to near Mowatari, before Chapar Bypass in the state ol Assam on HAM mode Package-1 (NHIDCL) (618288) (-) (-)	Assam	02/2024 (02/2025)	08/2027 (08/2027)	1081.15 (1081.15)	163.12	35
804	Construction and up gradation to 4-Lane of existing two lane with paved shoulder from Hapachara to Tulungia road of NH-117 of existing Km 0.00 to km 14.050 and Design Km 0.000 to km 14.660 under BMP on EPC mode (NHIDCL) (618289) (-) (-)	Assam	03/2020 (06/2020)	12/2022 (03/2026)	224.85 (224.85)	209.95	97.76

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
805	Construction of 4-Lane Panchgram Bypass from Design Chainage km 15500 on NH-37 Old NH-53 at Kalinagar Pt.-I Village to Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Package-2 (NHIDCL) (618308) (-) (-)	Assam	03/2023 (08/2024)	02/2027 (03/2027)	676.18 (728.97)	339.78	57.17
806	Widening/Improvement to 4-Laning and Greenfield alignment with Paved shoulder of Silchar-Badarpur Churaibari section of NH-37 & NH-8 from Design chainage 38.600 End point of proposed Badarpur Bypass to Km. 62.800 Start point of proposed Nilambazar/Cheragi Bypass in the state of Assam on HAM Mode Package-4 (NHIDCL) (618309) (-) (-)	Assam	02/2024 (08/2025)	08/2027 (08/2027)	1319.55 (1319.55)	185.17	23.07
807	Widening/Improvement to 4-L of Karimgani - sutarkandi section of NH 37 from design Ch 0020 Start of proposed Karimganj Bypass from NH -8 to design Chainage Km 14380 near Sutarkandi Spur Connectivity to Indo/Bangladesh Border on Silchar- Churaibari in the State of Assam on HAM Mode Package-7 (NHIDCL) (618310) (-) (-)	Assam	02/2024 (02/2025)	02/2027 (02/2027)	791.79 (791.79)	135.54	41.88
808	Widening/Improvement to 4-Lane with Paved shoulder for existing as well as Greenfield alignment of Badarpur Churaibari section of NH-8 from Design chainage 87.700 Chandkhira to Km. 106.500 Churaibari section Assam-Tripura border in the state of Assam on HAM Mode Package-6 (NHIDCL) (618311) (-) (-)	Assam	03/2024 (03/2025)	03/2027 (03/2027)	870.00 (870.00)	158.08	40.99
809	Widening/Improvement to 4-Lane with Paved Shoulder from existing road and Greenfield alignment form Design Ch. 62.800 start of proposed Nilambazar/Cheragi Bypass to Design Ch. 87.700 near Chandkhira Village of NH-8 on Silchar-Churaibari in the state of Assam on HAM Mode Package-5 (NHIDCL) (618312) (-) (-)	Assam	02/2024 (04/2025)	10/2027 (10/2027)	1258.13 (1258.13)	186.86	14.04
810	Widening/Improvement of Existing 2 lane to 4-Laning of Karimganj-Silchar section of NH-37 from Design Ch 0.000 near Silchar ISBT to Design Ch 15.970 near Kalinagar Pt I on NH-37 in Assam on HAM Mode Pkg-1 (NHIDCL) (618313) (-) (-)	Assam	03/2024 (09/2025)	09/2027 (09/2027)	1181.55 (1181.55)	178.62	41.26
811	4-Laning of Dhanehari Lailapur / Vairengte section from Existing Chainage km 12920 to km 43000 of NH 306 Design Chainage km 20000 to km 49360 on Silchar - Vairengte Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode. Project Length 29.360 km under NHO-NE Package-2 (NHIDCL) (618314) (-) (-)	Assam	03/2023 (02/2024)	08/2026 (03/2027)	1716.21 (1716.21)	1057.72	81.65
812	4-Laning of Silchar - Dhanehari section from Existing Chainage km 263800 of NH 37 to km 12920 of NH 306 Design Chainage km 0000 to km 20000 on Silchar - Vairengte - Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode Package-1 (NHIDCL) (618315) (-) (-)	Assam	02/2023 (01/2024)	07/2026 (03/2027)	1256.90 (1256.90)	632.2	59.65
813	Widening/Improvement to 4-Lane with Paved Shoulder from KM 38500 to Km 51246 Design Chainage 38500 to 50959 with proposed Daboka Bypass of Daboka- Parokhaowa of NH 29 on EPC under NHO-NE Package-1 (NHIDCL) (618326) (-) (-)	Assam	01/2023 (11/2023)	11/2025 (06/2026)	516.88 (516.88)	322.98	99.7
814	Improvement to 4-Lane with Paved Shoulder from existing km 260000 Design Ch.4560 km to existing km Ch.233000 D. Ch.24560 of Silchar near Nutan Dayapur village - Budha Nagar Section Length-20.00 Km of NH-37 under Package Silchar- Jiribam Pkg-1 in the state of Assam on HAM Mode (NHIDCL) (618331) (-) (-)	Assam	01/2024 (01/2025)	01/2028 (01/2028)	957.95 (957.95)	214.64	47.27
815	Widening/Improvement to 4-Lane with Paved Shoulder from km 626030 Nalani hulla Gaon to km 650450 Chotahapjan on existing Tinsukhia -Makum Bypass of NH-15 OLD NH-37 and Strengthening of existing NH-315 OLD NH-38 from Km 0000 Chotahapjan to Km 16900 Bogapani section 2-Lane PS in Assam on EPCMode under NHO-NE Package-3 (NHIDCL) (618340) (-) (-)	Assam	01/2023 (05/2023)	05/2025 (10/2026)	458.59 (458.59)	261.02	88.99
816	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 156.489 near P. Leikul to km 176.410 near Borowapu on EPC mode under NHO-NE Assam portion Package-10 (NHIDCL) (618351) (-) (-)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	890.33 (693.15)	605.43	90.5
817	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 136.500 near Hejaichak to km 156.489 near P. Leikul Package-9 on EPC mode under NHO-NE Package-9 (NHIDCL) (618352) (-) (-)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	860.37 (614.43)	559.51	87.5
818	Widening & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 116.480 near Hangrum to km 136.500 near Hejaichak Package-8 on EPC mode under NHO-NE Package 8 (NHIDCL) (618353) (-) (-)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	904.04 (904.04)	563.52	85.2

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
819	Wideinig & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 96.870 near Jiri River to km 116.550 near Hangrum Package-7 on EPC mode Package7 (NHIDCL) (618354) (-) (-)	Assam	12/2023 (03/2024)	03/2026 (12/2026)	846.82 (846.82)	481.81	90.36
820	Widening/Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Srirampur near Bhairiguri Village to Kachukhana Harichara Paglagaunj Package-I of Srirampur - Dhubri Section of NH-127B from existing Km 0.000 to Km 28.050 Design Km 0.000 to Km 27.650, Design Length27.650 Km under JICA ODA Loan assistance Phase-V -Balance work (NHIDCL) (618371) (-) (-)	Assam	03/2022 (11/2024)	11/2026 (11/2026)	613.89 (613.89)	384.6	89.5
821	Construction of 4-Lane Bridge including approaches over River Brahmaputra between Dhubri on North Bank,Assam and Phulbari on south Bank,Meghalaya on NH-127B under JICA ODA Loan assistance Phase-III (NHIDCL) (618373) (-) (-)	Assam	05/2019 (12/2020)	09/2028 (09/2028)	4997.04 (4997.04)	3081.08	77.14
822	4-Laning of Jamugurihat to end of Biswanath Chariali By-Pass from Km 182.000 to Km 208.000 of NH-52 on EPC mode in state of Assam under SARDP-NE (NHIDCL) (618436) (-) (-)	Assam	03/2015 (12/2016)	06/2019 (07/2025)	599.00 (599.00)	432.62	100
823	Construction of Balance Work of 4-Laning of NH-37 Section between End of Moran Bypass to Bogibeel junction near Lapetketa Km. 561.700-Km. 580.875 under SARDP-NE, Phase 'A' in the State of Assam on EPC mode Pkg-I Road works & Toll Plaza (NHIDCL) (618437) (-) (-)	Assam	01/2016 (09/2024)	03/2025 (08/2025)	274.34 (274.34)	116.66	100
824	4-Laning of NH-37 Section between Demow to End of Moran Bypass From Km. 534.800 to Km. 561.700 including Emergency Landing Facility ELF under SARDP-NE, Phase 'A' in the State of Assam on EPC mode (NHIDCL) (618438) (-) (-)	Assam	01/2016 (01/2023)	07/2024 (08/2025)	385.57 (385.57)	680.44	100
825	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 534.800, under SARDP- NE on EPC Mode in the state of Assam Pkg- IV Structures & Toll Plaza (NHIDCL) (618440) (-) (-)	Assam	01/2016 (10/2024)	10/2025 (10/2026)	187.09 (100.22)	16.71	58.19
826	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 501.800 11.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618441) (-) (-)	Assam	01/2016 (10/2024)	09/2025 (10/2026)	467.79 (476.50)	97.88	87.33
827	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 477.000 to Km 490800 13.800 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (618442) (-) (-)	Assam	01/2024 (02/2024)	08/2024 (06/2026)	358.72 (358.72)	100.4	100
828	Earthwork in Formation, Road Work, Construction of Bridges, Blanketing, P. Way Linking works including Supply of P. Way Fittings and Track Ballast in connection with Construction of Railway Siding from Jogighopa Railway Station to MMLP at Jogighopa from Ch. 00 to 3760 on Item Rate basis Package -3, Railway Siding from Jogighopa Railway Station to MMLP (NHIDCL) (618454) (-) (-)	Assam	02/2020 (12/2020)	06/2022 (09/2024)	693.97 (693.97)	40.17	93.23
829	Development of External Trunk Connectivity and Internal Infrastructure Works at Multi Model Logistics ParkMMLP at Jogighopa in the State of Assam on EPC Mode Package-I Road and Utility Works (NHIDCL) (618455) (-) (-)	Assam	02/2020 (09/2020)	04/2022 (09/2024)	693.97 (693.97)	308.85	100
830	Guwahati Ring Road in the State of Assam (NHAI) (618934) (-) (-)	Assam	08/2024 (01/2026)	01/2030 (01/2030)	5729.47 (5729.47)	328.42	0
831	2L with ES of Yagyi - Kalewa section from Milepost 40/0 to Milepost 115/5 in Myanmar (NHAI) (618958) (-) (-)	Assam	12/2017 (05/2018)	06/2023 (07/2027)	1200.14 (1200.14)	0	52
832	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 501.800 to Km 514.800 13.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-II Road Works (NHIDCL) (619013) (-) (-)	Assam	10/2014 (10/2024)	01/2026 (10/2026)	508.76 (542.87)	111.18	73.88
833	Construction of 4-Lane Badarpur Bypass from Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village to Design Chainage km 38600 on NH-37 Old NH-44 at Kandigram Chaita Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Pkg-3 (NHIDCL) (619057) (-) (-)	Assam	02/2023 (02/2024)	08/2026 (03/2027)	574.26 (574.26)	330.98	71.09

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
834	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 514.800 to Km 534.800 20.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (619060) (-) (-)	Assam	10/2014 (10/2024)	09/2025 (10/2026)	344.71 (619.70)	56.58	72
835	Balance work of 4L of NarimbangloJatinga Junction- Harangajoroad section from Km 0.000 to Km 49.230 of NH-27 (NHAI) (619089) (-) (-)	Assam	03/2022 (01/2023)	01/2026 (08/2026)	1909.98 (2745.74)	1393.08	98
836	Construction of proposed 4Lane Revelgunj bypass NH-19 in the State of Bihar on EPC mode connecting NH 19 to 85 origin (MoRTH) (617897) (-) (-)	Bihar	03/2022 (07/2023)	07/2025 (12/2026)	295.24 (295.24)	44.18	88.65
837	Widening & Strenthening from km132.895 to km 190.15 NH-80 (MoRTH) (617958) (-) (-)	Bihar	03/2021 (11/2022)	11/2024 (11/2026)	566.10 (566.10)	293.89	73.21
838	Gaya-Hisua-Rajgir-Nalanda-Biharsharif section km0.00 to 92.935 NH-82 (MoRTH) (617961) (-) (-)	Bihar	01/2014 (11/2016)	11/2019 (10/2026)	1408.85 (2138.16)	0	97
839	Rehabilitation and Upgrading to 2 lanes/2-lane with paved shoulders configuration and strengthening of of Birpur and Bihpur Section from km 0.0 to Km 106 of NH 106 under phase I of National Highways Interconnectivity Improvement Projects NHIIP ICB No. NHIIP-BR-106-7 [NHIIP-BR-106-7] (MoRTH) (617966) (-) (-)	Bihar	01/2014 (10/2016)	10/2019 (10/2026)	780.77 (961.33)	0.04	99.74
840	Construction of 4 Lane ROB and its approaches at the level crossing LC No 29 B of Km 29 Ekangarsarai at NH 110 New NH 33 & Railway Km 32.63 at Fatwa FUT Islampur IPR section in the state of Bihar on EPC mode. (MoRTH) (617969) (-) (-)	Bihar	03/2023 (07/2024)	07/2026 (12/2026)	201.08 (201.08)	0.01	62
841	Construction of Bhabhua Bypass from Ch. 10800Design Ch. 10800 to Ch. 19860 Design Ch. 18150 and Chand Bypass from Ch. 38060 Design Ch. 36250 to Ch. 40460 Design Ch. 38650 and widening of existing road to 2 - lane with Paved shoulder from Ch. 40460 Design Ch. 38650 to Ch. 46860 Design Ch. 45050 of NH-219 Total length-16.150 Kmunder EPC mode in the state of Bihar (MoRTH) (618004) (-) (-)	Bihar	02/2022 (06/2026)	12/2027 (12/2027)	179.86 (179.86)	2.37	2
842	Improvement to Two lane with Paved Shoulder from Junction of NH22 near Hajipur to Junction of NH -122 at Bachhwara via Mahnar and Mohiuddin Nagar from Km 0.00 to Km 29.730 of NH 122 B in the State of Bihar. (MoRTH) (618073) (-) (-)	Bihar	02/2024 (08/2024)	02/2026 (02/2027)	226.16 (226.16)	0	61
843	Pre construction activity of NH 122B from km 0 to 72.348 and Improvement to two lane with paved shoulders of NH 122B from km 29.730 to km 72.348 in state of Bihar under EPC mode (MoRTH) (618074) (-) (-)	Bihar	02/2022 (05/2023)	08/2026 (08/2026)	624.43 (624.43)	154.25	96
844	Improvement to two lane with paved shoulders of BH WB Border Amdabad Manihari section from design Km 0.000 to Km 23.945 of NH 131 A Total length 23.945 Km under EPC mode in the state of Bihar (MoRTH) (618080) (-) (-)	Bihar	01/2022 (05/2025)	11/2026 (06/2027)	353.27 (353.27)	0	7.5
845	construction of Four-Lane of chausa-Buxar Bypass from Km 45.000 to Km 65.915 Package - 2 in the State of Bihar on EPC Mode. (MoRTH) (618120) (-) (-)	Bihar	09/2022 (01/2026)	01/2028 (01/2028)	1060.16 (1060.16)	0.22	4
846	Improvement to two lane with paved shoulders of NH-319A from km 0 to km 45 in state of Bihar under EPC mode (MoRTH) (618121) (-) (-)	Bihar	02/2022 (06/2023)	12/2024 (11/2026)	427.29 (427.29)	198.23	93
847	Pre-Construction activities from Km 134.000 to Km 190.233 of NH-333A and Construction of 4 no. of Bypasses at Katoria, Lakhpura, Banka & Panjwara total length-14.359 Km to two lane with paved shoulders standard in State of Bihar. (MoRTH) (618126) (-) (-)	Bihar	11/2022 (12/2024)	12/2026 (03/2027)	479.37 (479.37)	67.37	58.75
848	Estimate for Improvement to two lane with paved shoulder from Ramnagar to Roseda from km 3.500 to 43.000 of NH 527 E on EPC mode in State of Bihar (MoRTH) (618146) (-) (-)	Bihar	01/2022 (10/2024)	04/2026 (04/2027)	495.16 (495.16)	0.38	39
849	construction of a new 4 lane Parallel to existing MG Setu with its approaces from km 0.00 to km 14.500 across river Ganga on NH-19 at Patna in the state of Bihar. (MoRTH) (618228) (-) (-)	Bihar	02/2019 (03/2021)	09/2024 (12/2027)	2926.42 (2926.42)	622.65	75.33
850	Construction of a new 4-lane major bridge across river Kosi at Phulaut including Rehabilitation and upgradation of existing Birpur and Bihpur section of NH-106 from km 106.000 to km 136.000 to 2-lane with paved shoulders in the State of Bihar on EPC mode (MoRTH) (618234) (-) (-)	Bihar	09/2018 (06/2021)	06/2024 (02/2027)	1478.40 (1478.40)	901.52	98.6

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
851	Construction of New 4-Lane Bridge Parallel to existing Vikramashila Setufrom km 8920 to Km 13375including approach road 35m Naugachhia side &53 m Bhagalpur sideacross River Ganga on newly declared NH-131B at Bhagalpur in the State of Bihar (MoRTH) (618246) (-) (-)	Bihar	07/2020 (05/2023)	05/2027 (03/2029)	1110.23 (1110.23)	522.58	52.6
852	Construction of 6-Lane Elevated / Extra Dose Cable Bridge on River Ganga parallel to & Western side of Digha-Sonepur Rail cum-Road Bridge of NH 139W in the State of Bihar (MoRTH) (618250) (-) (-)	Bihar	01/2024 (05/2024)	11/2027 (12/2028)	3064.45 (3064.45)	0	18.66
853	Improvement and Up gradation to four lane with Paved shoulder configuration from Existing Km 0000 to Km 39500 design km 0500 to Km 40342, Design length km of NH 227A near Mehrauna GhatUP Bihar Border to Siwan on the state of Bihar on Hybrid Annuity Model HAM basis (MoRTH) (618251) (-) (-)	Bihar	03/2023 (09/2025)	03/2028 (03/2028)	1661.25 (1661.25)	0.83	9.07
854	Permanent rectification of 3 nos. of black spots in project Highway NH-27 of U.P border - Dewapur - Kotwa section from Km.360.915 to km.440.000 Total Length of 79.085 Km of NH-27& Permanent rectification of 5 nos. of black spots of project Highway NH-27 of Kotwa - Mehsi - Muzaffarpur Section from km.440.000 to km.520.000 Total length 80.00Km (NHAI) (618571) (-) (-)	Bihar	04/2022 (12/2023)	12/2025 (12/2026)	227.25 (321.23)	233.7	83.01
855	6L Greenfield Varanasi-Ranchi-Kolkata Highway from Pachmon village to Anarbansalea village From KM. 116000 to KM. 151200 Package-6 (NHAI) (618725) (-) (-)	Bihar	03/2023 (09/2025)	09/2027 (09/2027)	1915.99 (1920.21)	431.04	24.8
856	6L Greenfield Varanasi-Ranchi-Kolkata Highway from junction with Chandauli-Chainpur Road near Khainti village to junction with Bhabhua-Adhaura road near Palka village from Km. 27.000 to Km. 54.000 Pkg-2 (NHAI) (618726) (-) (-)	Bihar	03/2023 (10/2025)	10/2027 (10/2027)	1240.93 (1341.52)	252.44	26.77
857	6L Greenfield Varanasi-Ranchi-Kolkata Highway from junction with Bhabhua-Adhaura road in Bhairampur village to Konki village From KM. 54.000 to KM. 90.000Pkg-3 (NHAI) (618727) (-) (-)	Bihar	03/2023 (10/2025)	10/2027 (10/2027)	1576.94 (1711.44)	328.2	26.31
858	6L Bridge and its approaches across River Ganga as Part of Patna Ring Road NH-131G starting from Km 8.480 near Sherpur to Km 23.000 near Dighwara (NHAI) (618738) (-) (-)	Bihar	09/2022 (09/2023)	09/2027 (03/2029)	6291.69 (3351.62)	734.19	22.05
859	4L Greenfield Alignment of Amas to Shivrampur from 0.000 Km. to 55.002 Km. of NH 119 D Pkg-I (NHAI) (618739) (-) (-)	Bihar	02/2022 (03/2023)	03/2025 (07/2027)	1390.92 (1427.43)	642.43	54.8
860	4L Greenfield Alignment of Shivrampur to Ramnagar from Km. 55.002 to Km. 109.300 of NH 119 D Pkg-II (NHAI) (618740) (-) (-)	Bihar	02/2022 (07/2023)	07/2025 (11/2027)	1494.31 (1546.07)	702.39	50.8
861	4L Greenfield Alignment from Kalyanapur to Tal Dashraha of NH-119D Pkg-III (NHAI) (618741) (-) (-)	Bihar	03/2022 (02/2023)	02/2025 (03/2028)	1857.58 (1969.30)	957.28	36.25
862	Construction of 6-lane Greenfield corridor from Ramnagar to Kacchi Dargah NH-119D from Km 109700 to Km 122300, including widening of the existing NH-31 from Km 196700 to Km 198600, as part of the Amas-Darbhanga. (NHAI) (618742) (-) (-)	Bihar	01/2025 (04/2026)	04/2028 (04/2028)	1113.46 (1113.46)	12.44	0.8
863	Ara Bypass (NHAI) (618775) (-) (-)	Bihar	03/2025 (10/2025)	04/2027 (04/2027)	226.32 (226.32)	5.95	25.78
864	Construction of four laning of Bakarpur- Manikpur road section starting from village Chitarsenpur km 0000 and terminating at SH-74 near Manikpur 38814 at NH-139W under Bharatmalapariyona (NHAI) (618790) (-) (-)	Bihar	03/2023 (10/2024)	04/2027 (09/2027)	1422.37 (1537.99)	635.91	49
865	4L PS under NH configuration of Manikpur-Sahebganj of NH-139W (NHAI) (618791) (-) (-)	Bihar	10/2024 (01/2026)	12/2027 (12/2027)	1538.76 (1538.76)	595.95	27.5
866	Simaria Km. 206.050 to Khagaria Km. 266.282 (NHAI) (618840) (-) (-)	Bihar	12/2015 (10/2016)	04/2019 (10/2026)	664.02 (891.64)	814.22	97.73
867	4L Elevated Section and at-grade improvements at Begusarai town Simaria - Khagaria section from Km. 221.047 to Km. 225.302 of NH-31 (NHAI) (618841) (-) (-)	Bihar	10/2021 (06/2022)	12/2024 (08/2026)	491.04 (348.38)	354.17	95.72

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
868	Bakhtiyarpur-Rajauli Pkg-II from km. 54.405 to km.101.630 (NHAI) (618861) (-) (-)	Bihar	09/2020 (04/2021)	07/2023 (08/2026)	897.45 (1397.47)	914.25	97.85
869	Bakhtiyarpur-Rajauli Pkg-III from km. 101.630 to km.152.520 (NHAI) (618862) (-) (-)	Bihar	09/2020 (12/2021)	06/2024 (08/2026)	2156.22 (3046.61)	1818.91	99.14
870	Maheshkunt-Saharsa-Purnea Pkg I km 0.00 to km. 90.00 of NH-107 (NHAI) (618902) (-) (-)	Bihar	02/2017 (12/2019)	12/2021 (09/2026)	662.44 (1311.22)	1126.22	90.07
871	Maheshkunt -Saharsa-Purnea Pkg II (NHAI) (618903) (-) (-)	Bihar	03/2017 (12/2018)	12/2020 (09/2026)	1245.33 (1244.09)	1230.43	94
872	Widening with additional 3L abetting Chhapra Bypass Section of NH-19 from Km. 143.200 to Km. 159.255 Pkg-1 (NHAI) (618905) (-) (-)	Bihar	02/2024 (08/2024)	08/2026 (10/2026)	470.50 (528.48)	302.74	77.28
873	4L Elevated Corridor and at-grade improvements from Design Ch0000 to Design Ch 19870 of Danapur Bihta Section, Design Ch0000 to Design Ch0231 connecting the existing RoB near Danapur station ,1.35 Km ramps and at-grade improvements to 4-lane section on Danapur side and Upgradation of existing Two lane carriageway to Four Lane carriageway from Design Ch19870 to Design Ch23500 of Bihta - Koilwar section (NHAI) (618914) (-) (-)	Bihar	10/2022 (03/2024)	09/2026 (08/2027)	4432.97 (2625.40)	1578.15	63.91
874	4L Greenfield starting from NH-30 near Saristabad Patna to Nathupur Project end point of Patna-Gaya-Dobhi Section of NH-83 (NHAI) (618917) (-) (-)	Bihar	07/2023 (03/2024)	08/2025 (09/2026)	488.24 (419.66)	101.06	88.3
875	4L of Siwan- Masrakh section of Ram Janki Marg from Km 230.385 to Km 281.391 of NH-227A (NHAI) (618926) (-) (-)	Bihar	08/2022 (11/2024)	11/2026 (11/2028)	1431.36 (1927.04)	504.03	10.97
876	Umagaon-Saharsa Package-IV Koshi Bridge & approach Road - Bheja-Bakaur (NHAI) (618953) (-) (-)	Bihar	02/2019 (02/2020)	08/2023 (03/2027)	1199.58 (1223.94)	1312.28	92.4
877	Umagaon - Saharsa Package - I Combined Umagaon-Kaluahi0.000KM to 21.609KM of NH227LSaharghat-Rahika0.000 Km to 26.130KM of NH227JRahika-Rampatti 0.00 KM to 15.00KM of NH527ABideshwarsthan-Bheja0.000KM to 25.915KM of NH527A. (NHAI) (618954) (-) (-)	Bihar	08/2022 (01/2025)	07/2027 (07/2027)	1473.20 (1703.02)	644.37	23.78
878	2L PS of Majhauri to Charout section from km. 0.00 to km. 63.655 (NHAI) (618955) (-) (-)	Bihar	01/2018 (11/2019)	11/2021 (08/2026)	638.29 (1067.51)	1096.16	99.8
879	Construction of Major Bridge over Baghmati and Lakhandei River along with Approaches from Design km.16.500 to km.21.500 (NHAI) (618956) (-) (-)	Bihar	02/2024 (10/2024)	04/2027 (03/2028)	498.97 (380.30)	57.23	26.84
880	4L of Greenfield Alignment from Km. 47.000 to Km. 89.210 of Balbhadarpur to Bela Nawda Section of NH-119D (NHAI) (619127) (-) (-)	Bihar	03/2022 (03/2024)	03/2026 (03/2028)	2185.75 (2118.46)	764.97	30.41
881	Rehabilitation and Upgradation of Chorma - Bairgania Section of National Highway No 227F to 2 lane with paved shoulders from Design Ch.0.000 to Ch. 34.566 (NHAI) (619136) (-) (-)	Bihar	06/2022 (02/2024)	01/2026 (08/2026)	610.78 (628.65)	337.4	100
882	Bakhtiyarpur Km 153.300 to Mokama Km 197.900 (NHAI) (619152) (-) (-)	Bihar	12/2015 (06/2017)	12/2019 (08/2026)	1898.84 (1898.84)	1799.23	99.95
883	Umagaon-Saharsa Package-V Bakaur-Parsarma-Bangaon-Bariyahi & Spur to Mahishi (NHAI) (619166) (-) (-)	Bihar	10/2022 (12/2023)	12/2025 (08/2026)	768.35 (968.42)	509.32	99.5
884	4L of Munger Mirzachauki section from Munger to Kharia village junction from Km 69520 to Km 95580 Pkg-1 (NHAI) (619289) (-) (-)	Bihar	01/2021 (03/2022)	03/2024 (10/2026)	1659.81 (1696.66)	685.48	82.72
885	Construction of Approach Road to Rail-cum- Road Bridge across river Ganga at Munger Ghat NH-333 B (NHAI) (619301) (-) (-)	Bihar	07/2013 (12/2018)	05/2021 (08/2026)	537.88 (633.91)	573.97	99.99
886	4L of Munger Mirzachauki section from start of existing Bhagalpur bypass to Rasulpur from Km 125000 to Km 157350 Pkg-3 (NHAI) (619305) (-) (-)	Bihar	01/2021 (04/2022)	04/2024 (12/2026)	1769.50 (2024.59)	675.5	77.3

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
887	4L of Munger Mirzachauki section from Km 95580 to Km 125000 Pkg-2 (NHAI) (619306) (-) (-)	Bihar	02/2021 (03/2022)	03/2024 (08/2026)	1020.84 (1235.65)	643	95.9
888	4L of Hajipur-Muzaffarpur Section of the existing NH-77 from Km. 0000 Ramashish Chowk to Km. 46300 and new bypass starting at Km. 46300 and connecting NH-28 of E-W Corridor at Km. 515045 (NHAI) (619317) (-) (-)	Bihar	08/2010 (08/2010)	02/2013 (09/2026)	2723.39 (2906.78)	2160.8	99.45
889	Bemetara Bypass NH 30 (MoRTH) (617908) (-) (-)	Chhattisgarh	01/2024 (04/2025)	04/2027 (04/2027)	161.96 (161.96)	0	42
890	Construction of 4 Nos Grade sepatort between km. 281.000 to km. 307.600 km. 286.400 kumhari km. 299.000 Transport Nagar km. 302.000 Power House km. 304.000 Chandra Moura Chowk to km. 305.000 supeia of NH-53 old NH-06 Raipur - Durg 4 Lane on EPC mode in the state of chhattisgarh job NO. NH-53old NH-06 CG-2017-18-56 (MoRTH) (617919) (-) (-)	Chhattisgarh	03/2018 (01/2019)	01/2021 (08/2025)	349.03 (349.03)	304.04	97.9
891	Up-gradation to Two/Four lane with paved shoulder Configuration of Kondagaon-Narayanpur from design ch. 0.00 - 48.693 Design Length 47.493 Km. 1.20 Km. retained on NH-130D under EPC mode in the State Chhattisgarh. (MoRTH) (617971) (-) (-)	Chhattisgarh	12/2022 (03/2025)	03/2027 (03/2027)	322.40 (322.40)	1.14	70
892	Upgradation to Two lane with Paved Shoulder Configuration of Narayanpur Kasturmeta pkg-II from design ch. 48.693 to 70.453 design length21.760 Km. on NH-130D under EPC mode in the state of Chhattisgarh. (MoRTH) (617972) (-) (-)	Chhattisgarh	12/2022 (12/2024)	06/2026 (-)	200.67 (200.67)	0	0
893	Upgradation of Ambikapur-Ramanujganj-Garwa road of NH-343, Package-III, Badki mahri village to Ramanujganj section from existing km 80.600 to km 110.330 Design Ch. 85.370 to Ch. 114.800 of total length 29.430 km to two lane with paved shoulders udner corridor scheme under EPC Mode in the of Chhattisgarh (MoRTH) (618014) (-) (-)	Chhattisgarh	03/2022 (05/2025)	10/2026 (10/2026)	199.05 (199.05)	53	38.56
894	Upgradation of Keonchi - Ratanpur Road of NH 45 Package-I, from design chainage km 237.860 to km 273.200 of length 35.340 km to two lane with paved shoulders under Corridor scheme on EPC mode in the state of Chhattisgarh. (MoRTH) (618015) (-) (-)	Chhattisgarh	03/2022 (07/2024)	01/2026 (12/2026)	225.41 (228.93)	83.75	60
895	Upgradation of Ambikapur Ramanujganj - Garhwa Road NH 343 of Package-I, Rajpuri Khurd Village to Padih Village section from existing km 7.830 to km 57.650 Design Ch. 13.700 to Ch. 62.700 of total length 49.00 km to two lane with paved shoulders under EPC mode in the state of Chhattisgarh (MoRTH) (618016) (-) (-)	Chhattisgarh	03/2022 (05/2025)	05/2027 (05/2027)	397.44 (397.44)	76.67	28.07
896	Upgradation of Keonchi - Ratanpur Road of NH 45 Package-II, from design chainage km 278.75 to km 321.348 of length 42.598 km to two lane with paved shoulders under Corridor scheme on EPC mode in the state of Chhattisgarh. (MoRTH) (618017) (-) (-)	Chhattisgarh	03/2022 (07/2024)	01/2026 (12/2026)	286.00 (286.00)	92.75	60
897	Upgradation of Bilaspur-Takhatpur-Mungeli-Pandariya-Pondi Road on N.H.-130A Package IIA Takhatpur By-pass from existing Ch. 26.542 to 32.093 [Design Ch. 18.700 to 25.900] & Mungeli By-pass from existing Ch. 45.786 to 56.275 [Design Ch. 29.600 to 51.600] and Package IIIB Pandariya By-Pass from existing Ch. 82.582 to 87.133 [Design Ch. 77.900 to 81.1000 & Pondi By-pass from existing Ch. 103.166 to 104.756 [Design Ch. 97.000 to 103.395] to two lane with paved shoulder configuration in the (MoRTH) (618018) (-) (-)	Chhattisgarh	03/2022 (01/2024)	07/2025 (12/2026)	351.19 (351.19)	11.63	11
898	Durg-Raipur Bypass Section Package - 1 from km. 0.00 to km. 44.50 near Tendesara to near Khatti Village (NHAI) (618589) (-) (-)	Chhattisgarh	06/2022 (07/2023)	07/2025 (03/2027)	1828.00 (1656.73)	1063.62	75.39
899	Durg-Raipur-Arang Package - 2 from km. 44.50 to km. 92.23 near Khatti Village to near Aurang (NHAI) (618590) (-) (-)	Chhattisgarh	06/2022 (06/2023)	05/2025 (03/2027)	1958.90 (1561.97)	1001.18	73.96
900	4L of Bilaspur to Urga km 0.00 to 70.2 of NH-130A (NHAI) (618639) (-) (-)	Chhattisgarh	04/2020 (03/2022)	03/2024 (12/2026)	1855.59 (2523.86)	1470.78	94.81
901	4L of Urga - Pathalgaon from Km. 70.200 to km. 157.745 of NH-130A (NHAI) (618640) (-) (-)	Chhattisgarh	03/2022 (02/2024)	08/2026 (08/2026)	2261.30 (2860.36)	1120.45	81.5
902	4L of Pathalgaon-Kunkuri-CG/JH Border section of NH-43 from Km. 00.000 to Km.104.250 (NHAI) (618646) (-) (-)	Chhattisgarh	08/2024 (04/2026)	04/2029 (04/2029)	3147.07 (3147.07)	0.03	0

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
903	Development of 6L of Jhanki Sargi Section Road from km 0.000 to km 42.800 of NH-130CD Pkg-CG-1 (NHAI) (618673) (-) (-)	Chhattisgarh	11/2021 (09/2022)	09/2024 (02/2027)	1368.19 (1129.14)	715.32	99.35
904	Development of 6L Sargi Basanwahi Section from km 42.800 to km 99.500 of NH-130CD Pkg-CG-2 (NHAI) (618674) (-) (-)	Chhattisgarh	12/2021 (01/2023)	01/2025 (08/2026)	1470.73 (1461.81)	757.62	100
905	Development of 6L of Basanwahi Marangpuri Section from km 99.500 to km 124.661 of NH-130-CD (NHAI) (618675) (-) (-)	Chhattisgarh	03/2022 (10/2023)	10/2025 (03/2027)	1307.16 (1303.63)	489.55	70.73
906	4 laning of Champa - Korba from km 0.00 to km 38.2 (NHAI) (618957) (-) (-)	Chhattisgarh	02/2021 (01/2022)	01/2024 (08/2026)	1002.33 (1304.47)	944.68	98.75
907	Balance Works of Rehabilitation and Up gradation of NH-43 New NH-30 from Krm 162120 to Krm 173500 Length 11.380 Km. Keshkal Bypass 4-Lane with Paved shoulder in the State Of Chhattisgarh under NHDP-IV through Engineering, Procurement & Construction EPC Basis (MoRTH) (619039) (-) (-)	Chhattisgarh	06/2025 (06/2026)	06/2028 (-)	307.96 (307.96)	0	0
908	4/6 Laning of Raipur-Simga Pkg-I from km. 0.00 to km. 48.58 (NHAI) (619103) (-) (-)	Chhattisgarh	10/2015 (04/2016)	04/2018 (08/2026)	1096.52 (1172.36)	905.32	100
909	4 Laning with PS of Pathrapalli-Katghora km 53.3 to km 92.6 Pkg-II of Bilaspur Kathghora (NHAI) (619167) (-) (-)	Chhattisgarh	12/2019 (12/2020)	12/2022 (11/2026)	865.10 (1275.26)	853.85	93.1
910	Balance Work Estimate of Rehabilitation and Up-gradation of NH- 43 from Km. 468.600 to Km. 531.250 Pathalgaon to kunkuri Section to two-lane with paved shoulder in the State of Chhattisgarh on SBD mode under NHO under Annual plan 2025-26 (MoRTH) (619347) (-) (-)	Chhattisgarh	03/2026 (06/2026)	06/2028 (-)	201.16 (201.16)	0	0
911	Widening of Existing Road from Intermediate Lane 2-lane to 4-lane Between Km 19.994 to Km 35.180 of NH-848A Rakholi-Khadoli-Velugam Section in U.T. of Dadra and Nagar Haveli and Daman and Diu (MoRTH) (619183) (-) (-)	Dadra & Nagar Haveli and Daman & Diu	10/2022 (02/2024)	06/2026 (08/2026)	198.06 (239.57)	77.74	80
912	Development of 6L UER II [Package - I] NH-1 Near Bakoli till Karala Kanjhawala Road from km. 0.70 to km.15.00 (NHAI) (618509) (-) (-)	Delhi	07/2020 (10/2021)	10/2023 (08/2026)	2089.94 (2203.45)	1834.91	99.99
913	8L of Dwarka Expressway Pkg-II RuB near Dwarka Sector 21-DL/HR Border from 5.300 Km.to 9.500 Km. of NH-248BB (NHAI) (619090) (-) (-)	Delhi	01/2018 (10/2019)	10/2021 (08/2026)	2067.67 (2670.22)	2381.53	100
914	Dwarka Expressway from Km -0.600 to Km 5.300 - Pkg-I Shivmurti Chowk-RuB near Dwarka Sector 21 (NHAI) (619202) (-) (-)	Delhi	03/2018 (09/2020)	09/2022 (08/2026)	2144.67 (3929.50)	3512.17	98.8
915	4-Laning from End of Zuari approaches to Start of Margao Bypass section of NH-66 from Km 536.800 to Km 543.450 (MoRTH) (617941) (-) (-)	Goa	07/2024 (02/2026)	02/2028 (02/2028)	398.25 (398.25)	0.28	1
916	Construction of Six lane Elevated Corridor from Km. 508.000 to Km. 513.150 including approaches on NH-66 (MoRTH) (617942) (-) (-)	Goa	04/2023 (04/2024)	04/2026 (10/2026)	641.46 (641.46)	0	99.08
917	4-laning of Navelim to Cuncolim Section of NH-66 from Km 554.245 to Km 561.480 on HAM Mode (MoRTH) (617943) (-) (-)	Goa	12/2024 (04/2026)	10/2028 (10/2028)	746.75 (746.75)	0	0
918	Construction of 4L Flyover from MES College Junction to Bogmalo Junction on NH-566 from Km. 7.106 to Km. 10.460 and 4L VUP at Queeny Nagar Junction from Km. 3.330 to Km. 4.550 (NHAI) (618609) (-) (-)	Goa	01/2024 (08/2024)	07/2026 (05/2027)	463.08 (316.28)	168.21	59.18
919	Up-gradation of Dhoraji-Jamkandorna-Kalavad Section of NH-927D from Design Chainage km 0/00 to km 58/115 to Two lane with PS configuration in the State of Gujarat on EPC (MoRTH) (617906) (-) (-)	Gujarat	10/2022 (01/2025)	01/2027 (01/2027)	246.60 (291.19)	0	35

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
920	Work of 6 laning/Construction of elevated corridor from km 0/0 to 10/170 Narol Junction to Sarkhej junction including 4 lane Shastri Bridge on Sabarmati river on NH 47 in the State of Gujarat on HAM mode (MoRTH) (617916) (-) (-)	Gujarat	03/2024 (08/2025)	02/2028 (02/2028)	1295.39 (1295.39)	0	35
921	Construction of new 4 lane major bridge with approaches on Sabarmati River near Dharoi at Km. 82/00 to 86/00 Design length 3.300 km on NH-58 in the State of Gujarat on Hybrid Annuity Mode HAM (MoRTH) (617926) (-) (-)	Gujarat	03/2024 (08/2025)	08/2027 (08/2027)	398.40 (398.40)	0	53
922	Widening to 2LPS between Km 0/0 to 56/0 Khokhara Gujarat Border Vijayanagar Antrasuba Mathasur road of NH 58 in the State of Gujarat (MoRTH) (617927) (-) (-)	Gujarat	03/2024 (09/2025)	09/2027 (09/2027)	699.19 (699.19)	0	36
923	Widening 2 lane to 4-lane from KM 92/320 to Km 115/320 Vav Chokdi-Satlasana to to Vrundavan Chokdi, Kheralu on NH-58 in the State of Gujarat. (MoRTH) (617928) (-) (-)	Gujarat	03/2022 (03/2024)	03/2026 (08/2026)	151.13 (171.27)	0	98
924	Work of development and construction of elevated corridorfrom km 38/660 to km 42/690 Iscon junction to start point of approach of sanand flyover of NH-147 in the sate of Gujarat (MoRTH) (617976) (-) (-)	Gujarat	03/2023 (06/2024)	06/2026 (09/2026)	530.20 (530.20)	58.29	90
925	Upgradation to two lane with paved Shoulder Configuraton from Km. 0/00 to 47/000 of NH 351 Mahuva to Badhada section in the State of Gujarat (MoRTH) (618022) (-) (-)	Gujarat	12/2022 (02/2024)	08/2025 (12/2026)	173.06 (219.08)	22.63	77
926	Upgradation of Mehsana-Visnagar-vadnagar-Kheralu-Idar section from km 0/00 to 81/300 of NH 168G Mehsana to Idar in the State of GujaratTotal Length 81.300 Km on Hybrid Annuity Mode HAM (MoRTH) (618107) (-) (-)	Gujarat	02/2024 (12/2025)	06/2028 (06/2028)	1155.21 (1155.21)	421.58	23
927	Up-gradation and strengthening to 2lanePS from Km 95/500 to km 129/775 of Nh 168G Idar-Bhiloda-Samlaji in the state of Gujarat Length 34.275 km (MoRTH) (618108) (-) (-)	Gujarat	09/2022 (12/2023)	12/2025 (12/2026)	237.28 (237.28)	41.55	64.5
928	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-26 Ch.696890 to Ch.726390 (NHAI) (618459) (-) (-)	Gujarat	09/2020 (12/2022)	08/2024 (02/2027)	1555.20 (1556.40)	1288.32	85.5
929	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-31 Ch.824920 to Ch.844382 [Junction near Pratap nagar Village - Junction near Dodka Village] (NHAI) (618462) (-) (-)	Gujarat	11/2019 (05/2021)	05/2023 (08/2026)	1644.85 (1651.14)	1297.76	100
930	Vadodara Mumbai Expressway Kim to Ankleshwar Phase IA - Pkg V (NHAI) (618463) (-) (-)	Gujarat	02/2018 (11/2019)	10/2021 (08/2026)	1324.84 (2807.48)	1546.7	91.34
931	Vadodara Mumbai Expressway Karvad - Jujuwa from Km. 128.000 to Km. 154.600 Phase-I Package-IX (NHAI) (618467) (-) (-)	Gujarat	07/2023 (04/2024)	10/2025 (07/2027)	2594.17 (2587.04)	235.55	21.75
932	Ahmedabad - Dholera Pkg III from km. 48.52 to km. 71.06 [Vejallka Village - Start of DSIR zone] (NHAI) (618503) (-) (-)	Gujarat	05/2020 (07/2021)	07/2023 (08/2026)	1034.04 (1155.41)	1125.55	100
933	Ahmedabad - Dholera Pkg IV from km. 71.06 to km. 109.019 [Start of DSIR zone - Adhelai Village] (NHAI) (618504) (-) (-)	Gujarat	05/2020 (12/2021)	12/2023 (08/2026)	1181.76 (1358.73)	1222.79	98.08
934	Balance work of Six Laning of Shamlaji-Motachiloda from Km. 401.200 to Km.494.410 section Design Chainage Km.447.385 to Km 540.595, Length- 93.210 Km of old NH-8 NH-48 in the state of Gujarat on single Percentage Item Rate Contract (NHAI) (618507) (-) (-)	Gujarat	06/2024 (08/2024)	06/2025 (08/2026)	466.80 (501.48)	577.62	91.83
935	Construction of Additional Structures including Approaches in Vadodara Surat Section of NH48 between existing Km. 108.000 to Km. 250.000 (NHAI) (618508) (-) (-)	Gujarat	03/2024 (01/2025)	01/2027 (06/2027)	907.39 (907.39)	368.63	48.73
936	6L with PS of Samakhiyali to Santalpur section from km. 339.700 to Km. 430.100 of NH-27 (NHAI) (618564) (-) (-)	Gujarat	01/2023 (12/2023)	12/2025 (03/2027)	1553.76 (34.34)	28.66	64.52
937	Sanchore - Santalpur from km 99.000 - km 130.073 of NH-754K AJ-RGBS-Package-4 (NHAI) (618615) (-) (-)	Gujarat	02/2020 (03/2021)	03/2023 (08/2026)	778.15 (835.55)	767.83	99.7

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
938	4L of Dhrol bypass section of NH-151A Approx. length 5.7 Km & widening upto 4 laning of missing link of Amran section of NH-151A Approx. length 6.55 Km from existing Ch. 42000 to 48500 of ongoing Dhrol-Bhadra-Pipaliya section of NH-151A (NHAI) (618616) (-) (-)	Gujarat	03/2024 (02/2025)	02/2027 (02/2027)	625.58 (455.54)	151.99	35.47
939	Upgradation to 4L PS from Bhimasar, Junction of NH-41 to Anjar- Bhuj upto Airport Junction from Km 0.000 to Km 65.478 of NH-341 (NHAI) (618787) (-) (-)	Gujarat	03/2022 (01/2023)	06/2025 (03/2027)	1373.06 (1687.25)	837.85	96
940	4L PS Divided Carriageway from Patan Near Rajpur to Gojariya From Km 52.000 to Km 128.940 of NH-68 (NHAI) (618901) (-) (-)	Gujarat	12/2021 (03/2023)	03/2025 (11/2026)	1181.34 (1098.23)	934.16	87.12
941	4L PS from Ch. 94.030 in Jabugam Village to Ch. 132.320 in Dhamasiya Village of NH-56 Pkg-III (NHAI) (618930) (-) (-)	Gujarat	03/2023 (11/2025)	11/2027 (11/2027)	1188.46 (898.00)	179.47	25.82
942	4L PS from Ch. 179.780 in Bitada/Movi Village to Ch. 208.900 in Nasarpore Village of NH-56 Pkg-V (NHAI) (618931) (-) (-)	Gujarat	03/2023 (11/2025)	11/2027 (11/2027)	764.02 (566.96)	82.38	10.08
943	Construction of 4 lane with PS Idar-Badoli bypass section from design km 81/300 to km 95/500 of NH 168G in the State of Gujarat (MoRTH) (619061) (-) (-)	Gujarat	03/2025 (05/2026)	05/2028 (05/2028)	705.09 (705.09)	0	7
944	Widening to 6L of Existing 4L Jetpur - Gondal - Rajkot Section from Km. 117.600 to Km. 185.00 on NH-27 (NHAI) (619087) (-) (-)	Gujarat	03/2022 (09/2023)	09/2025 (01/2027)	2070.44 (1390.29)	1117.01	76.83
945	Four Laning of Una to Kodinar from km. 180.478 to km. 221.610 Package-V (NHAI) (619145) (-) (-)	Gujarat	02/2016 (02/2017)	08/2019 (03/2025)	877.71 (1126.66)	1008.79	100
946	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-27 Ch.729.700 to Ch.756.052 (NHAI) (619197) (-) (-)	Gujarat	09/2020 (02/2022)	02/2024 (08/2026)	1185.69 (1259.27)	1045.08	98.9
947	Upgradation of Existing Two Lane Carriageway to Two Lane Carriageway with Paved Shoulder from Ch. 665686 Existing Km. 665.686 in Khanpur Village in Vansda Taluka to Ch. 710470 Existing Km. 710.483 in Karvad Village in Vapi Taluka Length 44.784 Km Section of NH-56 in the State of Gujarat on EPC Mode (NHAI) (619297) (-) (-)	Gujarat	02/2026 (07/2026)	07/2028 (01/2027)	647.20 (647.20)	9.24	0
948	Delhi-Amritsar-Katra Expressway Phase-I Pkg-I from Jussur Kheri on NH-KMP Expressway to Junction with Rohtak-Panipat road NH-709 near Rukhi Paani village Km 0000 to Km 34000 (NHAI) (618482) (-) (-)	Haryana	12/2020 (12/2021)	12/2023 (07/2026)	1866.49 (2429.90)	1609.72	99.91
949	Delhi-Amritsar-Katra Expressway Phase-I Pkg-II from Junction with Rohtak-Panipat road NH-709 near Rukhi Paani village to Junction with Jind-Panipat road NH-352A near Gangana village Km 34000 to Km 60800 (NHAI) (618483) (-) (-)	Haryana	12/2020 (01/2022)	01/2024 (07/2026)	1533.87 (1792.53)	1176.23	99.89
950	Construction of Additional Structures, Improvement of Service Road & Maintenance of Six Lane Gurgaon-Jaipur Section of NH-48 old NH-8 between km 42700 to km 107100 in the State of Haryana (NHAI) (618506) (-) (-)	Haryana	05/2024 (05/2025)	05/2027 (05/2027)	401.74 (240.02)	131.79	61.38
951	Gohana - Sonipat PKG-2 (NHAI) (618580) (-) (-)	Haryana	01/2019 (07/2020)	07/2022 (07/2026)	1275.31 (1957.44)	1225.85	97.86
952	4L Greenfield Jalbhera Shahbad section from km. 0.000 to km. 22.850 of NH-152G (NHAI) (618788) (-) (-)	Haryana	03/2022 (06/2023)	05/2025 (08/2026)	927.22 (1173.66)	550.65	87.05
953	4L Bhiwani-Hansi road section of NH-148B (NHAI) (618792) (-) (-)	Haryana	11/2022 (12/2023)	12/2025 (08/2026)	1330.23 (1144.21)	455.86	99.5
954	Jagadhari - Tajewala from Km -0.175 to 32.337 km of NH-344 (NHAI) (618936) (-) (-)	Haryana	03/2022 (02/2023)	02/2025 (03/2027)	1269.50 (919.43)	712.77	68
955	4L PS of Ambala Ring Road of New NH-44 (NHAI) (619080) (-) (-)	Haryana	02/2023 (10/2023)	10/2025 (09/2026)	1093.35 (1225.41)	595.59	92.97
956	4L of Jind-Gohana road Package-1 from km. 0.00 to km. 40.601 of NH-352 A under NHO (NHAI) (619092) (-) (-)	Haryana	01/2019 (07/2020)	07/2022 (07/2026)	994.22 (1606.82)	1064.47	99.97

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
957	4/6L of Gurgaon - Pataudi - Rewari from km. 0.00 to km.43.87 of NH-352W (NHAI) (619132) (-) (-)	Haryana	05/2020 (11/2021)	11/2023 (08/2026)	1810.04 (1917.50)	1267.55	77.76
958	Karnal ring road Lot-4/Pkg-1 (NHAI) (619201) (-) (-)	Haryana	11/2022 (08/2023)	08/2025 (10/2026)	1741.45 (2041.54)	834.54	96.66
959	Improvement/construction of existing CL-5 Road to NH Intermediate lane specification with hard shoulder from Km 166.000 to 203.77 net Length 37.770 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh on EPC mode under project Deepak, BRO (MoRTH) (618215) (-) (-)	Himachal Pradesh	06/2021 (06/2024)	06/2027 (06/2027)	274.36 (194.00)	0	22.26
960	Improvement/construction of existing CL-5 Road to NH Intermediate lane specification with hard shoulder from Km 133.000 to 166.000 net Length 33.000 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh on EPC mode under project Deepak, BRO (MoRTH) (618216) (-) (-)	Himachal Pradesh	03/2021 (07/2023)	06/2026 (09/2027)	230.55 (203.15)	31.4	23.24
961	Improvement/construction of existing Class-5 Road to NH Intermediate lane specification with hard shoulder from existing Km 76/340 to 134/940 Design chainage from Km 76/300 to 133/000 net Length 56.700 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh Package I (MoRTH) (618217) (-) (-)	Himachal Pradesh	03/2021 (05/2023)	05/2026 (08/2027)	314.67 (244.15)	93.27	62.28
962	Rehabilitation and Upgradation to 2-lane configuration of Kalwahn-Mandi Section km 208.950 to 250.592 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-3 (MoRTH) (618230) (-) (-)	Himachal Pradesh	08/2020 (10/2022)	04/2025 (12/2026)	314.32 (314.32)	0	70.58
963	Rehabilitation and Upgradation to 2-lane configuration of Hamirpur-Karnohal Section km 141.00 to 181.00 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-1 (MoRTH) (618231) (-) (-)	Himachal Pradesh	08/2020 (06/2022)	12/2024 (09/2026)	371.93 (371.93)	198.34	93.62
964	Rehabilitation and Upgradation to 2-lane configuration of Karnohal- Kalwahn Section km 181.00 to 208.950 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-2 (MoRTH) (618232) (-) (-)	Himachal Pradesh	08/2020 (11/2023)	05/2026 (12/2026)	251.62 (190.02)	77.84	58
965	Construction of missing link from Birhu to Lathiani from Km 35/550 Design chainage Km 0.000 to Km 42/800 Design Chainage Km 8.153on NH-503A including Lathiani Bridge on back water of Govindsagar and its approaches in Himachal Pradesh. (MoRTH) (618253) (-) (-)	Himachal Pradesh	06/2023 (03/2026)	03/2029 (03/2029)	870.95 (896.86)	0	0
966	Nerchowk km 190.000 to Pandoh including Pandoh bypass km221.305 (NHAI) (618850) (-) (-)	Himachal Pradesh	03/2016 (01/2018)	07/2020 (08/2026)	1464.12 (1651.67)	1574.85	100
967	Pandoh bypass 221.305 to Takoli 242.000 of NH-21 in the state of Himachal Pradesh (NHAI) (618851) (-) (-)	Himachal Pradesh	06/2017 (03/2018)	09/2021 (03/2027)	3419.95 (4465.94)	2883.58	95.65
968	4L Sundar Nagar Bypass from Km.173.900 to Km.179.600 of NH-21 (NHAI) (618852) (-) (-)	Himachal Pradesh	02/2022 (06/2022)	06/2024 (08/2026)	191.11 (192.11)	182.6	100
969	Rehabilitation and Upgradation to 4L configuration & Strengthening of Sihuni to Rajol from Km 51.000 to Km 72.000 of NH-154 Package-IIA (NHAI) (618878) (-) (-)	Himachal Pradesh	03/2022 (09/2023)	09/2025 (09/2026)	696.65 (776.59)	496.48	99.18
970	Rehabilitation and Upgradation to 2L PS configuration & Strengthening of Padhar to Bijni section from Km 180.000 to Km 202.815 of NH-154 Pkg-VA (NHAI) (618879) (-) (-)	Himachal Pradesh	06/2022 (11/2024)	11/2026 (11/2026)	930.86 (930.86)	666.12	99.86
971	Rehabilitation and Up-gradation to 4L configuration & Strengthening of Thanpuri to Paror section from Km 85.135 to Km 100.840 of NH-154 Pkg-IIC (NHAI) (618880) (-) (-)	Himachal Pradesh	07/2022 (03/2024)	12/2025 (04/2027)	815.68 (666.79)	496.91	56.61
972	4L PS bijni to mandi section from Km 202.815 to Km 208.000 of NH-20 New NH-154 of Pathankot-Mandi Package-VB (NHAI) (618881) (-) (-)	Himachal Pradesh	02/2023 (03/2025)	09/2027 (09/2027)	1113.02 (1112.39)	547.08	35.3
973	Rehabilitation and Up-gradation of existing road to 2L PS from End of Hamirpur Bypass near Chilbahal to Bhangbar section from Km. 138.295 to Km.175.270 of NH-88 Pkg-IV (NHAI) (618888) (-) (-)	Himachal Pradesh	03/2022 (04/2023)	04/2025 (12/2026)	1146.19 (1358.62)	987.35	97.2

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
974	4L of Bhangbar Near Ranital to Kangra Bypass Section of Old NH-88 New NH-303,503 up to Intersection with NH-154 from Km 175.270 to Km 193.400 Pkg-VB (NHAI) (618889) (-) (-)	Himachal Pradesh	03/2021 (12/2022)	12/2024 (09/2026)	1322.95 (1829.49)	1102.58	97.45
975	2L PS of Hamirpur Bypass from Km 121.175 to Km.138.295 of NH-103&3 (NHAI) (618890) (-) (-)	Himachal Pradesh	08/2022 (10/2023)	10/2025 (12/2026)	739.39 (754.82)	369.94	94.37
976	4L PS from Kalar Bala Village to Nauni Chowk of NH 205 from Km 41.000 to Km 58.450 (NHAI) (618891) (-) (-)	Himachal Pradesh	01/2024 (05/2025)	05/2027 (09/2027)	1244.43 (786.91)	145.72	31.46
977	4 Lane with Paved Shoulder from Dareota Village to Kalar Bala NH 205, Design Chainage -Km 33185 to Km 41000, Design Length-7.815 Km Package-IIB (NHAI) (618892) (-) (-)	Himachal Pradesh	06/2025 (06/2026)	06/2028 (06/2028)	992.85 (992.85)	5.27	0.68
978	4L of Kathlighat to Shakral Village from Km 128.835 to Km 146.300 of NH- 5 Shimla Bypass - Pkg I (NHAI) (618921) (-) (-)	Himachal Pradesh	03/2022 (04/2023)	04/2026 (07/2027)	1703.48 (2648.80)	1182.61	64.2
979	4L of Shakral Village to Dhalli Section from Km 146.300 to Km 156.560 Shimla Bypass - Pkg II and Shimla connectivity from Km 0.000 to Km 0.725 of NH-5 (NHAI) (618922) (-) (-)	Himachal Pradesh	04/2022 (03/2024)	03/2027 (12/2027)	1956.26 (2880.72)	1505.86	59.88
980	Solan - Kaithlighat Section of NH-22 Now NH-5 from Km. 106.139 to Km.129.05 (NHAI) (619003) (-) (-)	Himachal Pradesh	03/2018 (11/2018)	05/2021 (11/2026)	881.74 (1519.53)	1347.79	90.11
981	4L of HP/Punjab Border - Mo from km. 11.00 to km. 42.00 of Old NH-20 New NH-154 Package-IA (NHAI) (619153) (-) (-)	Himachal Pradesh	03/2021 (05/2022)	05/2024 (12/2026)	1002.11 (1363.04)	819.72	68.65
982	Construction of Shopian Bypass on NH-444 taking off from existing chainage Km 36500 and re-joining at km 47588 of existing Chainage New Design Ch. From km 28000 to km 36925 as 2- lane with paved shoulder in the UT of Jammu & Kashmir on EPC mode. (MoRTH) (618038) (-) (-)	Jammu and Kashmir	03/2024 (01/2026)	01/2028 (-)	224.44 (224.44)	0	3
983	Widening and strengthening to 2 lane with paved shoulder from existing Ch. Km 56720 to Km 100820 and Design Ch. From Km 62600 to Km 106360 Total Length43.760 Km on SRINAGAR -BARAMULA URINH-01 in the UT of Jammu & Kashmir under project BEACON, Border Roads Organization BRO on EPC mode. (MoRTH) (618201) (-) (-)	Jammu and Kashmir	09/2023 (11/2024)	11/2026 (06/2027)	702.10 (702.10)	0	51
984	Construction of 2 lane with paved shoulders Baramulla Bypass Greenfield bypass from existing Ch. Km 47020 to Km 56720 and Design Ch. From 48500 to 62600 Total length 14.100 km on road Srinagar Baramulla Uri NH-01 in the UT of Jammu & Kashmir under Project.Package-III (MoRTH) (618202) (-) (-)	Jammu and Kashmir	03/2023 (09/2024)	09/2026 (07/2027)	992.43 (992.43)	112.16	46.8
985	Construction of 4 lane with paved shoulder Pattan bypass Greenfield bypass from existing Ch. Km 24320 to Km 33760 and Design Ch. from Km 24400 to Km 35300, total length 10.900 km on road SrinagarBaramulla Uri NH-01 in the UT of Jammu & Kashmir under Project BEACON, Border Roads Organization BRO on EPC mode. Package-II (MoRTH) (618203) (-) (-)	Jammu and Kashmir	03/2023 (08/2024)	07/2026 (02/2027)	980.21 (980.21)	132.03	57
986	Construction of realignment between Pandrass- Pashkyun Total length 27.10 km on road Zozila-Kargil -Leh NH-1 to 2 lane specifications i.e. Drass alignment 9.30 km Kharboo realignment 6.30 km & Kargil alignment 11.50 km under project Vijayak BRO in the UT of Ladakh on EPC Mode (MoRTH) (618204) (-) (-)	Jammu and Kashmir	11/2021 (06/2023)	06/2025 (07/2027)	426.15 (426.15)	112.2	54.89
987	Construction of 4 lane with paved shoulder from Existing Ch. 14200 to 24320 Design Ch. 14200 to 24400, Ch. 33760 to 42780 Design Ch. 35300 to 44294 & Ch. 43440 to 47020 Design Ch. 44958 to 48500 Delina Flyover including construction of flyover length 1.704 km of total length 22.736 kms in AOR of 760 BRTF on road SRINAGAR BARAMULA URI NH-01 in the UT of Jammu & Kashmir under project BEACON, Border Roads Organization BRO Package-IJob No NH-1-J&K-2022-23-110 (MoRTH) (618205) (-) (-)	Jammu and Kashmir	06/2022 (08/2023)	08/2025 (12/2026)	823.46 (823.46)	298.96	85.5
988	Widening and Strengthening of Rafiabab-Kupwara-Chowkibal-Tangdhar-Chamkot NH-701 road from design Ch. From 0000 to 51000 to two lanes with paved shoulders under Project Beacon in the UT of Jammu & Kashmir on EPC mode Package-I. (MoRTH) (618206) (-) (-)	Jammu and Kashmir	03/2024 (11/2024)	05/2027 (-)	1404.94 (1404.94)	160.59	41.7
989	Rehabilitation and upgradation to 2 lane with paved shoulder from existing chainage Km 166.100 to Km 192.98 design chainage Km 146.700 to Km 162.800 including construction of Bhimber Gali Tunnel Total Length of Tunnel 1.100 Km under 31 BRTF on Akhnoor-Poonch Roads on EPC mode NH-144A Package-VII (MoRTH) (618221) (-) (-)	Jammu and Kashmir	09/2021 (07/2024)	07/2026 (07/2027)	734.64 (734.64)	0	60

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
990	Widening and Strengthening up gradation to 2 lane with paved shoulder from existing chainage Km 192.98 to Km 229.820 design chainage Km 162.800 to Km 198.18 under 31 BRTF on Akhnoor-Poonch Road NH-144A in the UT of Jammu and Kashmir under Project Sampark Border Roads Organisation BRO on EPC Mode Package-VIII Job No NH-144A-J&K-2022-2023-111 (MoRTH) (618222) (-) (-)	Jammu and Kashmir	10/2022 (01/2024)	01/2026 (03/2027)	562.45 (562.45)	158.68	71.27
991	Rehabilitation and up-gradation to 2 lane with paved shoulder from existing chainage km 64535 to km 85385 Design chainage km 55800 to km 74350 under 13 TF on Akhnoor-Poonch road NH-144A under Project Sampark BRO in the UT of Jammu & Kashmir on EPC mode Package-III Job no NH-144A-J&K-2019-20-79 (MoRTH) (618223) (-) (-)	Jammu and Kashmir	03/2020 (09/2021)	09/2023 (12/2026)	152.93 (152.93)	77.62	90.06
992	Rehabilitation and up-gradation to 2 lane with paved shoulder from existing chainage km 49150 to km 64535 Design chainage km 46.450 to km 55.800 including construction of Sungal Tunnel Total length of Tunnel 2.79 km under 13 TF on Akhnoor-Poonch road NH-144A under Project Sampark BRO in the UT of Jammu & Kashmir on EPC mode Package-II Job no NH-144A-J&K-2019-20-78 (MoRTH) (618224) (-) (-)	Jammu and Kashmir	03/2020 (08/2021)	08/2024 (08/2026)	796.97 (796.97)	440.97	92.1
993	Rehabilitation and up-gradation to 2 lane with paved shoulder from existing chainage km 134950 to km 166100 Design chainage km 116980 to km 146700 under 31 TF on Akhnoor-Poonch road NH-144A in the UT of Jammu & Kashmir under Project Sampark BRO on EPC mode Package-VI Job no NH-144A-J&K-2021-22-106 (MoRTH) (618225) (-) (-)	Jammu and Kashmir	07/2021 (07/2022)	07/2024 (12/2026)	395.25 (395.25)	162	89.2
994	Rehabilitation and upgradation to 2 lane with paved shoulder from existing chainage Km 30.053 to Km 49.150 design chainage Km 30.000 to Km 46.450 including Kandi Tunnel under 31 BRTF on Akhnoor-Poonch Road NH-144A Under Project Sampark in the UT of Jammu & Kashmir EPC modePackage-I Job no NH-144A-J&K-2020-21-83. (MoRTH) (618226) (-) (-)	Jammu and Kashmir	07/2020 (11/2022)	11/2024 (12/2026)	272.49 (272.49)	160.08	95.27
995	Up-gradation to 2-lane with Paved Shoulder from Km 12.850 to Km20.300 of 7.450Km length on Goha-Khellani section and a link road to Goha village of 2.016 km on NH-244 in UT of Jammu and Kashmir on EPC Mode Pkg-1 (NHIDCL) (618394) (-) (-)	Jammu and Kashmir	07/2020 (10/2020)	04/2022 (10/2026)	228.39 (225.37)	182.21	94.26
996	Construction & Upgradation to 2-lane with paved shoulder from Design Ch. Km 51700 at Premnagar km 66315 to Km 66535 New Thatri at Start of Km 83rd, Tunnel Km 82665 of 14.835 Km design length on Chenani-Sudhmahadev-Goha Khellani-Kishtwar-Vailoo Donipawa-Ashajipora section of NH-244 in the UT of J&K on EPC Mode under NHO-Gen Pkg - 2 (NHIDCL) (618395) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	02/2023 (10/2026)	512.43 (512.43)	164.66	53.49
997	Widening and Up-gradation to 2-Lane with Paved Shoulder of configuration and geometric improvement from Km 0.000 to Km 16.990 on Chenani Sudhmahadev section of NH-244 in UT of Jammu and Kashmir to be executed on EPC basis (NHIDCL) (618397) (-) (-)	Jammu and Kashmir	03/2018 (11/2018)	11/2020 (12/2025)	255.90 (255.90)	239.96	94.06
998	Up-gradation to 2-lane with Paved Shoulder from Km 20.300 to Km 29.030 of 8.730 Km length on Goha-Khellani section on NH-244 in UT of Jammu and Kashmir on EPC Mode Package II (NHIDCL) (618398) (-) (-)	Jammu and Kashmir	07/2020 (10/2020)	04/2022 (06/2026)	210.79 (210.79)	190.27	96.95
999	Construction of Kishtwar bypass with 2 lane with paved shoulder from Design Km. 80.675 Dulhasti to km 95.550 Bandarkoot of 14.88 km & a link road to Kishtwar town from 0000 to 1.871 of length1.871 Km on Khellani - Kishtwar - Chattoo section in UT of Jammu and Kashmir on EPC Mode Pkg-4 (NHIDCL) (618399) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	08/2023 (06/2027)	859.67 (859.67)	363.03	50.64
1000	Construction & Upgradation to 2-lane with paved shoulder from Design Km 67.805 at the end of Km 83rd Tunnel near Dhrabshalla Ex. Km 83905 to Km 80.675 start of Kishtwar Bypass - Dulhasti Ex. Km 970751 of 12.870 Km length on chenani-Sudhmahadev-Goha Khellani-Kishtwar-vailoo-Donipawa-Ashajipora seition of NH-244 in the UT of J&K on EPC Mode under NHO-Gen Pkg-3 (NHIDCL) (618400) (-) (-)	Jammu and Kashmir	03/2021 (07/2021)	12/2022 (08/2025)	398.51 (398.51)	120.09	98.55
1001	Up-gradation to 4-lane with Paved Shoulder of Jammu-Akhnoor road section of NH-144A from Ganesh Vihar Km 6.000 to Khati Chowk Km 26.350 in UT of Jammu and Kashmir on EPC basis Pkg-3A (NHIDCL) (618406) (-) (-)	Jammu and Kashmir	03/2018 (07/2019)	07/2021 (11/2026)	322.49 (322.49)	398.19	92.5
1002	Jammu-Akhnoor Road Pkg-I (NHIDCL) (618407) (-) (-)	Jammu and Kashmir	03/2018 (01/2023)	01/2025 (10/2026)	245.30 (245.30)	115.21	75.29
1003	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XV [Junction with Hiranagar Road near village Gurha Baildaran to Junction with Jammu Ring Road NH-244A near Jakh village from Km 468100 to Km 503250] (NHAI) (618494) (-) (-)	Jammu and Kashmir	10/2021 (09/2022)	09/2024 (12/2026)	2714.95 (3716.56)	1846.59	90.01

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1004	4/6L Access Control Expressway from Design Chainage Km 515.000 to 528.300 Kunjwani to Sidhra Section of NH-44 and from Design Chainage Km 550.900 to Km 566.520 Domel to Katra Section Phase II-Package XVII (NHAI) (618495) (-) (-)	Jammu and Kashmir	06/2022 (06/2023)	06/2025 (11/2027)	2894.74 (2894.74)	1016.96	66.74
1005	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XVI Existing Jakh Vijaypur-Kunjwani section of NH-44 including spur Connectivity to Jammu Airport NH-144A [Km 503500 to km 514500] (NHAI) (618496) (-) (-)	Jammu and Kashmir	09/2021 (09/2022)	09/2024 (09/2026)	1821.72 (2522.56)	1238.6	94.14
1006	Delhi Amritsar Katra Expressway Phase-II Pkg XVIII Development and Upgradation of Four lane Access Control Expressway from Design Chainage KM 530.00 to KM 545.300 Sidhra to Domel Section of NH-44 (NHAI) (618497) (-) (-)	Jammu and Kashmir	12/2022 (11/2023)	11/2025 (06/2027)	1025.73 (975.38)	631.2	70.17
1007	4L Ring road/bypass around Srinagar city from km 0.000 to km 42.100 Phase-I (NHAI) (618541) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	02/2024 (10/2026)	2919.96 (2604.76)	1832.29	89
1008	4L of existing Wayul Ganderbal Pandach Soura section of old NH-1 as a part of Srinagar Ring Road Phase IIA (NHAI) (618542) (-) (-)	Jammu and Kashmir	12/2024 (05/2026)	05/2028 (05/2028)	827.98 (827.98)	265.02	0.02
1009	4L of twin tube tunnel configuration including approaches from Marog to Digdol from Km.154.210 to Km.158.650 North Bound and from Km.155.940 to Km.160.260 South Bound of Ramban to Banihal Pkg-I of Old NH-1A New NH-44 (NHAI) (618543) (-) (-)	Jammu and Kashmir	07/2021 (08/2022)	08/2025 (12/2027)	1912.17 (1034.30)	406.09	30.5
1010	4L twin tube tunnel including approaches from Digdol to Khuni Nallah North Bound connecting with existing major bridge on NB and South Bound connecting with Tunnel T4 ,Single tube tunnel of Ramban to Banihal Pkg-II of Old NH-1A New NH-44 (NHAI) (618544) (-) (-)	Jammu and Kashmir	07/2021 (02/2022)	06/2024 (09/2026)	1401.87 (1020.99)	1054.8	87.1
1011	4L of Km.165.092 to Km.171.855 North Bound and from Km.166.895 to Km.173.638 South Bound, excl. certain reaches of North Bound and South Bound of Ramban to Banihal Pkg-III of Old NH-1A New NH-44 (NHAI) (618545) (-) (-)	Jammu and Kashmir	07/2021 (02/2022)	08/2024 (06/2027)	614.48 (444.76)	306.05	42.8
1012	2L NH-1 from km 8.660 to km 33.775 Sumbal to Wayul to 4L dual carriageway NH standard as part of Srinagar Ring Road PhaseII [Design Ch. 41.907 to Ch. 66.609] (NHAI) (618547) (-) (-)	Jammu and Kashmir	11/2022 (12/2023)	06/2026 (06/2027)	961.00 (643.64)	474.55	55.02
1013	Construction of twin tube tunnels on Jammu Kashmir Ring Road NH-244A Between Design Ch. 50600 to 51700 and design Ch. 53535 to 55700 on EPC mode under residual NHDP component of Bharatmala Pariyojna (NHAI) (618549) (-) (-)	Jammu and Kashmir	11/2022 (06/2023)	06/2025 (12/2026)	242.65 (731.59)	677.47	83.87
1014	Corridor Efficiency Improvement including removal of black spots in Lakhanpur - Samba section of NH-44 from Chainage Km. 16.300 to Km. 74.100 (NHAI) (618550) (-) (-)	Jammu and Kashmir	06/2022 (12/2022)	06/2024 (12/2026)	855.74 (215.68)	203.55	74.63
1015	Upgradation and Strengthening of Chenani to Nashri Section via Patnitop of NH244 from Km 0.000 to Km 39.100 (NHAI) (618967) (-) (-)	Jammu and Kashmir	03/2024 (08/2024)	08/2026 (03/2027)	295.06 (295.06)	176.25	64.88
1016	Construction/upgradation to 2-lane with paved shoulder from Design Km 95.55 Bandarkoot to Km. 111.06 Chattoo of 15.52 Km length on Khellani-Kishtwar-Chattoo section on NH-244 in UT of Jammu and Kashmir on EPC Mode Pkg-5 (NHIDCL) (619038) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	02/2023 (03/2026)	497.09 (497.09)	270.82	99.97
1017	Widening and Strengthening of existing paveemnt to two lane with paved shoulders from km 116.00 to km 176.355 of NH-75E in the State of Jharkhand on EPC mode. (MoRTH) (618060) (-) (-)	Jharkhand	01/2022 (01/2023)	07/2024 (10/2026)	315.21 (315.21)	162.16	89
1018	Construction of bypass around Lohardaga town of NH-143A in the Sate of Jharkhand under EPC mode. (MoRTH) (618083) (-) (-)	Jharkhand	02/2022 (01/2024)	01/2026 (09/2026)	458.78 (458.78)	2.32	5
1019	Widening to 2-lane with paved shoulder from km 0.00 to 44.00 Kuru-Ghaghra section of NH-143A including re-construction of culverts and bridges. (MoRTH) (618084) (-) (-)	Jharkhand	02/2020 (08/2021)	08/2023 (10/2026)	153.01 (133.67)	100.77	95
1020	Construction of 2- Lane with paved shoulder from km 56.45 Dharampur More to 93.050 Pakur of NH-333A in the State of Jharkhand on EPC mode (MoRTH) (618127) (-) (-)	Jharkhand	03/2023 (11/2025)	05/2027 (05/2027)	255.73 (255.73)	10.06	15

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1021	Widening and Reconstruction to 4-lane/4-lane with service road including structures from Pokharia More at Km 47.600 Ex. Km 50.230 to Govindpur at km 62.949 Ex. Km 65.325 of Nh-419 in the State of Jharkhand on EPC mode. (MoRTH) (618242) (-) (-)	Jharkhand	05/2022 (01/2024)	01/2026 (01/2027)	300.46 (300.46)	94.18	54.54
1022	Construction of Six lane elevated flyover including reconstruction/rehabilitation of existing pavement from Km 426230 to Km 430500 Length 4.27 Km at Nirsa in the Barwa Adda Panagarh section of NH-19 from Km.398.240 to Km.521.120 including Panagarh Bypass in the State of Jharkhand on EPC Mode. (NHAI) (618534) (-) (-)	Jharkhand	01/2025 (02/2026)	08/2028 (08/2028)	470.75 (470.75)	0.93	0
1023	Construction of Six lane elevated flyover including reconstruction/rehabilitation of existing pavement from Km 406100 to Km 411150 Length 5.05 Km at Gobindpur area in the Barwa Adda Panagarh section of NH-19 from Km.398.240 to Km.521.120 including Panagarh Bypass in the State of Jharkhand on EPC Mode. (NHAI) (618535) (-) (-)	Jharkhand	01/2025 (09/2025)	03/2028 (03/2028)	687.77 (442.52)	67.84	19.91
1024	4 Lane of CG/JH Border-Gumla from km 0.000 to km 32.370 of NH-43 in the State of Jhrkhand (NHAI) (618641) (-) (-)	Jharkhand	08/2024 (02/2026)	02/2028 (02/2028)	1325.80 (1325.80)	293.4	9.76
1025	4L of Palma to Gumla from km. 26.00 to km. 89.170 of NH-23 (NHAI) (618642) (-) (-)	Jharkhand	03/2020 (04/2022)	03/2024 (09/2026)	1882.93 (1895.75)	1371.55	99.9
1026	4L of Ormanjhi-Gola section from Km 81.450 to Km 53.600 of NH- 320BPKG-II (NHAI) (618644) (-) (-)	Jharkhand	02/2022 (06/2023)	06/2025 (12/2026)	1214.93 (1462.19)	993.6	86.57
1027	4L of Gola-BokaroJaina More section from Km 53.600 to Km 21.110 of NH-320PKG-1 (NHAI) (618645) (-) (-)	Jharkhand	02/2022 (06/2023)	06/2025 (10/2026)	1007.97 (1030.64)	617.85	78.1
1028	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Donoreshan village to junction with NH-20 in Bongabar village from km 288.600 to km 325.500 Pkg -11 (NHAI) (618729) (-) (-)	Jharkhand	03/2023 (07/2026)	07/2028 (07/2028)	1856.12 (1856.12)	261.78	0
1029	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Deoria village to Donoreshan village from km 253.000 to km 288.600 Pkg -10 (NHAI) (618730) (-) (-)	Jharkhand	03/2023 (05/2026)	05/2028 (05/2028)	1546.27 (1546.27)	183.44	5.65
1030	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Chatra to junction with NH- 100 in Deoria village from km 222.000 to km 253.000 Pkg -9 (NHAI) (618731) (-) (-)	Jharkhand	03/2023 (07/2026)	07/2028 (07/2028)	1418.16 (1418.16)	143.72	0
1031	6L Greenfield Varanasi- Ranchi- Kolkata Highway from junction with NH-20 in Bongabar village to junction with NH-30 in Lepo village from km 325.500 to km 358.500 Pkg -12 (NHAI) (618733) (-) (-)	Jharkhand	03/2023 (07/2026)	07/2028 (07/2028)	1525.52 (1525.52)	218.28	0.1
1032	4L Elevated corridor of Kalimandir-Dimna Chowk-Baliguma Jamshedpur Section of NH-33 New NH-18 from km 241940 to km 251961 Length 10.021 km (NHAI) (618736) (-) (-)	Jharkhand	03/2024 (09/2024)	03/2027 (03/2027)	936.26 (832.20)	328.76	49.5
1033	Grade separated Interchanges at Km. 113.730 junction with Ranchi Hazaribagh Road & Km. 139.225 junction with Ranchi Jamshedpur road on 4L Ranchi Bypass of NH-33 (NHAI) (618737) (-) (-)	Jharkhand	01/2025 (12/2025)	12/2027 (12/2027)	303.53 (5.58)	4.98	0
1034	4L from Km 147.450 Bhogu to Km 196.870 Sankha on NH-75 Sec-III (NHAI) (618830) (-) (-)	Jharkhand	10/2022 (11/2023)	11/2025 (03/2027)	1517.87 (1652.09)	1131.52	76.95
1035	4L from Km 95.400 Udaipura to Km 147.450 Bhogu on NH-75 Sec-II (NHAI) (618831) (-) (-)	Jharkhand	03/2023 (10/2024)	10/2026 (03/2027)	1436.80 (1301.54)	419.62	29.2
1036	4L from Km 55.00 Kuru to Km 95.400 Udaipura on NH-75 Sec-I (NHAI) (618832) (-) (-)	Jharkhand	02/2024 (01/2026)	01/2028 (01/2028)	1274.82 (1274.82)	253.64	11.1
1037	Barhi-Koderma Section of NH31 km 0.00 - km 27.5 (NHAI) (618863) (-) (-)	Jharkhand	02/2017 (11/2019)	08/2024 (08/2026)	662.44 (826.59)	825.2	98.5
1038	4L of NH-80 from km 215.00 to km 260.00 Mirza Chauki to Farkka Pkg-I (NHAI) (618947) (-) (-)	Jharkhand	03/2018 (12/2021)	07/2023 (10/2026)	1504.80 (1508.21)	1038.65	91.83
1039	4L of Basukinath- Deoghar Section of NH-114A (NHAI) (618949) (-) (-)	Jharkhand	09/2022 (12/2023)	12/2025 (08/2026)	1444.94 (1553.76)	781.51	90.53

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1040	Construction of Bypass to NH-114A Connecting NH-333 and NH-133 Deoghar Bypass from design km 0.000 to design Km 49.000 (NHAI) (618950) (-) (-)	Jharkhand	11/2024 (01/2026)	01/2028 (01/2028)	1565.47 (1565.47)	106.04	12
1041	Construction of bypass around Chatra Town on NH-22 old NH-99 in the state of Jharkhand under EPC Mode (MoRTH) (619005) (-) (-)	Jharkhand	03/2023 (01/2026)	01/2028 (01/2028)	235.42 (199.20)	0.86	13
1042	Construction of Elevated corridor from Km. 135.650 to 136.300 on 63, from Km. 249 to Km. 250.050 on old NH-4 and from Km. 192.910 to Km. 193.350 on NH-218 from decongestion of traffic in Ranichennamma circle in Hubli city in the state of Karnataka on EPC basis (MoRTH) (617935) (-) (-)	Karnataka	08/2020 (06/2021)	06/2024 (11/2026)	298.00 (349.49)	232.09	65
1043	Construction of Srinivasapura Bypass from existing Km 453.890 Design Ch. 0000 to existing Km 461.450 Design Ch 10080 on NH-69 in the State of Karnataka Under NH O in EPC mode under Annual Plan 2022-23 NH-69-KNT-2022-23-966 dated 22.11.2022 (MoRTH) (617950) (-) (-)	Karnataka	11/2022 (07/2025)	01/2027 (01/2027)	204.42 (204.42)	9.76	22
1044	Construction of Chintamani Bypass from Design Ch.0000 Existing Ch.428880 to Design Ch.15400 Existing Ch.444010 on NH-69 in the State of Karnataka in EPC Mode under NHO Annual Plan 2022-23. NH-69-KNT-2022-23-989 dated 24.03.2023 (MoRTH) (617951) (-) (-)	Karnataka	03/2023 (01/2026)	07/2027 (07/2027)	314.55 (314.55)	7.02	14
1045	Widening to two lane with paved Shoulders from Km 40.00 to Km 75.00 Existing chainages of Mangalore - Tumkur section of NH-73 in the State of Karnataka on EPC Mode under Annual Plan 2021-22 Job No NH-73-KNT-2021-22-945 (MoRTH) (617955) (-) (-)	Karnataka	03/2022 (03/2023)	03/2025 (12/2026)	718.52 (718.52)	312.83	85
1046	Construction of Major Bridge at Km.180.865 across river Krishna on NH 167 Hagari Jadcherla section (MoRTH) (617989) (-) (-)	Karnataka	03/2019 (05/2019)	11/2021 (04/2027)	157.32 (187.61)	103.33	69
1047	Widening of existing 2 lane to 4 lane with paved shoulder from Designed km 25.15 to km 56.70 Except Km 52.70 to 53.50 of NH-169 Nellisara Camp to Thirthahalli of NH-169 on Shimoga-Mangalore section in the state of Karnataka on EPC mode under Annual plan 2022-23 NH-169-KNT-2022-23-978 dated 08.03.2023 (MoRTH) (617997) (-) (-)	Karnataka	03/2023 (02/2026)	02/2028 (02/2028)	538.71 (538.71)	20.63	6
1048	Widening to existing 2 lane with paved Shoulder to 4 Lane with paved shoulder from design Km 153.00 to 168.27 Mala Gate to Karkala of NH -169 on Shimoga - Mangalore section in the state of Karnataka on EPC mode under Annula Plan 2021-22 Job No. NH-169-KNT-2021-22-949 (MoRTH) (617998) (-) (-)	Karnataka	03/2022 (02/2023)	02/2025 (11/2026)	177.94 (177.94)	115.6	83
1049	Widening to 2LPS from Km 67 to Km 115 on Kadur-Hosadurga section NH 173 in the state of Karnataka NH-173-KNT-2022-23-980 dated 13.03.2023 (MoRTH) (617999) (-) (-)	Karnataka	03/2023 (10/2024)	05/2026 (04/2027)	471.62 (471.62)	91.74	69.54
1050	Widening to 2-Lane with Paved Shoulders from Km 116.800 to 149.070Design Changes on Hosadurga - Holalkere Section of NH-173 in the State of Karnataka on EPC mode under Annual Plan 2021-22 Job no. NH-173-KNT-2021-22-946 (MoRTH) (618000) (-) (-)	Karnataka	03/2022 (10/2022)	02/2024 (06/2026)	170.34 (147.39)	111.33	100
1051	Widening to 2LPS from Km 71.00 to 104.00 Existing chainages Sarjapur to Pattadakallu on Bhanapur to Gaddanakeri section NH-367 in the State of Karnataka under NHO on EPC mode under Annual Plan 2022-23 NH-367-KNT-2022-23-972 dated 08.02.2023 (MoRTH) (618027) (-) (-)	Karnataka	02/2023 (03/2024)	03/2026 (12/2026)	445.62 (445.62)	198.15	90
1052	Construction of Bypass at Kuknoor, Yelburga, Gajendragada of Bhanapur Gaddanakeri section of NH-367 in the State of Karnataka under NHO on EPC mode under Annual Plan 2022-23. NH-367-KNT-2022-23-973 dated 08.02.2023 (MoRTH) (618028) (-) (-)	Karnataka	02/2023 (06/2025)	06/2027 (06/2027)	333.96 (333.96)	63.62	36
1053	Widening to 4 lane from Km. 133.00 to 158.04 design Chainage Km. 130.88 to 155.145 Shirur Cross to Gaddankeri of NH-367 in the State of Karnataka on EPC mode. Job No. NH-367-KNT-2021-22-930 (MoRTH) (618029) (-) (-)	Karnataka	01/2022 (01/2023)	01/2025 (03/2027)	350.69 (312.06)	203.12	83.33
1054	Balance work of Construction of Two/Four lane with paved shoulder from Km 422.000 to 523.600 Chitradurga to Shivamogga of NH-13 in the state of Kanataka on EPC mode. (MoRTH) (618031) (-) (-)	Karnataka	01/2021 (12/2021)	12/2025 (08/2026)	516.96 (516.96)	121.75	98

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1055	Widening to Two Lane with Paved Shoulders from KB Cross to Chunchanahalli ie., Design Ch. 485240 Km Existing Km 494.000 to Design Ch. 523393 Km Existing km 533.152 & From Design Ch. 530393 Existing Km 540.175 to Design Ch. 534476 Existing Km 544.200 at Nelligere of NH-150A on EPC mode under Annual Plan 2022-23 NH-150A-KNT-2022-23-977 dated 08.03.2023 (MoRTH) (618086) (-) (-)	Karnataka	03/2023 (07/2025)	01/2027 (01/2027)	617.28 (617.28)	8.03	48.5
1056	Widening to intermediate/two lane to 2 lane with paved shoulder from Existing chanages Km 112.750 to 142.00 Liingasur to Mudabal cross & from Km. 147.070 to Km. 149.070 Maski city limit of Jewargi Chamrajnagar setion of NH-150A in the state of Karnataka on EPC mode. Job No. NH-150A-KNT-2021-22-951 (MoRTH) (618087) (-) (-)	Karnataka	03/2022 (01/2023)	07/2024 (08/2026)	255.88 (255.88)	185.27	96
1057	Widening to Two Lane with Paved Shoulders from Km 0.00 Design Chainage 0.00 to Km 23.338 Design Chainage 23310 of NH-166E MH/KNT Border- Kanamadi- Bijjargi-Tikota section in the state of Karnataka in EPC Mode under Annual plan 2022-23 NH-166E-KNT-2022-23-974 (MoRTH) (618095) (-) (-)	Karnataka	02/2023 (09/2024)	03/2026 (03/2027)	196.05 (196.05)	72.94	75
1058	Widening to 4 lane from Km 51.60 to 76.20 Hebri to Parkala and from Km 85.20 to 88.90 Karavali junction to Malpe of Thirthahalli-Udupi-Malpe Section of NH-169A in the State of Karnataka on EPC Mode under Annual plan 2021-22 Job No. NH-169A-KNT-2021-22-927 (MoRTH) (618109) (-) (-)	Karnataka	01/2022 (12/2022)	12/2024 (11/2026)	355.72 (355.72)	217.46	88.33
1059	Widening to 2 Lane with Paved Shoulders from design Km 103.200 Existing Km 103.200 to design Km 116.700 Existing Km 118.470 on AP/KNT Border to Sira Section of NH-544E in the State of Karnataka on EPC mode under Annual plan 2022-23 (MoRTH) (618147) (-) (-)	Karnataka	01/2023 (03/2024)	09/2025 (08/2026)	166.58 (166.58)	46.69	65
1060	Widening to 4LPS of NH-548B from Km 80.000 Near Murgundi to Km 140.200 Near Chikkodi excluding length from Km 118.450 to Km 128.450 in the State of Karnataka under NH O on EPC Mode under Annual Plan 2022-23 - Package 1 NH-548B-KNT-2022-23-979 dated 09.03.2023 (MoRTH) (618148) (-) (-)	Karnataka	03/2023 (04/2026)	04/2028 (04/2028)	785.79 (785.79)	6.15	0
1061	Widening to two lane with paved shoulders from Km 0.00 to 102.310 Design Chainage of NH-548B Murum-Maharashtra Border in the State of Karnataka (MoRTH) (618149) (-) (-)	Karnataka	02/2023 (01/2025)	01/2027 (01/2027)	957.09 (957.09)	288.23	60.21
1062	Widening to 4LPS of NH-548B from Km 118.450 Near Shirguppi to Km 128.450 Near Ankali in the State of Karnataka under NH O on EPC Mode Under Annual Plan 2022-23 NH-548B-KNT-2022-23-982 (MoRTH) (618151) (-) (-)	Karnataka	03/2023 (05/2026)	05/2029 (-)	1084.29 (1084.29)	1.71	0
1063	Construction of 2 Lane with paved shoulder from km 55.6 to km 90.7 existing chainages of NH-766C complete Realignment of 13.76 km with 2 major Bridges across Sharavathi Backwaters on EPC mode under Annual Plan 2022-23 in the state of Karnataka NH-766C-KNT-2022-23 dated 14.10.2022 (MoRTH) (618184) (-) (-)	Karnataka	01/2023 (02/2024)	02/2026 (12/2027)	313.56 (313.56)	160.08	65
1064	Widening to 2LPS from Km 0.000 to 37.850 Except Ex. Km 24.45 to 27.20 of NH-766c Byndoor-Ranebennur Section in the state of Karnataka on EPC Mode under Annual Plan 2022-23 NH-766C-KNT-2022-23-969 dated 30.12.2022 (MoRTH) (618185) (-) (-)	Karnataka	12/2022 (08/2025)	08/2027 (08/2027)	394.95 (394.95)	15.68	12
1065	Widening to two lane with paved shoulder of NH-73New spur road Ujire - Dharmasthala - Periyashanthi in the State of Karnataka under NHO on HAM Mode Job No. NH-73Spur-KNT-2023-24-996 (MoRTH) (618189) (-) (-)	Karnataka	01/2024 (11/2025)	11/2027 (11/2027)	613.65 (613.65)	66.04	25.18
1066	4/6L of Bangalore - Pune Section of bypass connecting Dharwad - Hubli from km. 403.80 to km. 433.20 (NHAI) (618517) (-) (-)	Karnataka	12/2021 (03/2023)	09/2025 (05/2027)	1135.39 (763.36)	744.42	83.19
1067	Davanagere - Haveri of NH-48 Old NH-4 from km. 260.00 to km. 338.923 (NHAI) (618518) (-) (-)	Karnataka	01/2017 (01/2018)	07/2020 (12/2026)	1454.67 (1805.84)	1273.5	98.87
1068	4L of km 0.00 to km 42.00 of Dobbaspeta to Doddaballapura Bypass section of NH-648 old NH-207] [Bangalore Ring Road Pkg 1] (NHAI) (618520) (-) (-)	Karnataka	08/2020 (04/2021)	04/2023 (09/2026)	1438.74 (1786.57)	1294.84	99.2
1069	6L of MH/KN Border Nimbali Village to KN/TS Border Singnodi Village from Km. 26.000 to Km. 97.000 in Gulbarga of NH-150C Pkg-II (NHAI) (618630) (-) (-)	Karnataka	02/2022 (12/2022)	06/2025 (12/2026)	2355.56 (1923.30)	1012.1	81.35

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1070	4 Lane with PS from Des. Ch 228.500 to Des. Ch. 273.400 of Belgaum-Hungund-Raichur Section of NH 748 A Package-6 (NHAI) (618649) (-) (-)	Karnataka	03/2023 (11/2024)	11/2026 (06/2027)	1246.15 (1012.78)	399.31	53.8
1071	4 Lane with PS from Des. Ch 89.900 to Des. Ch. 136.100 of Belgaum-Hungund-Raichur Section of NH-748A Package-3 (NHAI) (618650) (-) (-)	Karnataka	01/2024 (04/2025)	04/2027 (02/2028)	1363.90 (1219.62)	306.09	24.5
1072	4 Lane with PS from Des. Ch 43.800 to Des. Ch. 89.900 of Belgaum-Hungund-Raichur Section of NH-748A Package-2 (NHAI) (618651) (-) (-)	Karnataka	02/2024 (03/2025)	02/2027 (07/2027)	1427.88 (1293.94)	594.55	58.7
1073	4LPS Access Controlled Highway of Bellary Bypass Balance work from Ch. 254750 to Ch. 266837 and construction of 4LPS from Ch. 277.690 to Ch. 278.690 at D. Hirehal Village Balance work of NH 150A of Bellary Byrapura Section (NHAI) (618697) (-) (-)	Karnataka	02/2024 (08/2024)	07/2026 (10/2027)	626.01 (284.05)	113.26	38.97
1074	4L of Addahole Near Gundya to Bantwal Cross section Pkg-02 from Design Km 270.270 to Design km 318.55 including flyover at Kalladka Town including approaches from Km. 311.57 to Km. 313.67 of NH-75 Old NH-48 (NHAI) (618702) (-) (-)	Karnataka	12/2020 (11/2021)	11/2023 (04/2027)	1660.19 (1318.24)	1452	94.21
1075	Bangalore-Nidagatta Pkg. I (NHAI) (618706) (-) (-)	Karnataka	02/2018 (05/2019)	11/2021 (09/2026)	3496.01 (4087.42)	4315.21	99.19
1076	Additional works under BM1 to ensure road safety under 6L of Bengaluru Mysuru Access control with close toll from Km.17.300 to Km.136.300 of NH-275 (NHAI) (618707) (-) (-)	Karnataka	11/2024 (01/2026)	01/2028 (05/2028)	738.37 (738.37)	32.83	12.67
1077	4L of Left-Over Works of Hospet-Bellary -Karnataka/AP border from Km.280.080 Dec.Ch. to Km.375450Des.Ch. of NH-63 New-67 (NHAI) (618709) (-) (-)	Karnataka	03/2023 (05/2023)	05/2025 (04/2028)	1340.15 (992.60)	929.02	92.51
1078	Belakeri Port to Kumta - Sirsi road from km 0.00 - km 4.265 of Belekeri Port Road Link Rd. and km 4.965 - km 60.00 of SH-69 (NHAI) (618799) (-) (-)	Karnataka	03/2018 (12/2020)	12/2022 (11/2026)	440.16 (456.79)	471.12	95.23
1079	4L PS from near Hemmige Village Periyapatna - Hassan Road Jn. to near Hunsur - KR Nagar Jn section from Km. 144.900 to Km. 169.000 of NH-275 Pkg. III (NHAI) (618870) (-) (-)	Karnataka	02/2023 (04/2025)	04/2027 (01/2028)	883.62 (1726.65)	447.11	27.8
1080	4L PS from Near Guddehosur to Start of Kushalnagara Bypass to near Hemmige Village Periyapatna - Hassan Road Jn from Km. 122.200 to Km. 144.900 of NH-275 Pkg. II (NHAI) (618871) (-) (-)	Karnataka	02/2023 (12/2025)	12/2027 (05/2028)	909.86 (896.42)	325.85	14.53
1081	4L PS from near Hunsur - KR Nagar Junction to near Yalachahalli village KR Nagara - Yelawala Road Junction ffrom Km 169.000 to Km 195.550 of NH-275 Pkg-IV (NHAI) (618872) (-) (-)	Karnataka	02/2023 (04/2025)	04/2027 (03/2028)	1062.76 (952.03)	272.55	19.58
1082	4L PS from near Yalachahalli village KR Nagara - Yelawala Road junction to Srirangapatna Bypass Near Paschima Vahini from km 195.550 to Km 214.535 of NH-275 Pkg-V (NHAI) (618873) (-) (-)	Karnataka	01/2023 (04/2025)	04/2027 (04/2028)	1272.71 (1203.20)	462.59	17.36
1083	4L of Bettadahalli- Shivamogga section from Km.170.415 to km. 226.750 of NH-206 Tumkur- Shivamogga Pkg-IV (NHAI) (618887) (-) (-)	Karnataka	01/2019 (10/2021)	10/2023 (03/2027)	2082.98 (2545.11)	1645.24	84.25
1084	4L of Sannur to Bikarnakatte section from Km 691.350 to Km 736.362 of NH-169 Karkala - Mangalore Package-III (NHAI) (618896) (-) (-)	Karnataka	03/2021 (10/2022)	10/2024 (04/2027)	1386.41 (2038.71)	1251.68	76.1
1085	4L Expressway from Km 26.400 to km 53.500 of Malur to Bangarpet section of Bangalore-Chennai Expressway Phase-I Package-II (NHAI) (619065) (-) (-)	Karnataka	12/2020 (09/2021)	09/2023 (09/2026)	1745.00 (1729.63)	1103.49	99.8
1086	Tumkur - Nelamangala 6L (NHAI) (619071) (-) (-)	Karnataka	03/2021 (08/2022)	08/2025 (03/2027)	2032.15 (1664.20)	1086.24	61.36
1087	Bangalore/TN border to Hoskote (NHAI) (619072) (-) (-)	Karnataka	02/2022 (02/2023)	02/2025 (11/2026)	1181.68 (1297.76)	1153.14	94.89

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1088	4L of 42.000 to km 80.00 of Dodaballapur Bypass to Hoskote section of NH-648 Old NH-207 [Bangalore Ring Road Pkg 2] (NHAI) (619073) (-) (-)	Karnataka	02/2020 (02/2021)	02/2023 (09/2026)	1317.74 (1846.52)	1367.2	99.2
1089	Goa / Karnataka Km.93.700 to Kundapur Km.283.30 (NHAI) (619096) (-) (-)	Karnataka	07/2012 (03/2014)	08/2016 (10/2026)	1644.92 (1990.99)	1849.51	97.94
1090	4 Lane with PS from Des. Ch 182.300 to Des. Ch. 228.500 of Belgaum-Hungund-Raichur Section of NH 748 A Package-5 (NHAI) (619106) (-) (-)	Karnataka	03/2023 (11/2024)	11/2026 (08/2027)	1141.88 (868.65)	255.41	40.63
1091	4 Lane with PS from Des. Ch 136.100 to Des. Ch. 182.300 of Belgaum-Hungund-Raichur Section of NH-748A Package-4 (NHAI) (619107) (-) (-)	Karnataka	02/2024 (09/2025)	09/2027 (04/2028)	1311.41 (1123.35)	227.73	15
1092	4 Lane with PS from Des. Ch 0.000 to Des. Ch. 43.800 of Belgaum-Hungund-Raichur Section of NH-748A Package-1 (NHAI) (619108) (-) (-)	Karnataka	02/2024 (06/2025)	06/2027 (10/2027)	1452.43 (1256.55)	490.31	40.21
1093	Hassan km 184.912 to Maranahally km 230.060 of NH - 75 in Karnataka (NHAI) (619117) (-) (-)	Karnataka	12/2015 (03/2017)	03/2019 (08/2026)	1021.57 (1091.40)	1068.91	97.8
1094	Nidagatta-Mysore Pkg II (NHAI) (619120) (-) (-)	Karnataka	02/2018 (12/2019)	06/2022 (09/2026)	2919.80 (4113.89)	3715.84	99.19
1095	Yekkambi-Haveri (NHAI) (619138) (-) (-)	Karnataka	09/2021 (03/2022)	03/2024 (02/2028)	294.62 (309.90)	94.8	24.7
1096	BRT Tiger Reserve Boundary Km.287.500 to Bangalore Section Km.458.420 of NH-209 in Karnataka (NHAI) (619150) (-) (-)	Karnataka	04/2016 (08/2017)	08/2019 (09/2026)	2082.69 (2859.93)	2242.71	99.7
1097	Belgaum-Khanapur Pkg I Km 0.000-Km 30.800 of NH-4A (NHAI) (619164) (-) (-)	Karnataka	03/2018 (03/2019)	09/2021 (03/2027)	1214.30 (1195.74)	917.82	75.72
1098	6L of MH/KN Border Nimbal Village to KN/TS Border Singnodi Village from Km. 97.000 to Km. 162.500 in Yadgir of NH-150C Pkg-III (NHAI) (619211) (-) (-)	Karnataka	03/2022 (04/2023)	10/2025 (11/2026)	2104.70 (2065.83)	984.28	73.9
1099	4L of Channarayapatna Bypass and Hassan Bypass with structures in Devihalli - Hassan section (NHAI) (619214) (-) (-)	Karnataka	04/2020 (01/2021)	01/2023 (10/2026)	688.00 (684.54)	600.43	82.34
1100	4L Tumkur-Shimoga Pkg-I from Mallasandra to Karadi village of NH-206 from Km. 12.300 to Km. 65.195 (NHAI) (619218) (-) (-)	Karnataka	02/2018 (10/2019)	10/2021 (08/2026)	1364.14 (1692.12)	1336.55	100
1101	4L of Tumkur-Shimoga Pkg-II from Km 65.195 Karadi to Km 121.900 Banawara of NH-206 (NHAI) (619219) (-) (-)	Karnataka	02/2018 (10/2019)	10/2021 (12/2026)	1505.85 (1989.89)	1298.78	99.98
1102	Tumkur-Shimoga Pkg-III from Km 121.900 Banawara to Km 170.415 Bettadahalli of Old NH-206 (NHAI) (619220) (-) (-)	Karnataka	02/2018 (03/2021)	03/2023 (12/2026)	1444.50 (1834.81)	872.97	98
1103	Widening to 2 Lanes with paved shoulders from Km.87/000 to 133/720 Nattukal to Thanau Jn. in Palakkad of NH-966 Old NH-213 on EPC mode Basis under NHO Annual Plan 2016-17 in the state of Kerala (MoRTH) (618070) (-) (-)	Kerala	02/2017 (08/2017)	08/2019 (06/2026)	294.28 (315.63)	0	98
1104	6L of Chengala - Neeleshwaram from km. 56.200 to km. 93.468 (NHAI) (618595) (-) (-)	Kerala	06/2020 (10/2021)	04/2024 (03/2027)	1746.45 (2538.06)	1447.45	90.82
1105	6L of Taliparamba to Muzhappilangad from Km 134.650 to Km 170.6 of NH-66 (NHAI) (618596) (-) (-)	Kerala	08/2020 (11/2021)	05/2024 (01/2028)	2714.60 (3557.65)	2020.35	83.7
1106	6L of Azhiyur-Vengalam from km. 189.200 to km. 230.400 of NH-66 (NHAI) (618597) (-) (-)	Kerala	10/2020 (10/2021)	07/2024 (03/2028)	3205.77 (3898.46)	2406.73	60.07
1107	6L Minor Bridge Paloli Palam at km. 203.160 & Major Bridge Morad at km. 204.895 and allied works (NHAI) (618598) (-) (-)	Kerala	03/2020 (12/2020)	06/2022 (09/2026)	210.00 (216.94)	190.46	100

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1108	6L of Ramanatukkara Junction to start of Valanchery bypass section of NH-66 (NHAI) (618599) (-) (-)	Kerala	01/2021 (01/2022)	07/2024 (08/2026)	4919.46 (4919.46)	3765.27	100
1109	6L of Valanchery bypass to Kappirikkad of NH 66 from km. 298500 to km 335850 (NHAI) (618600) (-) (-)	Kerala	02/2021 (01/2022)	07/2024 (08/2026)	4023.94 (4023.94)	2592.92	100
1110	6L of Kappirikkad to Thalikulam section from km 335.85 to km 369.015 of NH - 66 old NH-17 (NHAI) (618601) (-) (-)	Kerala	06/2021 (09/2022)	01/2025 (06/2027)	4225.59 (4225.59)	3345.3	95.27
1111	6L of Thalikulam to Kodugallur section from km 369.015 to km 397.850 of NH - 66 old NH-17 (NHAI) (618602) (-) (-)	Kerala	06/2021 (09/2022)	02/2025 (06/2027)	4302.06 (4302.06)	3312.68	95.05
1112	6L of Kodugallur to Edapppally section from km 397.750 to km 423.780 of NH - 66 old NH-17 (NHAI) (618603) (-) (-)	Kerala	11/2021 (10/2022)	04/2025 (05/2027)	3465.82 (3606.20)	2178.55	71.11
1113	Aroor-Thuravoor Thekku (NHAI) (618604) (-) (-)	Kerala	08/2022 (02/2023)	01/2026 (12/2026)	2429.52 (2382.83)	1802.58	91.63
1114	Thuravoor Thekku-Paravoor (NHAI) (618605) (-) (-)	Kerala	09/2021 (03/2022)	09/2024 (05/2027)	2878.97 (2638.67)	2514.83	81.49
1115	Paravoor-Kottankulangara (NHAI) (618606) (-) (-)	Kerala	12/2021 (08/2022)	02/2025 (03/2027)	3273.61 (3200.24)	2858.55	71.2
1116	Kottankulangara- Start of Kollam Bypass (NHAI) (618607) (-) (-)	Kerala	06/2021 (04/2022)	10/2024 (03/2027)	2842.14 (3680.49)	2373.2	73.89
1117	Widening/Development of Existing NH-85 from Km 0.000 to Km 124.636 section to 2L/LPS section in the state of Kerala on EPC Mode under Bharatmala Pariyojana (NHAI) (618708) (-) (-)	Kerala	09/2022 (06/2023)	06/2025 (03/2027)	1187.47 (1265.47)	782.54	81.98
1118	Kozhikode Bypass Calicut Bypass Vengalam Jn. to Ramanattukara Jn. (NHAI) (619098) (-) (-)	Kerala	02/2018 (02/2021)	02/2023 (08/2026)	1424.77 (2139.18)	1066.67	98.75
1119	6L of Perole Nileshtar town to Taliparamba from Km 94.248 to Km 134.650 of NH-66 (NHAI) (619206) (-) (-)	Kerala	06/2020 (10/2021)	01/2024 (03/2027)	3041.65 (3867.66)	2526.45	86.65
1120	Start of Kollam Bypass - Kadambattukonam (NHAI) (619207) (-) (-)	Kerala	06/2021 (10/2022)	03/2025 (06/2027)	2641.37 (3309.06)	1990.71	81.8
1121	Kadambattukonam-Kazhakuttom (NHAI) (619208) (-) (-)	Kerala	12/2021 (07/2022)	01/2025 (05/2027)	3635.64 (3526.33)	2124.13	44.34
1122	Kargil Zanskar Road (NHIDCL) (618408) (-) (-)	Ladakh	03/2021 (07/2021)	01/2023 (08/2026)	398.37 (398.37)	337.19	97.1
1123	Widening & Up-gradation to 2 lane with Paved shoulder of NH-301 Kargil- Zanskar Road from Design km 57.000 Ex. Km. 57.905 to Km 87.000 Ex. Km. 88.2491 of 30.000 Km length Pkg-III (NHIDCL) (618409) (-) (-)	Ladakh	03/2021 (07/2021)	01/2023 (08/2026)	381.01 (381.01)	313.34	91.01
1124	Widening & Up-gradation to 2 lane with paved shoulder of NH-301 Kargil- Zanskar Road from Design Km .30.040 Ex. Km. 30.000 to Design Km 57.000 Ex. Km. 57.905 of 26.960 Km length Pkg-II (NHIDCL) (618410) (-) (-)	Ladakh	03/2021 (07/2021)	01/2023 (10/2026)	404.89 (404.89)	360.06	84.94
1125	Construction of Rewa Bypass to 4-lane with paved shoulder along with service road from Ratahara Chowk to Chorhata Chowk Road section of NH-30 from km 00.000 to 19.200 in the State of Madhya Pradesh on Hybrid Annuity Mode HAM. (MoRTH) (617909) (-) (-)	Madhya Pradesh	03/2024 (02/2025)	02/2027 (02/2027)	648.05 (648.05)	0	50
1126	Rehabilitation and upgradation Umaria to Shahdol section of NH-78 from Existing Km. 68/4 to Km. 142/2 to 2LPS including construction of Birshinghpur and Shahdol Bypass on EPC mode under NHDP-IVA (MoRTH) (617911) (-) (-)	Madhya Pradesh	03/2015 (08/2015)	07/2017 (08/2026)	511.83 (613.16)	0	94.5

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1127	Upgradation and reconstruction of Shahpura-Dindori Section of NH 45 from Km 103.700 Design to Km 164.580 Design including 3 bypasses Total length 60.88km to Two lane with paved shoulder configuration along with One time improvement in 03 nos of bypassed built-up areas in a total length of 12.341 km in the State of Madhya Pradesh on EPC mode (MoRTH) (617914) (-) (-)	Madhya Pradesh	03/2022 (01/2024)	12/2025 (06/2027)	241.23 (250.09)	50.78	41.25
1128	Upgradation & widening of Jharkheda- Berasia - Dholkhedi from design km 0000 to km 87900 Design length 87.90km of NH-346 including 3 nos. bypasses of 13.10 Km in the State of Madhya Pradesh under EPC mode. (MoRTH) (618019) (-) (-)	Madhya Pradesh	03/2022 (05/2023)	05/2025 (09/2026)	365.21 (365.21)	200.67	91
1129	Rehabilitation & Upgradation of KurwaiMungaoliChanderi Road section of NH-346, from Design Chainge 0.000 to 81.300 Km Total length 83.1 km to Two lane with paved shoulder configuration along with One time improvement in 07 nos of bypassed built-up areas in a total length of 22.615 km in the state of Madhya Pradesh on EPC mode. (MoRTH) (618020) (-) (-)	Madhya Pradesh	03/2022 (02/2023)	02/2025 (12/2026)	386.49 (386.49)	164.84	67.57
1130	Up-gradation of Pichhore- Dinara section of NH-346 from Km 292.750 to 334.550 to two lane with paved shoulders in the state of Madhya Pradesh on EPC mode (MoRTH) (618021) (-) (-)	Madhya Pradesh	02/2024 (12/2025)	06/2027 (06/2027)	425.97 (425.97)	0	36.85
1131	Rehabilitation & Upgradation of existing intermediate lane to two Lane with paved shoulder from km. 0.600 Gulganj bypass on NH-34 to km. 43.00 Barna River length 42.400 km. on Gulganj-Amanganj-Pawai-Katni NH43 Extn. in the state of Madhya Pradesh on EPCmode. (MoRTH) (618035) (-) (-)	Madhya Pradesh	03/2023 (11/2024)	05/2026 (12/2026)	275.40 (275.40)	0	60.14
1132	Upgradation and reconstruction of existing intermediate lane to two Lane with paved shoulder configuration from km. 43.00 Barna River to km. 77.00 ken river length 34.00 km. on Gulganj-Amanganj-Pawai-Katni NH43 Extn. along with One time improvement in 01 no. of bypassed built-up area in a total length of 1.585 km in the state of Madhya Pradesh on EPCmode. (MoRTH) (618036) (-) (-)	Madhya Pradesh	03/2023 (11/2024)	11/2026 (03/2027)	315.55 (315.55)	0	43
1133	Upgradation and reconstruction of Dindori - Mandla Section of NH 543 from Km 77100 Design to Km 170580 Design Total length 93.48km to Two lane with paved shoulder configuration along with One time improvement in 04 nos of bypassed built-up areas in a total length of 7.23 km in the state of Madhya Pradesh on EPC mode (MoRTH) (618043) (-) (-)	Madhya Pradesh	03/2022 (01/2024)	07/2026 (09/2026)	492.12 (523.71)	0	88
1134	Upgradation of Shahdol- Sagartola Section of NH 543 from km 0000 to km 69400 to 2 lane with paved shoulders under Hybrid Annuity Mode HAM in the State of Madhya Pradesh (MoRTH) (618044) (-) (-)	Madhya Pradesh	02/2024 (03/2026)	03/2028 (-)	851.40 (851.40)	0	0
1135	Construction of Kaithi-Padaria Kala bypass, Patna-Tamoli bypass, Jaso bypass and Nagod bypass total length 15.44 Km to 2-lane with paved shoulders flexible pavement on NH-943 in the State of Madhya Pradesh on EPC Mode. (MoRTH) (618068) (-) (-)	Madhya Pradesh	03/2022 (10/2023)	10/2025 (12/2026)	158.36 (158.36)	36.36	62.8
1136	Upgradation of Nasrullagani-Rehti-Budhni Sction to 2-lane with paved shoulder from Km 0150 to Km 50500 of NH-146B in the state of Madhya Pradesh on EPC mode. (MoRTH) (618085) (-) (-)	Madhya Pradesh	12/2021 (04/2023)	10/2024 (10/2026)	305.12 (293.74)	0	92.33
1137	Construction of Kasrawad bypass, Selani bypass, Khargone bypass & Bistan bypass Total length. 31.950 km Section of NH-347 C to Two lane with paved shoulder configuration in the State of Madhya Pradesh on EPC mode. (MoRTH) (618129) (-) (-)	Madhya Pradesh	03/2023 (12/2024)	12/2026 (12/2026)	467.93 (467.93)	167.65	99.15
1138	Construction of Morena bypass, Ambah bypass & Porsa bypass Totat length 27.16 km Section of NH-552 Ext. to Two lane with paved shoulder configuration in the state of Madhya Pradesh on EPC mode (MoRTH) (618156) (-) (-)	Madhya Pradesh	02/2023 (10/2024)	10/2026 (10/2026)	492.66 (492.66)	0	73.5
1139	Construction of Ater realignment & Bhind bypass Total length. 21.50 km Section of NH-552Extn. to Two lane with paved shoulder configuration in the State of Madhya Pradesh on EPC mode. (MoRTH) (618157) (-) (-)	Madhya Pradesh	03/2023 (12/2024)	06/2026 (12/2026)	348.06 (348.06)	79.84	79
1140	Upgradation of Goras to Shyampur Road section of NH-552 Ext., from Design Chainge 48.400 to 111.800 Km Total length 63.40 km to two lane with paved shoulder configuration along with One time improvement of 8.91 km in the state of Madhya Pradesh on EPC mode (MoRTH) (618158) (-) (-)	Madhya Pradesh	03/2023 (12/2024)	12/2026 (12/2026)	416.96 (416.96)	0	16.52
1141	Construction of Two lane with paved shoulder configuration of Shujalpur Bypass section of NH-752C from km 33100 Design to km. 42570 Design total design length 10.470 km in the State of Madhya Pradesh on EPC mode. (MoRTH) (618170) (-) (-)	Madhya Pradesh	03/2023 (03/2024)	09/2025 (12/2026)	214.07 (214.07)	38.07	46.33

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1142	Work of Upgradation of Jirapur-Pachore Road including Pachore, Jirapur, Chhapiheda & Khujner Bypasses from 0000 to 58790 Design Length 58.79 Km section of NH-752C to 2LPS in the State of Madhya Pradesh under EPC mode (NHAI) (618171) (-) (-)	Madhya Pradesh	03/2022 (01/2024)	01/2026 (12/2026)	352.69 (352.69)	98.96	57.26
1143	Bypass on Western side of Gwalior City (NHAI) (618619) (-) (-)	Madhya Pradesh	03/2025 (01/2026)	01/2028 (01/2028)	998.95 (998.95)	195.31	0
1144	Additional works 2VUPs, MR-10 junction flyover and underpass in Six lane Indore-Dewas section of NH-52 in the state of Madhya Pradesh on EPC Mode (NHAI) (618620) (-) (-)	Madhya Pradesh	08/2022 (01/2023)	07/2024 (03/2027)	207.77 (211.27)	150.59	79.72
1145	Indore - Edlabad Pkg-II [Tejajinagar to Balwara] (NHAI) (618621) (-) (-)	Madhya Pradesh	03/2022 (01/2023)	01/2025 (10/2026)	1162.80 (1530.82)	824.5	87.3
1146	4L of Indore - Boregaon Pkg-III [Balwara to Dhangaon] from km. 42.260 to km. 82.660 of NH347BG & 753L (NHAI) (618622) (-) (-)	Madhya Pradesh	01/2021 (04/2022)	04/2024 (10/2026)	1001.69 (888.81)	835.15	92.5
1147	4L Boregaon Buzurg to Shahpur Pkg I of Boregaon Buzurg to Muktainagar of NH 753L (NHAI) (618623) (-) (-)	Madhya Pradesh	11/2022 (02/2024)	01/2026 (10/2026)	1504.37 (1132.34)	556.86	90.1
1148	4L Greenfield Rudhi to Deshgaon Pkg V of Betul-Khandwa/Deshgaon (NHAI) (618654) (-) (-)	Madhya Pradesh	11/2022 (10/2023)	10/2025 (08/2027)	521.21 (469.68)	199.48	63.79
1149	2L PS of Roshni to Ashapur Section of NH-347B from Design KM Ch. 89.900 to 114.000 KM Package III of Betul Khandwa (NHAI) (618655) (-) (-)	Madhya Pradesh	03/2024 (08/2024)	08/2026 (08/2026)	200.99 (120.75)	126.72	98.85
1150	4L from km 0.000 to 42.040 Bhopal Ratnaigiri Tiraha to Vidisha Morikodi (NHAI) (618661) (-) (-)	Madhya Pradesh	10/2024 (11/2025)	11/2027 (11/2027)	1032.30 (1038.18)	179.87	20.23
1151	4L Vidisha Gyarpur section of NH-146 from Design Chainage km 59475 existing chainage km 81240 to Design Chainage km 88361 existing chainage km 110.315 (NHAI) (618662) (-) (-)	Madhya Pradesh	10/2024 (03/2026)	03/2028 (03/2028)	980.20 (980.20)	113.09	12.25
1152	i 4L Vidisha to Hinotiya from km 0.000 to Km 27.000 Vidisha Mehulwa-Talbehat Pkg-I Section of NH- 346 and ii 4L Vidisha to Morikori from Km 39.000 to 59.476 section of NH-146 (NHAI) (618663) (-) (-)	Madhya Pradesh	09/2022 (12/2023)	12/2025 (12/2026)	1003.87 (941.12)	434.04	90.04
1153	Berkhedi to Godpehra on NH-44 Sagar link road (NHAI) (618664) (-) (-)	Madhya Pradesh	02/2022 (11/2022)	11/2024 (12/2026)	524.84 (471.31)	385.98	93.05
1154	4- Laning of Mohari to Satai Ghat section NH-934 from Km 50300 to Km 89875 Total length 39.575 km Package-2 in the State of Madhya Pradesh on EPC Mode (NHAI) (618666) (-) (-)	Madhya Pradesh	08/2022 (08/2024)	08/2026 (08/2026)	710.92 (539.08)	518.99	99.5
1155	4L of near Satai Ghat to Chowka section of NH-34 from D. Ch. 89.875 to D. Ch. 145.000 Package-3 (NHAI) (618667) (-) (-)	Madhya Pradesh	10/2024 (10/2025)	10/2027 (10/2027)	1005.59 (882.21)	193.4	38.26
1156	4-lanning of Rahatgarh to Berkhedi section of NH-146 from Design Ch 124470 to Ch. 134.549 (NHAI) (618671) (-) (-)	Madhya Pradesh	03/2025 (12/2025)	12/2027 (12/2027)	618.33 (342.69)	53.19	14.6
1157	4-lanning of Gyarpur to Rahatgarh section of NH-146 from Design Ch. 88361 to Ch 124470 in the state of MP on HAM mode (NHAI) (618672) (-) (-)	Madhya Pradesh	10/2024 (11/2025)	11/2027 (11/2027)	903.44 (592.44)	169.82	35.25
1158	Outer Ring Road of Jabalpur Town from Manegaon to NH-45 Pkg-2 (NHAI) (618684) (-) (-)	Madhya Pradesh	11/2022 (03/2024)	03/2026 (03/2027)	917.26 (786.47)	520.38	78.75
1159	Outer Ring Road of Jabalpur Town from NH45 to Kushner Pkg-3 (NHAI) (618685) (-) (-)	Madhya Pradesh	09/2022 (03/2024)	03/2026 (12/2026)	911.24 (773.23)	552.62	79.8
1160	Outer Ring Road of Jabalpur Town from Kushner to Amjhar Road including Airport Connectivity Pkg-IV (NHAI) (618686) (-) (-)	Madhya Pradesh	08/2022 (03/2024)	03/2026 (11/2026)	612.94 (509.82)	363.91	79.63
1161	Outer Ring Road of Jabalpur Town from Barela to Manegaon Pkg-1 (NHAI) (618687) (-) (-)	Madhya Pradesh	09/2022 (03/2023)	03/2025 (08/2026)	652.33 (651.88)	500.97	89.72

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1162	Outer Ring Road of Jabalpur Town from Amjhar Road including Airport Connectivity to barela Pkg-V (NHAI) (618688) (-) (-)	Madhya Pradesh	10/2024 (10/2025)	10/2027 (10/2027)	794.70 (539.90)	105.34	32.38
1163	Indore - Harda Pkg-I [Indore to Raghav Garh from km. 0.25 to km. 26.903] (NHAI) (618694) (-) (-)	Madhya Pradesh	01/2022 (11/2022)	10/2024 (08/2026)	1011.29 (813.03)	688.03	96.09
1164	4L of Chandesara to Khedakhajuriya from Km. 0.000 to - 750 & Km 0.000 to km 41.400 of NH-148NG Pkg-I (NHAI) (618735) (-) (-)	Madhya Pradesh	12/2021 (09/2022)	05/2024 (09/2026)	909.84 (976.55)	587.81	99
1165	2L PS of Hinotiya-Mehulwa section of NH-346 from Km. 27.000 to Km 75.700 Vidisha Mehulwa-Talbehat Pkg-II Section of NH- 346 (NHAI) (618751) (-) (-)	Madhya Pradesh	10/2022 (09/2023)	09/2025 (03/2027)	581.65 (592.71)	273.7	69.04
1166	Itarsi Km. 63.000 to Betul Km. 137.000 of NH-69 in Madhya Pradesh (NHAI) (618762) (-) (-)	Madhya Pradesh	08/2017 (02/2018)	02/2020 (08/2026)	950.27 (788.33)	663.67	100
1167	Balance works of 4 lane divided carriageway of Missing Link section of NH-39 Rewa Bypass from junction with NH 30 near Bela to Junction with MPRDC ring road near Silpara on SH 9 design length 13.100 km on EPC Mode under Bharatmala Pariyojana in the State of Madhya Pradesh (NHAI) (618784) (-) (-)	Madhya Pradesh	08/2023 (04/2024)	04/2026 (01/2027)	355.36 (355.36)	253.13	84.44
1168	Construction of 6 lane Indore western bypass from km 0000 to Km 34000 Pkg -I in the State of Madhya Pradesh on Hybrid Annuity Mode under NHO (NHAI) (618932) (-) (-)	Madhya Pradesh	02/2024 (01/2026)	12/2027 (12/2027)	1534.70 (1472.68)	657.89	27.6
1169	Construction of 6 lane Indore western bypass from km 34000 to Km 64000 Pkg-II in the state of Madhya Pradesh on Hybrid Annuity Mode under NHO (NHAI) (618933) (-) (-)	Madhya Pradesh	03/2024 (02/2026)	02/2028 (02/2028)	1430.56 (1430.56)	662.93	17.5
1170	4L of Budhni to Shahganj Bypass End Package-III of NH-146B from Km. 73.750 to Km. 102.000 (NHAI) (618962) (-) (-)	Madhya Pradesh	03/2024 (08/2025)	08/2027 (08/2027)	1102.97 (770.21)	196.68	28.28
1171	Construction work of 4-laning of Shahganj bypass end to Badi Package-IV of NH-146B from design km 102.000 to design km 142.357 Design length 40.357 km (NHAI) (618963) (-) (-)	Madhya Pradesh	02/2024 (03/2025)	03/2027 (03/2027)	784.14 (836.64)	318.16	52.15
1172	4 Laning of Sandalpur to Nasrullaganj Pkg-1 section of NH-146B Length 43.2 Km. (NHAI) (618964) (-) (-)	Madhya Pradesh	03/2025 (01/2026)	01/2028 (01/2028)	1425.98 (1425.98)	197.81	11.57
1173	Six laning with both sides Service Road of Ayodhya Bypass from Design Km 0000 near Ashram Tiraha on NH-46 to Km 16439 end at Ratnagiri Tiraha on Nh-146 (NHAI) (618966) (-) (-)	Madhya Pradesh	02/2024 (08/2025)	08/2027 (08/2027)	1123.17 (1103.22)	173.6	21.61
1174	Upgradation of Sarvardewlia to Pal MP/MH Border Road section of NH-347 C from Design Chainge km 81.600 to 137.400 Total length 55.80 km to two lane with paved shoulder configuration along with One time improvement of 1 .95 km in the State of Madhya Pradesh on EPC mode. (MoRTH) (619007) (-) (-)	Madhya Pradesh	03/2023 (01/2026)	01/2028 (-)	461.23 (461.23)	2.77	0
1175	Dhangaon - Borgaon section km 81.000 to km 139.000 [Indore - Edlabad Pkg IV] (NHAI) (619100) (-) (-)	Madhya Pradesh	01/2020 (08/2021)	08/2023 (08/2026)	866.00 (1185.04)	746.57	99.8
1176	Indore - Harda Pkg-II [Raghavgarh to Nanasa from km. 29.30 to km. 92.30] (NHAI) (619114) (-) (-)	Madhya Pradesh	01/2023 (03/2024)	03/2026 (11/2027)	1081.51 (1146.63)	369.46	40.25
1177	Construction of 6 lane flyover from Khapari ROB to Mihan Interchange design chainage km 8760 to 11450 L- 2.69 km and upgradation of existing 4L PS road to 6LPS with service road by flexible pavement design chainage km 11450 to 14500 L- 3.05 [total project length 5.74 km] in section of Nagpur - Hyderabad NH-44 Old NH-7 in Nagpur district in the state of Maharashtra on HAM mode. (MoRTH) (617912) (-) (-)	Maharashtra	03/2024 (10/2025)	10/2027 (10/2027)	619.55 (619.55)	18.35	8.24
1178	Construction of New Four Lane Bypass to Parbhani City Parwa to Asola Km 463/265 to Km 481/180 Design Ch. 19220 to Ch. 34434 Length-15.214 Km section of NH-61 on EPC mode in the State of Maharashtra. (MoRTH) (617932) (-) (-)	Maharashtra	03/2022 (07/2023)	10/2024 (10/2026)	496.64 (496.64)	210.17	70.14
1179	Nasratpur to Barasgaon section of NH-61 2L / 4L PS from Km.514/00 to 558/200 (MoRTH) (617934) (-) (-)	Maharashtra	07/2017 (09/2017)	09/2019 (08/2026)	406.54 (406.54)	528.24	95.84

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1180	Udgir Raavi Degloor Aadampur phata to Sagroli fata (MoRTH) (617937) (-) (-)	Maharashtra	11/2024 (04/2026)	04/2028 (-)	809.77 (809.77)	0.93	12
1181	Rehabilitation And Upgradation to four lane with paved shoulder configuration from km 24350 to km 61875 Jawale - Bargaon Kale of NH-63 in the State of Maharashtra on EPC mode under Annual Plan 2024-25 Total length - 37.525 Km. (MoRTH) (617938) (-) (-)	Maharashtra	12/2024 (09/2025)	03/2027 (03/2027)	574.18 (574.18)	7.54	20
1182	Balance work of NH-66 from design Km 84/00 to Km 87/100 Indapur Bypass and Km 91/600 to Km 99/100 Mangaon Bypass to four lane with paved shoulder in State of Maharashtra under NHO on EPC Mode. (MoRTH) (617945) (-) (-)	Maharashtra	03/2025 (10/2025)	04/2027 (04/2027)	354.21 (354.21)	0	67.16
1183	Kashedi to Parshuram Ghat section of NH-66 from Km 161/600 - Km 205/400 - 4L PS (MoRTH) (617946) (-) (-)	Maharashtra	03/2016 (02/2018)	02/2020 (12/2025)	1142.62 (1142.62)	427.48	97.5
1184	Arawali Kante section of NH-17New NH-66 4L PS from Km.241/300 to 281/300 (MoRTH) (617947) (-) (-)	Maharashtra	03/2016 (11/2017)	11/2019 (03/2026)	1006.99 (1443.09)	0.17	80.06
1185	Kante - Wakad section of NH-66 4L PS from Km.281/300 to 332/200 (MoRTH) (617948) (-) (-)	Maharashtra	03/2016 (11/2017)	11/2019 (11/2025)	1117.75 (2020.56)	375.93	90.14
1186	Kopargaon to Savali Vihir section (MoRTH) (617965) (-) (-)	Maharashtra	06/2022 (01/2023)	07/2024 (08/2026)	195.38 (195.38)	105.76	93.45
1187	Rehabilitation, upgradation & widening of existing highway to 2L/4LPS Rigid Pavement of NH 160 section- Phaltan to Mhaishal near Karnataka Border including Tasgaon Bypass, from existing chainage Km 301/430 to Km 458/415 in the State of Maharashtra- Package-II & Package III combined- starting from existing chainage Km 341/300 to Km 394/130 and design chainage Km 340/250 at Dahiwadi Village to Km 392/950 ending at Vita Village in the State of Maharashtra on EPC Mode. (MoRTH) (617978) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	631.76 (631.76)	213.18	85
1188	Rehabilitation, upgradation & widening of existing highway to 2L/4LPS Rigid Pavement of NH 160 section- Phaltan to Mhaishal near Karnataka Border including Tasgaon Bypass, from existing chainage Km 301/430 to Km 458/415 in the State of Maharashtra. Package-I starting from existing chainage Km 301/430 at Phaltan Village Junction of Phaltan Baramati Road Design Chainage -301/430km & ending at existing chainage Km 341/300 Dahiwadi Village Bus Stop Design chainage Km 340466km in the S (MoRTH) (617979) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (11/2026)	533.76 (533.76)	0	74.29
1189	Rehabilitation/ Upgradation of existing Highway to four lane standards in Kurkheda town from km.413257 to km 410775, Two lane in Shankarpur Gurnuli km 42400 to km 43100 section and Reconstruction of Major Bridge at Ch. 448558 Bhuti Nallah and Ch. 411695 Sati River bridge, Minor Bridge at Ch. 411477 and Ch. 405800 Lendhari Bridge of NH 543 Bhamhapuri-wadsa-kurkheda-korchi-Deori-Amgaon road on EPC mode in the State of Maharashtra (MoRTH) (618042) (-) (-)	Maharashtra	03/2022 (11/2023)	05/2025 (12/2026)	163.86 (163.86)	49.03	50.25
1190	Widening, Reconstruction & Up-gradation to 2 lane with Paved Shoulder/Four Lane configuration for the work of Ahmednagar to Sabalkhed & Ashti to Chinchpur Section of NH-561 from Design km 2915 to km 37728 & Design km 55100 to km 70000 in the State of Maharashtra on EPC mode. Length 49.713 km (MoRTH) (618047) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	657.16 (657.16)	0	88.56
1191	Up-gradation to 2/4 lane with paved shoulder configuration of NH-652 from Tuljapur Naldurg-Akkalkot road Chainage from Km. 00.000 to km 30.982 in the State of Maharashtra on EPC mode. (MoRTH) (618049) (-) (-)	Maharashtra	03/2024 (01/2025)	07/2026 (08/2026)	183.41 (183.41)	64.95	98
1192	Construction of four-lane Concrete Road from Police Headquarter Gondia City to Rawanwadi Village Birsi Airport Junction from design km 0.000 to km 15.781 existing km 39/720 of NH-753 to existing Km 8/400 of NH 543 on sections from Kohmara-Goregaon- Police HeadquarterKaranja - Collector Office Square - Balaghat T Point- Rawanwadi- Rajegaon of NH-753 and NH-543 in Gondia District in the state of Maharashtra. Total Length of the project 15.781 Km. (MoRTH) (618059) (-) (-)	Maharashtra	02/2023 (02/2024)	08/2025 (10/2026)	328.11 (328.11)	111.48	34.15
1193	Strengthening, Widening & Up-gradation of newly declared NH-761 from NH-61Junction-BelheAlkutiDevibhoyareNighojShirur, from Design chainage Km 0.000 to Km 37.970 from Single/Intermediate/2L to 2LPS in the State of Maharashtra on EPC Mode Length 37.970 Km (MoRTH) (618061) (-) (-)	Maharashtra	03/2024 (03/2025)	09/2026 (09/2026)	386.16 (386.16)	57.23	62.5

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1194	Rehabilitation/Upgradation of existing Highway to 2LPS/4 lane of Dhawali to Rajoli from Design Km.149476 to 163476 existing Km.150000 to 164000, Pandhasala to Mohadongri from design Km.170476 to 181476 existing Km.171000 to 182000, Ambeshivni Fata to Bodli from design Km.183476 to 185476 existing Km.184000 to 186000 and Made Tukum to Gadchiroli from design Km.188476 to 189476 existing Km.188000 to 18900 having length 28 km of NH-930 of Dhawali to Gadchroli road in the (MoRTH) (618065) (-) (-)	Maharashtra	03/2022 (03/2024)	09/2025 (03/2027)	316.44 (316.44)	49.78	37.2
1195	Nandurshingote to Kolhar (MoRTH) (618088) (-) (-)	Maharashtra	09/2024 (06/2025)	12/2026 (12/2026)	325.79 (325.79)	32.41	41.93
1196	Rehabilitation & Up-gradation of Mudkhed to Nanded section from Km. 372000 to Km 388400 of NH 161A i.e. Nanded-Bhokar-Himayatnagar-Kinwat-Mahur-Arani Road Design chainage from Km 372000 Mudkhed to Km 387650 Nanded of NH 161A Length 15.65 Km to 2/4Lane with paved shoulders configuration in the State of Maharashtra on EPC mode. (MoRTH) (618089) (-) (-)	Maharashtra	03/2022 (04/2023)	04/2025 (10/2026)	206.54 (206.54)	74.51	65.14
1197	Pen to Khopoli 2LPS (MoRTH) (618094) (-) (-)	Maharashtra	03/2018 (06/2018)	12/2019 (12/2025)	369.39 (369.39)	333.1	86.3
1198	Rehabilitation and Up-gradation to 2 lane road with paved shoulders configuration for the balance work of 13 km length on Helwak-Patan-Karad section Km. 85000 to 133 417 of NH-166E in the state of Maharashtra on EPC mode. (MoRTH) (618096) (-) (-)	Maharashtra	02/2024 (10/2024)	04/2026 (12/2026)	181.45 (181.45)	60.25	87
1199	Guhagar - Rampur - 2L-PS - km 0/00 Guhagar to 26/230 Rampur and 40/00 Mirjoli to 53/600 Sati on NH-166E (MoRTH) (618097) (-) (-)	Maharashtra	01/2017 (06/2017)	06/2019 (08/2025)	407.20 (407.20)	0	91.89
1200	Upgradation of exhistng 2 lane flexible pavement to 2 lane paved shoulders rigid pavement from design chainage Km 66.00 to Design Km 82.440 Start of Kolhapur Municipal corporation near Phulewadi to kale, design length 16.440 Km section on Talere Gaganbawada-Kolhapur road NH 166G in the state of Maharashtra on EPC mode (MoRTH) (618098) (-) (-)	Maharashtra	03/2021 (11/2022)	05/2024 (08/2026)	167.97 (167.97)	0	93.75
1201	Strengthening and Widening of road Sakoli- Wadsa-Armori-Gadchiroli-Ashti- Allapalli - Sironcha National highway NH 353C in Km 262/00 to 321/00 including 16 minor Bridges and 2 Major Bridge Total length 59 Km section from repanpalli to sironcha in Gadchiroli Dist in the State of Maharashtra. (MoRTH) (618133) (-) (-)	Maharashtra	03/2021 (06/2022)	05/2024 (03/2027)	280.57 (280.57)	144.61	67.39
1202	Rehabilitation /Upgradation from Lagam to Alapalli section Desing Km. 199/400 to km 227/400 Length 28.0 Km to 2 lane with Paved Shoulders/ 4 lane configuration section of NH-353 C Sakoli-Wadsa-Armori-Gadchiroli-Ashti-Alapalli Sironcha in Gadchiroli District on EPC mode in the state of Maharashtra. (MoRTH) (618134) (-) (-)	Maharashtra	02/2023 (09/2024)	09/2026 (09/2026)	459.39 (459.39)	132.28	81.42
1203	Rehabilitation and Up-gradation of Jarud - Sirsala section of NH-361F km 59500 to km11500 to Two lane with paved shoulder/ Four Lane in the state of Maharashtra on EPC mode Length 55.5 Km. (MoRTH) (618137) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	540.35 (540.35)	158.38	68.23
1204	Widening, Reconstruction & Up-gradation to 2 lane with Paved Shoulder/Four Lane configuration for the work of Sautada to Shirapur Section of NH-561 from Design km 86300 to km 125589 in the state of Maharashtra on EPC mode. Design length 39.289 km (MoRTH) (618138) (-) (-)	Maharashtra	03/2024 (05/2025)	11/2026 (11/2026)	349.57 (349.57)	0	54.04
1205	Rehabilitation and Up-gradation of Gangakhed Loha section of NH-361F from Km 169/00 to 210/00 to two lane with paved shoulder/ four lane configuration in the state of Maharashtra on EPC mode Length - 41.00 Km. (MoRTH) (618139) (-) (-)	Maharashtra	03/2024 (04/2025)	09/2026 (09/2026)	355.12 (355.12)	0	43.46
1206	Rehabilitation and Up-gradation of i. Deogaon phata to Digras phata Ch. 0/000 to 15/000 & Selu to Borgavhan Ch 20/900 to 35/800 [Length 29.9km] ii. Injegaon Dhamoni to Pohner Phata Ch.58/200 to Ch. 83/700 [Length25.5 km] and iii. Pohner phata to Pathri Design Ch. 42/700 to 58/200 [Length 15.5 km] sections of NH-548B to Two lane with paved shoulder configuartion in the state of Maharashtra on EPC mode Total project length 70.9 Km. (MoRTH) (618150) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	761.83 (761.83)	0	15
1207	Mhaswad to Tembhurni section of NH-548C - 2L PS (MoRTH) (618152) (-) (-)	Maharashtra	01/2017 (08/2017)	07/2019 (08/2026)	488.60 (488.60)	0	96.19
1208	Satara to Mhaswad (MoRTH) (618153) (-) (-)	Maharashtra	01/2017 (08/2017)	08/2019 (08/2026)	653.46 (653.46)	7.34	98.08

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1209	Rehabilitation & upgradation of Jamkhed to Sautada Section of NH548 D from km 195.375 to km 208.774, Length 13.399 Km to 2L PS /4L configuration with rigid pavement in the state of Maharashtra on EPC mode. (MoRTH) (618154) (-) (-)	Maharashtra	03/2022 (01/2023)	07/2024 (06/2026)	157.62 (157.62)	0	68.93
1210	Development/Widening of Talegaon Chakan Shikrapur Nhavara Section of NH-548D from existing chainage km. 54/000 to 82/300 and Design chainage Km. 54/000 to 82/120 Shikrapur to Nhavara Section to 2LPS/4L Configuration on EPC Mode in the State of Maharashtra. (MoRTH) (618155) (-) (-)	Maharashtra	03/2024 (01/2025)	07/2026 (09/2026)	396.17 (396.17)	99.7	76.2
1211	Paithan - Shirur section 2LPS Km 0.0 to 55.00 (MoRTH) (618172) (-) (-)	Maharashtra	03/2017 (06/2017)	06/2019 (10/2026)	341.80 (341.80)	208.25	82
1212	Shirur-Kharda section from 55937 km to 114486 km to 2LPS/4L (MoRTH) (618173) (-) (-)	Maharashtra	02/2017 (06/2017)	06/2019 (08/2026)	381.77 (381.77)	0	83.93
1213	Rehabilitation and Upgradation to two lane with paved shoulder configuration of NH-752G from Sakri to Pimpalner Section Design Ch km 0000 to Ch km 21411 in the state of Maharashtra on EPC Mode. Length 21.411 km. (MoRTH) (618174) (-) (-)	Maharashtra	03/2024 (04/2025)	10/2026 (10/2026)	226.58 (226.58)	0	100
1214	Rehabilitation and upgradation from ch km 50/200 to 56/800 and km 62/600 to 100/403 of Kolde to Visarwadi Near Junction with NH-6 section of NH 752G total length 44.40 to two-lane with paved shoulder / four lanes in the State of Maharashtra on EPC mode. (MoRTH) (618176) (-) (-)	Maharashtra	03/2025 (01/2026)	01/2028 (-)	349.08 (349.08)	39.95	35.45
1215	Pal Phata Phulambri - Khultabad 2LPS (MoRTH) (618177) (-) (-)	Maharashtra	03/2018 (06/2018)	12/2019 (12/2025)	227.19 (227.19)	5.78	95.29
1216	Widening and strengthening of Gangakhed to Kingaon section of NH-752K in Km 38/750 to 72/304 Flexible Pavement Length33.554 km to 2-lane configuration on EPC mode in the State of Maharashtra. (MoRTH) (618178) (-) (-)	Maharashtra	02/2024 (12/2024)	06/2026 (10/2026)	162.67 (162.67)	0	72
1217	Pune raigarh District Border To Mangaon Ch 69000 to 103775 NH-753F (MoRTH) (618180) (-) (-)	Maharashtra	03/2018 (06/2018)	12/2019 (07/2026)	223.46 (223.46)	0	89.08
1218	Rehabilitation and Up-gradation to 2 lane with paved shoulder configuration of Mahud Sangola road NH 965 G 159400 to 161900and 162400 to 183960 Design Chainage from km. 32/300 to km. 34/800 and km. 35/800 to km. 56/860 Rigid Pavement on EPC mode in the State of Maharashtra. (MoRTH) (618188) (-) (-)	Maharashtra	02/2023 (11/2023)	05/2025 (08/2026)	253.78 (253.78)	98.95	100
1219	Balance work of Rehabilitation and Up-gradation to 2-lane road with paved shoulders configuration for NH- 965DD from Pacharal-Mandangad-Mhapral-Rajewadi Upto Junction of NH-66 Ch-22700 to 75100 Km and Ambadave connector Birth place of Dr. Babasaheb Ambedkar Ch-0000 to 7325 Km length Km 59.725 in the state of Maharashtra on EPC mode. Balance Work (MoRTH) (618198) (-) (-)	Maharashtra	03/2018 (01/2022)	01/2024 (08/2026)	388.93 (341.69)	170.26	93.07
1220	Rehabilitation, Upgradation & Widening of existing Highway to Rigid Pavement 2 Lane with Paved Shoulder of NH 965DD from Lonand Shirval-Bhor Mandangad-Pchral Section ShindewadiPhata to Varandah Ghat Dist Border from Km 33/550 to 92/550 in the state of Maharashtra on EPC mode. (MoRTH) (618199) (-) (-)	Maharashtra	02/2023 (07/2024)	07/2026 (10/2026)	723.13 (723.13)	168.06	53.5
1221	Vadodara Mumbai Expressway Phase II - Pkg XIII [Km. 26.582 to Km. 50.700] Shirsad - Masvan (NHAI) (618469) (-) (-)	Maharashtra	06/2020 (02/2022)	02/2024 (08/2026)	3536.90 (4679.54)	1986.56	98.2
1222	Vadodara Mumbai Expressway Phase II - Pkg XIV [Km. 3.000 to Km. 20.200 of Spur] Shirsad - Akloli (NHAI) (618470) (-) (-)	Maharashtra	05/2021 (11/2022)	05/2024 (08/2026)	2058.79 (2324.72)	634.55	98
1223	Vadodara Mumbai Expressway Phase II - Pkg XV [Km. 20.200 to Km. 43.000 of Spur] Akloli - Amne (NHAI) (618471) (-) (-)	Maharashtra	05/2021 (11/2022)	05/2024 (08/2026)	2610.88 (2918.39)	651.95	94.6
1224	Vadodara Mumbai Expressway Phase II - Pkg XVI [Km. 43.000 to Km. 69.800 of Spur] Amne - Bhoj (NHAI) (618472) (-) (-)	Maharashtra	06/2021 (11/2022)	10/2024 (08/2026)	4051.80 (4315.56)	952.69	95.5
1225	Vadodara Mumbai Expressway Phase II - Pkg XVII [Km. 69.800 to Km. 79.783 of Spur] Bhoj - Morbe (NHAI) (618473) (-) (-)	Maharashtra	09/2021 (01/2023)	07/2025 (08/2026)	2208.68 (2463.02)	931.24	90.73

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1226	Upgradation & rehabilitation of Service Roads on both sides in urban areas of Pune City on PuneSatara section of NH48 (NHAI) (618511) (-) (-)	Maharashtra	01/2025 (06/2025)	06/2027 (06/2027)	604.59 (388.78)	66.39	24.08
1227	Tunnel at Khambataki Ghat Section and its approaches from existing Km. 771.730 to existing Km. 782.000 (NHAI) (618512) (-) (-)	Maharashtra	11/2017 (02/2019)	02/2022 (10/2026)	907.03 (816.12)	686.79	89.2
1228	6L of Kagal-Satara section from Km 592.500 to Km 658.000 of NH-48 Pkg-I (NHAI) (618513) (-) (-)	Maharashtra	12/2021 (01/2023)	01/2025 (02/2027)	2111.95 (1435.46)	634.07	51.14
1229	6L of Kagal-Satara section from Km 658.000 to Km 725.000 of NH-48 Pkg-II (NHAI) (618514) (-) (-)	Maharashtra	12/2021 (12/2022)	12/2024 (12/2026)	2330.71 (317.40)	206.68	90.12
1230	4L of Indora Chowk to Pachpaoli and Agrasen Chowk - Ashoka Chowk (NHAI) (618557) (-) (-)	Maharashtra	03/2023 (07/2023)	06/2026 (09/2026)	1038.84 (918.53)	696.83	84
1231	6L of Gonde Km. 439.038 to Pimpri Sado Km. 459.905 section of NH-848 Old NH-3 (NHAI) (618585) (-) (-)	Maharashtra	02/2024 (10/2024)	04/2027 (11/2027)	856.93 (718.84)	160.05	40.5
1232	Improvement and strengthening of existing 2 lane stretch to 2-Lane with PS 1.5m on both sides on Ghoti-Sinnar section of NH-160A using Thin White Topping 200mm thick in the State Of Maharashtra on EPC Mode (NHAI) (618586) (-) (-)	Maharashtra	03/2025 (06/2025)	06/2026 (08/2026)	254.78 (147.64)	115.05	77
1233	4L Mitigation Measure structures on CH/MH Border to Wainganga Bridge Section of NH-6 New NH-53 (NHAI) (618588) (-) (-)	Maharashtra	02/2021 (11/2021)	11/2023 (08/2026)	540.24 (468.92)	464.29	99.79
1234	Balance work of 4L Panvel to Indapur section of NH-66 Old NH- 17 from km 0.000 Panvel to km 42.300 Kasu (NHAI) (618594) (-) (-)	Maharashtra	12/2022 (03/2023)	10/2024 (08/2026)	329.82 (196.87)	184.17	98.66
1235	Four laning from Dive Ghat Km. 220.900 to Hadapsar Km. 234.150 of Mohol Alandi section Pkg VI of NH-965 (NHAI) (618626) (-) (-)	Maharashtra	12/2023 (10/2024)	10/2026 (04/2027)	819.52 (400.00)	141.4	70.01
1236	Construction of 7 Nos of Standalone safety structures/works at different locations on various NHs (NHAI) (618627) (-) (-)	Maharashtra	01/2025 (07/2025)	01/2027 (01/2027)	168.52 (112.03)	26.78	33.35
1237	Strengthening of Existing Alignment of Pandharpur Town Part Bypassed Section of NH 965 from KM 36.230 to KM 44.230 from Chh. Shivaji Maharaj Chowk to Wakhari (NHAI) (618628) (-) (-)	Maharashtra	08/2022 (11/2023)	10/2025 (03/2027)	150.21 (87.59)	76.45	69.25
1238	Loha-Waranga Section of NH-361 from km 187.800 to km 244.369 (NHAI) (618653) (-) (-)	Maharashtra	03/2018 (03/2019)	03/2021 (12/2026)	1236.08 (3466.58)	1503.59	96.22
1239	Bodhre - Dhule (NHAI) (618693) (-) (-)	Maharashtra	02/2021 (01/2022)	07/2024 (08/2026)	1344.78 (1292.70)	837.67	97.69
1240	Upgradation of 2L/4L with Paved Shoulder of Shirwal-Lonand Section from KM 159900 To KM 188025 of NH-965DD Section I and 2L With Paved Shoulder of Lonand-Satara Section from KM 51500 To KM 96246 Of NH-965D Section II in Satara District in the State of Maharashtra on EPC Mode under NHO- (NHAI) (618754) (-) (-)	Maharashtra	03/2025 (06/2025)	06/2027 (06/2027)	538.11 (307.24)	160.77	43.57
1241	Up-gradation to Four Lane with Paved Shoulder configuration of the highway starting from existing km 88.400 Savali Vihir to km 163.400 start of Ahmednagar bypass Design Length 75.000 km section of NH-160 in the State of Maharashtra under Bharatmala Pariyojana on EPC Mode (NHAI) (618766) (-) (-)	Maharashtra	10/2024 (04/2025)	04/2027 (04/2027)	862.00 (617.93)	298.45	48.55
1242	4L of Ratnagiri - Kolhapur section from km 67.140 to km 112.340 of NH-166 Pkg II (NHAI) (618836) (-) (-)	Maharashtra	02/2022 (05/2023)	05/2025 (01/2027)	1985.38 (1798.00)	1239.53	81.57
1243	4L of Ratnagiri - Kolhapur section from km 112.340 to km 145.300 of NH-166 PkgIII (NHAI) (618837) (-) (-)	Maharashtra	02/2022 (05/2023)	05/2025 (01/2027)	1939.23 (1910.41)	1079.17	68.95
1244	4L of Nagpur-Katol Section from Km. 13.00 to Km. 62.900 of NH-353J (NHAI) (618937) (-) (-)	Maharashtra	02/2021 (10/2021)	10/2023 (03/2027)	1166.96 (1432.82)	1181.42	81.54

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1245	Construction of Standalone Flyover cum ROB from Design Ch.66.600 to Design Ch.68.800 in Gadchandur Town on NH-353B (NHAI) (618939) (-) (-)	Maharashtra	02/2025 (07/2025)	07/2027 (07/2027)	191.31 (107.76)	37.07	40.11
1246	Rehabilitation and Up gradation of Charthana Jintur Section of NH 752 I Km 25100 to 47100 to 2 Lane with Paved Shoulder configuration Flexible Pavement in the state of Maharashtra on EPC mode. Reg- Resubmission of Annual Plan Estimate. (MoRTH) (619008) (-) (-)	Maharashtra	03/2025 (01/2026)	07/2027 (07/2026)	157.69 (157.69)	0.01	51
1247	Construction of six lane Flyover at Katraj junction at Km, 3/880 of NH 548-DD Vadgaon - Katraj - Kondhwa - Mantarwadi Chowk - Loni Kalbhor - Theur Phata - Lonikand Road in Pune Dist of the State of Maharashtra. On Engineering Procurement and construction EPC Basis mode L.1.326 Km, (MoRTH) (619042) (-) (-)	Maharashtra	02/2021 (03/2022)	02/2026 (02/2023)	163.51 (163.51)	80.23	83.19
1248	Capacity Augmentation in the stretch of DhulePimpalgaon section of NH60 Km. 261.720 to Km. 380.000 by Construction of Slip/Service Road on either side at various locations total length 30.30 Km LHSRHS and Flyover 2 x 30m at Sawadgaon Phata Km. 310.415 (NHAI) (619043) (-) (-)	Maharashtra	12/2025 (04/2026)	10/2026 (10/2027)	341.63 (341.63)	10.9	5.1
1249	Satara Km 725.000 to Pune Km 865.350 of NH - 4 New NH - 48 in Maharashtra (NHAI) (619069) (-) (-)	Maharashtra	09/2009 (10/2010)	05/2022 (12/2026)	361.72 (425.51)	387.04	99.05
1250	Balance works of 4L Panvel Indapur section of NH66 old NH17 from km 42.300 kasu to km 84.600 Indapur (NHAI) (619095) (-) (-)	Maharashtra	06/2022 (11/2022)	05/2024 (08/2026)	546.44 (472.10)	420.83	96.73
1251	4L of Ratnagiri - Kolhapur section of NH-166 from km 0.000 to km 19.769 and km 31.000 to km 67.140 Pkg I (NHAI) (619149) (-) (-)	Maharashtra	02/2022 (11/2022)	11/2024 (11/2026)	1774.03 (2108.41)	1444.74	97.4
1252	4L of Baramati to Indapur Pkg-II from km. 41.400 to km. 84.550 of NH-965G Saint Tukaram Marg (NHAI) (619163) (-) (-)	Maharashtra	01/2021 (09/2021)	09/2023 (12/2026)	1471.32 (1297.48)	1071	86.2
1253	Vadodara Mumbai Expressway Phase II - Pkg XII [Km. 50.700 to Km. 77.000] Masvan - Ganjad (NHAI) (619198) (-) (-)	Maharashtra	08/2020 (03/2022)	03/2024 (08/2026)	1711.38 (2388.52)	979.42	99.87
1254	Vadape to Thane from km 539.202 to km 563.000 section of NH-3 new NH-848 (NHAI) (619203) (-) (-)	Maharashtra	03/2018 (01/2019)	07/2021 (10/2026)	1252.92 (1371.27)	491.86	87
1255	Capacity Augmentation in the stretch of Pimpri Sado Vadape section of NH848 Km. 460900 to Km. 537000 by Construction of Slip/Service Road on either side at various locations total length 25.140 Km LHSRHS, Flyover 2 x 25m at Borivali Junction Km. 528550 & LVUP 1 x 15m at Sherekarpada Km. 528800 (NHAI) (619204) (-) (-)	Maharashtra	12/2025 (04/2026)	10/2027 (10/2027)	372.03 (372.03)	1.5	1
1256	Dharampuri-Lonand from km. 117.00 to 166.40 Pkg-IV on Mohol-Alandi Section (NHAI) (619210) (-) (-)	Maharashtra	01/2021 (09/2021)	09/2023 (09/2026)	1411.71 (1358.68)	1474.28	97.4
1257	Construction of 6 Lane Elevated corridor from KM 612582 to KM 617540 including construction of Service Roads in Kolhapur City on NH -48 in the State of Maharashtra on EPC mode under NHO (NHAI) (619298) (-) (-)	Maharashtra	02/2026 (06/2026)	06/2029 (06/2029)	1039.00 (1039.00)	0.06	0
1258	Construction of a 6-Lane Elevated Corridor from Km 593766 to Km 596620 Including Construction of Service Roads in Kagal City on NH-48 in the State of Maharashtra on EPC Mode. (NHAI) (619299) (-) (-)	Maharashtra	03/2026 (06/2026)	06/2028 (06/2028)	357.99 (357.99)	0.08	0
1259	Construction of Four Lane Nagpur-Katol section of NH-353J including Mitigation Structures from Design Ch. 37000 to Ch. 45990 Tiger Corridor-I Mitigation Structures from Design Ch. 37000 to Ch. 45990 Tiger Corridor-I in the State of Maharashtra on EPC Mode (NHAI) (619300) (-) (-)	Maharashtra	01/2026 (06/2026)	12/2027 (12/2027)	300.68 (300.68)	0	0
1260	Widening/Improvement of existing 2-Lane road to 4-Lane Divided Highway from Sekmai to Nilakuthi section of Imphal-Kohima Road Design Chainage from Km 297700 to Km 308729 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5B (NHIDCL) (618298) (-) (-)	Manipur	03/2021 (07/2021)	01/2023 (08/2026)	211.70 (211.70)	272.3	94.71
1261	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Daili to Kuraopokpi section of Imphal-Kohima road NH-02 Design Chainage from Km 274610 to Km 287000 in the state of Manipur on EPC mode Pkg-4B (NHIDCL) (618299) (-) (-)	Manipur	09/2020 (12/2024)	06/2026 (01/2027)	268.98 (268.98)	206.28	76.63

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1262	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Taphukuki to Daili section of Imphal-Kohima road NH-02 Design Chainage from Km 262175 to Km 274610 in the state of Manipur on EPC mode Pkg-4A (NHIDCL) (618300) (-) (-)	Manipur	09/2020 (10/2020)	04/2022 (08/2026)	379.39 (379.39)	314.73	91.39
1263	Widening/Improvement of existing 2-lane to 4-Lane Divided Highway from Kuraopokpi to Sekmai section of Imphal-Kohima Road Design Ch. km 287.00 to 297.700 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5A (NHIDCL) (618301) (-) (-)	Manipur	09/2020 (02/2025)	08/2026 (12/2026)	228.97 (228.97)	143.26	48.35
1264	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 16.900 to Km 30.970 of NH-202 in the state of Manipur on EPC mode Package-2 (NHIDCL) (618302) (-) (-)	Manipur	03/2020 (07/2020)	06/2022 (08/2026)	256.04 (256.04)	195	98.12
1265	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 0.000 to Km 16.900 of NH-202 in the state of Manipur on EPC mode Package-1 (NHIDCL) (618303) (-) (-)	Manipur	03/2020 (07/2020)	06/2022 (08/2026)	222.77 (222.77)	140.9	88.96
1266	Widening/Improvement to 2 Lane with earthen shoulder of Jessami to Laynen bridge Nagaland border section of NH-29 of Imphal -Ukhrul - Jessami Economic Corridor from km 0.000 to km 11.009 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-7 (NHIDCL) (618304) (-) (-)	Manipur	03/2023 (12/2024)	06/2026 (02/2027)	164.89 (164.89)	128.92	28.12
1267	Widening/Improvement to 2 lane with earthen shoulder of Marrem Khullen to Jessami section of NH-202 of Imphal - Ukhrul - Jessami Economic Corridor from Design Chainage km 95.700 to km 140.180 in the State of Manipur on EPC mode under Bharatmala Pariyojana under NHO-NE Package-6 (NHIDCL) (618305) (-) (-)	Manipur	03/2023 (12/2024)	12/2026 (08/2027)	554.66 (554.66)	225.73	26.22
1268	Widening/Improvement to 2 lane with earthen shoulder of Choithar to Marrem Khullen section of NH-202 of Imphal Ukhrul Jessami Economic Corridor from Design Chainage km 53.110 to km 95.700 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-5 (NHIDCL) (618306) (-) (-)	Manipur	03/2023 (05/2025)	03/2027 (08/2027)	564.05 (564.05)	173.58	14.5
1269	Widening to 2 lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 169570 Near Nungkao vllage under Tamenglong District to km 205974 near Jiribam Bridge under Jiribam district under NHO-NE PKG-7 (NHIDCL) (618333) (-) (-)	Manipur	01/2023 (12/2023)	12/2025 (12/2026)	760.16 (760.16)	428.13	92.52
1270	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 131.280 to km 169.570 on EPC mode in Manipur under NHO-TSP PKG-6 (NHIDCL) (618334) (-) (-)	Manipur	12/2021 (02/2023)	02/2025 (12/2026)	504.76 (504.76)	325.89	95.2
1271	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from Km 101280 Near Khongsang Village to Km 131280 near Puilon Kambiron Village on EPC Mode in Manipur PKG-5 (NHIDCL) (618335) (-) (-)	Manipur	12/2021 (11/2022)	05/2024 (12/2026)	410.68 (410.68)	382.67	91.02
1272	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 66.110 km to 101.280 Km Existing Chainage km 67.496 to km 103.557 on EPC Mode in Manipur PKG-4 (NHIDCL) (618336) (-) (-)	Manipur	09/2021 (06/2022)	12/2023 (12/2026)	579.63 (579.63)	408.21	86.05
1273	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 33.000 km to 66.390 Km Existing Chainage from km 33.395 to km 67.496 on EPC Mode in Manipur PKG-3 (NHIDCL) (618337) (-) (-)	Manipur	03/2021 (09/2021)	03/2023 (03/2026)	467.00 (467.00)	593.79	86.33
1274	Widening to 2-Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 15.940 km to 33.120 Km Existing Chainage Km 15.946 to Km 33.395 Total length17.180 Km in the State of Manipur on EPC mode PKG-2 - Balance Works & Rectification works (NHIDCL) (618338) (-) (-)	Manipur	03/2021 (03/2025)	03/2026 (10/2026)	195.14 (195.14)	162.71	93.1
1275	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from Design Chainage 69.875 Km to 121.769 Km in the State of Manipur on EPC mode Package-3 (NHIDCL) (618344) (-) (-)	Manipur	03/2021 (08/2021)	08/2023 (12/2026)	673.27 (673.27)	563.39	85.84
1276	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section from Km 48.587 to Km 69.875 in the State of Manipur on EPC mode under NHO Package-2B (NHIDCL) (618345) (-) (-)	Manipur	06/2020 (08/2020)	08/2022 (08/2026)	365.53 (365.53)	198.28	88.2

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1277	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 32.835 to km 48.587 in the State of Manipur on EPC mode under NHO Package-2A (NHIDCL) (618346) (-) (-)	Manipur	04/2020 (07/2020)	06/2022 (08/2026)	232.99 (232.99)	155.44	100
1278	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 13.747 to km 32.835 in the State of Manipur on EPC mode under NHO Package-1B (NHIDCL) (618347) (-) (-)	Manipur	04/2020 (07/2020)	06/2022 (08/2026)	241.52 (241.52)	164.85	100
1279	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from km 130.000 to km 141.029 Package-4B in the State of Manipur on EPC Mode (NHIDCL) (618348) (-) (-)	Manipur	06/2020 (11/2025)	11/2026 (11/2026)	177.76 (177.76)	97.93	9.17
1280	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from Design Chainage km 118850 to km 130000 Package-4A in the State of Manipur on EPC Mode (NHIDCL) (618349) (-) (-)	Manipur	04/2020 (08/2025)	08/2026 (08/2026)	204.12 (204.12)	112.41	25.93
1281	Construction of of 2 -Lane with paved shoulders road from Tamenglong-Tousem-Lisang-Mahur Road NH-137 starting near Dialong Village from km 10.000 at Dialong to km 31.430 near Old Tamenglong , near Barak River on EPC Mode Package-2 (NHIDCL) (618355) (-) (-)	Manipur	07/2021 (09/2021)	03/2023 (03/2026)	483.87 (483.87)	375.87	95.28
1282	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur in the state of Manipur from km 31.430 at Old Tamenglong to km 43.480 ending near Phelong on EPC Mode Package-3 (NHIDCL) (618356) (-) (-)	Manipur	03/2021 (06/2021)	12/2022 (04/2026)	234.08 (234.08)	201.13	98.5
1283	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 in Manipur starting from km 54.180 near Azuram to km 80.630 near Mandeu on EPC Mode Package 5 (NHIDCL) (618357) (-) (-)	Manipur	09/2021 (11/2021)	05/2023 (01/2026)	477.86 (477.86)	330.13	84.87
1284	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 starting from km 80.630 near Mandeu to km 96.870 near Jiri River on EPC Mode Package-6 (NHIDCL) (618358) (-) (-)	Manipur	09/2021 (11/2021)	05/2023 (12/2025)	311.18 (311.18)	231.08	86.87
1285	Construction of 2-laning with Hard shoulder of Ukhrul Tolloi - Tadubi section of NH-102A from Design Chainage km 9450 to km 50850 in the State of Manipur on EPC mode under NHO-NE Package-2 (NHIDCL) (618387) (-) (-)	Manipur	03/2023 (03/2024)	03/2026 (12/2026)	578.98 (578.98)	278.6	80.04
1286	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 50.850 km to 81.870 km in the State of Manipur on EPC mode under NHO-TSP Package -3 (NHIDCL) (618388) (-) (-)	Manipur	09/2021 (07/2023)	01/2025 (12/2026)	315.56 (315.56)	257.41	94.5
1287	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 81.870 km to 105.825 km in the State of Manipur on EPC mode under NHO-TSP Package -4 (NHIDCL) (618389) (-) (-)	Manipur	09/2021 (08/2022)	02/2024 (08/2026)	310.76 (310.76)	287.73	97
1288	Improvement of existing road to 2 laning with Hard Shoulders of Maram-Peren section Package-1B, length- 17.660 km from Design Chainage 22.340 km to 40.000 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618415) (-) (-)	Manipur	02/2021 (06/2021)	12/2022 (03/2026)	188.36 (188.36)	0	100
1289	Improvement of existing road to 2 laning with Hard Shoulders of Maram -Peren section Package-1A, length- 22.340Km from Design Chainage 0.000 km to 22.340 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618416) (-) (-)	Manipur	02/2021 (06/2021)	12/2022 (03/2027)	226.32 (226.32)	190.19	75.08
1290	Rehabilitation and Up-gradation of Nongstoin Wahkaji section of Project Road Km 0000 to Km 43060 to Intermediate Lane with earthen shoulder under SARDP-NE Phase-A in the State of Meghalaya on EPC mode. Job No- SARDP-NE ong-Don-Maw/MG/2020-21/294 (MoRTH) (617885) (-) (-)	Meghalaya	08/2020 (02/2022)	08/2023 (08/2026)	302.88 (302.88)	187.77	99.62
1291	Improvement and Widening two lannig with paved Shoulder of NH 127B from km 31.500 Goeragre to km 63.224 Package-II in state of Meghalaya (MoRTH) (618076) (-) (-)	Meghalaya	12/2023 (05/2025)	05/2027 (-)	504.00 (350.67)	0	4.5

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1292	Improvement and Widening of National Highway No. 127B Darugiri - Songsak - Williamnagar Junction Section to two lane with paved shoulder from design Km 0000 to Km 36635 Design length 36.635 Km existing Km 112000 to Km 151060 of NH-1278 under Bharatmala Pariyojana Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618294) (-) (-)	Meghalaya	03/2023 (09/2025)	09/2027 (09/2027)	801.07 (801.07)	176.55	26.8
1293	Improvement/Widening of New NH-217 Dainadubi-Darugiri section to Two lane with paved shoulder in Meghalaya from design Km 0000 to Km 40840 existing Km 8600 to Km 53000 of Old NH-62 under BMP Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618295) (-) (-)	Meghalaya	03/2023 (03/2025)	03/2027 (03/2027)	705.83 (705.83)	0	46.38
1294	Improvement/Widening to 2-L with Paved Shoulder/ 4-Laning of NH-40 section from Km 151330 to Km 163400 design Km 63.530 to Km 71.520 including Dawki Bridge of length 368 m between Shillong-Dawki under JICA ODA Loan assistance Phase-II Pkg-5 -Balance work (NHIDCL) (618374) (-) (-)	Meghalaya	07/2020 (05/2024)	11/2026 (11/2026)	284.21 (284.21)	170.81	42.91
1295	Improvement/Widening to 2-Lane with Paved Shoulder from design Km 45.760 to Km 63.530 between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance work Pkg-4 (NHIDCL) (618375) (-) (-)	Meghalaya	07/2020 (04/2024)	04/2026 (10/2026)	445.51 (445.51)	42.39	53.43
1296	Improvement/Widening to 2-Lane with Paved Shoulder between Shillong-Dawki road up to Bangladesh Border from design Km 10.670 to Km 37.550 under JICA ODA Loan assistance Phase-II -Balance Work-Pkg-2 (NHIDCL) (618376) (-) (-)	Meghalaya	07/2020 (02/2024)	08/2026 (12/2026)	525.67 (525.67)	0	53.21
1297	Improvement/Widening to 2-L with Paved Shoulder/4-L from Km 81740 to Km 93490 design Km 0000 to Km 10670 of NH-40 New NH-106 & 206 section & 4-L from design Km 0.00 to Km 0.930 of NH-44 section between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance Work Pkg-1 (NHIDCL) (618377) (-) (-)	Meghalaya	07/2020 (10/2023)	10/2025 (06/2026)	351.12 (351.12)	243.15	100
1298	Rehabilitation and up gradation of Nongstoin-Rambrai-Kyrshai road up to Meghalaya-Assam border from Km 0.335 to km 34.039 to 2-Lane under NHO - NE in the State of Meghalaya Package-1 (NHIDCL) (618418) (-) (-)	Meghalaya	09/2021 (05/2022)	05/2024 (12/2026)	359.86 (359.86)	310.07	83.05
1299	Construction of 2-Lane with paved shoulders of Shillong Western Bypass starting from NH-06 near Ladumsaw existing Km 60.900 of old NH40 to NH106 old NH 44E Package-III, from km 24700 to km 38256 under SARDP-NE PHASE A in the state of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618419) (-) (-)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	562.48 (562.48)	340.17	52.28
1300	Construction of 2 lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw existing km 60.900 of old NH-40 to NH-106 old NH-44E, Package-II km 12800 to km 24700 under SARDP-NE Phase A in the State of Meghalaya on EPC Mode (NHIDCL) (618420) (-) (-)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	686.03 (686.03)	357.32	50.48
1301	Construction of 2-Lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw Existing km 60.900 of old NH-40 to NH106 old NH-44E, km 0000 to km 12800 Package-I under SARDP-NE PHASE A in the State of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618421) (-) (-)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	620.30 (620.30)	332.95	74.85
1302	4-Laning of Vairengte - Chhimluang section Package-3 of NH-306 from Existing Chainage km 43000 to Km 59700 Design Chainage km 46000 to km 60850 on Silchar - Vairengte- Sairang road in the State of Mizoram under Bharatmala Pariyojna under NHO-NE. Package-1&2 in Assam state (NHIDCL) (618316) (-) (-)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	491.39 (491.39)	238.01	17.86
1303	4-Laning of chhimluang-Kolasib from section pkg-4 of NH-306 & NH-6 existing chainage km 59700 to km 86000 design chainage km 61000 to km 77500 on Silchar-vairengte-sairang road in the state of Mizoram under Bharatmala Pariyojna on EPC mode Vairengte - Sairang Pkg-4 (NHIDCL) (618317) (-) (-)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	561.91 (561.91)	223.99	17.12
1304	4-Laning of Kolasib - Sethawn section Package-5 of NH-6 from Existing Chainage km 86000 to km 107850 Design Chainage km 77500 to km 95500 on silchar - voirengte - sairang road under Bharatmala Pariyojna on EPC mode under NHO-NE Vairengte - Sairang Pkg-5 (NHIDCL) (618318) (-) (-)	Mizoram	11/2021 (07/2025)	07/2027 (06/2027)	720.40 (720.40)	259.85	11.86
1305	4-Laning of Sethawn - N. Kawnpui section Package-6 of NH-6 from Existing Chainage km 107850 to km 126315 Design Chainage km 95500 to km 111850 on Silchar-Vairengte- Sairang road, Vairengte - Sairang Pkg-6 (NHIDCL) (618319) (-) (-)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	595.65 (595.65)	189.39	6.72

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1306	Construction of 4-Laning of N. Kawnpui N. Mualvum Mualkhang via Khamrang Village section Package-7 of NH-6 from Existing Chainage km 127200 to km 142000 Design Chainage km 111850 to km 123400 on Silchar - Vairengte - Sairang road in the State of Mizoram on EPC mode (NHIDCL) (618320) (-) (-)	Mizoram	02/2024 (10/2025)	10/2028 (-)	866.32 (866.32)	190.01	18.9
1307	Construction of 4-Laning of West Serawlg-Sairang section of NH-6 from Existing Chainage km 142000 to km 158900 Design Chainage km 123400 to km 136260 on Silchar - Vairengte - Sairang road in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-8 (NHIDCL) (618321) (-) (-)	Mizoram	02/2024 (11/2025)	11/2028 (-)	875.79 (875.79)	288.34	13.95
1308	Construction of Twin Tube Uni-directional Aizawl Bypass Tunnel of 2.5 km and its approaches of 2.1 km from km 10.600 to km 15.200 on Sarrang - Phaibawk section of NH-6 in the State of Mizoram on EPC Mode under NHO-NE Package-2 (NHIDCL) (618323) (-) (-)	Mizoram	01/2024 (12/2025)	12/2028 (-)	1313.28 (1313.28)	0.11	0
1309	Construction of 2-lane Aizawl Bypass from km 15.200 to km 34.500 Package-3 on Sairang - Phaibawk section of NH-6 in the State of Mizoram under Bharatmala Pariyojna on EPC Mode under NHO-NE (NHIDCL) (618324) (-) (-)	Mizoram	02/2023 (10/2025)	11/2028 (-)	720.72 (720.72)	102.62	15.1
1310	Construction of 2-laning with hard shoulder of Lunglei to Chhumkhum from Design Chainage Km 0.000 to Km 37.420 of NH-302 [Lunglei-Tlabung] Package-A (NHIDCL) (618362) (-) (-)	Mizoram	03/2021 (06/2021)	12/2022 (11/2026)	698.45 (698.45)	553.89	64.78
1311	Construction of 2-laning with hard shoulder configuration of Chhumkhum to Tlabung from Design Chainage Km 37.420 to Km 74.950 of NH-302 in Mizoram under Bharatmala Pariyojana on EPC mode [Pkg-B] (NHIDCL) (618363) (-) (-)	Mizoram	06/2021 (07/2021)	01/2023 (12/2026)	740.58 (740.58)	494.49	61.34
1312	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 208. 000 to Km 250.000 Package-5 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-5 (NHIDCL) (618379) (-) (-)	Mizoram	09/2019 (10/2019)	04/2023 (06/2026)	752.89 (752.89)	125.64	95.35
1313	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 125. 000 to Km 166 Package-3 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-3 (NHIDCL) (618380) (-) (-)	Mizoram	09/2019 (10/2019)	04/2023 (06/2026)	867.09 (867.09)	525.13	97.51
1314	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 339.00 to km 380.00 Siaha on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-8 (NHIDCL) (618383) (-) (-)	Mizoram	09/2019 (03/2020)	09/2023 (06/2026)	637.06 (637.06)	547.01	99.82
1315	2-laning of Zorinpui - Longmasu section of NH-502A from km 0.000 to km 28.244 in the State of Mizoram on EPC mode under NHO-NE, stretch of IMBR (NHIDCL) (618452) (-) (-)	Mizoram	02/2023 (12/2024)	12/2026 (07/2027)	781.85 (781.85)	48.26	4.71
1316	Up-gradation to 2 lane with paved shoudters of Pawlrang - Rulchawm section- of NH-102B of Aizawl - Imphal Economic Corridor from Existing Chainage km 72.030 to km 104.129 including 2.459 km re-alignment section from Tuivai River to Rulchawm connecting km 48.150 of NH-6 [Design Chainage km 68.170 to km 98.579] in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-3 Keifang- Tuivai Pkg-3 (NHIDCL) (619010) (-) (-)	Mizoram	12/2021 (11/2023)	05/2025 (07/2026)	500.88 (500.88)	443.61	99.52
1317	Balance work of widening to two laning/re-alignment and geometric improvement from Km. 11000 to Km. 114618 with rectification of damaged stretches and provision of protection works in vulnerable location of NH-44 in the State of Mizoram. (MoRTH) (619321) (-) (-)	Mizoram	10/2025 (05/2026)	05/2028 (-)	170.96 (170.96)	0	2
1318	Bangalore Chennai Expressway Phase-II Pkg-I from km.71.000 to Km 96.000 Bethamangala in the state of Karnataka to Byreddypalli (NHAI) (619199) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	12/2020 (10/2022)	10/2024 (09/2026)	1410.01 (1410.01)	744.42	99.2
1319	6L Aluru - Jakkuva Section of NH-130CD Road from km 365.033 to km 396.800 Pkg. 1 (NHAI) (618681) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	02/2021 (03/2022)	03/2024 (08/2026)	1216.12 (1241.66)	703.33	99.63
1320	Bangalore Chennai Expressway Phase-III Package I Gudipala to Walajhpet from Km 156.000 to Km 180.000 (NHAI) (618477) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	10/2020 (05/2022)	05/2024 (08/2026)	1481.87 (1481.87)	746.74	99.02
1321	6L of Veera Kaveri Raja Puram to Pondavakkam from km 61.380 to km 96.040 of NH 716B Pkg-III (NHAI) (618634) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	03/2021 (01/2023)	01/2025 (09/2026)	1439.77 (1439.77)	808.62	98.89

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1322	Walajahpet/Ranipet to TN/AP Border Section of from Km.106.800 to Km.133.36 NH-4 (NHAI) (618769) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	12/2024 (09/2025)	09/2027 (09/2027)	1338.14 (1214.70)	240.77	15.58
1323	6L of Kumarajapet to Veera Kaveri Raja Puram from km 43.800 to km 61.380 of NH-716B Pkg-II (NHAI) (618772) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	02/2021 (10/2023)	10/2025 (09/2026)	702.52 (799.36)	405.81	99.8
1324	6 laning of Balance Work of Chennai - Tada from km. 21.40 to km. 54.40 (NHAI) (619077) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	12/2017 (03/2018)	03/2020 (08/2026)	464.62 (472.37)	389.77	100
1325	Khammam-Devarapalle Pkg III [4L Access Controlled Greenfield from Chintagudem village to Recherla village Design Chainage 63117 to 105236] (NHAI) (618747) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	01/2021 (09/2022)	09/2024 (08/2026)	829.50 (1227.07)	649.55	98.82
1326	4L Access Controlled Greenfield Highway section on NH-163G Khammam Vijayawada from Remidicherla village at Design Ch. 280.200 Km to Jakkampudi village on NH-16 at Design Ch. 309.909 Km Package-III (NHAI) (618818) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	03/2023 (10/2025)	05/2027 (12/2027)	1183.23 (1225.14)	228.68	5.8
1327	4L Access Controlled Greenfield Highway section on NH-163G Khammam Vijayawada from BrahmanapalliK village at Design Ch. 250.400 Km to Remidicherla village at Design Ch. 280.200 KmPackage-II (NHAI) (619143) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	03/2023 (03/2025)	03/2027 (06/2027)	826.01 (862.58)	175.85	25.78
1328	6L Access Controlled Greenfield Highway of Julekal village to Dinnedevaram village from Km 242.200 to Km 280.400 Pkg-2 (NHAI) (619212) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	01/2022 (01/2023)	01/2025 (04/2027)	1227.57 (1315.87)	539.17	70.6
1329	Widening/Improvement to 4-Lane with Paved Shoulder from km 55000 Nagabang Gamsuk to km 82514 Oyan in the State of Assam and Arunachal Pradesh on EPC mode under Bharatmala Pariyojna of Length 27.514 Km Package-3 (NHIDCL) (618359) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	03/2023 (09/2024)	03/2027 (03/2027)	665.47 (665.47)	380.59	96.7
1330	6L of Aurangabad to Bihar-Jharkhand border Chordaha section from km. 180.000 to km. 209.827 of NH-2 PKG-01 (NHAI) (618531) (-) (-)	Multi-States (Bihar, Jharkhand)	02/2021 (12/2024)	12/2026 (12/2026)	1054.46 (786.81)	202.27	37.93
1331	6L Greenfield Varanasi-Ranchi-Kolkata Highway from Anarbansalea village to Sagrapur village From KM. 151200 to KM. 184700Package-7 (NHAI) (618724) (-) (-)	Multi-States (Bihar, Jharkhand)	03/2023 (07/2025)	06/2027 (06/2027)	1719.20 (1723.42)	340.33	28.16
1332	6L Greenfield Varanasi- Ranchi- Kolkata Highway from Sonepurbigha village to junction with NH- 22 Chatra Bypass near Chatra from km 184.700 to km 222.000Pkg - 8 (NHAI) (618732) (-) (-)	Multi-States (Bihar, Jharkhand)	03/2023 (05/2026)	05/2028 (05/2028)	1728.17 (1728.17)	200.25	3.94
1333	Hariharganj to Parwa Mode section from km 23.284 to km 57.049 of NH-98 (NHAI) (618951) (-) (-)	Multi-States (Bihar, Jharkhand)	09/2020 (03/2022)	02/2024 (08/2026)	1125.78 (1186.56)	830.06	91.3
1334	4L of Sahibganj - Manihari Ganga Bridge including Manihari Bypass (NHAI) (618952) (-) (-)	Multi-States (Bihar, Jharkhand)	10/2016 (11/2020)	10/2024 (10/2027)	1954.77 (1978.01)	2025.05	87.02
1335	Six Laning of Bihar - Jharkhand Border Chordaha - Gorhar section of NH-2 from km 249.525 to km 320.810 (NHAI) (619078) (-) (-)	Multi-States (Bihar, Jharkhand)	12/2017 (06/2019)	11/2021 (12/2026)	1772.70 (1689.17)	1275.76	78
1336	4L of Munger Mirzachauki section from Km 157350 to Km 193931 Pkg-4 (NHAI) (619307) (-) (-)	Multi-States (Bihar, Jharkhand)	02/2021 (08/2022)	08/2024 (08/2026)	1376.56 (1481.58)	893.34	92.74
1337	Six Laning of Varanasi to Aurangabad from km. 786.00 to km. 978.40 of Old NH-2 (NHAI) (618530) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	02/2009 (09/2011)	03/2014 (08/2026)	3241.56 (3241.56)	2860.22	99.92
1338	6L Greenfield Varanasi-Ranchi-Kolkata Highway from junction with NH-19 & Varanasi Ring Road near Rewasa village to junction with Chandauli-Chainpur road near Khainti village from Km. 0.000 to Km. 27.000 - Pkg-1 (NHAI) (618728) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	03/2023 (11/2024)	11/2026 (05/2027)	1433.39 (1564.15)	559.01	47.63
1339	Construction of additional 3-Lane Bridge over River Ganga for connection between Buxar and Bharauli on NH-922 in the State of Uttar Pradesh and Bihar on Hybrid Annuity Mode (NHAI) (618882) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	03/2024 (08/2025)	02/2028 (02/2028)	531.61 (444.92)	47.11	22.26

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1340	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package III [from Pindari km 78.150 to Rawalganj Bypass Km 117.120] on EPC Mode in the state of Uttar Pradesh. (NHAI) (619154) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	10/2022 (08/2023)	08/2025 (10/2026)	1493.50 (1493.59)	1044.81	86.11
1341	4L of Kishanganj - Bahadurganj section from Km. 0.000 to Km. 23.649 & interchange at Start Point Length - 1.200 Km of NH-27 (NHAI) (618584) (-) (-)	Multi-States (Bihar, West Bengal)	01/2025 (12/2025)	12/2027 (12/2027)	962.84 (855.56)	181.12	20.14
1342	Vadodara Mumbai Expressway Talsari to Karvad Phase IB - Pkg X [Km 103.400 to Km 128.000] (NHAI) (619064) (-) (-)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	10/2020 (03/2022)	03/2024 (12/2027)	1909.74 (2652.24)	1097.32	36.23
1343	Balance work of 2L PS from Km 30.800 to Km 70.800 and 2L with Rigid Carriageway from Km 70.800 to km 84.120 of Khanapur- KA/GOA Border section of NH-4A (NHAI) (618942) (-) (-)	Multi-States (Goa, Karnataka)	01/2022 (11/2022)	05/2024 (03/2027)	226.76 (149.44)	110.31	84.7
1344	Bal. Works of Fagne Km. 510.000 to Maharashtra/Gujarat Border Km. 650.794 (NHAI) (618637) (-) (-)	Multi-States (Gujarat, Maharashtra)	12/2019 (09/2020)	09/2022 (12/2026)	1654.07 (1672.89)	1447.76	99.7
1345	Delhi-Amritsar-Katra Expressway Phase-I Pkg-V from Junction with Ambala-Kaithal-Hissar road NH-152 near Kharak Pandwa village to Junction with Patiala-Samana-Patran road SH-10 near Ghagga village Km 120250 to Km 157920 (NHAI) (618486) (-) (-)	Multi-States (Haryana, Punjab)	01/2021 (05/2022)	05/2024 (08/2026)	1741.86 (2281.02)	1508.2	98.7
1346	4L Ismailabad to Ambala Section of NH-152 Lot-4/Package-1 (NHAI) (619093) (-) (-)	Multi-States (Haryana, Punjab)	02/2023 (12/2023)	12/2025 (02/2027)	609.32 (454.34)	308	76.3
1347	6L of Ambala-Chandigarh greenfield section from Km. 0.000 to Km. 25.000 with 4L spur to Lalru from Km. 0.000 to Km. 5.828 & spur to PR-7 road from Km. 0.000 to Km. 11.157 (NHAI) (619134) (-) (-)	Multi-States (Haryana, Punjab)	03/2022 (10/2023)	10/2025 (09/2026)	1641.66 (1904.79)	1277.92	90.01
1348	6L access Controlled Greenfield Highway from Adhoya Musalmana to Sadopur section of Shamli -Ambala Package-III Design Ch. Form km 84.400 to km 121.786 (NHAI) (619216) (-) (-)	Multi-States (Haryana, Punjab)	05/2022 (05/2023)	05/2025 (12/2026)	1491.72 (1122.86)	791.92	81.33
1349	Additional Structures on 6LGurgaon-Jaipur Section of NH-48 between KM 42.700 to KM 273.00 (NHAI) (618505) (-) (-)	Multi-States (Haryana, Rajasthan)	08/2022 (12/2022)	06/2024 (08/2026)	409.64 (290.64)	200.31	88.9
1350	4 laning of Aligarh-Palwal Section from Km. 46.390 Design Chainage to Km. 69.110 Terminating at junction EPE Package-II from Kurana- Eastern Peripheral Expressway of NH-334D (NHAI) (618691) (-) (-)	Multi-States (Haryana, Uttar Pradesh)	03/2024 (08/2025)	08/2027 (08/2027)	939.17 (903.94)	250.21	17.16
1351	6L access Controlled Greenfield Highway from Ranipur Barsi to Adhoya Musalmana section of Shamli -Ambala Package-II Design Ch. Form km 45.500 to km 84.400 (NHAI) (618723) (-) (-)	Multi-States (Haryana, Uttar Pradesh)	06/2022 (05/2023)	05/2025 (02/2027)	1554.21 (1241.89)	847.9	82.75
1352	Construction of Greenfield Connectivity to Jewar International Airport from DND-Faridabad-Ballabhgarh Bypass KMP Link - Spur to Delhi Mumbai Expressway (NHAI) (619068) (-) (-)	Multi-States (Haryana, Uttar Pradesh)	07/2022 (06/2023)	06/2025 (04/2027)	2920.69 (3485.77)	1772.67	76.3
1353	2L/4L of Hoshiarpur to Una section including Hoshiarpur Bypass of NH 503A (NHAI) (618907) (-) (-)	Multi-States (Himachal Pradesh, Punjab)	03/2023 (05/2025)	05/2027 (05/2027)	571.34 (481.88)	257.79	26.43
1354	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XIV from Junction with Pathankot-Gurdaspur road NH-54 near Balsua to Junction with Hiranagar Road near village Gurha Baildaran km 423500 to km 468100 (NHAI) (619066) (-) (-)	Multi-States (Jammu and Kashmir, Punjab)	10/2021 (09/2022)	09/2024 (10/2026)	3044.02 (3707.91)	1776.5	87.3
1355	Barwa Adda Km. 398.240 to Panagarh Km. 521.120 (NHAI) (618533) (-) (-)	Multi-States (Jharkhand, West Bengal)	08/2010 (04/2014)	09/2016 (08/2026)	1560.39 (1568.22)	1694.94	100
1356	6L Greenfield Varanasi- Ranchi- Kolkata Highway from junction with NH-320 in Lepo village to Kamlapur villageJH/WB border from km 358.500 to km 387.200 Pkg -13 (NHAI) (618734) (-) (-)	Multi-States (Jharkhand, West Bengal)	03/2023 (09/2025)	09/2027 (09/2027)	1154.49 (1319.18)	330.27	24.76
1357	2L PS of JH / WB Border km. 70.524 - Purulia km.84.400 & Purulia km. 94.30 - Chandil Junction with NH-33 km. 153.705 of Old NH-32 (NHAI) (618909) (-) (-)	Multi-States (Jharkhand, West Bengal)	03/2018 (12/2019)	08/2022 (10/2026)	1652.40 (1771.88)	1652.04	97.65

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1358	4L of NH-80 section of Mirza Chauki to Farakka section from existing km 190.00 to design km 200.75 junction at km 3.100 of NH 133 B and from existing km 260.00 to existing km 283.00 design km 274.133 in the state of Jharkhand package - II (NHAI) (618948) (-) (-)	Multi-States (Jharkhand, West Bengal)	02/2025 (02/2026)	01/2028 (01/2028)	782.18 (782.18)	224.06	8.65
1359	Six Laning of KT/KL Border Thalapaddy -Chengala from Km. 17.200 to Km. 57.20 (NHAI) (619205) (-) (-)	Multi-States (Karnataka, Kerala)	05/2020 (11/2021)	05/2024 (08/2026)	1981.07 (2681.48)	1701.33	100
1360	6L from Sankeshwar Bypass to MH-KNT Border from Km. 555.017 to Km. 592.853 of NH-48 Pkg-II (NHAI) (618516) (-) (-)	Multi-States (Karnataka, Maharashtra)	01/2022 (10/2022)	04/2025 (05/2027)	1388.70 (1066.86)	1183.98	85.3
1361	Akkalkot MH/KN border New Greenfield corridor from Km 512.000 to Km 548.400 of NH-150C part of Akkalkot KN/TS Border section Package XIV (NHAI) (618636) (-) (-)	Multi-States (Karnataka, Maharashtra)	03/2023 (10/2024)	10/2026 (06/2027)	1370.75 (1403.49)	322.92	57.62
1362	Bangalore Ring Road STRR-NH-948A- Package-I of Phase-III from Belagondapalli TN to TN/KNT border from km 144.480 to 179.969 (NHAI) (618519) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	03/2022 (05/2023)	05/2025 (12/2026)	1260.74 (1218.47)	777	92.95
1363	Hosur to Dhamrapuri Pkg-1 [Neraluru - Thorapalli Agraharam] (NHAI) (618581) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	10/2021 (10/2022)	10/2024 (01/2027)	1828.66 (1828.66)	1464.36	78.7
1364	6L of MH/KN Border Nimbal Village to KN/TS Border Singnodi Village from Km. 162.5 to Km. 203.100 in Raichur of NH-150C Pkg-IV (NHAI) (618631) (-) (-)	Multi-States (Karnataka, Telangana)	03/2022 (11/2022)	05/2025 (08/2026)	1499.73 (1457.48)	840.31	99.51
1365	6L Access Controlled Greenfield Highway of Nandinne village to Julekal village from Km 202.900 to Km 242.200 Pkg-1 (NHAI) (618632) (-) (-)	Multi-States (Karnataka, Telangana)	02/2022 (01/2023)	01/2025 (08/2026)	972.06 (1044.06)	459.49	93.79
1366	Thalassery Mahe Bypass Km 170.600 to Km 189.200 of NH-17New NH-66 in Kerala (NHAI) (619097) (-) (-)	Multi-States (Kerala, Puducherry)	09/2017 (12/2017)	05/2020 (08/2026)	1181.12 (1573.18)	1534.73	100
1367	4L Shahpur to Muktainagar from Km. 186.000 to km 216.278 of NH 753L Pkg II of Boregaon Buzurg to Muktainagar (NHAI) (619101) (-) (-)	Multi-States (Madhya Pradesh, Maharashtra)	12/2022 (03/2024)	03/2026 (10/2026)	784.35 (659.52)	330.42	64
1368	Construction of 26 VUPs, Major Bridge, Service Road etc. on Lalitpur-Sagar-Lakhnadon section of NH-44 NS (NHAI) (618556) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	02/2023 (03/2024)	03/2026 (08/2026)	665.91 (665.91)	574.39	97.4
1369	4L of Chowka to Kaimaha near MP/UP Border section NH-34 from D. Ch. 145.000 to D. Ch. 197.266 excluding existing Chhatarpur bypass from D. Ch. 160.307 to D. Ch. 168.630 Package-4 (NHAI) (618668) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	10/2024 (09/2025)	09/2027 (08/2026)	996.50 (846.68)	312.98	49.18
1370	4L of Bamni - Rajura - Warur - Devada upto M.S. Border of NH - 930D from km 19.000 to km 51.985 (NHAI) (618941) (-) (-)	Multi-States (Maharashtra, Telangana)	03/2022 (03/2024)	03/2026 (12/2026)	968.05 (1187.19)	826.96	78.16
1371	Viluppuram Km.0.000 to Puducherry Km.29.000 (NHAI) (618844) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (11/2021)	11/2023 (09/2026)	1358.31 (1162.44)	526.41	98.32
1372	Puducherry Km.29.000 to Poondiyanuppam Km.67.000 (NHAI) (618845) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (11/2021)	11/2023 (09/2026)	1588.40 (1415.90)	460.45	98.75
1373	Sattanathapuram to Nagapattinam from Km 123.800 to Km 179.555 (NHAI) (618847) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (10/2020)	10/2022 (12/2026)	2899.77 (2899.77)	1595.37	85.6
1374	6L with access control provision Saharanpur bypass to Ganeshpur section from 13.89 Km to 41.820 Km of Delhi- Dehradun Economic Corridor package-2 (NHAI) (618711) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	04/2022 (11/2022)	11/2024 (08/2026)	796.65 (560.03)	508.43	99.29
1375	4-laning of Pilibhit - Sitarganj from Km. 32.500 to Km. 70.800 Pkg-2 of NH-30 (NHAI) (618783) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	01/2023 (03/2024)	03/2026 (10/2027)	1471.19 (1471.19)	470.11	44.41
1376	Road Safety Improvement of Critical Junctions on MuzaffarnagarHaridwar Section of NH-334 from Km 143000 to Km 196000 (NHAI) (618886) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	04/2025 (10/2025)	10/2027 (10/2027)	238.66 (0.10)	42.08	22.64

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1377	Improvement & Up-gradation of NH-734 Section of Moradabad-Thakurdwara Kashipur including Moradabad & Kashipur Bypass Package-III Kashipur Bypass Length 14.490 Km., Starts from Ch. 38770 and ends at Ch. 53260 existing Ch. 05560 (NHAI) (618928) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	02/2023 (03/2024)	09/2025 (03/2027)	936.12 (717.50)	386.34	53.84
1378	4/6L of Spur to Haridwar Greenfield from Km. 0.000 to Km. 50.70 (NHAI) (618969) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	11/2021 (02/2023)	02/2025 (09/2026)	2155.95 (2612.30)	1543.12	92.98
1379	4L of Haridwar-Nagina section from km. 0.00 to km. 71.614 of NH-74 (NHAI) (619217) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	12/2015 (01/2018)	07/2020 (08/2026)	1659.12 (1622.49)	1546.89	99.85
1380	Widening of existing Single lane / Intermediate lane road to 2 lane from Km 101 to Km 125 of NH 61 (MoRTH) (617886) (-) (-)	Nagaland	06/2020 (06/2024)	06/2026 (04/2027)	252.20 (252.20)	0	44.46
1381	Widening to Existing single lane /intermediate lane to 2 lane from Km185.00 to Km 220.00 of NH-61 New NH-02 in the state of Nagaland. (MoRTH) (618072) (-) (-)	Nagaland	03/2021 (07/2022)	07/2024 (03/2026)	297.25 (297.25)	155.15	100
1382	Construction of 2-lane with Paved shoulder of Kohima- Bypass Road Connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29, NH-39New NH-02 from Design Km 32.00 to Design Km 43.454Design Length-11.454 Km in the State of Nagaland under SARDP-NE on EPC Mode Package-IV (NHIDCL) (618290) (-) (-)	Nagaland	07/2020 (10/2020)	04/2022 (12/2026)	202.36 (202.36)	102.32	46.77
1383	Construction of 2-lane with Paved shoulder of Kohima-Bypass Road connecting NH-39 New NH-02, NH150New NH-02, NH7-61 New NH-29 and NH-39 New NH-02 from Design km 21.000 to km 32.268 [Design length11.268 km] in the state of Nagaland Under SARDP-NE on EPC Mode Package- 3 (NHIDCL) (618291) (-) (-)	Nagaland	07/2020 (06/2023)	06/2025 (12/2026)	159.85 (342.29)	128.32	39.54
1384	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting New NH-02 and New NH-29 from Design Km 10.500 to design Km 21.000 [Design Length-10.500 km] including TUNNEL of 500m at Ch. 11.000 in the state of Nagaland Under SARDP-NE on EPC Mode Package-2 (NHIDCL) (618292) (-) (-)	Nagaland	07/2020 (10/2020)	10/2022 (10/2027)	277.44 (277.44)	201.99	69.76
1385	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29 and NH-39New NH-02 from design Km 0.00 to Km 10.500 in the State of Nagaland under SARDP-NE on EPC Mode Package-1 -Balance work (NHIDCL) (618293) (-) (-)	Nagaland	07/2020 (11/2023)	11/2026 (11/2026)	232.29 (350.88)	120.92	27.24
1386	Balance work of Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 old NH-150 from existing km 98.380 near Chizami vill. to km120.367 Nagaland/Manipur Border [Design km 95.700 to design km 117.200] [Design Length 21.500 km] in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode Package-V under NHO (NHIDCL) (618296) (-) (-)	Nagaland	03/2020 (11/2023)	11/2025 (07/2026)	330.80 (330.80)	268.18	98.39
1387	Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 Old NH-150 from existing Km 30.474 Near Kidwema road Chakahabama to existing Km 53.220 Near Kikruma Village Design Km 29.60 to Km 51.50 Design length-21.90 Km in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode under NHO Package-II -Balance work (NHIDCL) (618297) (-) (-)	Nagaland	03/2020 (01/2024)	01/2026 (12/2026)	355.79 (355.79)	0	43.13
1388	4-Laning of Balance work of Dimapur-Kohima Road from design km 152.490 to km 166.700 Existing km 156.000 to km 172.900 Excluding Dimapur & Kohima Bypass under SARDP-NE Package-III (NHIDCL) (618328) (-) (-)	Nagaland	03/2016 (09/2023)	09/2025 (09/2026)	562.98 (794.75)	542.85	84.32
1389	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-I Design Chainage 0000 Km to 34795 Km, in the State of Nagaland on EPC mode under NH O-NE (NHIDCL) (618364) (-) (-)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	430.24 (430.24)	0	87
1390	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-III Design Chainage 69875 Km to 106816 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618365) (-) (-)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	497.18 (497.18)	0	85.67
1391	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-II Design Chainage 34795 Km to 69875 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618366) (-) (-)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	442.54 (442.54)	0	58.5

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1392	Construction of 2 laning with Hard shoulder of Peren-Dimapur section on NH 129A from Design Km 146.208 to Km 163.592 Length- 17.384 km in the state of Nagaland on EPC mode under NHO-TSP Package-III (NHIDCL) (618413) (-) (-)	Nagaland	02/2021 (06/2023)	06/2025 (08/2026)	177.77 (199.02)	111.71	95.62
1393	Construction of Balance work for 2-lane with hard shoulder of Peren- Dimapur section on NH-129A from Design Km 126.775 to Km 146.208 Length 19.433 Km in the state of Nagaland on EPC mode under NHO-TSP Package-II (NHIDCL) (618414) (-) (-)	Nagaland	01/2021 (09/2023)	09/2025 (09/2025)	258.52 (258.52)	136.09	96.53
1394	Construction of 2-lane with hard shoulders of Merangkong-Tamlu-Mon road Wakching Twon portion on EPC basis from existing Chainage Km 59000 to Km 73640 [Design Km. 59000 to Km, 72450] Design length - 13.450 Km under SARDP-NE package-V Balance work (NHIDCL) (618422) (-) (-)	Nagaland	03/2021 (09/2023)	09/2025 (07/2026)	161.73 (161.73)	101.28	99.75
1395	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon MTM Road from existing Km 20.456 to Km 41.065 Design Km. 20 to Km. 40.0 Design Length- 20.000 Km in the State of Nagaland under SARDP-NE Phase-A Pkg-2 Balance work (NHIDCL) (618423) (-) (-)	Nagaland	03/2018 (08/2023)	08/2025 (03/2026)	215.79 (215.79)	173.12	100
1396	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon Road on EPC Basis from existing road Km. 76.640 to Km 98.065 Design chainage Km. 63.800 to Km. 86.835 Design Length-23.035 Km in the state of Nagaland under SARDP-NE PKG-IV Balance work (NHIDCL) (619059) (-) (-)	Nagaland	03/2018 (09/2023)	09/2025 (12/2026)	323.98 (323.98)	147.37	79.03
1397	New construction of Major Bridge with Approaches from Km 0.000 to 1.200 Madhopur -Badabanta section of NH-20 under NHO in Annual Plan 2022-23 in the State of Odisha (MoRTH) (617898) (-) (-)	Odisha	03/2023 (04/2025)	10/2027 (10/2027)	199.50 (199.50)	0.32	0
1398	Widening and Strengthening to 4LPS/2LPS from km 0.000 to 35.800 Kuakhia - Mangalpur section of NH 20 in the state of Odisha on Annual Plan 2021-22 (MoRTH) (617899) (-) (-)	Odisha	03/2022 (02/2024)	02/2026 (11/2026)	636.10 (636.10)	296.5	56.11
1399	construction or By-pass road on NH-26 for Nabrangpur Town (MoRTH) (617902) (-) (-)	Odisha	03/2023 (12/2024)	12/2026 (12/2026)	168.95 (168.95)	11.13	38
1400	Construction of Bypass road to Balangir town from km 72/400 Desing km 0/0 to km 79/800 Design km 11/670 of NH-26 in the State of Odisha. (MoRTH) (617904) (-) (-)	Odisha	02/2022 (04/2023)	10/2025 (12/2026)	238.78 (238.78)	6.79	55
1401	Construction of 4 lane ROB with approaches in lieu of LC No. RV-172 at km 176.00 of NH-201 present NH-26 at Kesinga including land acquisition in the state of Odisha on EPC mode under Annual Plan 2021-22 (MoRTH) (617905) (-) (-)	Odisha	12/2021 (05/2023)	05/2025 (05/2027)	324.09 (324.09)	88.48	78
1402	Widening and Strengthening of existing S/L, I/L, & D/L to 2 Lane with PS from Km 256/455 to 256/503, 256/820 to 256/960, 265/760 to 266/010, 266/010 to 266/800, 270/975 to 271/055, 276/460 to 276/560, 276/560 to 276/700, 276/700 to 277/480, 285/780 to 288/290, 288/290 to 291/050 and construction of 3 Nos. of Bypass from Km 266/800 to 267/300, 270/025 to 270/975, & 284/700 to 285/780 on NH-53 under NHO in Annual Plan 2022-23 for the State of Odisha. (MoRTH) (617918) (-) (-)	Odisha	03/2023 (06/2026)	12/2027 (-)	174.21 (174.21)	6.43	0
1403	Widening and Strengthening to 2LPS including LA from km 318.970 to 353.450 Balikuda-Mulkani Section of NH-55 under NHO in Annual Plan 2022-23 in the State of Odisha. Job No. NH-55-OD-2022-23-656 (MoRTH) (617920) (-) (-)	Odisha	01/2022 (06/2025)	06/2027 (06/2027)	511.54 (511.54)	7.64	3
1404	Widening and strengthening to 2LPS including LA of Kandarpur-Balikuda from km 277/500 to 318/970 of NH-55 in the State of Odisha under Annual Plan 2021-22. (MoRTH) (617921) (-) (-)	Odisha	03/2022 (06/2023)	06/2025 (11/2026)	499.79 (499.79)	131.36	66
1405	Construction of Jharsuguda Bypass including Land acqusition on NH-49 from km 258.636 to km 283.300 design chainage 258.636 to km 289.876 under NHO in Annual Plan 2022-23 for the state of Odisha Job No.NH-49-OD-2022-23-655 (MoRTH) (617922) (-) (-)	Odisha	09/2021 (01/2025)	07/2027 (07/2027)	587.10 (587.10)	52.58	25
1406	Construction of Daspalla Bypass from km 195.250 To 200.635 of NH-57 including land acquisition in the state of Odisha on EPC mode under Annual Plan 2022-23. (MoRTH) (617923) (-) (-)	Odisha	02/2023 (05/2025)	05/2027 (05/2027)	155.97 (155.97)	53.05	25
1407	Construction of Bypass to Khordha town from Km 294/000 to 300/300 on NH-57 including LA in the State of Odisha on EPC mode. (MoRTH) (617925) (-) (-)	Odisha	02/2022 (05/2023)	11/2024 (08/2026)	157.49 (157.49)	33.69	92

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1408	Construction of Bypass on NH-59 from Km 336/350 to 349/910 13.56 km near Berhampur town including 4-lane RoB in the state of Odisha. (MoRTH) (617930) (-) (-)	Odisha	03/2021 (03/2022)	12/2025 (12/2026)	196.94 (196.94)	59.55	70
1409	Construction of four lane ROB and its approaches in lieu of existing Level Crossing No. RV-71 at km 435 on NH-217 New NH-353 at Khariar including land acquisition under NHO in Annual Plan 2021-22 for the state of Odisha for F.Y. 2021-22 to F.Y 2033-34 (MoRTH) (618003) (-) (-)	Odisha	11/2021 (06/2023)	12/2024 (09/2026)	154.49 (154.49)	25.17	90
1410	Widening & strengthenlng to 2LPS from km 0,000 to 40.000 Dhaugaon- Podamari section of NH 326 in the State of Odisha under Annual Plan 2021.22. (MoRTH) (618012) (-) (-)	Odisha	03/2022 (02/2024)	02/2026 (12/2026)	186.52 (186.52)	46.39	60
1411	Construction of Dharmagarh Bypass on NH-130C including land acquisition in the state of Odisha on EPC Mode under Annual plan 2022-23. (MoRTH) (618079) (-) (-)	Odisha	03/2023 (04/2025)	10/2026 (10/2026)	172.66 (172.66)	0	15
1412	Widening to 2 lane with paved shoulded of Jareikela Jharkhand/Odisha Border - Dhabaleswar section from 0/0 to 36/0 of NH-320D in the State of Odisha under Annual Plan 2021-22. (MoRTH) (618122) (-) (-)	Odisha	03/2022 (10/2024)	10/2026 (10/2026)	172.09 (172.09)	7.42	34
1413	Bhadrak KM 136.500 to Baleshwar KM 199.141 (NHAI) (618523) (-) (-)	Odisha	11/2014 (03/2019)	09/2021 (11/2026)	844.67 (1394.82)	783.98	91.32
1414	Construction of 6-lane flyover at Ainthapali junction and a 2-lane ROB LHS on NH-53 Earlier NH-6 in Sambalpur, on EPC mode in Odisha under NHO (NHAI) (618591) (-) (-)	Odisha	03/2024 (06/2024)	12/2026 (12/2026)	374.17 (211.74)	106.91	54.2
1415	Balance work of 8 nos. of Elephant Underpasses EUPs, 1 no. of Vehicular Underpass VUP, 1 nos. of Light Vehicular Underpass LVUP, 1 nos. of Pedestrian Underpass PUP, 1 nos. of Foot Over Bridge FOB and A2 side approach of Jharpokharia Flyover at Km.215.270 in Baharagora-Singhara section of NH-49 (NHAI) (618592) (-) (-)	Odisha	09/2023 (11/2024)	05/2026 (10/2027)	320.64 (244.85)	55.3	25.04
1416	Balance work of Rehabilitation and Upgradation to four laning of Baharagora Singhara section of NH-49 from Km.229.727 to Km.238.990 Length 9.263 Km. including construction of five nos. of Elephant Underpasses EUP and fourteen nos. of Animal Underpasses AUP inside the buffer zone of Similipal Tiger Reserve Area in Bangriposi Ghat section in the State of Odisha on EPC Mode (NHAI) (618593) (-) (-)	Odisha	03/2025 (05/2025)	11/2027 (11/2027)	263.32 (163.07)	13.82	9.95
1417	6L Greenfield Kaliagura Baunsaguar Section of NH-130-CD Road from km 249000 to km 293000 Package OD-5 (NHAI) (618677) (-) (-)	Odisha	09/2021 (05/2022)	05/2024 (11/2026)	1539.75 (1918.49)	1026.67	97.8
1418	6L Greenfield Baunsaguar - Baraja Section of NH-130-CD Road from km 293000 to km 338500 Package OD-6 (NHAI) (618678) (-) (-)	Odisha	08/2021 (06/2022)	05/2024 (08/2026)	1265.59 (1635.44)	1001.24	99.6
1419	6L Greenfield Kandili - Aluru Section of NH-130-CD Road from km 342500 to km 365033 Package-OD-8 (NHAI) (618680) (-) (-)	Odisha	12/2021 (10/2022)	10/2024 (08/2026)	1492.74 (1912.84)	1088.96	99.9
1420	6L Flyover including RE Wall approaches with Flexible Pavement in the Elephant Corridor of Angul Sambalpur Section of NH-42 New NH-55 Km.202.533 (NHAI) (618704) (-) (-)	Odisha	09/2023 (06/2024)	01/2027 (08/2026)	150.86 (106.32)	106.14	100
1421	4L Godibandha to Ballhar Chhak, Ballhar Chhak to Banarpal & Banarpal to Start of Angul bypass at Km.314.130 to Km.321.035 of NH53, at Km.75.200 to Km.84.000 of NH149 & at Km.84.000 to Km.86.100 of NH55 (NHAI) (618705) (-) (-)	Odisha	12/2024 (02/2026)	02/2028 (02/2028)	973.12 (973.12)	241.06	5.4
1422	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.39.000 to Km.60.00 Package-3 (NHAI) (618820) (-) (-)	Odisha	03/2023 (12/2023)	12/2025 (03/2027)	861.84 (938.55)	395.96	92.02
1423	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km 18.00 to Km 39.00 in the State of Odisha on HAM mode Package-2 (NHAI) (618821) (-) (-)	Odisha	03/2023 (12/2023)	12/2025 (11/2026)	920.47 (950.40)	424.45	98.22
1424	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.0.00 to Km.18.00Package-1 (NHAI) (618822) (-) (-)	Odisha	03/2023 (12/2023)	12/2025 (01/2027)	929.91 (869.45)	398.91	96.75

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1425	3L Major Bridge over River Brahmani at Km. 401.250 Duburi - Chandikhole Section of NH-200 New NH -53 (NHAI) (618908) (-) (-)	Odisha	04/2022 (08/2022)	01/2025 (09/2027)	153.61 (103.68)	73.76	38
1426	6L of Badakumari - Karki Section from Km 179.000 to km 226.500 of NH-130-CD Package OD-3 (NHAI) (619109) (-) (-)	Odisha	03/2021 (04/2022)	04/2024 (08/2026)	1101.76 (1374.43)	713.46	99.7
1427	Four Laning of Angul to Sambalpur from Km.112.000 to Km.265.000 (NHAI) (619118) (-) (-)	Odisha	09/2016 (03/2017)	08/2019 (08/2026)	2510.04 (2632.91)	2464.91	99.98
1428	Cuttack-Angul Section of NH-42 New NH-55 from km 0.400 to km 60.200 Pkg-I in the State of Odisha (NHAI) (619119) (-) (-)	Odisha	10/2017 (01/2018)	07/2020 (09/2026)	999.32 (1178.31)	1128.52	99
1429	4 Laning of Talcher to end of Kamakhyanagar Bypass km 8.844 - km 15.725 of NH-149 and km 301.875 - km 335.946 of NH-53 Pkg-I (NHAI) (619157) (-) (-)	Odisha	01/2018 (02/2019)	08/2021 (10/2026)	795.18 (810.71)	715.74	99
1430	4 Laning of Duburi Chandikhole from km 388.376 to km 428.074 Pkg-III (NHAI) (619158) (-) (-)	Odisha	01/2018 (02/2020)	08/2022 (10/2026)	789.00 (907.61)	724.96	86
1431	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.60.000 to Km.76.646 Package-4 (NHAI) (619181) (-) (-)	Odisha	03/2023 (11/2024)	10/2026 (12/2027)	882.45 (1009.92)	196.67	36.02
1432	6L of Hatibena - Badakumari Section from Km 146.50 to km 179.00 of NH-130-CD Package OD-2 (NHAI) (619213) (-) (-)	Odisha	02/2021 (03/2022)	03/2024 (08/2026)	791.17 (1070.63)	733.61	99.99
1433	Cuttack-Angul Section of NH-42 New NH-55 from Km.60.200 to Km. 112.000 Pkg-II in the State of Odisha (NHAI) (619215) (-) (-)	Odisha	10/2017 (03/2018)	09/2020 (09/2026)	991.41 (1168.82)	1083.8	99.66
1434	Development to 4-lane with paved shoulder for the road section Talwandi Sabo-Raman road to refinery Road junction with Bathinda Dabwali Road of NH-254 from existing Km 131.600 to Km 155.650 Design Km 131600 to km 155600 in the State of Punjab. Job No NH-254-PB-2022-23-565 (MoRTH) (618010) (-) (-)	Punjab	03/2023 (05/2025)	11/2026 (11/2026)	546.67 (546.67)	0	45
1435	Up-gradation to two lane with paved shoulder configuration of NH-354 Section Arifkes-Ferozepur-Muktsar-Malaut from Km 201.500 to Km 212.500 & Km 229.690 to Km 269.960 and strengthening of existing pavement from Km 212.500 to Km 229.690 excluding Km 218.500 to 223.690 of NH-354 on EPC Mode in the State of Punjab. Job No. NH-354-PB-2020-21-532 (MoRTH) (618024) (-) (-)	Punjab	03/2021 (10/2023)	04/2025 (09/2026)	263.19 (263.19)	0	83
1436	Delhi-Amritsar-Katra Expressway Phase-I Pkg-IX from Junction with Ludhiana-Moga road NH-5 near Mullanpur Dakha to Junction with Jalandhar - Moga road NH-703 near Kang Sahibu village Km 260860 to km 303900 (NHAI) (618489) (-) (-)	Punjab	12/2020 (07/2022)	07/2024 (03/2027)	1851.47 (2407.14)	1935.88	73.35
1437	Delhi-Amritsar-Katra Expressway Phase-I Pkg-XII from Junction with Amritsar-Mehta-SriHargobindpur-Tanda road NH-503A near SriHargobindpur to Junction with Pathankot-Gurdaspur road NH-54 near Gurdaspur Km 362420 to km 397700 (NHAI) (618492) (-) (-)	Punjab	03/2021 (02/2025)	02/2027 (06/2027)	1734.18 (1538.47)	780.61	27.6
1438	Delhi-Amritsar-Katra Expressway Phase-I Spur-I from Jn. with Kapurthala - Sultanpur Lodhi Road NH-703A near Isharwal village to Jn. with Kapurthala - Tarn Taran road NH-703AA near Goinwal Sahib [Km 24000 to Km 41000 of Amritsar connectivity] (NHAI) (618493) (-) (-)	Punjab	12/2021 (04/2023)	04/2026 (03/2028)	2165.23 (1519.60)	618.22	34.79
1439	Greenfield connectivity from Govindsar village on Delhi Amritsar Katra Expressway to Talwara village on NH-44 Pathankot by-pass (NHAI) (618551) (-) (-)	Punjab	11/2024 (07/2025)	07/2027 (07/2027)	666.81 (690.47)	217.52	29.01
1440	Development of 6L Greenfield Jalandhar Bypass starting from Kahlwan NH-03 ending at Kang Sahbu NH-703 via Sarmastpur NH-44 - Madara NH-03 - Khajurla NH-44 (NHAI) (618552) (-) (-)	Punjab	03/2021 (01/2023)	01/2025 (06/2027)	1754.84 (2167.39)	1252.02	56.7
1441	6L of Jodhpur Romana Bathinda - Mandi Dabwali Punjab Haryana Border section of NH-54 from km. 0.000 to km. 27.400 of NH-54 (NHAI) (618610) (-) (-)	Punjab	05/2020 (08/2023)	08/2025 (08/2026)	789.26 (1318.91)	719.18	99

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1442	6L Amritsar-Bathinda Greenfield section from village Tiba on NE-5A to Jn. with Moga Jalandhar road NH-703 near Dharamkot from km 0.000 to km 39.000 of NH-754A Pkg-1 (NHAI) (618617) (-) (-)	Punjab	03/2021 (11/2022)	11/2024 (12/2027)	1229.38 (1549.32)	1014.98	72.41
1443	6L Amritsar-Bathinda Greenfield section from Jn. with Bhagta Bhai Ka-Bhadaur Road near Dyalpura Bhai Ka to Jn. with Mandi Dabwali Bathinda Road on NH-54 near Sangat Kalan from km 93.000 to km 154.866 of NH-754A Pkg-3 (NHAI) (618618) (-) (-)	Punjab	03/2021 (06/2024)	06/2026 (07/2027)	2029.17 (2677.23)	1442.16	74
1444	6L Access Controlled Ludhiana-Bathinda Greenfield highway from Jn. with Amritsar-Bathanda Greenfield Road NH-754A near Rampura Phul to Jn. with Moga-Barnala Road NH-703 near village Tallewal from Km 0.0 to Km 30.3 of NH-754AD Pkg-1 (NHAI) (618647) (-) (-)	Punjab	06/2021 (09/2023)	09/2025 (10/2026)	906.51 (1020.52)	687.82	81.5
1445	Development of 6-lane Greenfield Southern Ludhiana Bypass from intersection with NH-44 near Village Rajgarh to intersection with Delhi Katra Expressway NE-5 near Village Ballawal, km 0000 to km 25240 (NHAI) (618648) (-) (-)	Punjab	11/2024 (03/2026)	03/2028 (03/2028)	1424.55 (1424.55)	162.39	5.79
1446	Moga - Bagha Purana - Bajakhana from km. 0.00 to km. 43.32 (NHAI) (618764) (-) (-)	Punjab	05/2020 (12/2022)	12/2024 (12/2026)	1032.59 (1264.17)	799.77	76
1447	4L of Greenfield section from Sirhind to Mohali (NHAI) (618776) (-) (-)	Punjab	03/2022 (05/2023)	05/2025 (09/2026)	1237.65 (1301.15)	1391.6	98.66
1448	4/6L Greenfield LudhianaRupnagar highway from Jn. with NE-5 village near to ManewalLudhiana to Jn. with NH-205 near Bheora Village Rupnagar from Km 66.0 to Km 91.0 i/c spur to Kharar from Km 0.0 to Km 19.5 with Ludhiana bypass of NH-205K Pkg-3 (NHAI) (618785) (-) (-)	Punjab	07/2021 (02/2023)	02/2025 (12/2026)	1501.02 (1815.13)	1162.52	80.25
1449	4L of Phagwara - Hoshiarpur (NHAI) (618786) (-) (-)	Punjab	11/2022 (03/2025)	03/2027 (07/2027)	1196.38 (1503.79)	556.23	20.03
1450	4L of Fazilka to Abohar section of NH-07 including construction of Greenfield Abohar & Fazilka Bypasses (NHAI) (618793) (-) (-)	Punjab	03/2023 (04/2024)	04/2026 (08/2027)	1409.88 (1674.04)	913.89	67
1451	Amritsarairport Junction - Ramdas from km. 100.835 to km. 139.813 Pkg - IV (NHAI) (618794) (-) (-)	Punjab	12/2020 (03/2022)	09/2023 (09/2026)	524.88 (416.58)	395.48	96
1452	Amritsar Bypass Pkg III from km. 71.496 to km. 105.158 (NHAI) (618795) (-) (-)	Punjab	02/2021 (08/2022)	08/2024 (12/2026)	1474.77 (1228.42)	1222.67	82.88
1453	4L of Beas-Mehta-Batala-Dera Baba Nanak from intersection with Jalandhar-Amritsar Highway NH-3 near Beas till start of Batala Bypass near Village Acchhal from Km. 0.000 to Km. 31.300 Pkg-1 (NHAI) (618809) (-) (-)	Punjab	08/2021 (06/2023)	06/2025 (05/2027)	809.51 (966.99)	670.85	68.2
1454	4L of existing Beas Baba Bakala - Dera Baba Nanak Section from start of Batala Bypass till intersection with Ajnala Gurdaspur Highway NH 354 near Dera Baba Nanak from Km. 31.300 to Km. 69.100 with Additional batala Bypass Pkg-II (NHAI) (618810) (-) (-)	Punjab	10/2021 (06/2023)	06/2025 (03/2027)	1003.38 (993.60)	800.86	80.9
1455	4L of Amritsar-Ghoman - Tanda - Una Section from Km 8.270 to Km 54.000 of NH-503A Package-I (NHAI) (618906) (-) (-)	Punjab	12/2020 (06/2022)	06/2024 (03/2027)	857.91 (1443.47)	772.91	68.9
1456	6L Amritsar-Bathinda Greenfield section from Jn. with Moga Jalandhar road NH-703 near Dharamkot to Jn. with Bhagta Bhai Ka-Bhadaur Road near Dyalpura Bhai Ka from km 39.000 to km 93.000 of NH-754A Pkg-2 (NHAI) (619099) (-) (-)	Punjab	03/2021 (06/2024)	06/2026 (06/2027)	1801.37 (2172.71)	1268.39	66.53
1457	6L Access Controlled Ludhiana-Bathinda Greenfield highway from Jn. with Moga-Barnala Road NH-703 near village Tallewal to Jn. with Delhi-Katra Expressway NE-5 near Ludhiana village Ballawal from Km 30.300 to Km 75.543 of NH-754AD Pkg-2 (NHAI) (619105) (-) (-)	Punjab	07/2021 (09/2025)	09/2027 (09/2027)	1555.13 (1564.66)	711.39	25.55
1458	Delhi-Amritsar-Katra Expressway Phase-I Spur-III from Junction with Amritsar-Jalandhar road NH-3 near Bhishampapura to Junction with Amritsar-Anjala road NH-354 near Amritsar Airport [Km 71000 to Km 99000 of Amritsar connectivity] (NHAI) (619200) (-) (-)	Punjab	03/2021 (11/2022)	10/2024 (10/2027)	1641.75 (1951.70)	1364.2	33.85

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1459	4/6L Greenfield Ludhiana Rupnagar highway from Jn. with NE-5 village near to ManewalLudhiana to Jn. with NH-205 near Bheora Village Rupnagar from Km. 0.00 to Km. 37.7 including spur to Kharar with Ludhiana bypass of NH-205K Pkg-1 (NHAI) (619318) (-) (-)	Punjab	05/2021 (12/2022)	12/2024 (12/2027)	1368.91 (1382.48)	533.33	15.31
1460	Widening of Pachpadra-Bagundi Section to 4 Lane from Km 73/60 to 95/70 of NH-25 on EPC mode in the state of Rajasthan. (MoRTH) (617901) (-) (-)	Rajasthan	01/2022 (12/2022)	12/2024 (07/2026)	194.88 (194.88)	55.29	98.58
1461	Construction of 2 lane with paved shoulder for the work of Development of remaining sections of NH-325 Balotra to sanderao via Jalore to 2 lane with paved shoulder configuration by Construction of Byasses for town portions1 Asotra- Brahmdham bypass 2Siwana Bypass 3 Mokalsar Bypass 4 Major realignment at Kathadi 5 Major realignment at Bishangarh 6 Jalore Bypass 7 Ahore Town portion 8 Dujana Bypass in the state of Rajasthan on EPC Mode (MoRTH) (618011) (-) (-)	Rajasthan	12/2021 (05/2022)	05/2024 (10/2026)	411.44 (411.44)	85.69	92.77
1462	Upgradation to Two-lane with paved shoulder of Hanumangarh to Kenchiyan section from Km 0.000existing chainage-Km 23.200 to Km 49.605existing chainage-Km 74.645 of NH-54 in the State of Rajasthan on EPC mode. (MoRTH) (618069) (-) (-)	Rajasthan	03/2022 (10/2024)	10/2026 (10/2026)	334.64 (334.64)	0	72
1463	Up-gradation to 2 lane with paved shoulder from Neechli Oden Nathdwara at Design Km 88.800 existing km 55.95 to Bhatewar at Design Km 142.028 existing km 0.00 of NH-162E in the State of Rajasthan on EPC mode. (MoRTH) (618092) (-) (-)	Rajasthan	02/2023 (10/2024)	10/2026 (10/2026)	606.61 (606.61)	304.62	63.52
1464	Upgradation to 2-Lane with Paved Shoulder from Design Km 36300 to Design Chainage 47918 and from Design Ch 69900 to Design Ch 83940 of NH-248A Natni Ka Bara in the State of Rajasthan on EPC Mode. (MoRTH) (618117) (-) (-)	Rajasthan	02/2024 (11/2024)	05/2026 (08/2026)	154.89 (154.89)	15.13	23
1465	Construction of 2 lane with Paved Shoulder for Northern Bypass Phase-II of Kota city in the State of Rajasthan. (MoRTH) (618200) (-) (-)	Rajasthan	03/2022 (10/2023)	04/2025 (11/2026)	317.74 (317.74)	6.14	50.33
1466	Balance work of Rehabilitation and Up-gradation to 4-Lane configuration of Ras-Beawar Section Km 00.000 to km 30.050 of NH-158 in the State of Rajasthan under Green National Highway Corridor Project GNHCP. (MoRTH) (618235) (-) (-)	Rajasthan	01/2025 (06/2025)	12/2026 (12/2026)	278.10 (278.10)	99.13	56.2
1467	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-10 Ch. 292.950 to Ch. 319.400 [End of Interchange on NH-166 near village Mui to Hardeoganj village near Indergarh] (NHAI) (618457) (-) (-)	Rajasthan	11/2019 (05/2021)	05/2023 (09/2026)	1272.97 (1265.16)	1150.13	95.25
1468	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-15 Ch. 419.000 to Ch.427.300 [Junction with NH-12 near village Ummedpura to Major bridge over Takli river near Nayagaon Jageer village] (NHAI) (618458) (-) (-)	Rajasthan	07/2020 (07/2021)	01/2024 (08/2026)	1854.68 (1854.68)	1530.92	98.28
1469	Sangariya near Chautala-Rasisar near Bikaner section of NH-754K Phase-I AJ/SR-Package-7 (NHAI) (618611) (-) (-)	Rajasthan	02/2019 (06/2021)	06/2023 (08/2026)	520.63 (548.42)	450.59	100
1470	Deogarh near Dhandhaniya-Rajasthan/Gujarat Border Phase-I AJ/DRGB-Package-6 (NHAI) (618612) (-) (-)	Rajasthan	10/2019 (08/2021)	08/2023 (08/2026)	846.59 (740.62)	705.48	100
1471	Deogarh near Dhandhaniya-Rajasthan/Gujarat Border Phase-I AJ/DRGB-Package-7 (NHAI) (618613) (-) (-)	Rajasthan	10/2019 (07/2021)	07/2023 (08/2026)	662.08 (597.77)	561.75	99.2
1472	6L access controlled Highway from Km 40080 to Km 86513 Mator to Barodameo Section (NHAI) (618757) (-) (-)	Rajasthan	09/2022 (03/2024)	03/2026 (06/2027)	2010.20 (1565.88)	708.28	37.27
1473	6L accesscontrolled highway from km 0000 to km 40080 Paniyala to Mator Section of Paniyala-Barodameo ICR (NHAI) (618758) (-) (-)	Rajasthan	09/2022 (09/2024)	09/2026 (08/2026)	1764.86 (1239.24)	571.41	42.75
1474	Tanot -Ramgarh-Bhadasar-Jaisalmer NH-68 and BhadasarMokal-Sarkaritala up to Pakistan Border NH-968 Pkg-BM/5 (NHAI) (618796) (-) (-)	Rajasthan	02/2018 (04/2019)	04/2021 (08/2026)	828.58 (830.37)	755.88	100

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1475	Widening Strengthening of 2-Lane with Paved Shoulder from MyajlarJaisalmer from Design Chainage 0000 to 98350 Section of NH-11 & SundraMyajlarAmbasingh ki Dhani Road from Design Chainage 46000 to 81601, part of MunabaoTanot Road Section of NH-70 along with Strengthening/Widening of Existing Connection of NH-70 & NH-11 of length 0.914 km in the State of Rajasthan under NHO on Hybrid Annuity Mode (NHAI) (618797) (-) (-)	Rajasthan	03/2025 (12/2025)	12/2027 (12/2027)	1237.71 (927.02)	94.08	21.22
1476	4L of Karwar Km. 281.980 of NH-62 Nagaur road to Dangiyavas of Jodhpur Ring Road Pkg-II (NHAI) (618838) (-) (-)	Rajasthan	11/2021 (08/2022)	08/2024 (08/2026)	736.75 (512.77)	463.98	100
1477	Construction of Four lane Elevated Structure at Raniwada Circle in Sanchore City on NH-68 (NHAI) (618853) (-) (-)	Rajasthan	01/2024 (07/2024)	07/2026 (11/2026)	353.30 (241.34)	192.88	89.37
1478	Construction of two lane with paved shoulder of Ghatol Bypass from km 133.250 to km 140.950 of NH-56 old NH No. 113 on EPC mode in the State of Rajasthan. (MoRTH) (619251) (-) (-)	Rajasthan	03/2025 (03/2026)	09/2027 (-)	170.49 (170.49)	0	17
1479	Upgradation of 6 laned Jaipur- Kishangarh section of NH-48 from km 274100 to 363885 involving construction of flyovers and Service road in Rajasthan On Engineering, Procurement & Construction EPC Mode (NHAI) (619270) (-) (-)	Rajasthan	03/2026 (08/2026)	01/2029 (08/2028)	910.91 (910.91)	0	0
1480	Construction of Elevated Corridor at Kherwara Town on Udaipur Ratanpur Shamlaji Section of NH-48 in Udaipur District in the State of Rajasthan on EPC mode (NHAI) (619271) (-) (-)	Rajasthan	03/2026 (07/2026)	01/2029 (01/2029)	363.89 (363.89)	0.38	0
1481	Construction of two lane with paved shoulder Gangtok Bypass Road from Ranipool to Burtuk Ch 0.00 Km to 23.316 L23.316 Km in the State of Sikkim (MoRTH) (618071) (-) (-)	Sikkim	10/2021 (05/2022)	05/2024 (12/2026)	385.15 (342.89)	203.36	92
1482	Construction/Up gradation of Existing road to 2 Lane with Paved Shoulder including Geometric Improvement from Ranipool to Pakyong Balance work from Km 2.000 to 16.167 of NH-717-A on EPC basis under SARDP-NE Phase A in the State of Sikkim (NHIDCL) (618426) (-) (-)	Sikkim	03/2018 (01/2023)	07/2024 (12/2026)	264.84 (380.94)	127.34	87.03
1483	Realignment of NH-717A from Design Ch.0.00 Km 77.800 of NH-10 to Design Ch.2.00 Km 3.100 of NH-717A with two lane paved shoulder including Major Bridge of 680 m in the State of Sikkim on EPC Mode-COS work (NHIDCL) (618428) (-) (-)	Sikkim	01/2021 (04/2021)	04/2023 (05/2026)	264.84 (380.94)	70.71	100
1484	Construction & Upgradation of existing road to 2-lane with paved shoulder from New Rolep Bridge at km 37.600 to Chochenpheri at km 52.00 in the section of Rongli to Chochenpheri of NH 717B Pkg-II C (NHIDCL) (618446) (-) (-)	Sikkim	10/2020 (05/2021)	05/2024 (09/2026)	493.42 (478.79)	395.19	79.13
1485	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Helipad near Menla at Km 82000 to Menla at Km 94030 of Rhenock-Menla Spur NH-717B Package-IIIB on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618447) (-) (-)	Sikkim	01/2021 (02/2021)	02/2024 (05/2027)	410.60 (379.30)	241.77	82.64
1486	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Chochenpheri at Km 52000 to Helipad near Menla at Km 82000 of Rhenock-Menla Spur NH-717B Package-IIIA on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618448) (-) (-)	Sikkim	10/2020 (12/2020)	12/2023 (05/2027)	816.79 (786.60)	474.96	64.31
1487	Construction & Upgradation of existing road to 2-lane with paved shoulder from km27.200 End of Rongli bypass to km37.600New Rolep Bridge of Rhenok-Menla spur NH-717B on EPC Mode under SARDP-NE Phase-A in Sikkim Pkg-II B (NHIDCL) (618449) (-) (-)	Sikkim	07/2020 (10/2020)	04/2023 (09/2026)	230.45 (244.91)	249.71	86.19
1488	Rehabilitation & Upgradation of existing road to 2-lane with paved shoulder including geometric improvement of section from start of Rabangla km33.600 to km58.840 under SARDP-NE Phase A Pkg- IV (NHIDCL) (618450) (-) (-)	Sikkim	07/2020 (10/2020)	05/2022 (12/2026)	292.80 (292.80)	253.63	65.15
1489	Construction of Bypass to Madurai Achambathu Viratipathu in between km 6/850 10/382 of NH 49 Extn New NH 85 including Land Acquisition on Engineering, Procurement & Construction EPC basis Contract under NH O Annual Plan 2021-22 in the state of Tamil Nadu job No.NH-49 Extn New NH 85 - TN-2021-22-997 (MoRTH) (617962) (-) (-)	Tamil Nadu	03/2022 (09/2024)	08/2026 (08/2026)	238.97 (260.07)	126.56	94
1490	Bangalore Chennai Expressway Phase-III Package II Walajahpet to Arakkonam from Km 180.000 to Km 204.500 (NHAI) (618478) (-) (-)	Tamil Nadu	01/2021 (07/2022)	07/2024 (08/2026)	1106.65 (1106.65)	593	93.04

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1491	Bangalore Chennai Expressway Phase-III Package III Arakkonam to Kancheepuram from Km 204.500 to Km 230.000 (NHAI) (618479) (-) (-)	Tamil Nadu	12/2020 (08/2022)	07/2024 (12/2027)	1525.10 (1525.10)	360.95	53.56
1492	Construction of Trumpet Interchange Connecting Bangalore Chennai Expressway km.261705 to km. 262800 with Maduravoyal to Walajapet Section of NH 48 near Sriperumbudur Toll Plaza at km. 35700 (NHAI) (618480) (-) (-)	Tamil Nadu	05/2023 (02/2024)	08/2025 (10/2026)	162.55 (162.56)	54.98	38.52
1493	4L Bangalore-Chennai Expressway from Km. 230.000 to Km. 261.705 of Kancheepuram to Sriperumbudur Section Phase-III/Package-IV (NHAI) (618481) (-) (-)	Tamil Nadu	02/2021 (07/2022)	07/2024 (10/2026)	3605.73 (3605.73)	987.38	89.97
1494	Karaipettai to Walajapet from Km 71.015 to 107.091 (NHAI) (618521) (-) (-)	Tamil Nadu	08/2018 (02/2019)	02/2021 (08/2026)	766.51 (766.51)	613.76	93.55
1495	Balance Works for six laning of Sriperumbudur to karaipettai section of NH-4 New NH-48 from 37000 Existing Km 37000 to Km 71015 Existing Km 71000 in Tamilnadu on EPC mode underNHDP Phase-V (NHAI) (618522) (-) (-)	Tamil Nadu	06/2024 (01/2025)	10/2026 (03/2027)	411.16 (411.16)	134.65	38.26
1496	Improving the Alignment of Thoppur Ghat Section from Km 158.500 to Km 165.100 in Dharmapuri - Salem Section of NH-44 (NHAI) (618561) (-) (-)	Tamil Nadu	03/2024 (03/2025)	03/2028 (03/2028)	904.99 (731.09)	211.34	47.84
1497	4L of Madurai Ring Road Phase 1 [Vadipatti-Thamrapatti] from km 0.00 - km 29.960 (NHAI) (618563) (-) (-)	Tamil Nadu	12/2018 (03/2020)	03/2022 (08/2026)	900.05 (900.05)	903.57	99.42
1498	4L of left-over works including additional structures from Kerala/Tamil Nadu border to Kanyakumari Section from Km 43.0 to Km 96.174 of NH66 (NHAI) (618608) (-) (-)	Tamil Nadu	11/2022 (08/2023)	08/2025 (12/2026)	1564.23 (1263.42)	980.14	81.85
1499	6L of Pondavakkam to Kannigaipair from km 96.040 to km 116.100 of NH 716B Pkg-IV (NHAI) (618635) (-) (-)	Tamil Nadu	02/2021 (01/2023)	01/2025 (12/2027)	1359.81 (1359.81)	409.35	44.53
1500	4L of Thirumangalam to Vadugapatti section from km 0.000 to km 36.000 of NH-744 (NHAI) (618744) (-) (-)	Tamil Nadu	03/2022 (02/2023)	02/2025 (08/2026)	1076.97 (791.60)	685.52	95.95
1501	Melur - Pilayarpatti - Karaikudi from km 99.920 of NH 38 to km 12.9 of NH 383 Ext. (NHAI) (618756) (-) (-)	Tamil Nadu	12/2018 (03/2020)	03/2022 (08/2026)	1103.86 (1085.41)	956.44	98.12
1502	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package II from Km 4.604 to Km 9.700 (NHAI) (618800) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1616.97 (1616.97)	250.4	18.13
1503	Construction of New Double Tier 4-lane Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from Km -0342 to Km 20223 Package 1 from Km -0342 to Km 4604 (NHAI) (618801) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1388.59 (1388.59)	275.2	22.8
1504	Poondiyankuppam Km.67.000 to Sattanathapuram Km.123.800 (NHAI) (618846) (-) (-)	Tamil Nadu	03/2018 (01/2022)	01/2024 (09/2026)	2565.63 (2319.35)	1210.2	99.8
1505	4L of Madathukulam - Pollachi from km. 74.38 to km. 116.95 of old NH-209 New NH-83 (NHAI) (618894) (-) (-)	Tamil Nadu	01/2019 (12/2020)	12/2022 (09/2026)	1772.13 (1772.13)	1062.67	97.65
1506	Kamalapuram to Oddanchatram from km. 0.00 to km. 35.822 (NHAI) (618895) (-) (-)	Tamil Nadu	01/2019 (01/2021)	01/2023 (09/2026)	1319.42 (1319.42)	649.83	93.6
1507	Balance Works for Four laning of Vikravandi to Sethiyathope section from Km 0.0 to Km 65.96 of NH-45C in Tamil Nadu under NHDP Phase-IV on EPC mode (NHAI) (618898) (-) (-)	Tamil Nadu	01/2025 (06/2025)	06/2027 (06/2027)	1163.17 (834.46)	264.13	37.62
1508	Kallagam km.38.700 to Meensurutti Km.98.433 of NH-227 in Tamil Nadu (NHAI) (618899) (-) (-)	Tamil Nadu	02/2018 (04/2019)	04/2021 (08/2026)	1499.12 (1499.12)	1111.9	100
1509	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package IV from Km 14.185 to Km 20.593 (NHAI) (619045) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1205.40 (1210.21)	88.16	8.58

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1510	6-laning of Krishnagiri Km.0.000 to Walajahpet Km.148.300 section on NH-46 under NHDP-V (NHAI) (619074) (-) (-)	Tamil Nadu	12/2009 (06/2011)	12/2013 (08/2026)	1673.17 (781.74)	707.81	99.99
1511	Chengapalli km 102.035 to Neelambur Km144.680 and Madukkarai Km 170.880 to Walayar K183.010 Package No. NS-2/BOT/TN-08 (NHAI) (619086) (-) (-)	Tamil Nadu	10/2009 (09/2010)	03/2013 (10/2026)	1247.43 (285.55)	7.24	100
1512	Thorapalli - Agraharam - Jittandahalli Section from km 23.350 to km 60.100 [Hosur to Dhamrapuri Pkg-2] (NHAI) (619094) (-) (-)	Tamil Nadu	02/2019 (12/2021)	12/2023 (12/2026)	1243.57 (1272.11)	827.88	77.57
1513	Mahabalipuram - Pondicherry Pkg-I [Mamallapuram to Mugaiyur] (NHAI) (619129) (-) (-)	Tamil Nadu	02/2019 (05/2022)	05/2024 (01/2027)	1360.54 (1477.94)	904.84	58.65
1514	Mahabalipuram - Pondicherry Pkg-II [Mugaiyur to Marakkanam] (NHAI) (619130) (-) (-)	Tamil Nadu	02/2019 (12/2023)	12/2025 (03/2027)	1116.13 (1463.75)	804.69	53.41
1515	Four Laning of Chettikulam to Natham section of NH-785 (NHAI) (619131) (-) (-)	Tamil Nadu	03/2018 (11/2018)	11/2020 (06/2026)	837.61 (823.93)	641.93	99.75
1516	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package III from Km 9.700 to Km 14.185 (NHAI) (619139) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1299.36 (1299.36)	193.34	17.24
1517	4 Laning of Paramakudi to Ramanathapuram Section of NH-87 Old NH-49 (NHAI) (619156) (-) (-)	Tamil Nadu	07/2025 (05/2026)	05/2028 (05/2028)	1853.16 (1853.16)	169.53	0
1518	Access Controlled Highway of 4 Lane with Paved Shoulders from Tiruvallur Design Chainage Km 1756 to TN/AP Broder Design Chainage Km 6151 of NH-716 Chennai-Tirupati Package-1 (NHAI) (619161) (-) (-)	Tamil Nadu	03/2024 (12/2024)	12/2026 (03/2027)	1376.10 (1247.70)	181.78	46.31
1519	Balance works of four lane from km 43.950 Thiruvallur Bypass to km 61.470 Veppampattu Bypass passing through Thannerkulam, Thozur and Sevapet Bypass 17.520 kms of Tirupathi- Tiruttani- Chennai section of NH 205 (NHAI) (619222) (-) (-)	Tamil Nadu	03/2022 (09/2022)	09/2024 (08/2026)	467.99 (699.68)	595.08	97.92
1520	6-laning of km 9.900 to km 19/948 Aramgarh to Shamshabad Section of Hyderabad-Bangalore section of NH-44 Under NHO EPC basis in the state of Telangana (MoRTH) (617913) (-) (-)	Telangana	01/2018 (05/2018)	05/2020 (06/2026)	283.15 (300.70)	480.41	92.62
1521	Widening to two/four lane with paved shoulder from Km.180.600 to Km.223.000 of NH-63 on Nizamabad-Jagadapur road on EPC mode under NHO in the state of Telangana. (MoRTH) (617936) (-) (-)	Telangana	10/2016 (03/2017)	03/2019 (-)	253.99 (183.26)	0	100
1522	6-Laning of Pune-Hyderabad Section of NH-65 from Km 493/0 to Km 524/0 from Sangareddy X Roads to Madinaguda in the State of Telangana (MoRTH) (617939) (-) (-)	Telangana	03/2023 (07/2024)	07/2026 (08/2026)	1297.75 (1297.75)	0	45.85
1523	Rehabilitation and Upgradation of LB-Nagar to Malkapur section to 6-Lane main carriageway with service roads, drains cum footpath, including VUPs and widening of Minor bridge & road safety provisions from Km. 15/00 to Km 40/00 of NH-65 Old NH-9 under NH O for the year 2020-21 in the state of Telangana on EPC Mode. (MoRTH) (617940) (-) (-)	Telangana	03/2021 (07/2022)	07/2024 (12/2026)	545.11 (545.11)	290.36	83.47
1524	Construction of six lane elevated corridor from km 7.950 Uppal to km 14.200 of NH-163 to De-Congest the urban limits of Hyderabad-Bhoopalapatnam section on EPC mode in the state of Telangana (MoRTH) (617980) (-) (-)	Telangana	03/2018 (07/2018)	07/2020 (12/2027)	626.76 (626.76)	24.4	54.26
1525	Widening & Strengthening of Existing 2LPS to 4 lane PS from Km 150000 to Km 159000 and Km 165400 to Km 186000 of NH-163 old NH-202 under NH O for the year 2020-21 on EPC Mode in the state of Telangana. (MoRTH) (617983) (-) (-)	Telangana	03/2021 (07/2022)	07/2024 (08/2026)	317.19 (300.56)	190.86	91
1526	Rehabilitation and upgradation of NH-167 from design km 113.900 to 154.479 Mallepally Haliya section to two lane with paved shoulders on EPC mode in the stte of Telangana (MoRTH) (617994) (-) (-)	Telangana	02/2018 (06/2018)	11/2019 (12/2025)	294.13 (257.61)	249.23	88.22

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1527	Widening to Two Lane with Paved Shoulders from Km 67.000 to Km 114.425 of Kalwakurthy- Mallapally Section of NH 167 Erstwhile section of SH 18 in the State of Telangana on EPC mode under NH O Annual Plan 2016-17 (MoRTH) (617995) (-) (-)	Telangana	01/2017 (05/2017)	05/2019 (12/2026)	300.00 (300.00)	175.12	99.2
1528	Construction of 4-lane flyover at Amberpet-X road, Hyderabad on NH-202 in the State of Telangana (MoRTH) (618001) (-) (-)	Telangana	05/2018 (06/2021)	06/2023 (06/2026)	216.53 (265.88)	172.17	92.1
1529	Rehabitation and upgradation from km 121/000 to 154/000 Nakrekal to Mallampally section of NH-365 to 2 lane with paved shoulders in the state of Telangana in the EPC mode (MoRTH) (618025) (-) (-)	Telangana	03/2018 (06/2018)	12/2019 (09/2026)	192.67 (192.67)	141.82	96
1530	Widening to two lane with paved shoulders from Km 0/000 to Km 45/946 of Nizampet-Narayankhed-bidar section of NH-161B in the state of Telangana under Annual Plan 2021-22 on EPC mode under NHO (MoRTH) (618091) (-) (-)	Telangana	03/2022 (02/2024)	02/2026 (03/2027)	512.98 (512.98)	152.49	46
1531	Widening to two lane with paved shoulders from Km 0/000 to Km 79/300 of Kalwakurthy - Kollapur section of NH-167K in the state of Telangana under annual plan 2021-22 on EPC mode under NHO. (MoRTH) (618104) (-) (-)	Telangana	03/2022 (07/2023)	07/2025 (08/2026)	886.69 (886.69)	620.25	90.05
1532	Widening and strengthening to 4 lane / 2-lane with paved shoulders of Mahabubnagar - Chincholi section from km 60/255 to Km 102/834 of NH-167N in the State of Telangana on EPC mode. (MoRTH) (618105) (-) (-)	Telangana	03/2022 (10/2023)	10/2025 (11/2026)	631.49 (631.49)	125.34	46.63
1533	Widening and Strengthening to 2/4 lane with paved shoulders of Mahabubnagar Chincholi section from Km 0/0 to Km 60/255 of NH-167N in the state of Telangana under Annual plan 2021-22 on EPC modepackage-I under NHO Job No.167N-TS-2021-22-75 (MoRTH) (618106) (-) (-)	Telangana	01/2022 (05/2026)	11/2027 (03/2026)	703.68 (703.68)	304.65	90.69
1534	Widening to 2 lane with paved shoulders from 0.00 to 32.970 ofAdilabadto Bela section of NH 353B in the State of Telangana (MoRTH) (618130) (-) (-)	Telangana	10/2022 (05/2024)	05/2026 (12/2026)	490.92 (490.92)	149.79	79.07
1535	Widening to two/four lane with paved shoulders from Km.34.250 to Km.71.830 of NH-365A on Kodad-Khammam-Kurvi road. (MoRTH) (618140) (-) (-)	Telangana	10/2022 (02/2025)	01/2027 (01/2027)	445.76 (445.76)	18.32	13.33
1536	Widening and Improvement of existing carriage way to 2 lane with paved shoulders from Km. 86/160 to 131/730 of Jangaon-Duddeda section of NH-365B in the State of Telangana on EPC Mode (MoRTH) (618141) (-) (-)	Telangana	01/2022 (12/2022)	12/2024 (12/2026)	423.48 (423.48)	184.83	77.85
1537	Widening to Two lane with paved shoulders from 106/830 to 158/496 of Yellareddy-Rudrur Section of NH-765D in the state of Telangana on EPC mode under NHO under Annual plan 2022-23 (MoRTH) (618182) (-) (-)	Telangana	10/2022 (07/2024)	07/2026 (05/2027)	499.88 (499.88)	207.08	68.9
1538	Widening to 2 lane with paved shoulders from Km 62/920 to km 106/830 of Medak - Yellareddy section in the State of Telangana under Annual Plan 2022-23 on EPC mode under NHO (MoRTH) (618183) (-) (-)	Telangana	10/2022 (08/2024)	08/2026 (08/2026)	399.01 (399.01)	146.04	70.6
1539	Rehabilitation and Up-gradation of Valigonda to Thorrur Section to Two Lane with Paved Shoulders from Km 39.180 to Km 108.300 of NH-930P in the State of Telangana on Engineering, Procurement and Construction EPC Basis (MoRTH) (618186) (-) (-)	Telangana	01/2022 (12/2022)	12/2024 (09/2026)	549.28 (549.28)	325.77	94.97
1540	Widening to two lane with paved shoulders of 'Bodhan Basar Bhainsa ' section from Km 38/900 to 95/300 of NH-161BB in the state of Telangana under Annual Plan 2021-22 on EPC Mode under NH O. (MoRTH) (618190) (-) (-)	Telangana	03/2022 (03/2023)	03/2025 (08/2026)	644.45 (644.45)	403.48	98.6
1541	Widening to 2 lane with Paved Shoulders of Siddipet-Elkathurthy section from Km 69/978 to km 133/619 of NH-765DG in the State of Telangana under Annual plan 2021-22 on EPC mode (MoRTH) (618196) (-) (-)	Telangana	01/2022 (12/2022)	09/2024 (12/2026)	578.85 (578.85)	0	85
1542	Widening to 2 lane with Paved Shoulders of Medak - Siddipet section from Km 0/0 to km 69/978 of NH-765DG in the State of Telangana under Annual plan 2021-22 on EPC mode (MoRTH) (618197) (-) (-)	Telangana	01/2022 (01/2023)	01/2025 (12/2026)	882.18 (882.18)	383.75	74.06

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1543	Khammam-Devarapalle Pkg I [4L Access Controlled Greenfield from Thallampadu village to Somavaram village Design Chainage 0000 to 33604] (NHAI) (618746) (-) (-)	Telangana	01/2021 (10/2022)	10/2024 (10/2026)	797.36 (1337.18)	684.62	97.26
1544	4L of Karimnagar-Warangal section from km 49.500 to km 117.820 of NH-563 (NHAI) (618765) (-) (-)	Telangana	03/2022 (07/2023)	07/2025 (08/2026)	2146.86 (2486.51)	1272.62	92.4
1545	4L Access Controlled Greenfield Highway Section Mancherial Warangal from Pangidipalle village at Design Ch. 72.350 Km to Oorugonda village at Design Ch. 112.240 KmPackage-III (NHAI) (618811) (-) (-)	Telangana	03/2023 (10/2025)	10/2027 (01/2028)	1183.71 (1170.64)	209.72	5.63
1546	4L Access Controlled Greenfield Section Mancherial Warangal from Puttapaka village at Design Ch. 35.300 Km to Pangidipalle village at Design Ch. 72.350 KmPackage-II (NHAI) (618812) (-) (-)	Telangana	01/2023 (06/2025)	06/2027 (12/2027)	1129.33 (1145.41)	210.45	9.04
1547	4L Access Controlled Greenfield Section Mancherial Warangal from Narva village at Design Ch. 3.834 Km to Puttapaka village at Design Ch. 35.300 Km Package-I (NHAI) (618813) (-) (-)	Telangana	03/2023 (12/2024)	12/2026 (10/2027)	1127.90 (1104.27)	161.67	11.28
1548	4L Access Controlled Greenfield Highway section on NH163G Warangal-Khammam from Oorugonda village in Hanamkonda District at Design Ch. 112.240 Km to Venkatpur village in Warangal District at Design Ch. 150.240 KmPackage-I (NHAI) (618814) (-) (-)	Telangana	03/2023 (06/2025)	06/2027 (05/2028)	1142.60 (1140.82)	160.19	0.5
1549	4L Access Controlled Greenfield Highway section on NH-163G Warangal-Khammam from Venkatpur village in Warangal District at Design Ch. 150.240 Km to Thallasenkesa village in Mahabubabad District at Design Ch. 189.650 kmPackage-II (NHAI) (618815) (-) (-)	Telangana	03/2023 (04/2024)	04/2026 (03/2027)	1092.88 (1083.11)	408.59	77.65
1550	4L Access Controlled Greenfield Highway section on NH-163G Warangal-Khammam from Thallasenkesa village at Design Ch. 189.650 km to V.Vekatayapalem village in Khammam District at Design Ch. 220.480 KmPackage-III (NHAI) (618816) (-) (-)	Telangana	03/2023 (07/2025)	07/2027 (07/2027)	1105.25 (1098.05)	168.28	10.11
1551	4L Access Controlled Greenfield Highway section on NH-163G Khammam Vijayawada from V. Venkatayapalem village at Design Ch. 220.480 Km to BrahmanapalliK village at Design Ch. 250.400 Km Package-I. (NHAI) (618817) (-) (-)	Telangana	03/2023 (03/2025)	03/2027 (06/2027)	973.45 (1021.96)	271.03	45.89
1552	Hyderabad - Maneguda (NHAI) (618944) (-) (-)	Telangana	10/2021 (11/2024)	11/2026 (05/2027)	958.86 (1218.49)	431.45	24.2
1553	4L of Kodad Design Km 0.00/Existing Km 185.00 of NH-65 to Khammam Design Km 31.800/Existing Km 29.400 of NH-365A (NHAI) (618945) (-) (-)	Telangana	01/2021 (01/2022)	05/2024 (08/2026)	1149.17 (1606.99)	871.58	99.98
1554	Upgradation to Two Lane with Paved Shoulders from Km 0.000 to Km 41.920 Green Field Alignment of Gowrelly to Valigonda Section of NH-930P in the State of Telangana on EPC Mode under Annual Plan 2022-23 (MoRTH) (619009) (-) (-)	Telangana	11/2022 (05/2026)	04/2028 (03/2028)	690.33 (690.33)	0	0
1555	Khammam-Devarapalle Pkg II [4L Access Controlled Greenfield from Somavaram village to Chintagudem village Design Chainage 33604 to 63117] (NHAI) (619128) (-) (-)	Telangana	01/2021 (09/2022)	09/2024 (08/2026)	615.78 (981.64)	524.11	98.02
1556	Thanamcherla-Jamandlapally 2LPS (NHAI) (619165) (-) (-)	Telangana	11/2013 (03/2014)	02/2023 (12/2026)	177.18 (18.65)	8.3	100
1557	Rehabilitation and upgradation of NH-221 from km 121/0 to 165/0 Rudrampur to Bhadrachalam section to two lane with paved shoulder under NHDPIV in the state of Telangana through EPC mode (MoRTH) (619193) (-) (-)	Telangana	01/2015 (02/2015)	02/2017 (08/2026)	295.47 (334.82)	375.14	82.76
1558	Construction of 4 lane Bypass to Nalgonda Town Iroon Km 000 Existing Ch. 181590 to Km 14.00 Existing Ch. 28/685 ol Nakrekal to Nagarjunsagar Section of NH -565 in the State of Telangara on EPC under Annual Plan 2024 -25 (MoRTH) (619253) (-) (-)	Telangana	10/2024 (10/2025)	10/2027 (10/2027)	516.17 (516.17)	0	55.62
1559	Rehabilitation & Upgradation of Thorrru to Nehru Nagar section to Two Lane with Paved shoulders from Km 109/420 to Km 178/500 of NH 930P in the state of Telangana on EPC mode under Annual Plan 2022-2023 (MoRTH) (619265) (-) (-)	Telangana	01/2025 (07/2026)	07/2028 (07/2028)	675.45 (675.45)	0	0

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1560	Rehabilitation and up-gradation of road from km 16.077 to km 43.935 total length 27.858 km of Lalchara-Kanchanpur section via Shivbari on NH-44A to 2 lane with paved shoulder in the state of Tripura on EPC Mode Pkg-2 under BharatMala Pariyojana Manu-Simlung -2 (NHIDCL) (618307) (-) (-)	Tripura	02/2022 (01/2023)	01/2025 (01/2026)	456.88 (456.88)	205.69	54.56
1561	Improvement & widening of existing NH-08 to 4-lane with Paved Shoulder from Champak Nagar to Khayerpur section design Km 242500 to Km 261610 in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618350) (-) (-)	Tripura	12/2023 (09/2024)	09/2026 (03/2027)	920.66 (920.66)	404.6	48.3
1562	Improvement and Widening to 2-lane with paved shoulder of road from design Km 72.000 Pati Chhari to design Km 107.654 Harina Total length 35.654 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-4 (NHIDCL) (618367) (-) (-)	Tripura	01/2024 (12/2024)	12/2026 (06/2027)	726.90 (726.90)	100.25	9.5
1563	Improvement and Widening to 2-lane with paved shoulder of road from design Km 36.000 Rangamati to design Km 72.000 Pati Chhari Total length 36.000 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-3 (NHIDCL) (618368) (-) (-)	Tripura	01/2024 (09/2024)	09/2026 (05/2027)	670.90 (670.90)	183.24	14.7
1564	Improvement and Widening to 2-lane with paved shoulder of road from existing Km 438.170 Khowai Chowmuhani to existing Km 439.410 South Pulinpur of NH-08 and from design Km 0.000 South Pulinpur to design Km 36.00 near Rangamati of NH 208 on Khowai Teliamura- Harina section Total length 37.24 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-2 (NHIDCL) (618369) (-) (-)	Tripura	01/2024 (09/2024)	09/2026 (03/2027)	657.21 (657.21)	301.86	60.7
1565	Improvement and Widening to 2-lane with paved shoulder of road from Km 101.300 to km 127.319 Total Length 26.019 Km i.e. the Khowai Teliamura-Amarpur-Harina-Sabroom section of NH 208 in the state of Tripura on EPC under JICA ODA Loan Phase VI Package-1 (NHIDCL) (618370) (-) (-)	Tripura	01/2024 (07/2024)	07/2026 (04/2027)	431.78 (431.78)	265.36	63.15
1566	Rehabilitation and up-gradation of road from design km 25.250 to km 36.460 Total length 11.210 km of Kailashahar-Kurti Bridge section on NH-208A to 2-lane with paved shoulder on EPC basis under NHO Package-III- Balance Work (NHIDCL) (618385) (-) (-)	Tripura	02/2020 (09/2024)	03/2026 (03/2026)	174.43 (174.43)	67.1	53.14
1567	Melaghar-Srimantapur section on NH-08 Spur from Km 23 to Km 34.500 11.5 Km and overlay from Km 20.30 to Km 22.00 1.7 Km Total Length 13.2 Km (NHIDCL) (618411) (-) (-)	Tripura	01/2023 (05/2023)	11/2024 (10/2026)	195.95 (195.95)	95.54	72.48
1568	Construction of 4-Lane with paved shoulder Agartala bypass Western side, length 25.402 km connecting NH-8 near Amtali to NH-108B near Lembuchhera in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618417) (-) (-)	Tripura	03/2023 (03/2024)	03/2027 (03/2027)	2026.05 (2026.05)	462.34	9.2
1569	Rehabilitation and upgradation to four lane road from km 70.500 to km 78.600 of NH-92 under EPC mode in the State of Uttar Pradesh (MoRTH) (617963) (-) (-)	Uttar Pradesh	01/2022 (01/2025)	01/2027 (01/2027)	296.02 (351.78)	75.38	39
1570	Widening to Four Lane rigid pavement configuration from Km 90.00 to Km 100.800 on NH-96 Km 42.0 to Km 53.300 as per new NH-330,design length of 11.300 km under EPC mode in the state of Uttar Pradesh. (MoRTH) (617964) (-) (-)	Uttar Pradesh	12/2022 (11/2024)	11/2026 (11/2026)	309.63 (309.63)	41.92	31.09
1571	Balance work of Construction of Ring Road for Raebareli City on eastern side of NH-24B Phase-1 on EPC mode. (MoRTH) (618009) (-) (-)	Uttar Pradesh	12/2019 (10/2020)	04/2022 (12/2026)	319.96 (347.80)	0	95
1572	Construction of Balrampur bypass with 2L flexible pavement configuration from km.223.000 of NH-330 to km.328.300 of NH-730 under EPC mode (MoRTH) (618054) (-) (-)	Uttar Pradesh	12/2022 (08/2024)	02/2026 (12/2026)	515.69 (515.69)	128.55	56
1573	Construction of Pratapgarh Bypass Extension connecting NH-31 to NH-330 on EPC mode in the State of Uttar Pradesh. (MoRTH) (618055) (-) (-)	Uttar Pradesh	10/2022 (01/2024)	06/2025 (09/2026)	225.17 (225.17)	66.96	78
1574	Improvement and Up-gradation to two Lane with Paved Shoulder Configuration from existing km. 420.00 Shohratgarh to km. 454.00 Uska Bazar of NH-730 in the state of Uttar Pradesh EPC basis (MoRTH) (618056) (-) (-)	Uttar Pradesh	01/2022 (03/2024)	09/2025 (12/2026)	509.65 (484.42)	120.57	62
1575	Construction of Shohratgarh Bypass on NH-730 under EPC mode in the State of Uttar Pradesh (MoRTH) (618057) (-) (-)	Uttar Pradesh	10/2022 (11/2023)	05/2025 (12/2026)	189.31 (189.31)	31.42	54

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1576	Widening & Strengthening of section from Bharthana chowk to Kodarkoot km.0.00 to km.40.00 of NH-91-A on EPC mode (MoRTH) (618063) (-) (-)	Uttar Pradesh	03/2020 (03/2023)	09/2024 (12/2026)	262.37 (343.77)	115.38	94
1577	Construction of Amethi bypass Part-II at km.30.050 of NH-931 under EPC mode in the state of Uttar Pradesh (MoRTH) (618066) (-) (-)	Uttar Pradesh	12/2022 (02/2025)	02/2027 (02/2027)	283.86 (283.86)	38.69	48
1578	Rehabilitation & Up-gradation from design Km. 0.000 to Km. 69.280 of NH-931 Pratapgarh - Amethi - Gauriganj -Musafirkhana to two lane with paved shoulder on Engineering, Procurement & Construction EpC mode in the State of Uttar Pradesh (MoRTH) (618067) (-) (-)	Uttar Pradesh	05/2023 (11/2025)	11/2027 (11/2027)	1086.30 (1086.30)	24.29	9.32
1579	Construction of two lane with paved shoulder from existing Km.0.000 to Km.55.610 design km. 0.000 to km. 54.048 of NH-124D (MoRTH) (618075) (-) (-)	Uttar Pradesh	12/2021 (02/2024)	02/2026 (03/2027)	840.93 (773.58)	210.11	77
1580	Construction of Mariahu Bypass with four lane paved shoulder configuration Km. 53.540 to Km.59.200 of NH-135A on EPC mode in the state of Uttar Pradesh (MoRTH) (618081) (-) (-)	Uttar Pradesh	03/2023 (02/2024)	02/2026 (12/2026)	438.24 (362.39)	81.45	55
1581	Widening & Upgradation to four lane configuration from Km.34.900 Bhadohi to km.73.134 Jaunpur of NH-135A on EPC mode (MoRTH) (618082) (-) (-)	Uttar Pradesh	03/2021 (11/2022)	05/2024 (09/2026)	395.62 (392.03)	0	95
1582	Improvement and upgradation to two lane with paved shoulder configuration from existing km 90.00 to 130.00 Design length 39.15 of NH-227A near Sikriganj to Barhalganj in the State of UP on EPC Mode. (MoRTH) (618111) (-) (-)	Uttar Pradesh	08/2021 (12/2023)	06/2025 (08/2026)	403.36 (345.34)	142.17	96
1583	Improvement and up-gradation of NH-227B 84 Kosi Parikrama Marg Package I, from km 228.920 Jagarnathpur to Km 235.960/0.000 MakhaudaDham to Km 29.000 Sarpur in the State of Uttar Pradesh on EPC basis (MoRTH) (618112) (-) (-)	Uttar Pradesh	03/2022 (05/2025)	11/2026 (05/2027)	912.50 (912.50)	8.72	8
1584	Improvement and up-gradation of NH-227B 84 Kosi Parikrama Marg Package III, from Km.47.800 Gosaiganj to Km.73.300 Bikapur in the State of Uttar Pradesh on EPC basis. (MoRTH) (618113) (-) (-)	Uttar Pradesh	03/2022 (05/2025)	11/2026 (05/2027)	587.97 (587.97)	80.16	50.72
1585	Improvement and up-gradation of NH-227B 84 Kosi Parikrama Marg PackageV, from Design Km.140.960 Patranga to Km.160.200 Bahuvan Madar Majha on EPC mode in the State of Uttar Pradesh (MoRTH) (618114) (-) (-)	Uttar Pradesh	03/2023 (02/2026)	08/2028 (08/2028)	1192.33 (1192.33)	0	4
1586	Improvement and Up-gradation from Km. 73.300 Bikapur to Km.140.960 Patranga of NH-227B 84 Kosi Parikrama Marg to 2LPS along with Parikrama Path (MoRTH) (618116) (-) (-)	Uttar Pradesh	11/2022 (01/2026)	01/2028 (01/2028)	1679.75 (1679.75)	172.89	40.45
1587	Rehabilitation and upgradation from km 51.600 to km 75.700 of NH-321G Nuhkhas to Etah section to two lane with paved shoulder configuration under EPC mode in the State of Uttar Pradesh (MoRTH) (618124) (-) (-)	Uttar Pradesh	01/2022 (02/2024)	08/2025 (11/2026)	343.54 (343.54)	88.97	73
1588	Improvement and up-gradation to 2LPS of NH-227B 84-Kosi Parikrama Marg PackageVI, Design Km 160200 Bahuvan Madar Majha to Km 224040 Jagarnathpur under HAM (MoRTH) (618162) (-) (-)	Uttar Pradesh	05/2023 (01/2026)	01/2028 (01/2028)	2008.70 (2008.70)	0	20
1589	Rehabilitation and Up-gradation from km. 0000 to km.40390 of NH-730S MaharajganjNichloulThuthibari to two lane with paved shoulders in the State of U.P. on Engineering, Procurement & Construction EPC Basis. (MoRTH) (618163) (-) (-)	Uttar Pradesh	03/2023 (06/2024)	12/2025 (12/2026)	809.25 (603.19)	167.84	59.5
1590	Construction of four lane highway with paved shoulder from Km.74.700 to Km.112.950 of NH-731A i/c Yamuna Bridge on HAM in the state of Uttar Pradesh. (MoRTH) (618164) (-) (-)	Uttar Pradesh	03/2022 (06/2024)	06/2026 (08/2026)	1141.67 (1157.31)	0	100
1591	Construction of 4-lane green field highway from Km. 35.000 to Km. 49.155 of NH-731A with paved shoulders on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) (618166) (-) (-)	Uttar Pradesh	01/2022 (10/2023)	10/2025 (07/2026)	697.66 (697.66)	0.04	100
1592	Widening to four lane with paved shoulder from Design Km.49.200 to Km.89.285 of NH-731B on EPC mode in the state of Uttar Pradesh (MoRTH) (618168) (-) (-)	Uttar Pradesh	03/2022 (01/2024)	01/2026 (01/2027)	917.91 (965.30)	134.41	56

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1593	Construction of Two Lane with paved shoulder highway from Design Ch.0.000 to Ch.49.200 of NH-731B on EPC Mode (MoRTH) (618169) (-) (-)	Uttar Pradesh	03/2022 (11/2023)	11/2025 (09/2026)	640.18 (602.76)	270.82	98
1594	Rehabilitation and upgradation of Salon - Jais - Jagdishpur Road section of NH-931A, from design Chainage km 0.000 to km 5.740 to four lane divided carriageway and from design Chainage km 5.740 to km 53.500 to two lane with paved Total length km 53.500 along with One time improvement in 04 no's of realigned/bypassed built-up areas in a total length of 9.732 km in the state of Uttar Pradesh on EPC mode (MoRTH) (618187) (-) (-)	Uttar Pradesh	05/2023 (10/2025)	10/2027 (10/2027)	947.15 (947.15)	26.64	9.06
1595	Construction of 6-lane bridge on Ganga on NH-96 and its approaches in Phaphamau Allahabad on EPC mode (MoRTH) (618233) (-) (-)	Uttar Pradesh	07/2018 (02/2021)	02/2024 (09/2026)	1948.25 (1465.41)	0.43	91
1596	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Bewar-naer Karri village section Km0.00 to Km30.00 Pakage-I of NH-92 in state of Uttar Pradesh undergreen national Highway Corridor Project GNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618240) (-) (-)	Uttar Pradesh	04/2020 (09/2022)	03/2024 (08/2026)	236.47 (236.47)	0	100
1597	Construction of Basti Ring Road Phase-I with 4L configuration for Basti City in the state of Uttar Pradesh on HAM mode (MoRTH) (618243) (-) (-)	Uttar Pradesh	12/2022 (06/2025)	06/2027 (06/2027)	1138.72 (1138.72)	0.07	36.67
1598	Construction of Raebareli Ring Road Phase-2 with four Lane configuration for Raebareli City in the state of Uttar Pradesh on Hybrid Annuity Model HAM basis (MoRTH) (618244) (-) (-)	Uttar Pradesh	03/2022 (05/2025)	05/2027 (05/2027)	1273.72 (1273.72)	0	55
1599	Construction of 4 lane Mirzapur bypass including bridge over river Ganga from km 0.000 to km 15.000 of NH 135A in the State of Uttar Pradesh on HAM Mode. (MoRTH) (618247) (-) (-)	Uttar Pradesh	03/2024 (01/2026)	01/2029 (01/2029)	1708.62 (1708.62)	0	7
1600	Widening to 4 lane from km. 139.00 to km 179.20 of NH-135A Pkg-III Jaunpur Akbarpur section and Akbarpur bypass on Hybrid Annuity Mode in the state of Uttar Pradesh. (MoRTH) (618248) (-) (-)	Uttar Pradesh	05/2023 (01/2026)	01/2028 (01/2028)	1653.15 (1653.15)	0	22
1601	Widening to 4 lane from km. 108.50 to km 139.00 of NH-135A Pkg-II Jaunpur Akbarpur section on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) (618249) (-) (-)	Uttar Pradesh	03/2023 (03/2025)	03/2027 (03/2027)	1511.57 (1511.57)	0	40
1602	Improvement and Up-gradation to two Lane with Paved Shoulder/Four Lane configuration from existing Km 130.000 to Km 191.000 design km 131.500 to Km 188.735, Design length 57.235 Km of NH-227A near Barhalganj to Mehrauna Ghat in the state of Uttar Pradesh on Hybrid Annuity Model HAM basis (MoRTH) (618252) (-) (-)	Uttar Pradesh	01/2022 (11/2024)	05/2027 (05/2027)	974.19 (1344.61)	1.2	58
1603	Construction of Salempur bypass to 4LPS from km 64.000 of NH-727A Km 171.00 of Sonauli Balia Marg, old SH-01, near Mahadahan Chauraha to km 61.500 of NH-727B Km 178.500 of Sonauli Balia Marg, old SH-01, near near Ahirauli Village under Hybrid Annuity Mode HAM in the State of Uttar Pradesh (MoRTH) (618260) (-) (-)	Uttar Pradesh	03/2022 (11/2025)	11/2027 (11/2027)	1348.06 (1348.06)	0	35
1604	Construction of Deoria Bypass from existing Km. 27.140 to existing Km. 46.780 Design Km. 49.109 on NH727A Design length 21.969 Km. to four lane with paved shoulder configuration under Hybrid Annuity Mode HAM in the State of Uttar Pradesh (MoRTH) (618262) (-) (-)	Uttar Pradesh	03/2023 (08/2025)	07/2027 (07/2027)	1734.70 (1734.70)	0	10
1605	Rehabilitation and Up-gradation to 2LPS from Km. 0.000 to Km. 7.800 and Km. 35.400 to Km. 52.345 Design length 24.745 Km., except Bihar portion of NH-727B Tamkuhiraj to Bihar Border and Bihar Border to Majhauri on EPC mode in the State of Uttar Pradesh (MoRTH) (618263) (-) (-)	Uttar Pradesh	03/2023 (01/2025)	07/2026 (08/2026)	701.02 (701.02)	156.4	81.18
1606	Widening and Strengthening to two Lane with Paved Shoulder/Four Lane with paved shoulder configuration from km. 61.500 of NH-727B near Nawalpur km 178.500 of Sonauli Balia Marg, Old SH-01 i.e. end point of Salempur Bypass to km. 106.495 of NH-727B near Sikanderpur under EPC mode (MoRTH) (618264) (-) (-)	Uttar Pradesh	05/2023 (12/2025)	05/2028 (05/2028)	2061.86 (2061.86)	222.2	41
1607	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Miranpur Katra to radhaita section of NH-730CKm.114.000 to Km 137.250package-III in state of Uttar Pradesh undergreen national Highway Corridor ProjectGNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618265) (-) (-)	Uttar Pradesh	04/2020 (07/2022)	07/2024 (12/2026)	172.50 (169.56)	0.13	92

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1608	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Bewar-Allahaganj- section of NH-730C Km.0.000 to Km 52.770 pakage-I in state of Uttar Pradesh undergreen national Highway Corridor Project GNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618266) (-) (-)	Uttar Pradesh	04/2020 (11/2022)	11/2024 (09/2026)	325.24 (340.16)	0	99
1609	Widening/Upgradation to four lane configuration of Shahjahanpur-Bisalpur section from km 0.00 to km 47.026 of NH-731K on Hybrid Annuity Mode in the state of Uttar Pradesh. (MoRTH) (618267) (-) (-)	Uttar Pradesh	03/2023 (05/2026)	05/2028 (05/2028)	1590.20 (1590.20)	0	0
1610	6L Elevated Kanpur - Lucknow Exeressway Pkg-1 from Km. 10980 to Km. 28500 (NHAI) (618499) (-) (-)	Uttar Pradesh	12/2021 (02/2023)	07/2025 (08/2026)	1972.94 (1943.27)	770.81	100
1611	Construction of 4L Connector from Delhi Meerut Expressway Km 50.000 of Pkg IV to Km 8.520 of NH-235 Pkg-5 (NHAI) (618500) (-) (-)	Uttar Pradesh	09/2021 (03/2022)	03/2024 (08/2026)	1081.39 (1116.19)	455	78
1612	Varanasi Ring Road Pkg-II connecting Sandaha Village km 11.70 / NH-29 with Revasa Village km 818.80 / NH-2 (NHAI) (618529) (-) (-)	Uttar Pradesh	12/2017 (02/2019)	02/2022 (10/2026)	1991.71 (1832.66)	1751.26	96.86
1613	Construction of Ring Road around Kanpur from Ch.68.650 to Ch.93.209 Jarkala to Pakari Package-IV in State of Uttar Pradesh. (NHAI) (618536) (-) (-)	Uttar Pradesh	02/2023 (12/2024)	06/2027 (06/2027)	1603.53 (1192.16)	266.36	39.2
1614	Construction of Ring Road around Kanpur from Km.000 to Km. 23.325 Chachendi Sachendi I to Maharajpur Package-I (NHAI) (618537) (-) (-)	Uttar Pradesh	01/2023 (12/2023)	06/2026 (02/2027)	1753.75 (1311.70)	479.56	62.15
1615	Construction of Ring Road around kanpur from Ch.51.200 to Ch. 68.650 Badarka to Harbanch-Uchti Pkg-III (NHAI) (618538) (-) (-)	Uttar Pradesh	09/2023 (01/2025)	07/2027 (07/2027)	1792.68 (1126.75)	284.83	34.8
1616	Construction of Ring Road Kanpur from Ch. 32.090 to Ch.51.200 Transganaga to Sathara Package-II B (NHAI) (618539) (-) (-)	Uttar Pradesh	08/2024 (03/2025)	09/2027 (09/2027)	1089.41 (1106.92)	54.19	20.4
1617	Construction of Ring Road around Kanpur from Ch.23.325 to Ch.32.090 Chaudhariya to Transganga Package-IIA (NHAI) (618540) (-) (-)	Uttar Pradesh	08/2024 (11/2025)	10/2027 (04/2028)	1089.41 (977.45)	252.18	49.85
1618	Construction of left out portion of Agra Inner Ring Road connecting village Deori to NH-44 village Bad from Km. 0.000 to Km. 7.772 (NHAI) (618554) (-) (-)	Uttar Pradesh	07/2022 (03/2023)	09/2024 (08/2026)	879.26 (787.58)	629.11	94
1619	4L Green Field Northern East side Gorakhpur Bypass 26.616 Kms starting from NH-29E Chainage 83.308 and end at NH-28 Chainage 285.100 (NHAI) (618566) (-) (-)	Uttar Pradesh	02/2023 (01/2024)	01/2026 (01/2027)	1973.98 (1244.44)	1035.52	73.78
1620	4/6L of Northern Ayodhya Bypass starting Km. 112.540 and ending Km. 139.928 north of existing NH-27 part-1 and part-2 south of NH-27 from km 0.000 to km 5.000. (NHAI) (618567) (-) (-)	Uttar Pradesh	08/2024 (07/2025)	01/2028 (01/2028)	2289.34 (1834.25)	285.67	33.53
1621	4/6L Southern Ayodhya Bypass from Km 5.000 to Km 37.172 starting near Km. 112.540 and ending at Km. 153.281 of NH-27 (NHAI) (618568) (-) (-)	Uttar Pradesh	08/2024 (03/2025)	09/2027 (09/2027)	2541.13 (1983.05)	318.53	39.5
1622	4 -Laning of MP/UP Border to Kabarai section of NH-34&35 from km 197.000 to km 242.991 Length 45.991 Km Sagar-Kabrai Package-5 under Bharat Mala Pariyojana EC in MP & UP on HAM (NHAI) (618669) (-) (-)	Uttar Pradesh	10/2022 (02/2025)	02/2027 (02/2027)	1632.93 (1425.43)	574.07	61.77
1623	4 lanning of Aligarh Palwal section from km 0.00 to km 46.39 package -1 from khereshwar junction-kurana of NH33D , including khair & jattari bypass in the state of UP on HAM mode (NHAI) (618690) (-) (-)	Uttar Pradesh	03/2024 (03/2025)	03/2027 (03/2027)	1663.38 (1685.69)	590.53	21.25
1624	DL/UP Border - EPE Crossing Pkg-02 (NHAI) (618710) (-) (-)	Uttar Pradesh	09/2020 (05/2021)	11/2023 (08/2026)	2002.79 (1889.78)	1739.72	100
1625	6L access Controlled Greenfield Highway from Gogwan Jalalpur Shamli to Ranipur Barsi Saharanpur of Shamli -Ambala section Package-I Design Ch. Form km 00.600 to km 45.500 (NHAI) (618722) (-) (-)	Uttar Pradesh	06/2022 (05/2023)	05/2025 (03/2027)	1843.59 (1247.55)	759.32	68.2

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1626	4L Spur of Meerut-Garh-Mukteshwar section connecting NH-119 and NH-58 bypassing Meerut Town of NH 709 A (NHAI) (618761) (-) (-)	Uttar Pradesh	10/2021 (02/2023)	02/2025 (08/2026)	991.89 (977.73)	865.93	96.98
1627	Four laning of Agra-Aligarh Section from Km. 0.000 Junction of NH-34 Aligarh Km 144.60 to Km. 28.000 near Asroi village in Hathras of NH-509 Package-I (NHAI) (618768) (-) (-)	Uttar Pradesh	06/2024 (03/2026)	03/2028 (11/2028)	1309.08 (1309.08)	310.08	3.96
1628	4L of Bareilly-Pilibhit-Sitarganj from Km. 0.000 to Km. 32.500 of NH-30 Pkg-1 (NHAI) (618782) (-) (-)	Uttar Pradesh	02/2023 (03/2024)	03/2026 (03/2027)	1394.14 (1394.14)	622.58	64.12
1629	4L of Sonauli - Gorakhpur (NHAI) (618798) (-) (-)	Uttar Pradesh	12/2021 (03/2023)	03/2025 (09/2026)	2555.50 (2275.43)	1328.22	89
1630	2L PS Greenfield bypass laiganj ajhara, mohanganj and Raniganj on Raebareli - Jaunpur Section Design km 0.00 to Km 53177 of NH-31 (NHAI) (618842) (-) (-)	Uttar Pradesh	12/2024 (06/2026)	06/2028 (12/2026)	1280.68 (1280.68)	199.56	0
1631	Construction of two lane with paved shoulders bypass to Mungrabadshapur town starting from near Kodahu at Km 47/225 of NH-319D and ending near Nauwadandi at Km 219/720 of NH-31 under NHO in the state of Uttar Pradesh on EPC mode (NHAI) (618843) (-) (-)	Uttar Pradesh	02/2025 (09/2025)	03/2027 (03/2027)	197.60 (165.28)	54.54	22.79
1632	Construction of Underpass beneath airport runway on NH-31 old NH-56 for proposed expansion of runway of Babatpur Airport Varanasi (NHAI) (618848) (-) (-)	Uttar Pradesh	02/2025 (09/2025)	09/2027 (09/2027)	649.44 (649.44)	0.09	22
1633	Improvement and Up-Gradation of Existing Road to 4L PS from Km 123.650 to 175.080, from Start of Shahabad Bypass to End of Hardoi bypass of NH 731 Pkg-2B (NHAI) (618856) (-) (-)	Uttar Pradesh	09/2022 (11/2023)	11/2025 (03/2027)	1101.79 (1212.26)	519.69	68.8
1634	Improvement and Up-Gradation of Existing Road to 4L PS from Km 88.750 to 123.650, from Start of Shahjahanpur Bypass to start of Shahabad bypass of NH 731Pkg.-2A (NHAI) (618858) (-) (-)	Uttar Pradesh	09/2022 (01/2024)	01/2026 (03/2027)	955.34 (955.34)	369.94	70.56
1635	Improvement and Up-Gradation of Existing Road to 4L PS from Km 229.070 to 260.800, End of Hardoi District to Lucknow Ring road of NH 731 Pkg-4 (NHAI) (618859) (-) (-)	Uttar Pradesh	09/2021 (10/2022)	10/2024 (08/2026)	575.66 (553.61)	390.09	99.33
1636	Four Lane Highway from Chandan Nagar Existing Km. 59.025 of NH 530B/Design Km. 179.5000 to Bareilly BypassStartExisting Km. 59.025 of NH 530B/Design Km. 218.000 Section of NH 530B, in the State of Uttar Pradesh on HAM Mode under NHO (NHAI) (618866) (-) (-)	Uttar Pradesh	12/2024 (11/2025)	11/2027 (11/2027)	2077.00 (1112.44)	486.09	34.5
1637	4L Kasganj-Badaun Section from Km. 123.100 to Km. 179.500 Pkg-III of NH530B (NHAI) (618867) (-) (-)	Uttar Pradesh	03/2023 (05/2025)	05/2027 (12/2027)	2009.11 (1936.61)	590.99	40
1638	4L from Devinagar Bypass End Existing Km. 208.000 of NH 530B/Design Km. 66.000 to Kasganj Bypass End Existing Km.150.100 of NH 530B/ Design Km. 123.100 of NH 530B (NHAI) (618868) (-) (-)	Uttar Pradesh	03/2023 (06/2024)	06/2026 (12/2026)	2289.52 (2223.71)	1027.01	77
1639	Construction of 4/6 lane Highway of Southern Bareilly Bypass, starting at Ch. 237000 of NH 530 near Jhumka chauraha, Dhantiya village and ending at Ch. 267000 of NH 30 near Invertis University including Trumpet Interchange (NHAI) (618869) (-) (-)	Uttar Pradesh	12/2024 (12/2025)	06/2028 (06/2028)	1122.02 (1869.59)	620.25	16.4
1640	Construction of Four Lane Highway form Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package I [from Hridaipur km 0.000 to Shahapur km 42.500] on EPC Mode in the state of Uttar Pradesh. (NHAI) (618883) (-) (-)	Uttar Pradesh	10/2022 (07/2023)	07/2025 (08/2026)	1706.47 (1579.59)	1447.58	100
1641	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package II [from Shahapur km 42.500 to Pindari km 78.150] on EPC Mode in the state of Uttar Pradesh. (NHAI) (618884) (-) (-)	Uttar Pradesh	10/2022 (10/2023)	10/2025 (08/2026)	1493.65 (1311.44)	775.96	98.4
1642	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package IV [from Buxur Spur of length km 17.270 on EPC Mode in the state of Uttar Pradesh. (NHAI) (618885) (-) (-)	Uttar Pradesh	10/2022 (06/2023)	06/2025 (11/2026)	617.88 (549.02)	286.1	90.57
1643	Varanasi Gorakhpur Section Packege IV from km. 149.540 to km. 215.160 Mau- Gorakhpur (NHAI) (618893) (-) (-)	Uttar Pradesh	04/2015 (04/2017)	10/2019 (08/2026)	2966.63 (3475.65)	3455.15	97.35

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1644	4L Greenfield Western Side spur of Rampur-Rudrapur Section from Km 0.000 to Km 13.700 connecting NH-24 to NH-87 bypassing rampur town (NHAI) (618911) (-) (-)	Uttar Pradesh	12/2021 (05/2023)	11/2024 (02/2027)	646.27 (637.83)	369.67	63.79
1645	4L Behsuma at Km 39.250 Ex. Km 39240 To Bijnor at Km 78.810 Ex. Km 86590 Design Length 39.560 Km of NH-119 Pkg-II (NHAI) (618923) (-) (-)	Uttar Pradesh	03/2023 (05/2024)	05/2026 (12/2026)	2158.20 (2553.12)	1234.06	70.12
1646	2L PS of Najibabad Kotdwar section from 112.575 to Km. 138.635 of NH 119 (NHAI) (618924) (-) (-)	Uttar Pradesh	10/2021 (03/2024)	09/2025 (10/2026)	188.87 (99.20)	51.17	55.9
1647	Bijnor-Kotawali (NHAI) (618925) (-) (-)	Uttar Pradesh	02/2021 (11/2021)	05/2023 (08/2026)	300.58 (334.48)	299.77	99.02
1648	4L of Moradabad-Thakurdwara-Kashipur Section from Km. 0.000 to Km. 38.77 of NH-734 Pkg-II (NHAI) (618927) (-) (-)	Uttar Pradesh	10/2022 (03/2024)	03/2026 (06/2027)	2006.82 (1890.05)	981.64	54.55
1649	4L of Moradabad western side spur connecting NH-734 & NH-24 from Km. 0.000 to Km. 33.200 Pkg-I (NHAI) (618929) (-) (-)	Uttar Pradesh	11/2022 (09/2023)	09/2025 (12/2026)	1841.92 (1843.54)	1132.25	83.06
1650	4 Lane Inner Ring Road around Allahabad City Pkg-2 Prayagraj Southern Bypass 43.200 - 50.860 (NHAI) (618960) (-) (-)	Uttar Pradesh	08/2023 (12/2023)	06/2026 (06/2027)	1377.51 (1007.62)	448.99	44.64
1651	4 Lane Inner Ring Road around Allahabad City Pkg-1 Prayagraj Southern Bypass 34.400 43.200 (NHAI) (618961) (-) (-)	Uttar Pradesh	02/2025 (12/2025)	12/2027 (12/2027)	775.94 (498.97)	70.02	24.55
1652	6L access control Greenfield highway of Vill-Khyawari to Vill-Latifpur at Saharanpur Bypass from Km. 82.000 to Km. 119.790 Pkg-4 (NHAI) (618968) (-) (-)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (08/2026)	1428.19 (1439.35)	1394.63	99.24
1653	6L access control Greenfield highway of Vill-Lohadda to Vill-Karaunda Mahajan from Km. 27.000 to Km. 56.500 Pkg-2 (NHAI) (618970) (-) (-)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (08/2026)	1335.45 (1335.38)	1253.61	98.06
1654	4L of Najibabad Bypass from Km. 105.423 to Km. 118.373 excluding 2.45 Km. of NH-74 Bypass of NH-119 (NHAI) (619162) (-) (-)	Uttar Pradesh	01/2022 (12/2022)	06/2024 (08/2026)	578.02 (566.90)	440.93	100
1655	6L access controlled Greenfield highway of Junction of EPE Vill.-Mavikalan to Vill.-Lohadda from Km. 0.000 to Km. 27.000 Pkg-1 (NHAI) (619168) (-) (-)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (08/2026)	1602.48 (1497.94)	1423.29	99.29
1656	Construction of Four Lane Gola Flyover at Km 99.850 of NH 730 Major Junction with State Highways -93 of Engineering, Procurement and Construction EPC mode in the State of Uttar Pradesh. (MoRTH) (619194) (-) (-)	Uttar Pradesh	03/2025 (05/2026)	10/2027 (10/2027)	168.05 (168.05)	0	12
1657	6L access-controlled highway from Ganeshpur tonear Mohand of Ganeshpur Dehradun section from Km.0 to Km.8.3 of NH-72A Package-1 (NHAI) (619308) (-) (-)	Uttar Pradesh	11/2020 (10/2021)	10/2023 (08/2026)	836.24 (835.74)	811.86	98.92
1658	Landslide treatment work on NH 58 from Kodyala Km. 266.130 to Devprayag Km. 296.925 10 location under EPC mode in the State of Uttarakhand on EPC Mode (MoRTH) (617888) (-) (-)	Uttarakhand	01/2023 (02/2024)	02/2025 (07/2026)	192.54 (192.54)	0	99
1659	Treatment of landslide zone from location no. 01 to 28 km 62.860 to 152.750 on NH-12509 in the State of Uttarakhand under EPC mode in NHO Annual Plan 2022-23 (MoRTH) (617889) (-) (-)	Uttarakhand	11/2022 (06/2023)	06/2024 (07/2026)	192.22 (192.22)	0	98.5
1660	Construction of Champawat Bypass with two lane with paved shoulder configuration starting from existing chainage 121.700 to existing chainage 129.450 Design Length 9.847 of NH-125 in District-Champawat in the state of Utrrakhand on EPC mode. (MoRTH) (617890) (-) (-)	Uttarakhand	02/2025 (01/2026)	12/2027 (-)	220.89 (220.89)	0	8.5
1661	Construction of 2 lane with paved shoulder of Kund Bypass from Design Km 35.130 to Km 47.700 existing Km 33.130 to Km 41.260 of NH-109 in the State of Uttarakhand (MoRTH) (617929) (-) (-)	Uttarakhand	02/2018 (05/2018)	05/2020 (12/2026)	247.41 (247.41)	114.6	73.5

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1662	Construction of Rudraprayag tunnel of length 900.30 MTR including approaches and one major bridge on river Alaknanda connecting NH-107/old-109 to NH-07old-58 on EPC mode in the state of Uttarakhand. (MoRTH) (617967) (-) (-)	Uttarakhand	02/2021 (01/2023)	07/2025 (07/2026)	251.88 (251.88)	108.94	99
1663	Construction & Widening Including Augustmuni Bypass Ch-16.545 to Ch - 19.890 to 2L/PS from Km 16.545-Km 33.130 & 45.980 -57.975 Augustmuni to Kund & Guptkashi to Sitapur on NH 109 in UK (MoRTH) (617968) (-) (-)	Uttarakhand	03/2017 (02/2018)	02/2020 (03/2024)	418.89 (418.89)	426.18	95
1664	Rehabilitation and upgradation of 2 lane with paved shoulder from existing km. 195.175 to km. 220.000 Design Chainage km71.300 to Km. 95.947 Excluding existing chainage Km 200.300 to Km 202.400 Design chainage Km 76.400 to Km 78.400 on Dharasu to Yamunotri Road of NH- 134 Old NH-94 (MoRTH) (617974) (-) (-)	Uttarakhand	05/2025 (10/2025)	04/2028 (-)	344.73 (344.73)	0	53.74
1665	Widening to 2 Lane from Existing Chainage Km 74.700 Km 100.660 Design Chainage Km 53.365 to Km 78.785 on NH- 507 in the State of Uttarakhand. (MoRTH) (618039) (-) (-)	Uttarakhand	01/2024 (10/2025)	04/2028 (-)	346.82 (346.82)	0	31.75
1666	Rehabilitation and Upgradation to Two lanes with Paved Shoulders configuration and Strengthening from Km 175.00 to Km 196.00 Gumkhal to Satpuli of NH-119 New NH-534 in the State of Uttarakhand under NHO Annual Plan 2021-22 under EPC mode (MoRTH) (618040) (-) (-)	Uttarakhand	03/2022 (01/2025)	01/2027 (-)	452.81 (452.81)	0	42
1667	Rehabilitation and upgrading to two lanes with paved shoulders and Strengthening of Kotdwar-Pauri-Srinagar road section from Km 232.00 to 274.470 on NH-119 New 534 Paidul to Srinagar in the State of Uttarakhand on EPC Mode under NHO Annual Plan 2021-22. (MoRTH) (618041) (-) (-)	Uttarakhand	02/2022 (12/2025)	12/2027 (-)	299.31 (299.31)	0	2
1668	Rehabilitation and up-gradation to 2-lane configuration of Bageshwar to Kangarchina road from km 129.600 to Km 161.600 Existing Chainage 136.00 to Km 169.00 of NH-309Ain the State of Uttarakhand Package-IV under NHO Annual Plan 2021-22 (MoRTH) (618119) (-) (-)	Uttarakhand	03/2022 (08/2024)	02/2027 (-)	472.23 (472.23)	0	67
1669	Widening to 2-lane with Hard Shoulder configuration of Mana Ch. 0.00 to Mana Pass Ch. 50.987 road on NH-07 under Bharatmala Pariyojna in the state of Uttarakhand under Annual Plan 2022-23 length 50.987 (MoRTH) (618207) (-) (-)	Uttarakhand	10/2022 (10/2023)	10/2027 (10/2028)	573.96 (573.96)	0	21.03
1670	Construction & up gradation of existing road to 2-Lane with paved shoulder from existing chainage km 468000 to km 489350 Design Chainage km 465150 to km 471500 of NH-07 Old NH-58 including Joshimath bypass on EPC mode in the state of Uttarakhand Length 6.35 km (MoRTH) (618209) (-) (-)	Uttarakhand	03/2022 (09/2022)	09/2025 (08/2027)	258.85 (258.85)	0	37.23
1671	Rehabilitation and upgradation of Askot-Lipulekh on EPC Basis for Phase-I Existing Km 72.00 to 107.620 Design Chainage Km 21330 to Km 56935 under Project Hirak of BRO in the state of Uttarakhand under Bharatmala Pariyojna Phase-I on EPC Mode Length-35.605 Km CA No EPC/MORT&H/HRK/01/2021-22 (MoRTH) (618210) (-) (-)	Uttarakhand	09/2020 (12/2021)	12/2023 (07/2026)	603.92 (603.92)	0	81.17
1672	Improvement/construction of 2-lane with paved shoulder of Askote Llipulekh road from Tawaghat village to Budhi village design km. 56935 to km 95748 and from end of Tunnel portal to Kali Mandir design km 113828 to km. 133078 [total design length 58.063 km] under project Hirak of BRO in the state of Uttarakhand under Bharatmala Pariyojna on EPC Mode (MoRTH) (618211) (-) (-)	Uttarakhand	05/2022 (11/2024)	11/2026 (07/2027)	649.60 (649.60)	0	37.19
1673	STABILIZATION OF LAND SLIDE AND SLOPE PROTECTION AT KM 11.00 TO KM 11.08, 29,730 KM TO 30,060 KM, 30,400 KM TO 31,060 KM, 34,750 KM TO 35,300 KM, 38,950 KM TO 39,030 KM & 39,460 KM TO 39,540 KM TWO LOC CLUBBED, KM 40,400 TO KM 40,650, KM 43,500 KM 43,680, 52,460 RISHIKESH - DHARASU ROAD NH-94 ON EPC MODE IN THE STATE OF UTTARAKHAND. NOSE OF LAND SLIDE - 12 NOS (MoRTH) (618212) (-) (-)	Uttarakhand	01/2024 (10/2025)	04/2027 (-)	197.26 (197.26)	0	22
1674	Rehabilitation and Upgradation of road Rishikesh Dharasu Old NH-94 with 2-lane with paved shoulder from km 76.000 to km 110.000 Design Chainage from km 74.733 to km 107.347 32.614 km including construction of Kamand re-alignment from existing Chainage Km 105.200 to Km 108.600 design chainage Km 103.436 to Km 105.949 - total length 2513 mtrs and land slide treatment work between design chainage Km 73.800 to Km 74.00 200m on EPC mode under improvement to NH connectivity to Chardham in (MoRTH) (618213) (-) (-)	Uttarakhand	03/2018 (01/2019)	01/2021 (07/2026)	273.76 (273.76)	0	96.46

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1675	Rehabilitation and upgradation to 2 lane / 2 lane with paved shoulder configuration for design chainage km 107.347 to km 129.208 & km 133.878 to km 138.570 existing chainage km 110.000 to km 133.020 & km 137.330 to km 142.028 and land slide treatment at existing km 138.500 Design chainage km 134.970 of NH -94 on EPC mode under improvement to NH connectivity to Chardham in the state of Uttarakhand. (MoRTH) (618214) (-) (-)	Uttarakhand	03/2018 (01/2019)	07/2021 (06/2024)	346.50 (346.50)	0	100
1676	Rehabilitation & upgradation of existing road to 2-lane with hard shoulder from Joshimath km 0.00 to Saraihotra km 29.725 road on NH-107B under Bharatmala Pariyojna on EPC mode in the state of Uttarakhand (MoRTH) (618218) (-) (-)	Uttarakhand	10/2022 (05/2023)	05/2025 (03/2027)	338.38 (338.38)	0	80
1677	Upgradation to 2-lane with Hard shoulder configuration of Suraihotra Ch. 29.725 km to Malari Ch. 60.550 km road on NH- 107B under in the state of Uttarakhand. (MoRTH) (618219) (-) (-)	Uttarakhand	10/2022 (05/2024)	05/2026 (12/2026)	292.76 (292.76)	0	76.67
1678	Construction, Operation & Maintenance of 2-L Bi-directional Silkyara Bend- Barkot Tunnel with escape passage including approaches Tunnel-4.531 & Approach road- 0.328 on Dharasu-Yamunotri section b/w Chainage 25.400km and 51.00km falling along NH-134 Old NH-94 on EPC mode (NHIDCL) (618390) (-) (-)	Uttarakhand	03/2018 (07/2018)	07/2022 (03/2027)	1383.78 (1383.78)	842.44	76.03
1679	Construction for Mitigation Measures of 5 Nos. Landslides, 05 No. Sinking Zones and 01 No. Bridge from Ch. 450.00 to Ch. 468.00 18 Km. Length on NH-07 Package-III (NHIDCL) (618391) (-) (-)	Uttarakhand	12/2023 (06/2024)	12/2025 (02/2027)	250.33 (250.33)	100.93	88.12
1680	Construction for Mitigation Measures of 5 Nos. Landslides, 5 Nos. Sinking Zones in between Ch. 433.00 to 450.00 BANERPANI VILLAGE on NH-07 on EPC mode in the state of Uttarakhand Package-2 (NHIDCL) (618392) (-) (-)	Uttarakhand	12/2023 (12/2024)	06/2026 (01/2027)	259.64 (259.64)	0	68.45
1681	Construction for Mitigation Measures of 10 Nos. Landslides, 01 No. Sinking Zones and 1 No. of Minor Bridge in between at Ch. Km 368.00 to Km 433.00 on NH-07 on EPC Mode in Uttarakhand Package-1 (NHIDCL) (618393) (-) (-)	Uttarakhand	12/2023 (06/2024)	12/2025 (02/2024)	216.68 (216.68)	117.83	99.97
1682	4L of Haridwar Nagina section Design Ch. LME from km 13.829 to km 17.110 & km 26.077 to km 27.508 and Design Ch. RME from km 13.839 to km 17.120 & km 26.078 to km 27.509 of EUP mitigation measures on NH74 (NHAI) (618875) (-) (-)	Uttarakhand	11/2021 (08/2022)	02/2024 (12/2026)	183.92 (142.11)	119.67	70.42
1683	Construction of 4-lane connectivity to Banbasa ICP at India Nepal border from NH-09 old NH-125 Sitarganj-Tanakpur at Km 40.00 near Jagbuda bridge under Bharatmala Priyojana of NH-109D on EPC mode in the State of Uttarakhand (NHAI) (619142) (-) (-)	Uttarakhand	06/2022 (03/2023)	09/2024 (04/2027)	216.97 (237.01)	213.92	75.24
1684	Upgradation and 4L of Haridwar Bypass from Km 0.000 Km 188.100 of NH-58 to Km. 15.100 Km 5.100 of NH 74 PKG-1 (NHAI) (619155) (-) (-)	Uttarakhand	11/2021 (10/2022)	10/2024 (11/2026)	1602.89 (1423.89)	770.27	80.36
1685	Realignment of Rudrapur-Kathgodam Section of NH-87 New NH-109 From Design Chainage 000 Existing Chainage Km.54050 To Design Chainage 7875 Existing Chainage Km.61550 Due To Proposed Expansion Of Pantnagar Airport in the state of Uttarakhand. (NHAI) (619221) (-) (-)	Uttarakhand	08/2025 (06/2026)	09/2027 (09/2027)	252.97 (252.97)	0.14	0
1686	4L Medinipur to Ballupur from Km. 458.65 to Km. 487.65 of NH-07Pkg-2 (NHAI) (619292) (-) (-)	Uttarakhand	03/2022 (02/2023)	02/2025 (08/2026)	1092.90 (1072.50)	739.13	93.9
1687	Construction of 4 Lane Access Controlled Bypass for Dehradun on NH307 from Design Chainage km 0050 Jhajra on NH-07 to Design Chainage km 12220 Asharori on EPC Mode in the State of Uttarakhand under NHO (NHAI) (619293) (-) (-)	Uttarakhand	12/2023 (04/2025)	04/2027 (04/2027)	715.97 (337.11)	191.78	62.79
1688	Road Safety Improvement of existing four lane section of Dehradun-Lal Tappar-Nepali Farm Section of NH-7 and Nepali Farm-Motichur NH-34 on EPC Mode in Uttarakhand under NHO. (NHAI) (619294) (-) (-)	Uttarakhand	05/2025 (02/2026)	08/2028 (08/2028)	720.67 (388.19)	10.86	5.13
1689	Four/Six laning of Bhaniyawala-Jollygrant-Rishikesh spur section of NH-07 from Km. 0.000 to Km 19.780 (NHAI) (619295) (-) (-)	Uttarakhand	02/2023 (12/2025)	11/2027 (11/2027)	742.43 (664.92)	13.35	0

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1690	Construction of additional major Bridge with 4- lane configuration of length 1.48 km on NH-60 NH-14 over River Kangshabati from Km. 117.770 to Km 119.250 and additional major Bridge with 4- lane configuration of length 0.900 km on NH-60 NH-14 over River Shilabati from Km. 173.220 to Km 174.120 in the district of Paschim Medinipur of West Bengal under Annual Plan for FY 2023-24 on EPC mode. Job No 014-W8-2023-24/527 . (MoRTH) (617893) (-) (-)	West Bengal	11/2023 (11/2025)	05/2028 (05/2028)	304.83 (304.83)	0.15	0
1691	Construction or 4 lane Raniganj Bypass of length 5.261 km on NH-60 new NH-14 from km 273.00 of NH to km 478.18 of NH-2 New NH 16 in paschim Bardhaman, West Bengal in EPC Mode- reg. Job No. 014-WB-2022-23/514 (MoRTH) (617894) (-) (-)	West Bengal	03/2023 (03/2024)	03/2026 (05/2027)	410.83 (410.83)	184.64	67.28
1692	Construction of ROB and its approaches in lieu of LC No. 10/B/T at Km 307.050 of NH-60. (MoRTH) (617931) (-) (-)	West Bengal	03/2016 (08/2023)	08/2025 (10/2027)	155.87 (138.57)	20.6	17.08
1693	Construction of new road at the missing link portion of NH-81 along approved alignment between Harishchandrapur and Eastern approach of Kalindri Bridge from Km 46.550 to Km 59.697 in the district of Malda. Job No-081-WB-2015-16/400 (MoRTH) (617960) (-) (-)	West Bengal	08/2016 (11/2016)	11/2018 (10/2026)	271.17 (291.20)	216.61	85.56
1694	Development to 4/6-lanning of NH-31 New NH-10 with both side service roads from km 569.258 to km 581.030 end of AH-02 project on NH- 31 near Shivmandir to Sevoke Army Cantonment in districts of Darjeeling and Jalpaiguri in the state of West Bengal on EPC Mode Job No. 010/WB/2021-22/490 (MoRTH) (618227) (-) (-)	West Bengal	03/2022 (03/2023)	09/2025 (03/2027)	995.04 (1059.20)	590.78	74.98
1695	Construction & upgradation of existing road to 2-lane with paved shoulder including geometric improvement of Kafer- Lava More section from km 40.00 to km 61.100 of NH717-A on EPC under SARDP-NE A in state of West Bengal Pkg-VA (NHIDCL) (618427) (-) (-)	West Bengal	06/2020 (10/2020)	04/2023 (12/2026)	311.02 (273.78)	268.2	95.98
1696	Construction & upgradation of existing road to 2-lane with paved shoulder including geometric improvement of sect. from Pedong bypass to Reshi Border km 79.700 to km 96.254 of NH-717A under SARDP-NE-A on EPC as part of Alternate connectivity to Gangtok Lava More-Reshi Border Pkg-VB (NHIDCL) (618429) (-) (-)	West Bengal	06/2020 (10/2020)	04/2022 (08/2026)	345.38 (395.59)	418.73	97.22
1697	Construction of alternative highway to Gangtok in Sikkim via Bagrakot -Chuikhim-Nimbong -Kafer-Bakhim-Algarah-Rhenock in the State of West Bengal and from Rhenok-Rorathang-Pakyong along with spur from Aritar-Rolep-Menla in the State of Sikkim from Km 0.00 to Km 13.00 of Bagrakot -Kafer section of NH 717A on EPC Mode under Phase-A of SARDP-NE in the State of West Bengal PKG- IVA (NHIDCL) (618430) (-) (-)	West Bengal	03/2018 (10/2019)	04/2022 (08/2026)	402.94 (402.94)	261.9	99.23
1698	Construction of alternative highway to Gangtok in Sikkim via Bagrakot -Chuikhim-Nimbong -Kafer-Bakhim-Algarah-Rhenock in the State of West Bengal and from Rhenok-Rorathang-Pakyong along with spur from Aritar-Rolep-Menla in the State of Sikkim from Km 13.00 to Km 25.60 of Bagrakot -Kafer section of NH 717A on EPC Mode under Phase-A of SARDP-NE in the State of West Bengal PKG- IVB (NHIDCL) (618431) (-) (-)	West Bengal	03/2018 (10/2020)	04/2023 (12/2026)	295.97 (295.97)	255.94	97.73
1699	Binnaguri Bypass-Descoped portion of Ghoshpukur-Dhupguri Section of NH-31Dpkg-1 (NHAI) (618572) (-) (-)	West Bengal	03/2025 (11/2025)	11/2027 (11/2027)	309.99 (306.02)	4.77	3.67
1700	Balance Works of 4L of NH-31D from Km. 113.200 to Km. 154.854 Package-II A Ghoshpukur-Salsalabari Section (NHAI) (618574) (-) (-)	West Bengal	11/2023 (12/2024)	06/2027 (06/2027)	1818.46 (962.31)	461	61.1
1701	6L Elevated Kona Expressway from Km. 0.145 to Km. 7.337 of NH-117 (NHAI) (618808) (-) (-)	West Bengal	03/2023 (06/2024)	12/2026 (12/2027)	1212.56 (1203.11)	433.18	39.99
1702	4 laning of Barasat - Barajaguli Section of NH-12 from Km. 31.000 to Km. 48.679 in the district of North 24 - Parganas (NHAI) (618823) (-) (-)	West Bengal	02/2024 (08/2024)	02/2026 (10/2027)	352.01 (346.39)	97.88	43.52
1703	Development to 4-laning of the de-scoped stretches from Km 115.342 to Km 191.700 of NH-34 in Nadia District 3.962 & Murshidabad District 5.538 pertaining to Krishnagar to Berhampore section of NH-34 New NH-12 , in the state of West Bengal under NHO. (NHAI) (618824) (-) (-)	West Bengal	03/2024 (07/2024)	01/2026 (06/2027)	201.10 (197.74)	64.63	54.79
1704	Bridge over Ganga River at d/s of Farraka Barrage including Approaches connecting Farakka-Raiganj (NHAI) (618825) (-) (-)	West Bengal	08/2018 (12/2018)	12/2021 (09/2026)	622.04 (646.10)	628.08	96.71

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1705	Construction of Dubrajpur Bypass with 4-lane configuration of length 5.676 km on NH-60 new NH-14 from design chainage 0.00 existing km 316.135 on NH-60 to design chainage 5.676 existing km 320.980 on NH-60 in the district of Birbhum, West Bengal under Annual Plan 2022-23 in EPC Mode- reg. Job. No. 014-WB-2022-23/518 (MoRTH) (619004) (-) (-)	West Bengal	03/2023 (12/2025)	12/2027 (12/2027)	560.79 (560.79)	0.31	8
1706	Slope protection and landslide mitigation at 4 vulnerable locations km 1.950 to Km 2.100, km 11.100 to 11.450, km 22.435 to km 22.485 and km 22.610 to km 22.680 within Sevoke-Rangpo section of NH-10 old NH-31A in Darjeeling & Kalimpong district in the State of West Bengal on EPC mode (NHIDCL) (619187) (-) (-)	West Bengal	02/2024 (06/2025)	06/2027 (06/2027)	152.27 (152.27)	21.2	34.47
	Total (993)				945370.67	460544.81	
	Department of Telecommunications						
	Telecommunication						
1707	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance [Erstwhile NICF]) (709859) (-) (-)	Delhi	10/2014 (04/2018)	02/2020 (09/2026)	248.20 (248.20)	237.43	98
1708	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598) (-) (-)	Meghalaya	09/2019 (09/2020)	03/2022 (06/2026)	971.96 (180.46)	167.23	99.84
1709	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase 1 Upgradation (Department of Telecommunications [DoT]) (617413) (-) (-)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	04/2022 (05/2024)	05/2025 (12/2026)	1884.60 (1884.60)	376.8	99.31
1710	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 (Department of Telecommunications [DoT]) (701599) (-) (-)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	05/2018 (09/2021)	03/2023 (11/2026)	1577.57 (604.60)	492.2	89.98
1711	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha (Department of Telecommunications [DoT]) (701602) (-) (-)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	11/2021 (05/2022)	11/2023 (01/2027)	3685.00 (1448.61)	1108.02	81.47
1712	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (09/2026)	1255.49 (276.62)	237.98	99.84
1713	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajastha and Uttar Pradesh (Department of Telecommunications [DoT]) (704495) (-) (-)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	12/2019 (03/2021)	03/2022 (06/2026)	421.65 (228.94)	152.96	99.59
1714	Amended BharatNet Program - KTK, GOA, PY (Department of Telecommunications) (108841) (-) (-)	PAN India	08/2023 (06/2025)	06/2028 (-)	3742.00 (3742.00)	435.31	8.15
1715	Amended BharatNet Program - HR (Department of Telecommunications) (124199) (-) (-)	PAN India	08/2023 (03/2026)	03/2029 (-)	837.00 (837.00)	83.68	0
1716	Amended BharatNet Program - PB (Department of Telecommunications) (171218) (-) (-)	PAN India	08/2023 (02/2025)	02/2028 (-)	1245.00 (1245.00)	0	26.58
1717	Amended BharatNet Program - MP, DD and DNH (Department of Telecommunications) (175860) (-) (-)	PAN India	06/2023 (05/2025)	05/2028 (-)	4943.00 (4943.00)	562.13	8.4
1718	Amended BharatNet Program - WB & ANI (Department of Telecommunications) (210914) (-) (-)	PAN India	08/2023 (02/2025)	02/2028 (-)	1674.00 (1674.00)	223.41	15.13
1719	Amended BharatNet Program - AS (Department of Telecommunications) (240484) (-) (-)	PAN India	08/2023 (03/2026)	03/2029 (-)	832.00 (832.00)	83.16	0
1720	Amended BharatNet Program - OD (Department of Telecommunications) (317725) (-) (-)	PAN India	08/2023 (07/2026)	07/2029 (-)	1713.00 (1713.00)	0	0

All Ongoing Projects

JULY 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1721	Saturation 4G mobile coverage of Uncovered Villages through USOF (Department of Telecommunications [DoT]) (400013) (-) (-)	PAN India	07/2022 (07/2022)	06/2024 (03/2027)	26316.00 (15392.84)	8722.82	87.7
1722	Amended BharatNet Program - J&K, LAD (Department of Telecommunications) (437130) (-) (-)	PAN India	08/2023 (06/2025)	06/2028 (-)	1621.00 (1621.00)	170.05	8.28
1723	Amended BharatNet Program - MGH, MZM, TRP (Department of Telecommunications) (462136) (-) (-)	PAN India	08/2023 (04/2025)	04/2029 (-)	768.00 (768.00)	0	0
1724	Amended BharatNet Program - HP (Department of Telecommunications) (476006) (-) (-)	PAN India	08/2023 (02/2025)	02/2028 (-)	1292.00 (1292.00)	148.93	23.18
1725	BharatNet Phase-II (Department of Telecommunications) (547243) (-) (-)	PAN India	07/2017 (11/2017)	05/2023 (-)	22174.56 (22174.56)	20691.72	93.33
1726	Amended BharatNet Program - KL (Department of Telecommunications) (660056) (-) (-)	PAN India	08/2023 (06/2025)	06/2028 (-)	765.00 (765.00)	94.95	1.63
1727	Amended BharatNet Program - UKD (Department of Telecommunications) (665021) (-) (-)	PAN India	08/2023 (05/2025)	05/2028 (-)	1821.00 (1821.00)	209.87	20.54
1728	4G Services by BSNL (Department of Telecommunications [DoT]) (701593) (-) (-)	PAN India	11/2020 (11/2020)	03/2024 (03/2026)	28466.00 (19592.00)	9165.04	98.56
1729	BharatNet (Department of Telecommunications [DoT]) (706775) (-) (-)	PAN India	07/2017 (10/2011)	08/2023 (03/2019)	61109.00 (12709.00)	48809.69	99.98
1730	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (709856) (-) (-)	PAN India	05/2023 (05/2023)	08/2024 (08/2026)	645.13 (645.13)	407.9	92.1
1731	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. (BSNL) (709857) (-) (-)	PAN India	05/2023 (06/2023)	06/2025 (09/2026)	24544.55 (24544.55)	9165.89	98.56
1732	Amended BharatNet Program - BR (Department of Telecommunications) (914467) (-) (-)	PAN India	08/2023 (03/2025)	03/2028 (-)	1550.00 (1550.00)	222.77	17.76
1733	Amended BharatNet Program - RJ (Department of Telecommunications) (938832) (-) (-)	PAN India	08/2023 (03/2026)	03/2029 (-)	2839.00 (2839.00)	283.93	0
1734	Amended BharatNet Program - SKM (Department of Telecommunications) (946208) (-) (-)	PAN India	08/2023 (06/2026)	06/2029 (-)	160.00 (160.00)	0	0
1735	Amended BharatNet Program - ARP, NGL, MNP (Department of Telecommunications) (976009) (-) (-)	PAN India	08/2023 (06/2025)	06/2028 (-)	1168.00 (1168.00)	123.28	0.61
1736	Amended BharatNet Program - UP (East) (Department of Telecommunications) (222253) (-) (-)	Uttar Pradesh	08/2023 (02/2025)	02/2028 (-)	5008.00 (5008.00)	502	7.65
1737	Amended BharatNet Program - UP (West) (Department of Telecommunications) (708687) (-) (-)	Uttar Pradesh	08/2023 (02/2025)	02/2028 (-)	1917.00 (1917.00)	0	7.2
	Total (31)				207194.71	102879.15	
	Department of Water Resources, River Development & GR						
	Waste & Water						
1738	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616600) (-) (-)	Bihar	10/2017 (03/2022)	02/2025 (12/2026)	413.29 (413.29)	126.67	97
1739	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616611) (-) (-)	Bihar	08/2017 (07/2019)	12/2025 (09/2026)	824.00 (824.00)	403.34	59
1740	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh Patna under Hybrid annuity based PPP mode Namami Gange Programme (NMCGI) (616612) (-) (-)	Bihar	08/2017 (07/2019)	12/2025 (-)	578.89 (578.89)	174.61	55

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1741	Sewer Network, SPS and STP at Begusarai (National Mission for Clean Ganga) (616615) (-) (-)	Bihar	03/2010 (03/2018)	04/2025 (12/2026)	230.06 (230.06)	261.82	97
1742	Sewer Networks, SPS and STP at Hajipur (National Mission for Clean Ganga) (616616) (-) (-)	Bihar	03/2010 (03/2018)	06/2025 (12/2026)	305.19 (305.19)	346.46	95
1743	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme (National Mission for Clean Ganga) (616594) (-) (-)	Uttar Pradesh	05/2020 (04/2023)	04/2025 (12/2026)	842.25 (842.25)	208.64	84
1744	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP (National Mission for Clean Ganga) (616605) (-) (-)	Uttar Pradesh	05/2020 (11/2024)	12/2024 (03/2027)	690.71 (690.71)	34.79	57
1745	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP (National Mission for Clean Ganga) (616604) (-) (-)	West Bengal	05/2018 (12/2021)	03/2025 (08/2026)	154.73 (154.73)	102.04	94
Total (8)					4039.12	1658.37	
Water Resources							
1746	Sardar Gouthu Latchanna Thotapalli Barrage Project (Water Resources-AP) (400100) (-) (-)	Andhra Pradesh	04/2005 (01/2006)	12/2019 (06/2026)	353.05 (1023.24)	879.15	95.88
1747	Gundlakamma project (Water Resources-AP) (400101) (-) (-)	Andhra Pradesh	04/2005 (04/2005)	12/2019 (03/2027)	397.41 (697.39)	624.78	98.3
1748	Polavaram Irrigation Project (Water Resources-AP) (701415) (-) (-)	Andhra Pradesh	01/2009 (11/2009)	04/2022 (03/2026)	10151.04 (55548.87)	27961.55	86.15
1749	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370) (-) (-)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55.44
1750	Kelo Irrigation Project (Water Resources-CT) (400111) (-) (-)	Chhattisgarh	04/2008 (04/2008)	12/2019 (06/2026)	459.97 (727.04)	620.15	73
1751	Kudali Irrigation Project (Department of Water Resources, River Development & GR) (701399) (-) (-)	Chhattisgarh	04/2009 (12/2009)	12/2025 (03/2026)	382.29 (382.29)	249.06	86.31
1752	Sardar Sarovar Project (Narmada and Water Resources, Water Supply and Kalpsar Department-GJ) (701372) (-) (-)	Gujarat	04/1996 (04/1996)	12/2019 (03/2026)	20718.17 (33412.50)	31969.4	93.7
1753	Subernarekha Multipurpose Project, Jharkhand (Department of Water Resources-JH) (701376) (-) (-)	Jharkhand	04/2011 (01/2012)	12/2019 (03/2026)	3807.77 (9579.58)	6040.27	70
1754	Upper Tunga Irrigation Project (Water Resources-KA) (701377) (-) (-)	Karnataka	04/2014 (04/2014)	12/2019 (03/2026)	770.16 (1606.07)	1515.6	99.32
1755	Bargi Diversion Project Phase - IV [km. 154 to km 197] (Water Resources-MP) (400115) (-) (-)	Madhya Pradesh	04/2008 (01/2009)	12/2019 (03/2026)	751.03 (893.35)	814.02	75
1756	Bargi Diversion Project Phase - III [km. 104 to km 154] (Water Resources-MP) (400116) (-) (-)	Madhya Pradesh	04/2007 (04/2007)	12/2019 (12/2026)	1229.15 (1399.70)	2270.96	81.52
1757	Bodwad Parisar Sinchan Yojna (Department of Water Resources-MH) (617422) (-) (-)	Maharashtra	05/2002 (01/2017)	07/2027 (-)	1923.81 (1923.81)	338.91	49.6
1758	Waghur Project (Department of water resources-MH - II) (701383) (-) (-)	Maharashtra	04/1996 (04/1996)	12/2019 (03/2026)	1058.99 (1758.51)	1642.5	89.57
1759	Gosikhurd Project (Department of water resources-MH - II) (701386) (-) (-)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2028)	7196.47 (12770.10)	14439.46	72.65
1760	Aruna Medium Irrigation Project (Department of water resources-MH - II) (701391) (-) (-)	Maharashtra	04/2009 (01/2010)	12/2019 (06/2026)	210.45 (1472.14)	1734.71	100
1761	Lower Pedhi Project (Department of water resources-MH - II) (701396) (-) (-)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2026)	255.97 (1480.70)	3066.05	65

All Ongoing Projects

JULY 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1762	Nardave Medium Irrigation Project (Department of water resources-MH - II) (701398) (-) (-)	Maharashtra	04/2009 (04/2009)	12/2019 (06/2026)	211.46 (781.85)	879.8	75
1763	Thoubal Multipurpose Project (Water Resources Department-MN) (701400) (-) (-)	Manipur	04/1997 (04/1997)	12/2019 (12/2026)	1449.44 (1822.24)	1848.17	99
1764	North Koel Reservoir Project (Department of Water Resources, River Development & GR) (701412) (-) (-)	Multi-States (Bihar, Jharkhand)	08/2017 (01/2021)	03/2021 (06/2027)	1622.27 (2430.76)	345.94	47
1765	Ken-Betwa Linking Development Project (Department of Water Resources, River Development,) (701530) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	NA (03/2022)	03/2029 (-)	21030.00 (21030.00)	8530.86	0
1766	Integrated Anandpur Barrage Project (Water Resources-OR) (603945) (-) (-)	Odisha	04/1997 (01/1998)	12/2019 (06/2026)	567.03 (2990.05)	2810.1	62.85
1767	Subernarekha Project, Odisha (Department of Water Resources, River Development & GR) (701402) (-) (-)	Odisha	12/1995 (01/1998)	12/2019 (03/2026)	3055.88 (7023.19)	8327.62	95.5
1768	Kanupur Irrigation Project (Irrigation and CAD-TG) (701404) (-) (-)	Odisha	04/2003 (01/2004)	12/2019 (06/2026)	989.43 (2301.28)	2804.16	79.5
1769	Relining of Rajasthan feeder and Sirhind Feeder canal (Department of Water Resources-PB) (701410) (-) (-)	Punjab	02/2016 (04/2018)	06/2021 (06/2026)	1441.26 (2462.16)	2364.12	95
1770	Shahpur Kandi Dam Project (Department of Water Resources-PB) (701411) (-) (-)	Punjab	02/2010 (04/2018)	06/2022 (06/2026)	2285.81 (2715.70)	2201.94	88
1771	Sri Ram Sagar Project Stage - II (Irrigation and CAD-TG) (400102) (-) (-)	Telangana	04/1996 (04/2005)	12/2019 (12/2025)	736.13 (949.87)	971.47	97
1772	Indiramma Flood Flow Canal Project (Irrigation and CAD-TG) (400103) (-) (-)	Telangana	04/1996 (01/2006)	12/2019 (12/2026)	1331.30 (5940.09)	4491.08	92
1773	J. Chokka Rao Devadula Lift Irrigation Scheme (Irrigation and CAD-TG) (701405) (-) (-)	Telangana	04/2006 (04/2006)	12/2019 (12/2025)	8200.71 (14730.00)	4841.09	87.7
1774	Madhya Ganga canal Phase-II (Irrigation & Water Resources-UP) (701408) (-) (-)	Uttar Pradesh	04/2008 (04/2008)	12/2019 (12/2025)	1060.67 (4417.21)	4575.74	82.39
1775	Jamrani Dam Multipurpose Project (Irrigation-UK) (613787) (-) (-)	Uttarakhand	10/2023 (11/2023)	06/2029 (-)	2584.10 (2584.10)	1307.15	26.22
Total (30)					96487.38	140510.51	

Note:

1. The completed projects with IDs 617933, 617917, 617944, 617957, 617977, 618006, 618007, 618046, 618062, 618090, 618144, 618181,618167, 618192, 618208, 618220, 618229, 618005, 618023, 618165 and 618179 have not been published in the current month's Flash Report due to inconsistencies in the Cumulative Expenditure data, and they will be published once the data is rectified.

2. Project ID 706775 has been split into 26 sub-projects, including the original project. Currently, 20 projects (1 Original+ 19 sub-projects) are available (706775, 976009, 240484, 914467, 476006, 124199, 437130, 660056, 108841, 462136, 175860, 317725, 171218, 938832, 946208, 665021, 222253, 708687, 210914, and 547243), while the remaining 6 sub-projects will be onboarded later.

3.Projects with Revised Cost Less than Rs. 150 cr may or may not be correct, the data is under reconciliation.



सत्यमेव जयते

Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <https://paimana-proj.mospi.gov.in/>
