



488th ————— *Flash Report on* **Central Sector Infrastructure Projects —————**



Scan the QR code to access
the PAIMANA Portal.

**(₹150 crore
& above)**

JUNE 2026

<https://paimana.mospi.gov.in> @GoIStats f/GoIStats GoIStats Ministry of Statistics & PI



CONTENTS

I.	Overview*	2-4
II.	North Eastern Region	5-6
III.	As per Harmonized Master List (HML) 2022	7-13
IV.	Major Infrastructure Central Ministries & Departments	14-19
V.	Appendix : <i>List of Tables</i>	20 onwards
	Table 1: Ministry-wise Ongoing Projects	
	Table 2: State-wise Ongoing Projects	
	Table 3: Completed Projects	
	Table 4: Newly Added Projects	
	Table 5: Ongoing Projects of North Eastern Region	
	Table 6: All Ongoing Projects	

**Note: This report is web-generated from the PAIMANA portal (<https://paimana-proj.mospi.gov.in>) as of June 2026, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies on the CRIP portal (<https://paimana-crip.mospi.gov.in/home>) latest by 24th July 2026.*





Overview





Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above

JUNE 2026

1847 | 17

Ongoing Projects |
Line Ministries & Departments

₹ 35,61,721

Original Cost
(crores)

₹ 40,54,473

Revised Cost
(crores)

₹ 21,96,664

(54.18% of Revised Cost)
Expenditure
(crores)

130


Commissioned during month

17

Newly Added during month


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

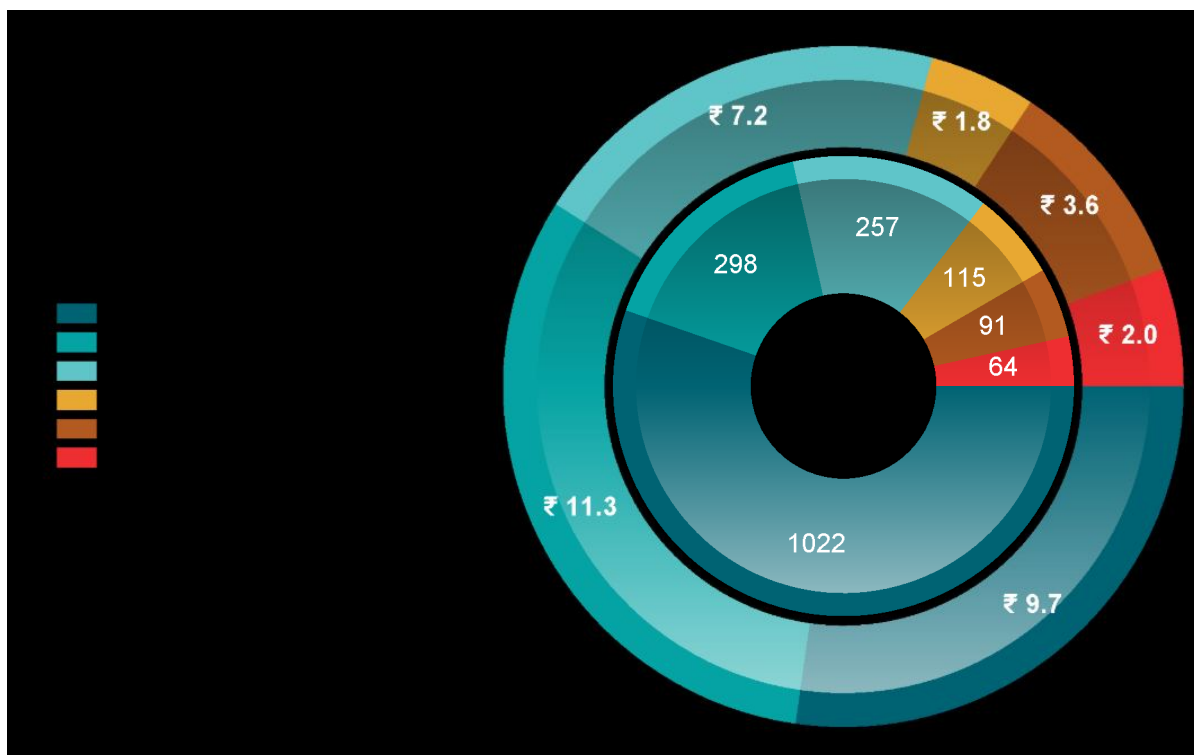


Ministry Comparison : Major Ministries*


[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

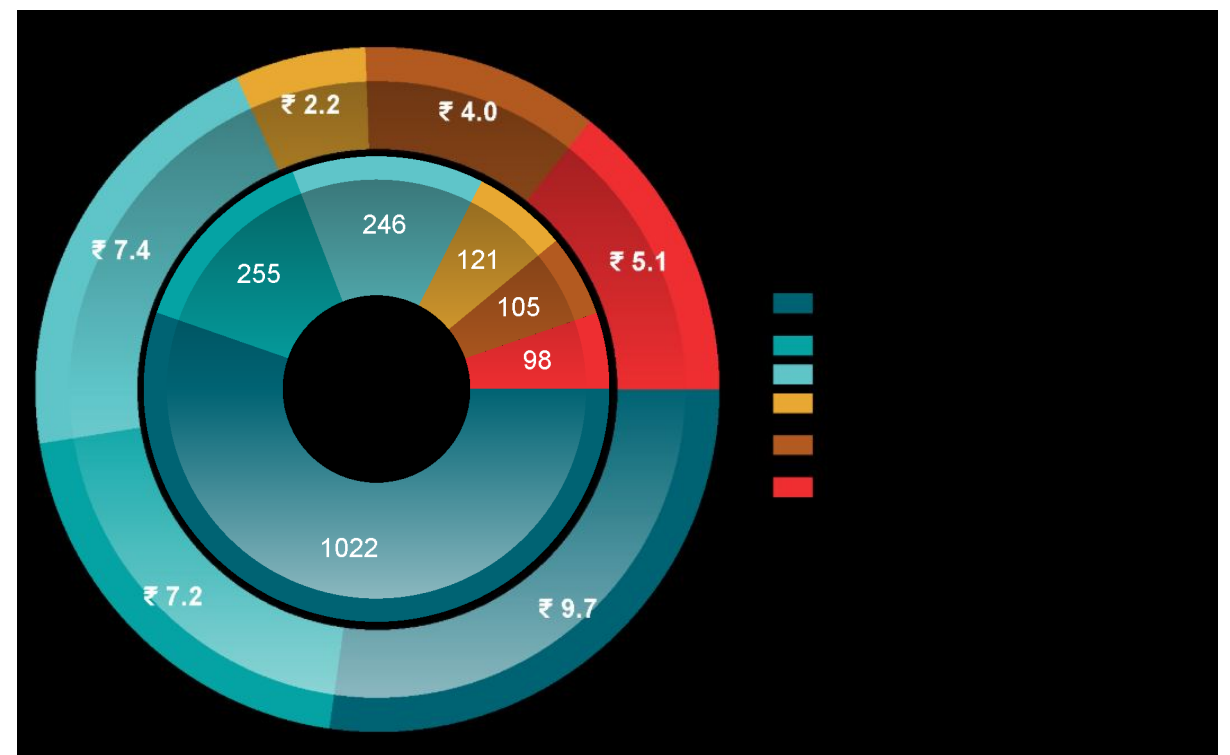

Cost Analytics : Major Sectors*

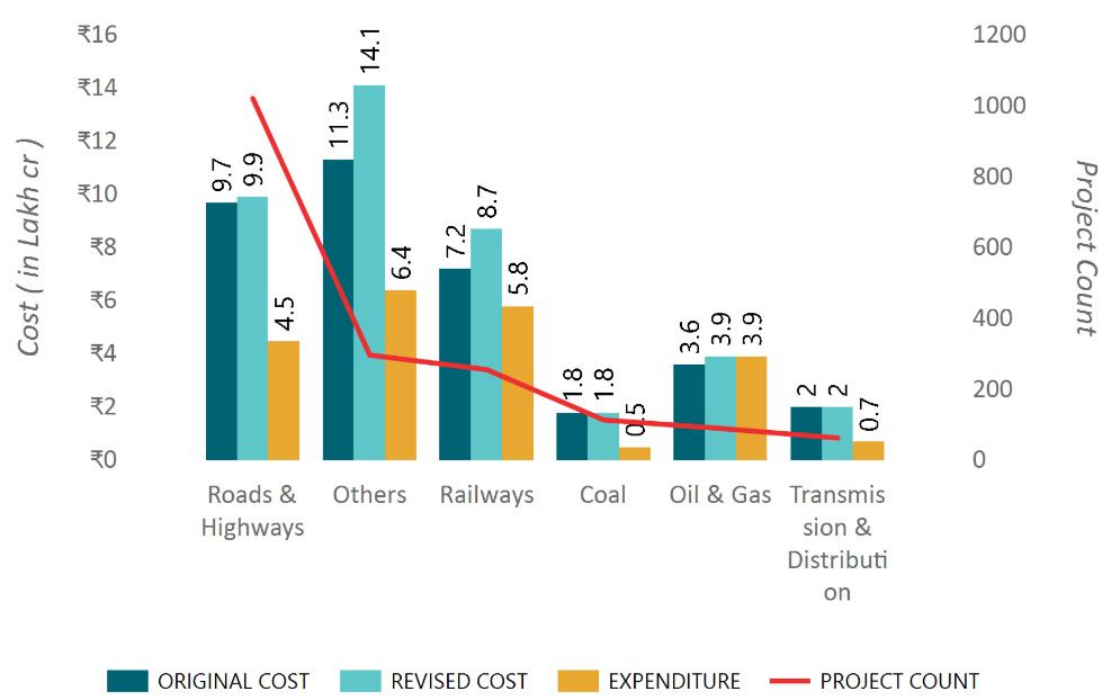


Cost Analytics : Major Ministries*

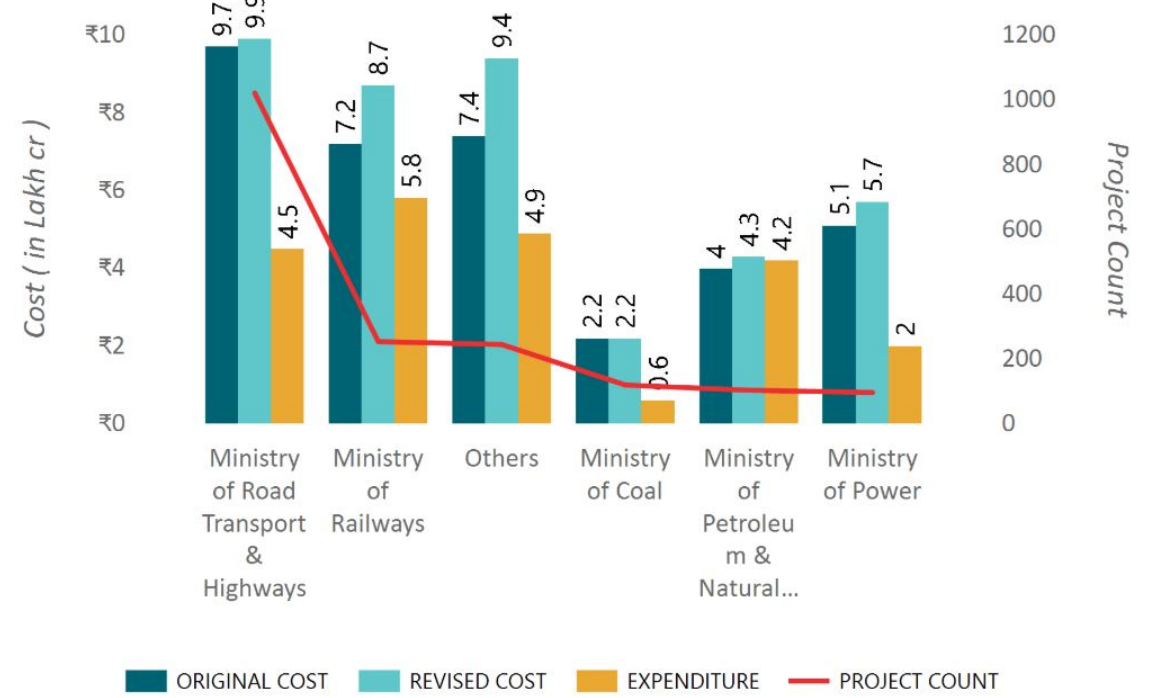


Note: * as per Project Count

Analytics: as per HML

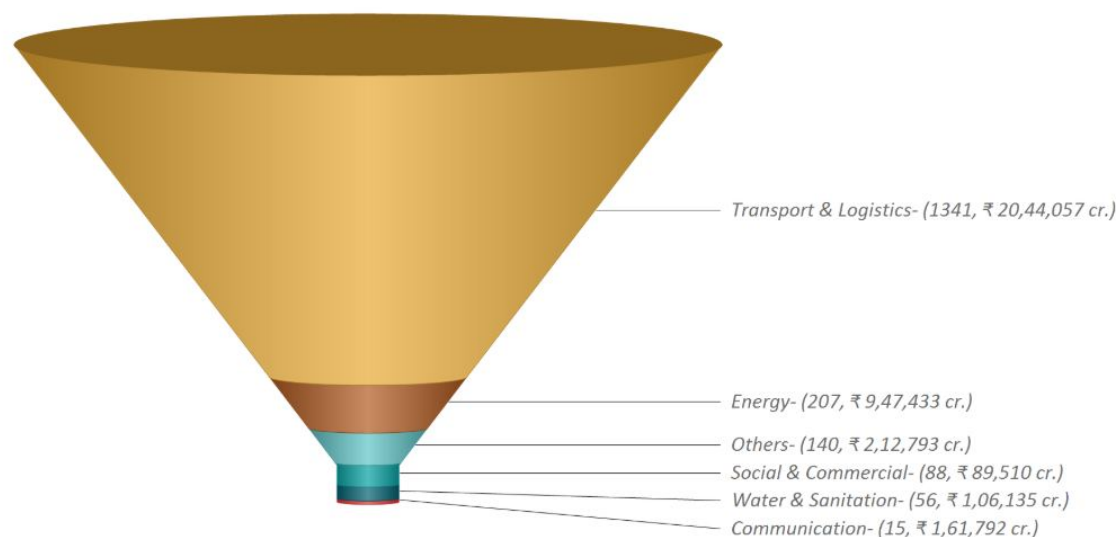


Note: all indicated legends are in format (Project count, Original Cost in crores)

Cumulative Physical & Financial progress (%) : Project count

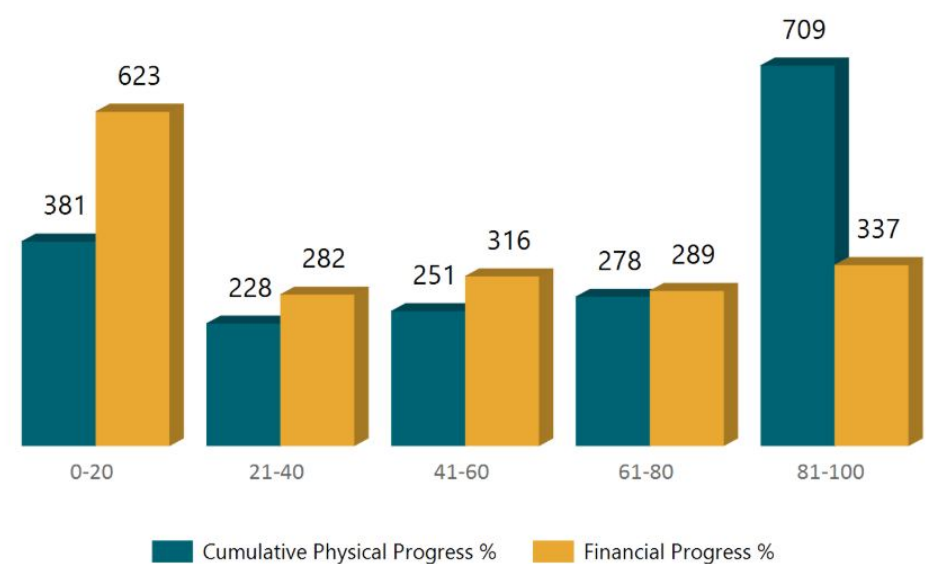




State Comparison : Major States*

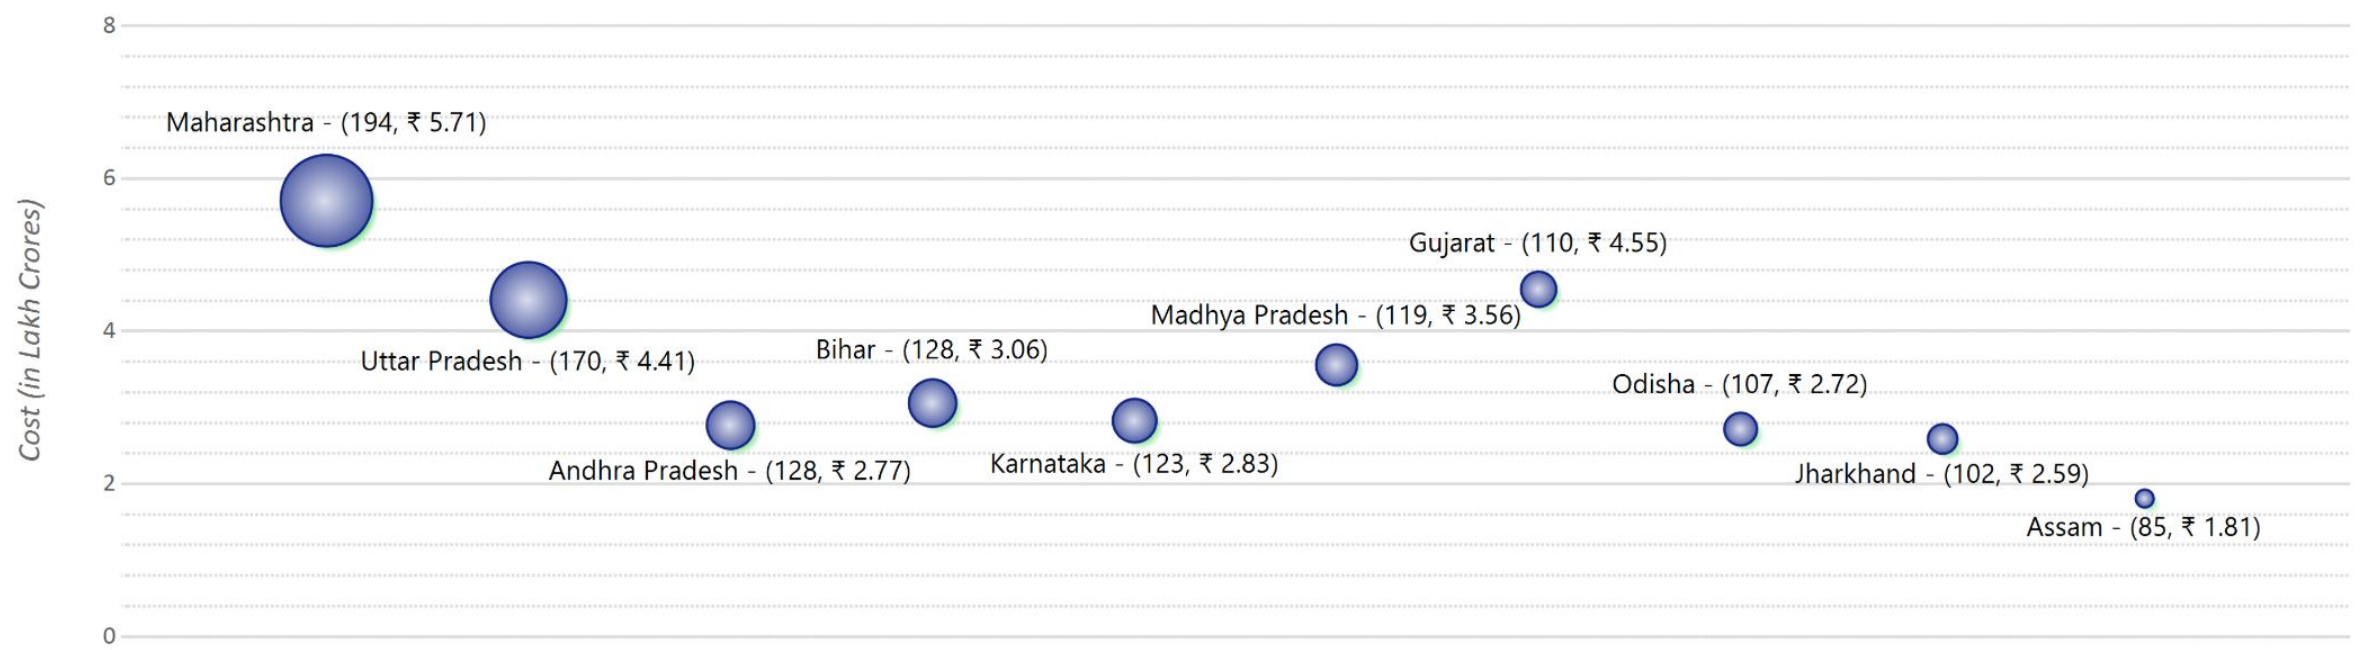


Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count


Ministry-wise Distribution of total 709 projects with reported Physical Progress between 81-100%

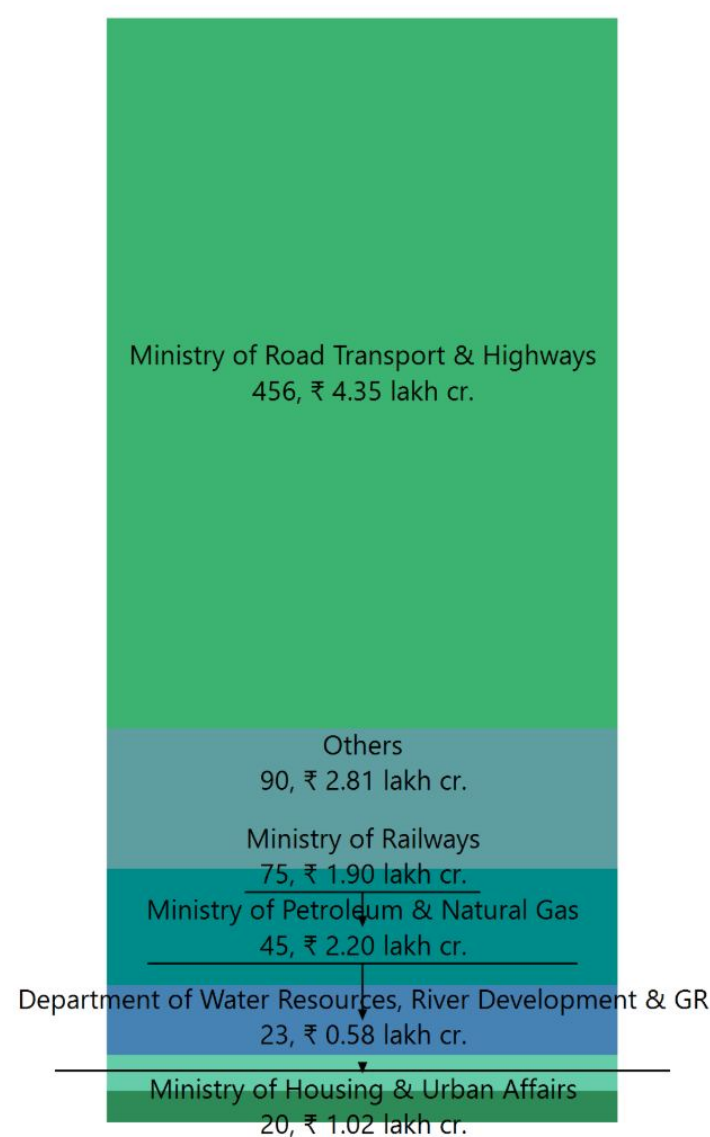

Total Ongoing Projects: Mega & Major

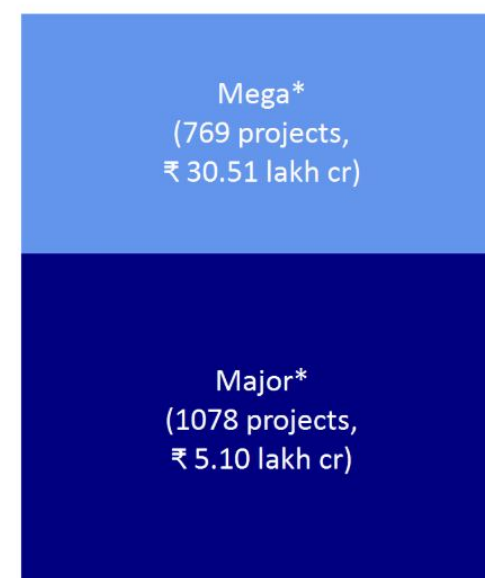

Total North East Region Ongoing Projects: Mega & Major



Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost >= 1000 crore
* Major project if having original cost < 1000 crore

Project volume (nos.)



Change in Project Count : +63%

Total Project value (in lakh crore)



Change in Total Value : +170%

Cumulative Expenditure (in lakh crore)



Change in Expenditure : +261%



North Eastern Region





Special Focus : North Eastern Region

JUNE 2026

218 | 11

Ongoing Projects |
Line Ministries & Departments

₹ 3,40,401

Original Cost
(crores)

₹ 5,22,844

Revised Cost
(crores)

₹ 2,22,601

(42.57% of Revised Cost)
Expenditure
(crores)

13


Commissioned during month

3


Newly Added during month

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

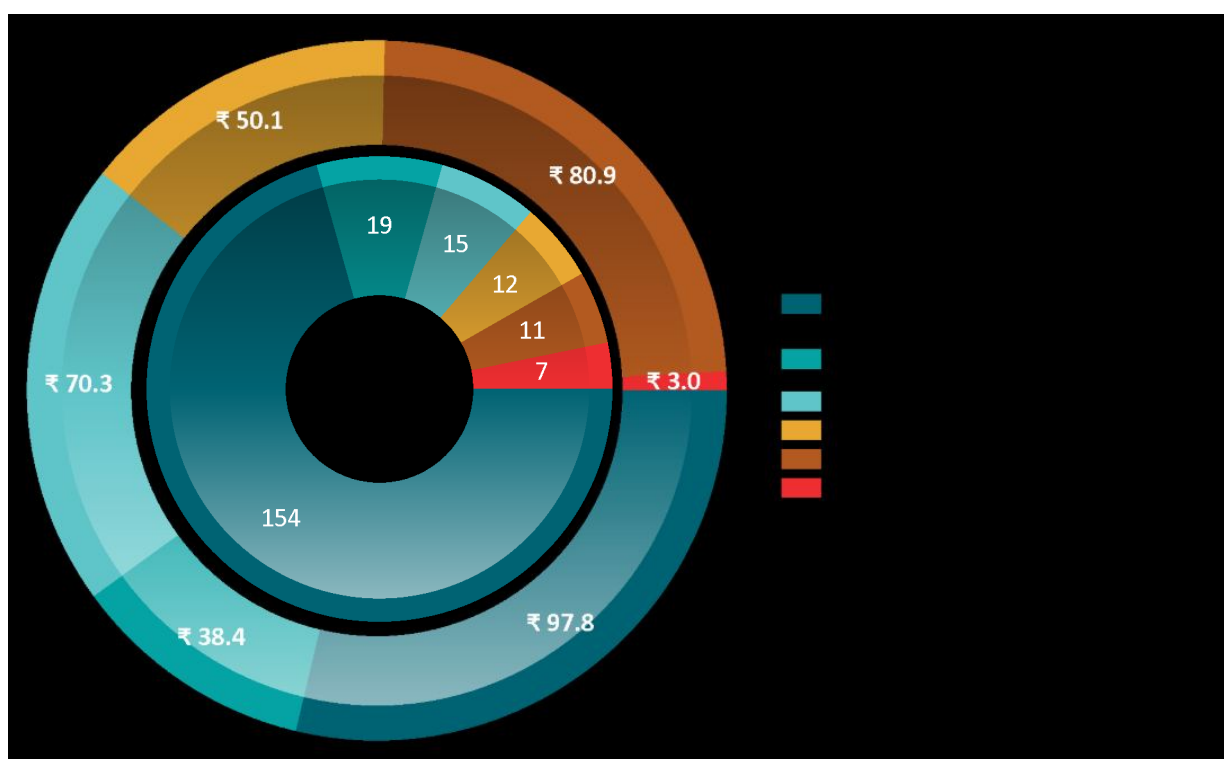


Cost Analytics : Major Ministries*

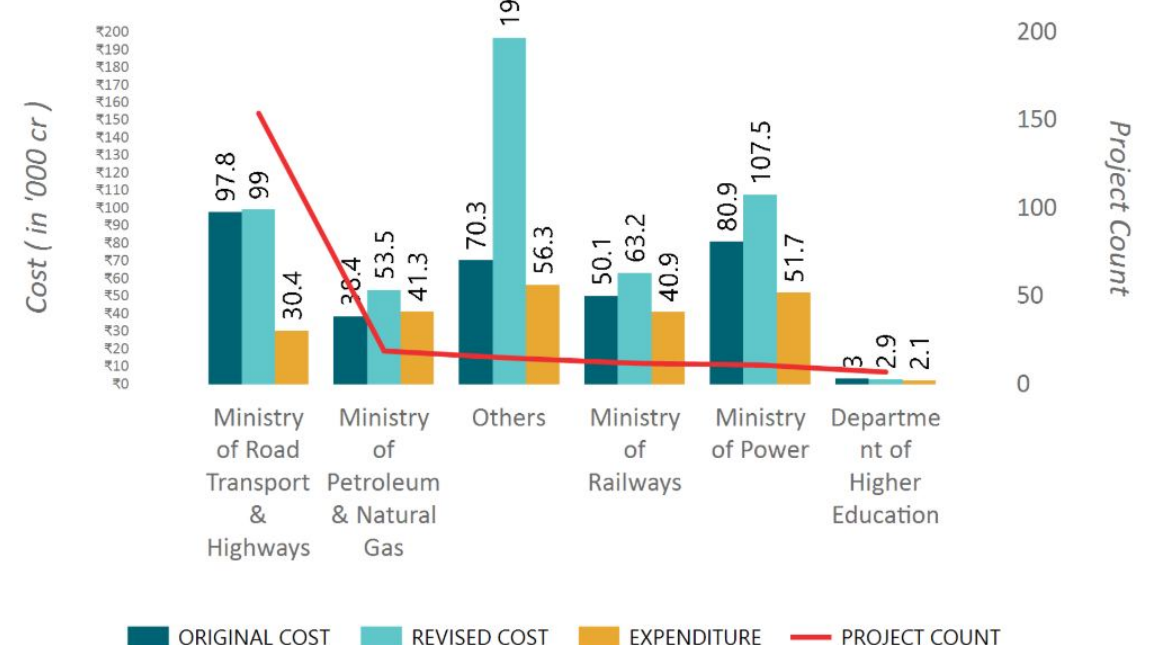


Note: * as per Project Count

Analytics: as per HML

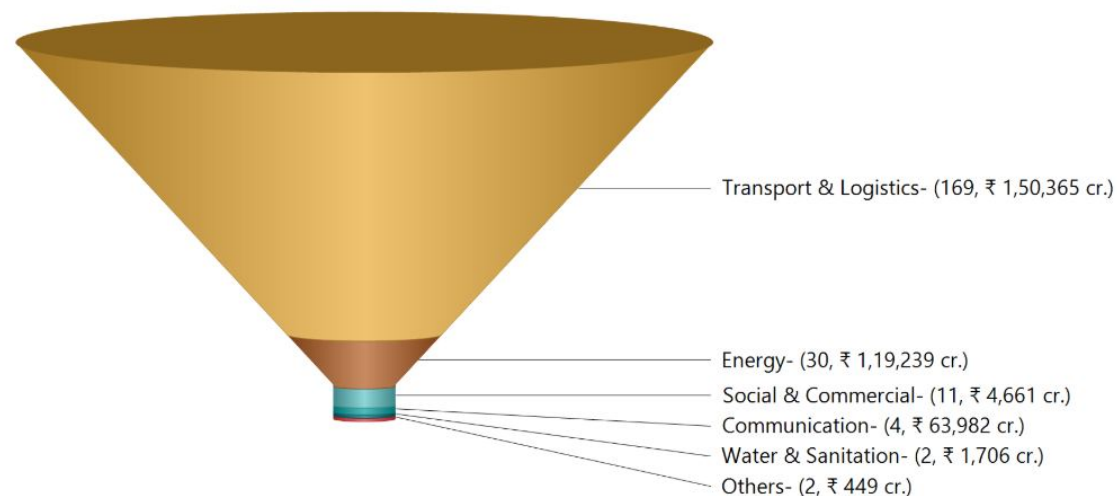


Note: all indicated legends are in format (Project count, Original Cost in crores)

Cumulative Physical & Financial progress (%) : Project count

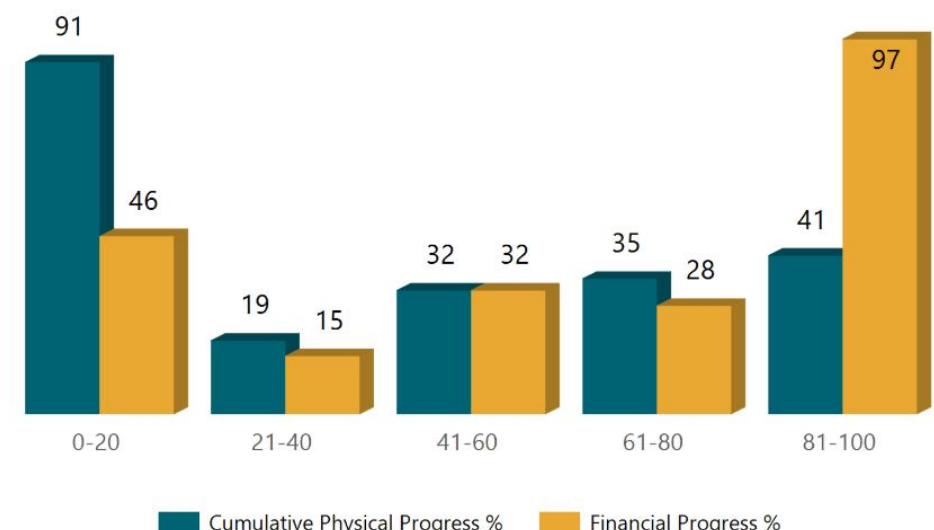

State Comparison : All States

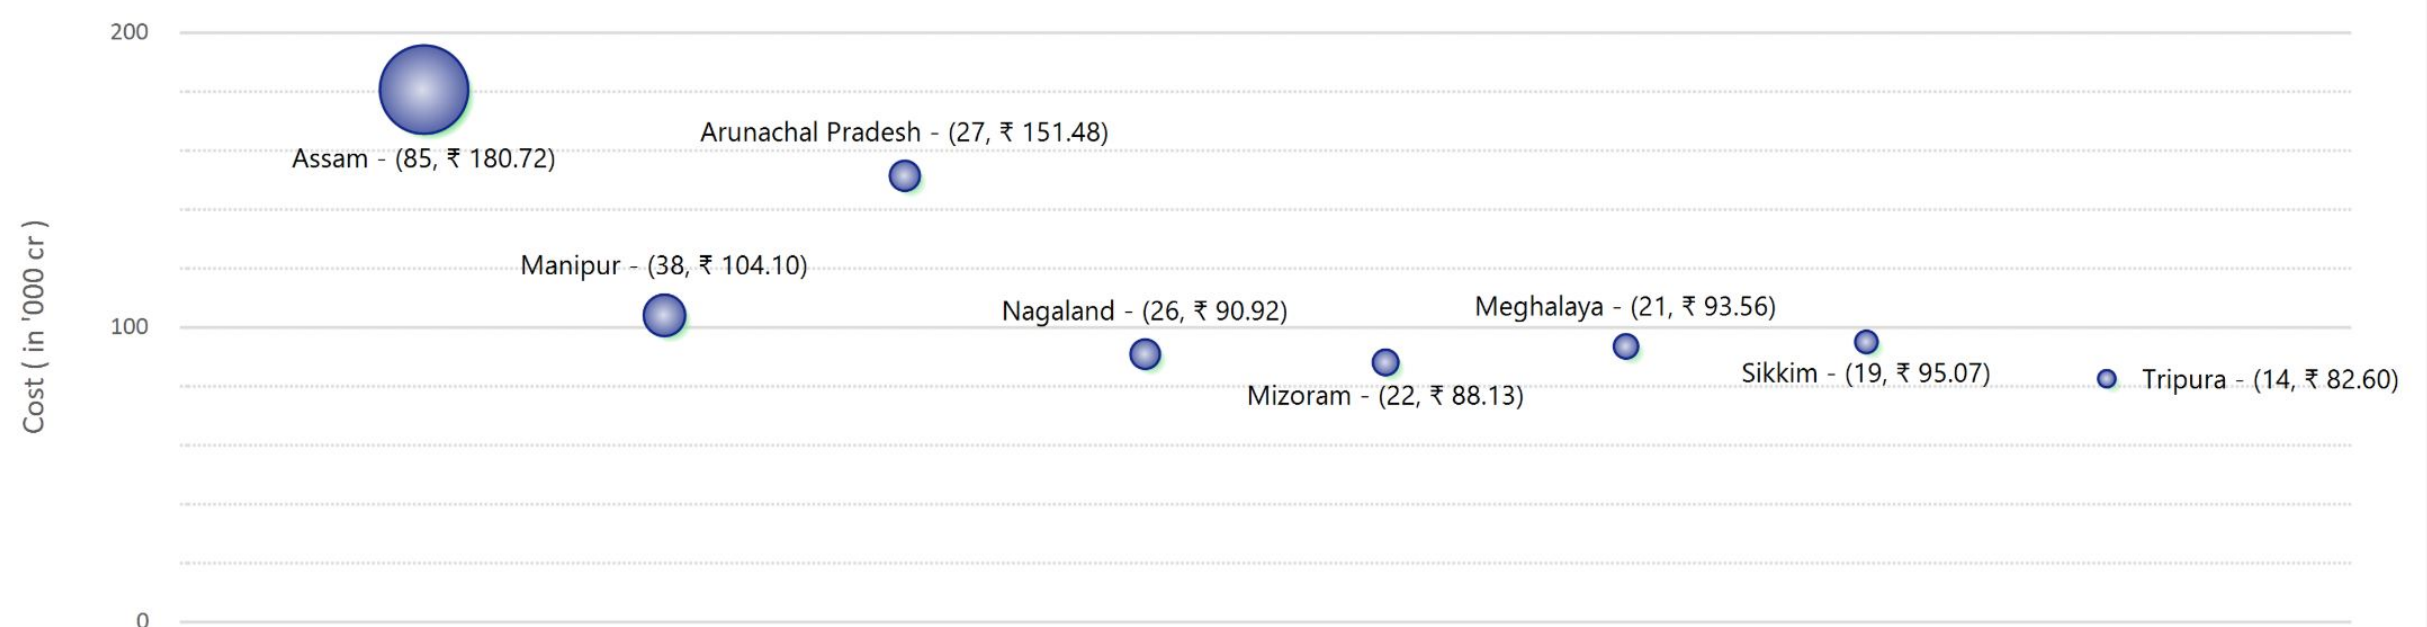

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022





HML Category 1 : Transport & Logistics

JUNE 2026

1341

Ongoing Projects

₹ 20,44,057

Original Cost
(crores)

₹ 22,32,327

Revised Cost
(crores)

₹ 12,32,900

(55.23% of Revised Cost)
Expenditure
(crores)


121

Commissioned during month


14

Newly Added during month

Cost Analytics : All Sectors

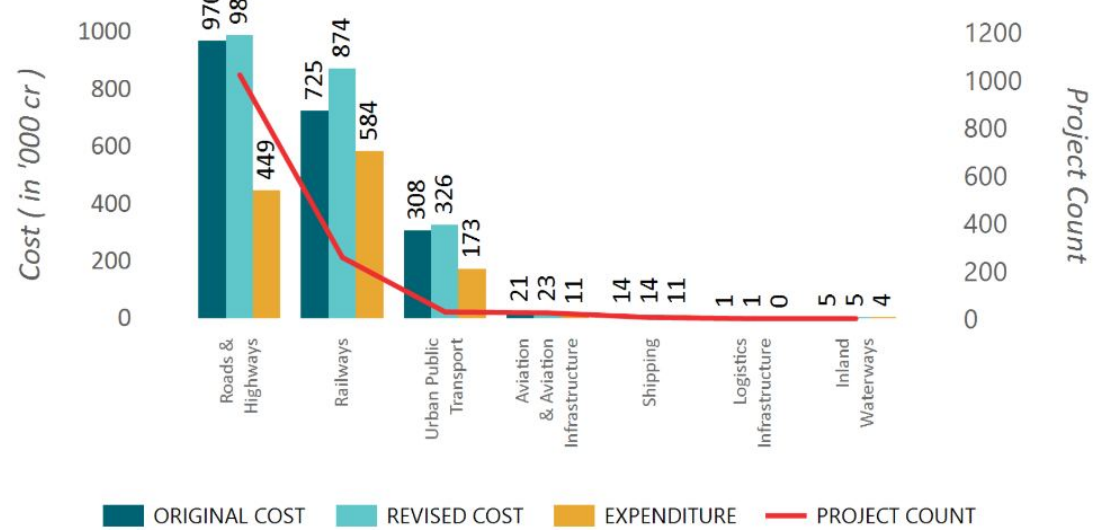

Cumulative Physical & Financial progress (%) : Project count

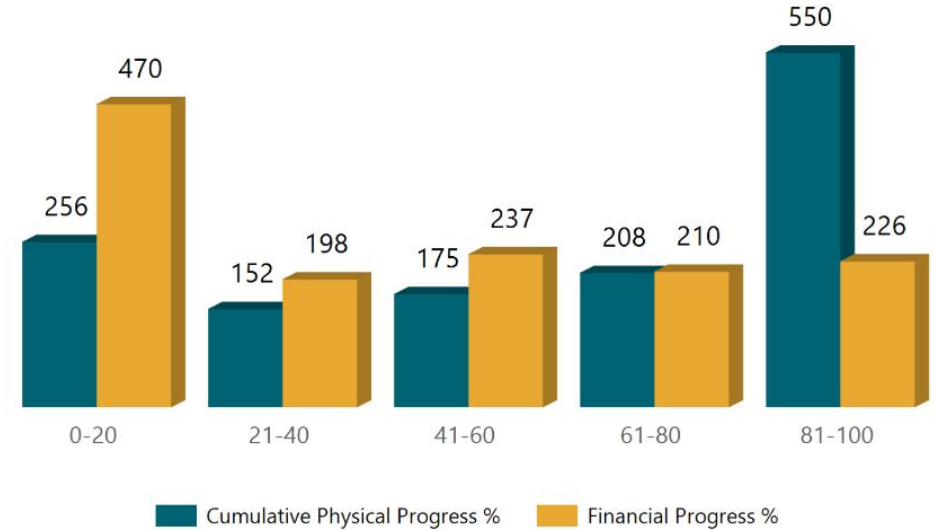

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Roads & Highways	1022	969,677	989,066	448,973
2	Railways	257	724,664	873,994	584,469
3	Urban Public Transport	29	307,835	326,438	172,730
4	Aviation & Aviation Infrastructure	25	21,345	22,559	11,209
5	Shipping	6	14,405	14,445	10,972
6	Logistics Infrastructure	1	763	763	430
7	Inland Waterways	1	5,369	5,061	4,118

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	90,967	60.87
2	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		33,774	53.36
3	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
4	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	28,828	77.5
5	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	3,854	25

HML Category 2 : Energy

JUNE 2026

207
Ongoing Projects

₹ 9,47,433
Original Cost
(crores)


₹ 10,38,402
Revised Cost
(crores)

₹ 6,27,953
(60.47% of Revised Cost)
Expenditure
(crores)


7
Commissioned during month

0
Newly Added during month

Cost Analytics : All Sectors

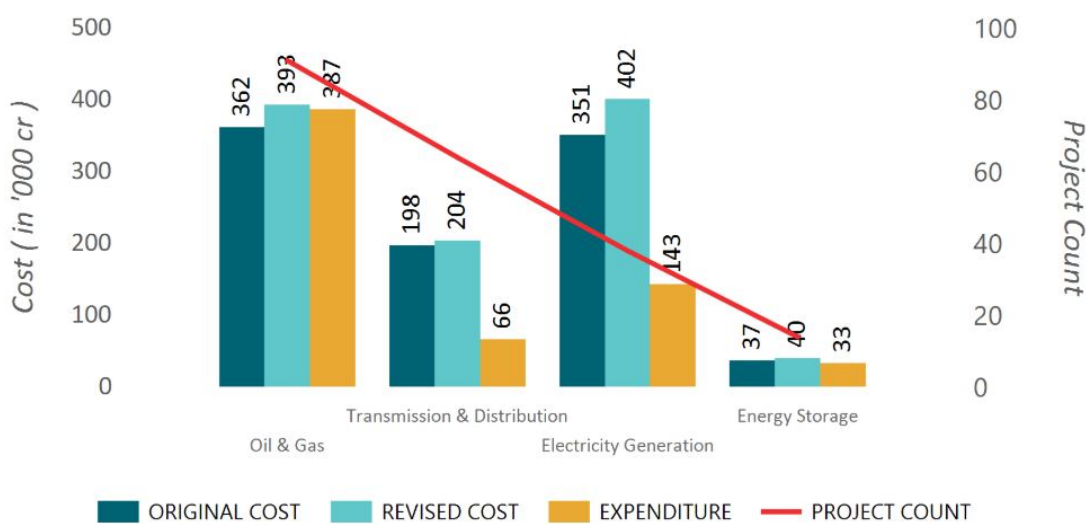

Cumulative Physical & Financial progress (%) : Project count

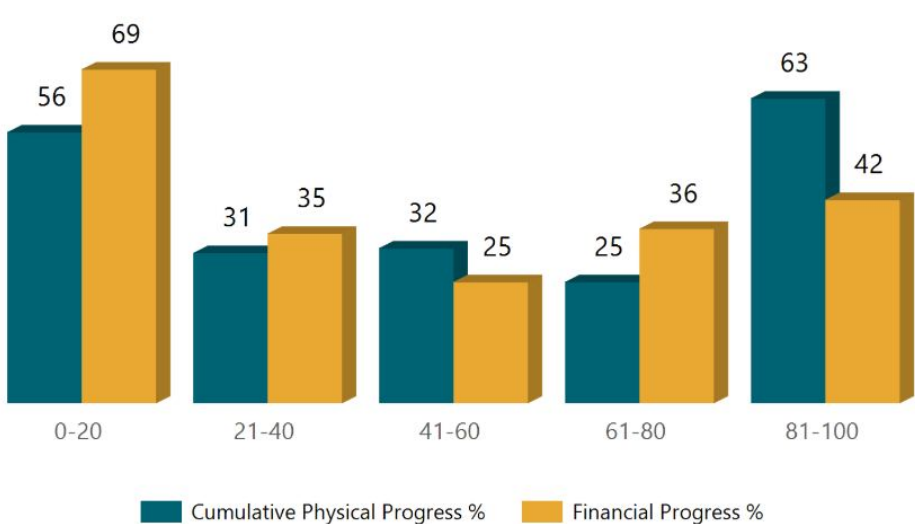

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	91	362,124	392,963	386,636
2	Transmission & Distribution	64	197,615	203,579	65,919
3	Electricity Generation	38	350,856	401,582	142,643
4	Energy Storage	14	36,838	40,279	32,754

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	5,596	30.7
2	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	27,518	94
3	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,114	96.8
4	602182	DIBANG MULTIPURPOSE PROJECT	31,876		4,750	17.78
5	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,590	10.2

HML Category 3 : Water & Sanitation

JUNE 2026

56
Ongoing Projects



₹ 1,06,135
Original Cost
(crores)

₹ 2,07,964
Revised Cost
(crores)

₹ 1,48,261
(71.29% of Revised Cost)
Expenditure
(crores)

0
Commissioned during month

0
Newly Added during month

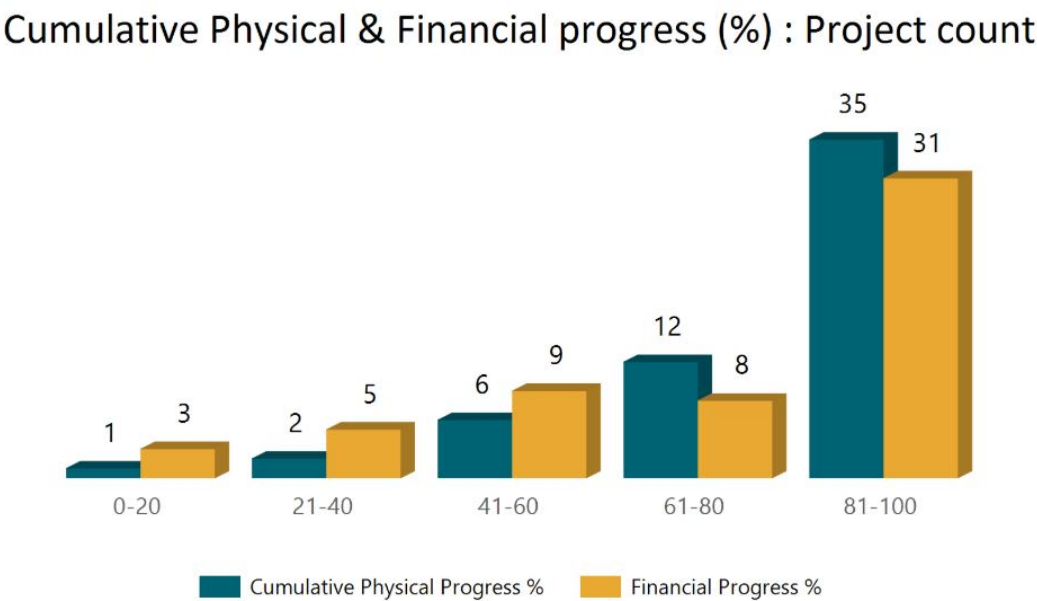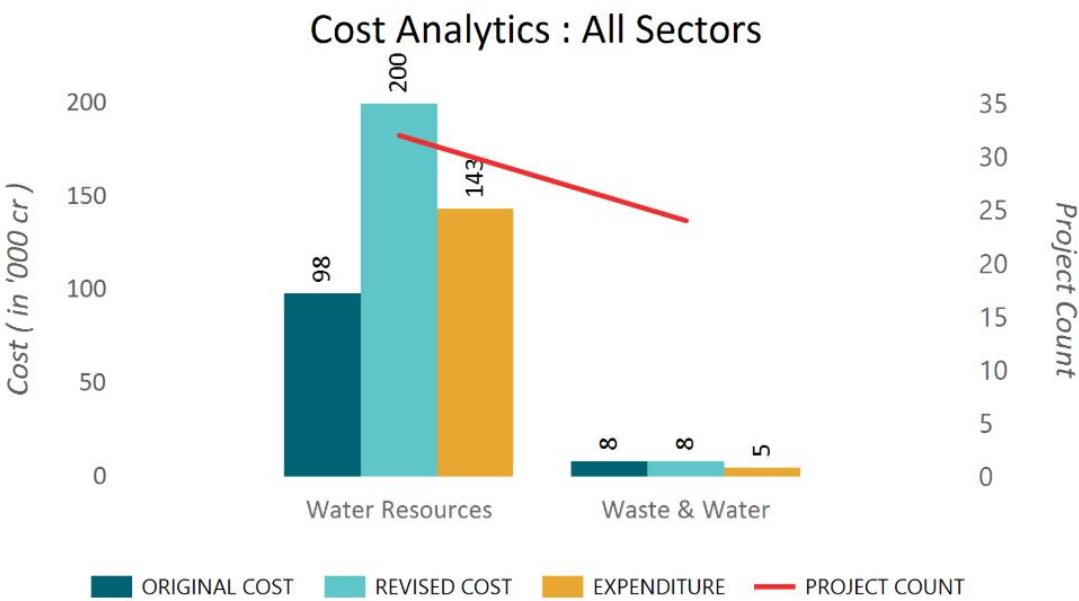

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	32	98,109	199,840	143,454
2	Waste & Water	24	8,026	8,125	4,806

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701530	KEN-BETWA LINKING DEVELOPMENT PROJECT	21,030		8,531	0
2	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,943	93.7
3	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	27,726	86.14
4	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,841	87.7
5	701386	GOSIKHURD PROJECT	7,196	12,770	14,386	72.65

HML Category 4 : Communication

JUNE 2026

15
Ongoing Projects

₹ 1,61,792
Original Cost
(crores)


₹ 2,63,714
Revised Cost
(crores)

₹ 79,930
(30.31% of Revised Cost)
Expenditure
(crores)


0
Commissioned during month

3
Newly Added during month

Cost Analytics : All Sectors

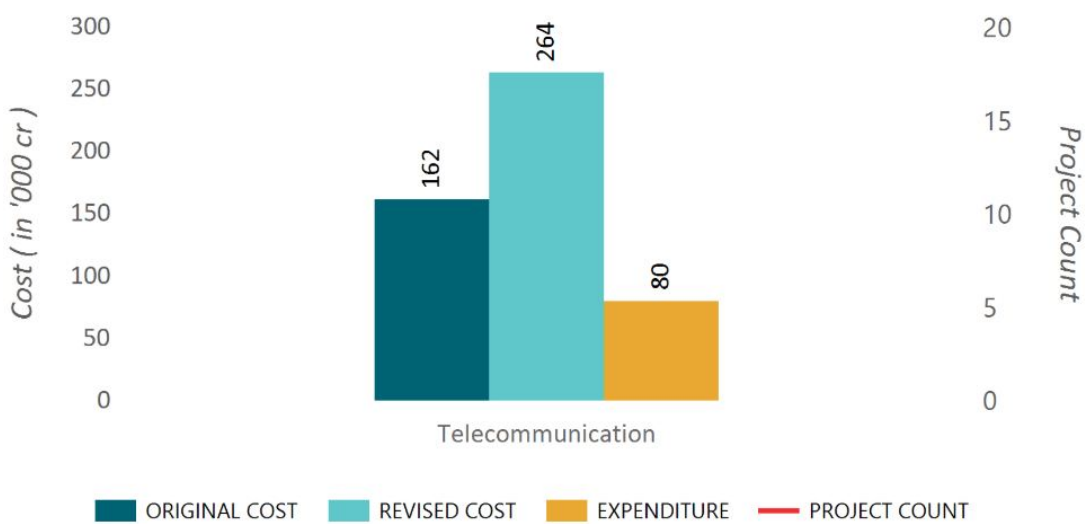

Cumulative Physical & Financial progress (%) : Project count

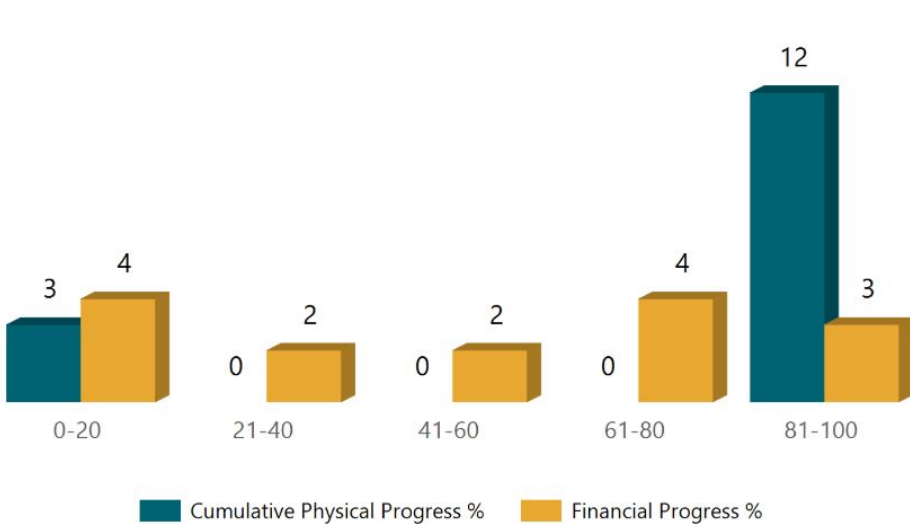

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	15	161,792	263,714	79,930

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	706775	BHARATNET	61,109	188,000	48,810	99.98
2	701593	4G SERVICES BY BSNL	28,466	19,592	9,143	98.4
3	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	15,393	8,553	85
4	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		9,143	98.41
5	222253	AMENDED BHARATNET PROGRAM - UP (EAST)	5,008		502	0

HML Category 5 : Social & Commercial

JUNE 2026

88
Ongoing Projects



₹ 89,510
Original Cost
(crores)

₹ 94,143
Revised Cost
(crores)

₹ 38,060
(40.43% of Revised Cost)
Expenditure
(crores)

0
Commissioned during month

0
Newly Added during month

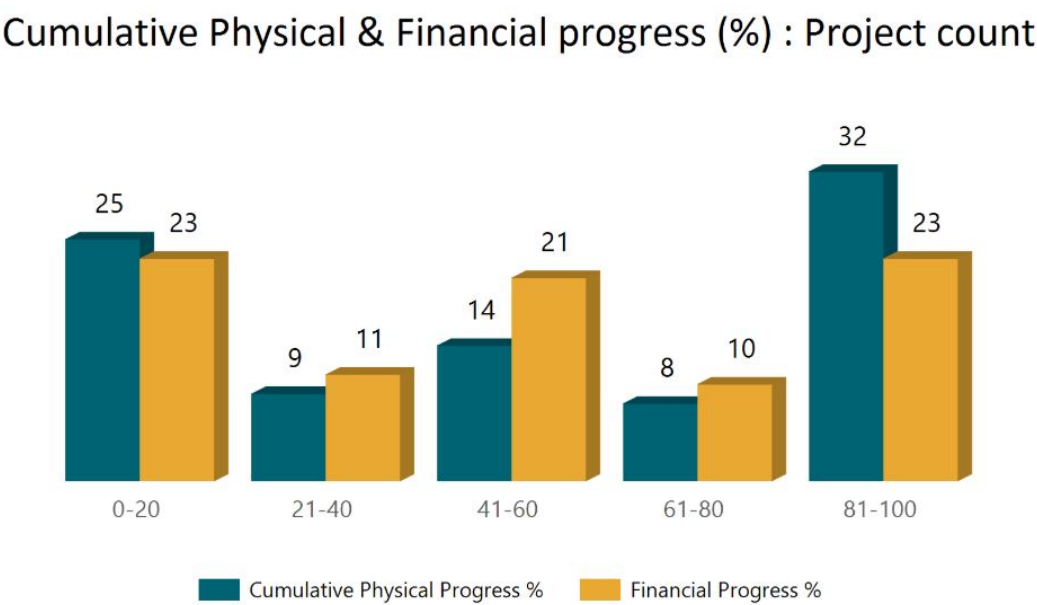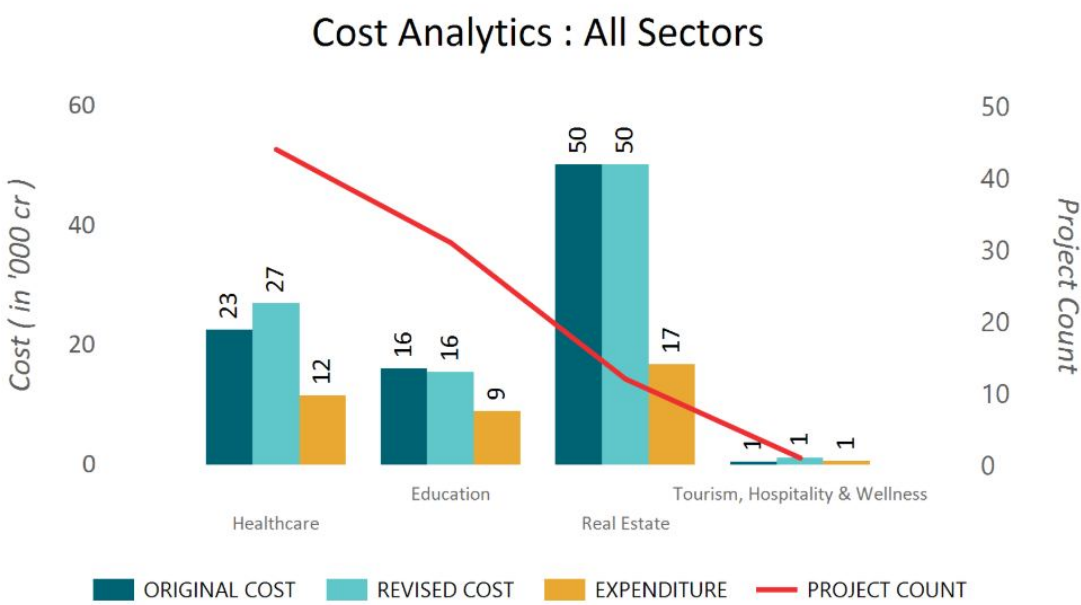

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Healthcare	44	22,607	27,023	11,594
2	Education	31	16,072	15,558	9,000
3	Real Estate	12	50,258	50,324	16,830
4	Tourism, Hospitality & Wellness	1	573	1,238	637

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850	32,841	14,370	46.7
2	617883	REDEVELOPMENT OF RESIDENTIAL COLONIES AT AYUR VIGYAN NAGAR AND WEST ANSARI NAGAR CAMPUSES OF AIIMS, NEW DELHI	4,441		44	57
3	701668	DEVELOPMENT OF PALAKKAD NODE UNDER EXTENSION OF CBIC TO KOCHI	3,805		0	5.25
4	617727	ORVAKAL INDUSTRIAL AREA	2,786		279	12.81
5	601812	DEVELOPMENT OF ZAHEERABAD NODE UNDER HYDERABAD NAGPUR INDUSTRIAL CORRIDOR	2,360		43	3.58

Other Sectors

JUNE 2026

140
Ongoing Projects

₹ 2,12,793
Original Cost
(crores)


₹ 2,17,923
Revised Cost
(crores)

₹ 69,559
(31.92% of Revised Cost)
Expenditure
(crores)

1
Commissioned during month

0
Newly Added during month

Cumulative Physical & Financial progress (%) : Project count

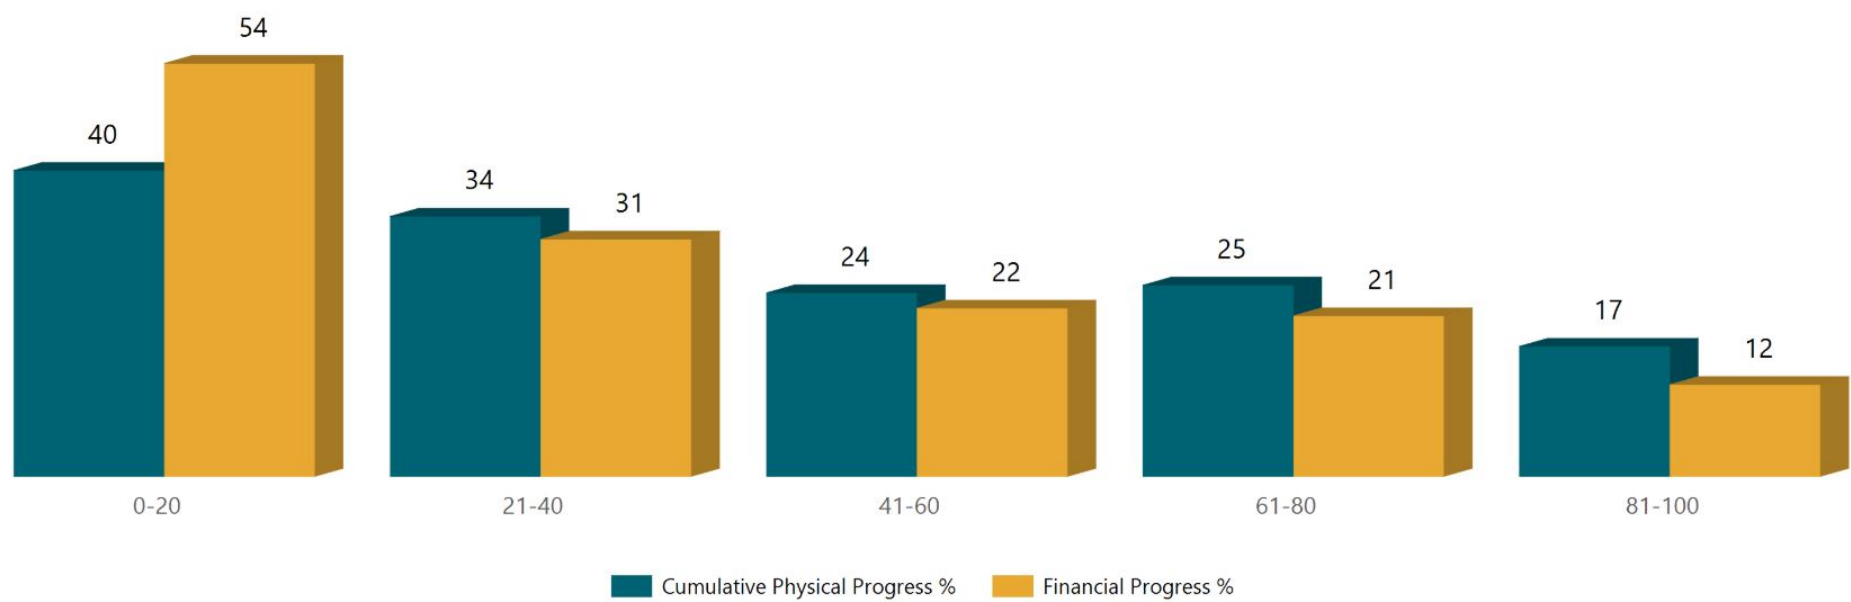

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	115	184,906	182,644	51,084
2	Steel	17	17,298	20,536	10,585
3	Metals & Mining	6	9,689	13,843	7,615
4	Construction	2	899	899	275

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	619032	JAYANT EXPN. [20 TO 38 MTPA]	25,560		257	2.02
2	400424	GEVRA OC [70 MTY]	11,816		6,960	78.48
3	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,777	35.69
4	400150	RPR MAGADH EXP OCP	6,964		2,298	39.42
5	617416	REVISED JHARIA MASTER PLAN FOR DEALING WITH FIRE, SUBSIDENCE & REHABILITATION OF AFFECTED FAMILIES IN JHARIA COALFIELD- REG.	5,940		328	31



Major Infrastructure Central Ministries & Departments





Ministry of Road Transport & Highways

JUNE 2026

1022

Ongoing Projects

₹ 9,69,677

Original Cost
(crores)

₹ 9,89,066

Revised Cost
(crores)

₹ 4,48,973

(45.39% of Revised Cost)

Expenditure
(crores)

383 | ₹ 655,389

Mega Projects
Count | Original Cost (crores)

639 | ₹ 314,288

Major Projects
Count | Original Cost

120


Commissioned during month

14

Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

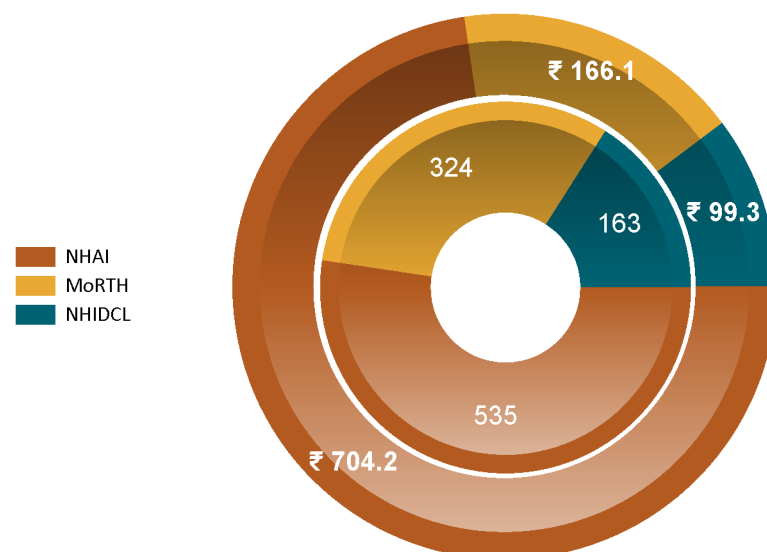


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Cumulative Physical & Financial progress (%) : Project count

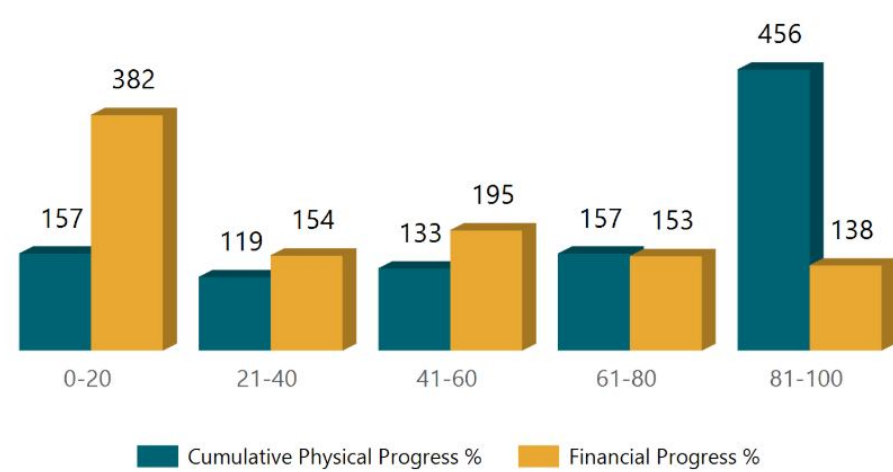

Cost Analytics : Major Sectors*

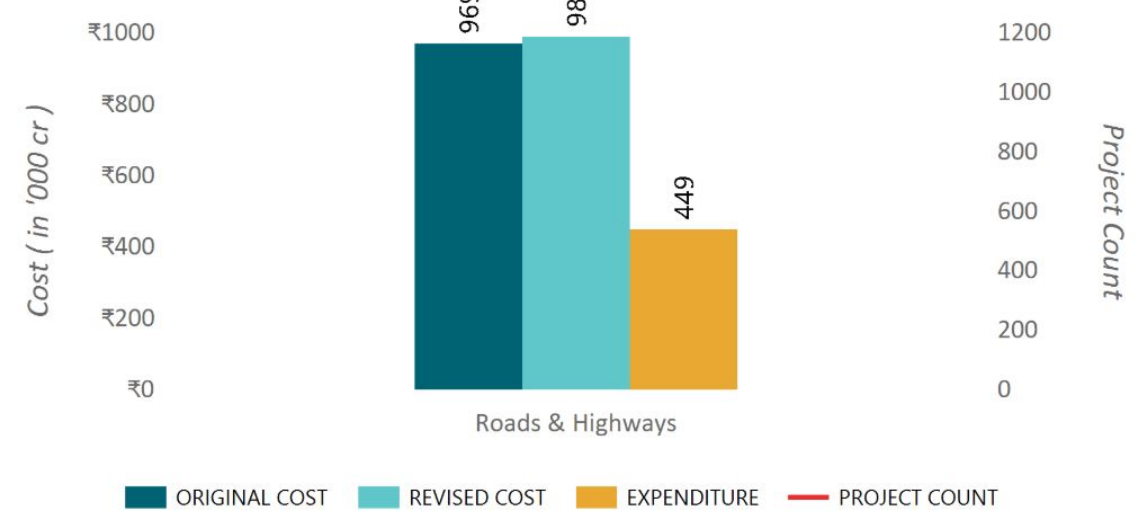

State Comparison : Major States*

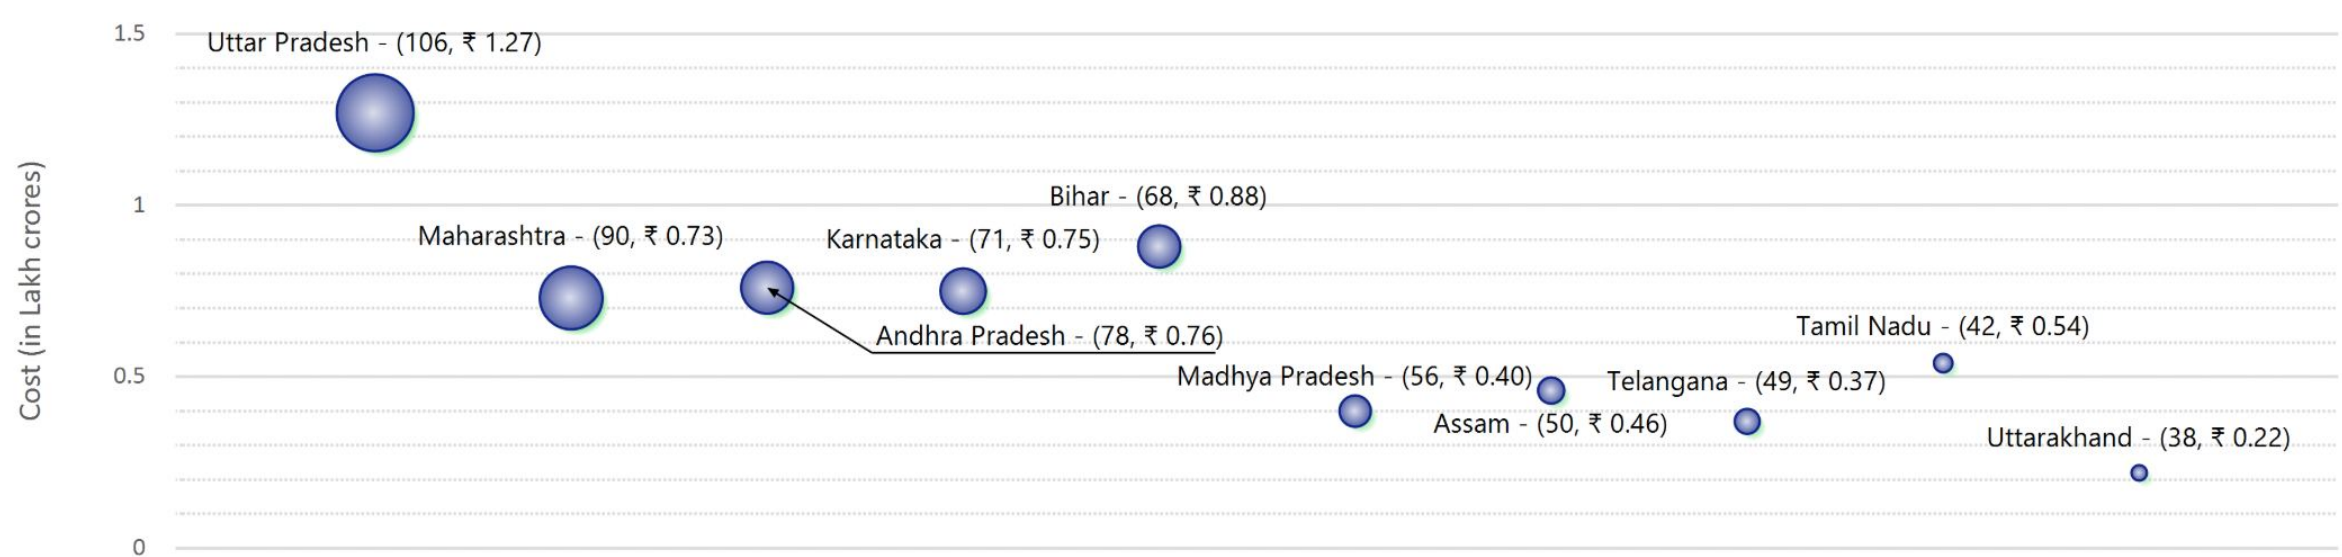

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	618412	CONSTRUCTION OF I CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL ROAD LENGTH 18.475KM AND II 14.150 KM LONG 2-L BI-DIRECTIONAL SINGLE TUBE ZOJI-LA TUNNEL ACROSS ZOJILA PASS ON SONAMARG - KARGIL SECTION FROM KM 82 TO KM 118 OF NH-01 UNDER PMDP	6,809	6,809	3,549	68.8
2	618738	6L BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD NH-131G STARTING FROM KM 8.480 NEAR SHERPUR TO KM 23.000 NEAR DIGHWARA	6,292	3,352	734	21.21
3	618934	GUWAHATI RING ROAD IN THE STATE OF ASSAM	5,729	5,729	328	0
4	618373	CONSTRUCTION OF 4-LANE BRIDGE INCLUDING APPROACHES OVER RIVER BRAHMAPUTRA BETWEEN DHUBRI ON NORTH BANK,ASSAM AND PHULBARI ON SOUTH BANK,MEGHALAYA ON NH-127B UNDER JICA ODA LOAN ASSISTANCE PHASE-III	4,997	4,997	3,034	77.14
5	618599	6L OF RAMANATUKKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66	4,924	4,919	3,635	100



Ministry of Railways

JUNE 2026

255

Ongoing Projects

₹ 7,21,178

Original Cost
(crores)

₹ 8,68,991

Revised Cost
(crores)

₹ 5,81,963

(66.97% of Revised Cost)
Expenditure
(crores)

137 | ₹ 663,180

Mega Projects
Count | Original Cost (crores)

118 | ₹ 57,998

Major Projects
Count | Original Cost

0


Commissioned during month

0

Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

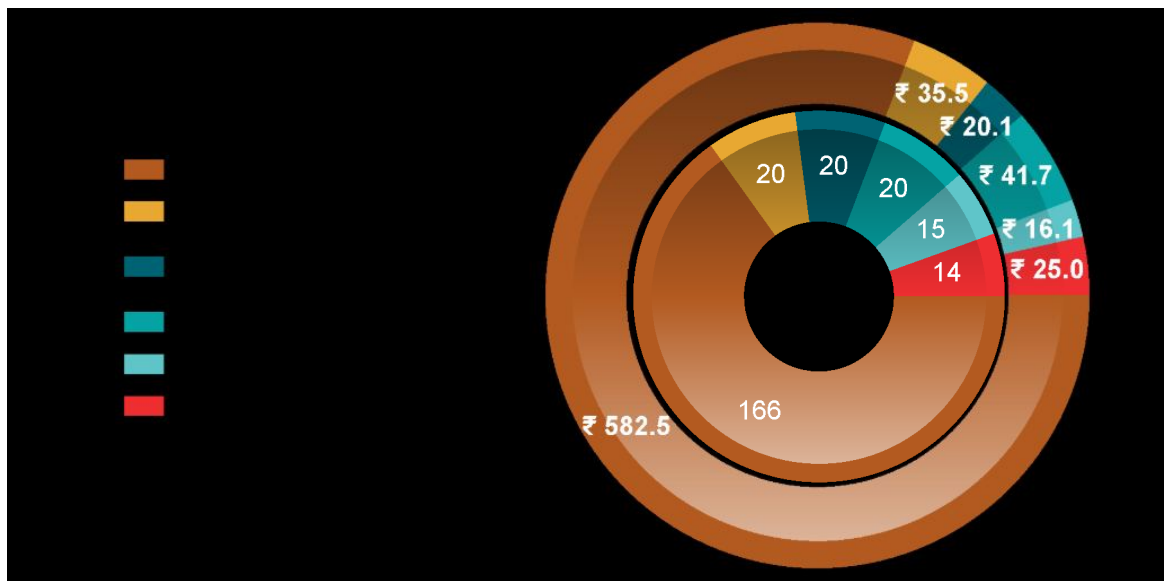


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Cumulative Physical & Financial progress (%) : Project count

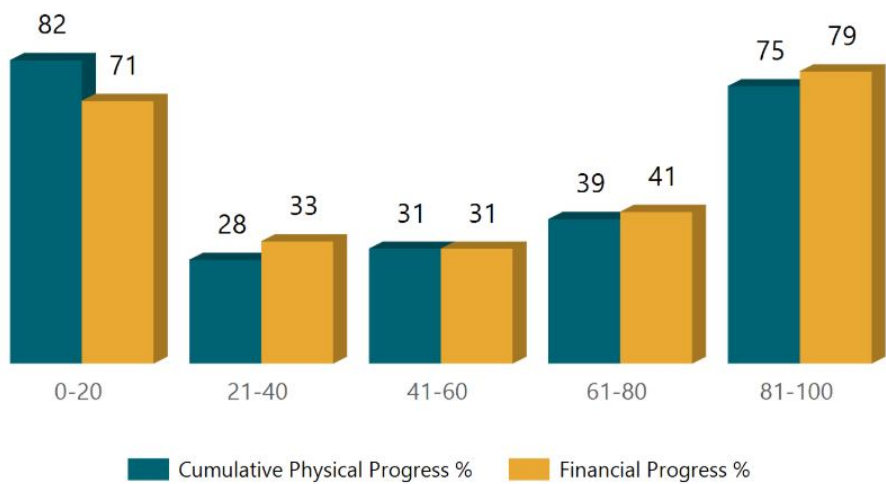

Cost Analytics : Major Sectors*

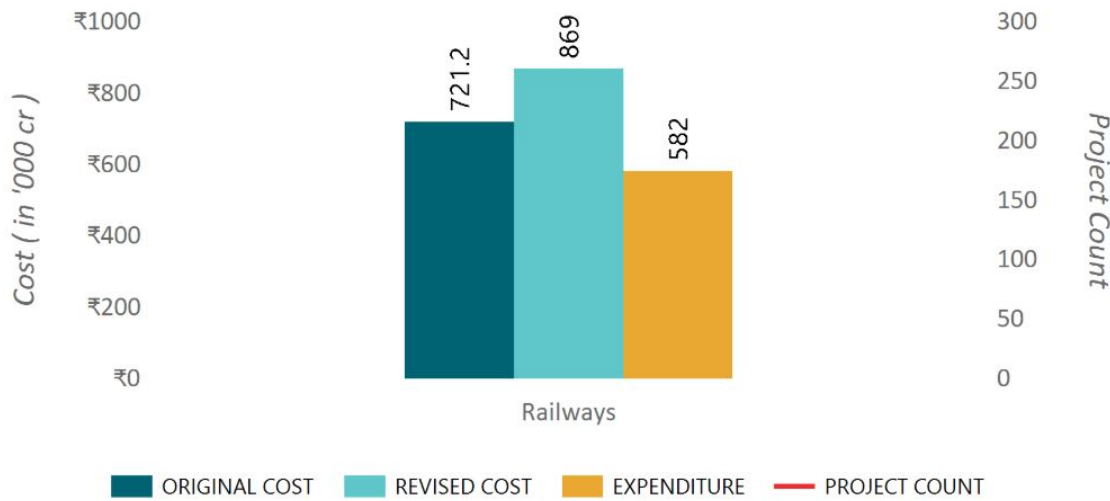

State Comparison : Major States*

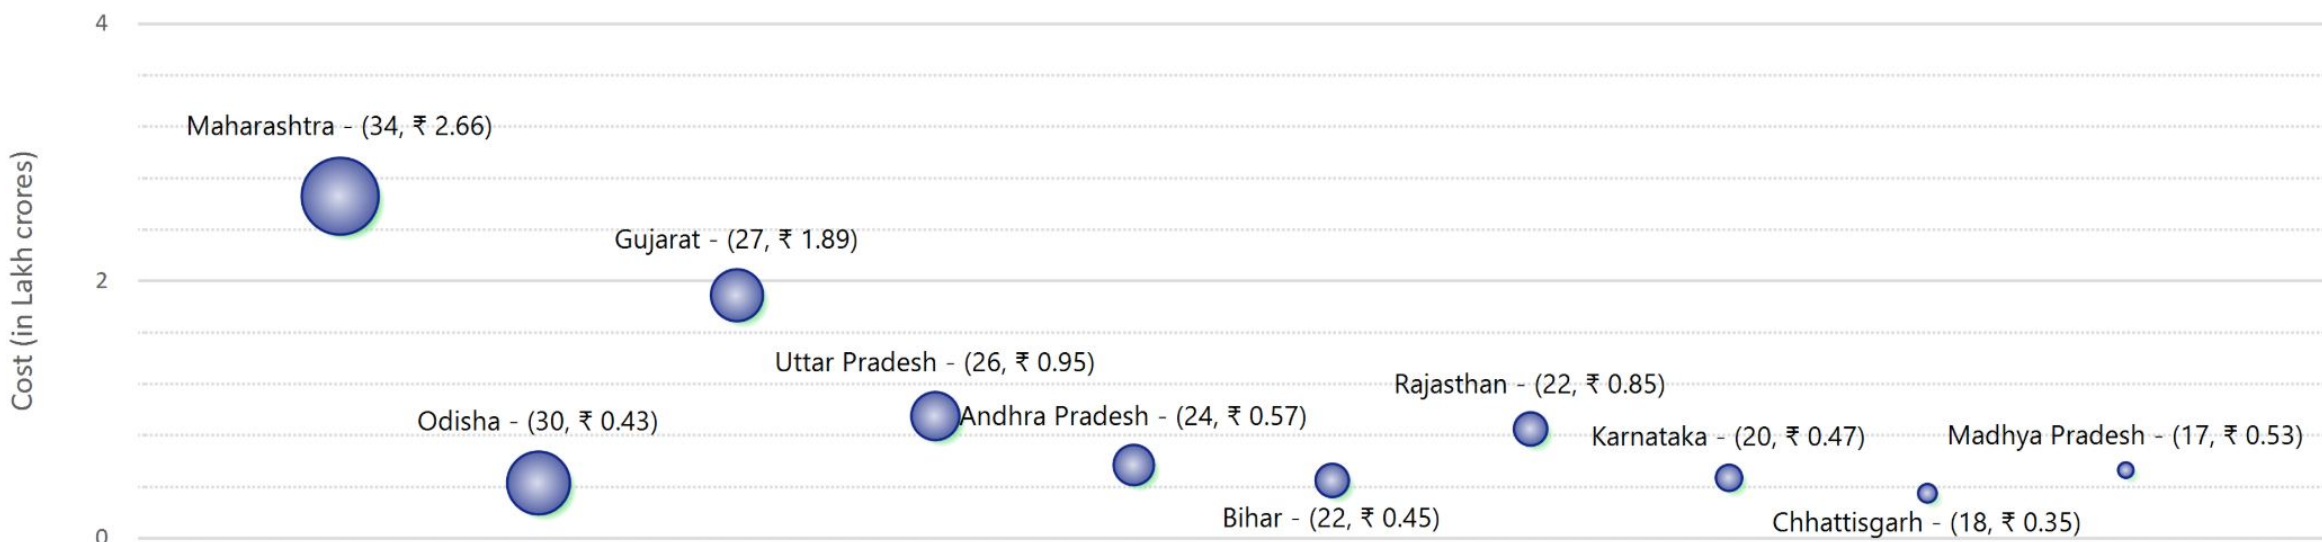

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	90,967	60.87
2	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
3	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	28,828	77.5
4	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	3,854	25
5	705941	BANGALORE SUBURBAN RAILWAY PROJECT	15,767	15,767	3,278	20.02



Ministry of Coal

JUNE 2026

121

Ongoing Projects

₹ 2,23,091

Original Cost
(crores)

₹ 2,22,064

Revised Cost
(crores)

₹ 58,702

(26.43% of Revised Cost)
Expenditure
(crores)

41 | ₹ 183,146

Mega Projects
Count | Original Cost (crores)

80 | ₹ 39,945

Major Projects
Count | Original Cost

0


Commissioned during month

0

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

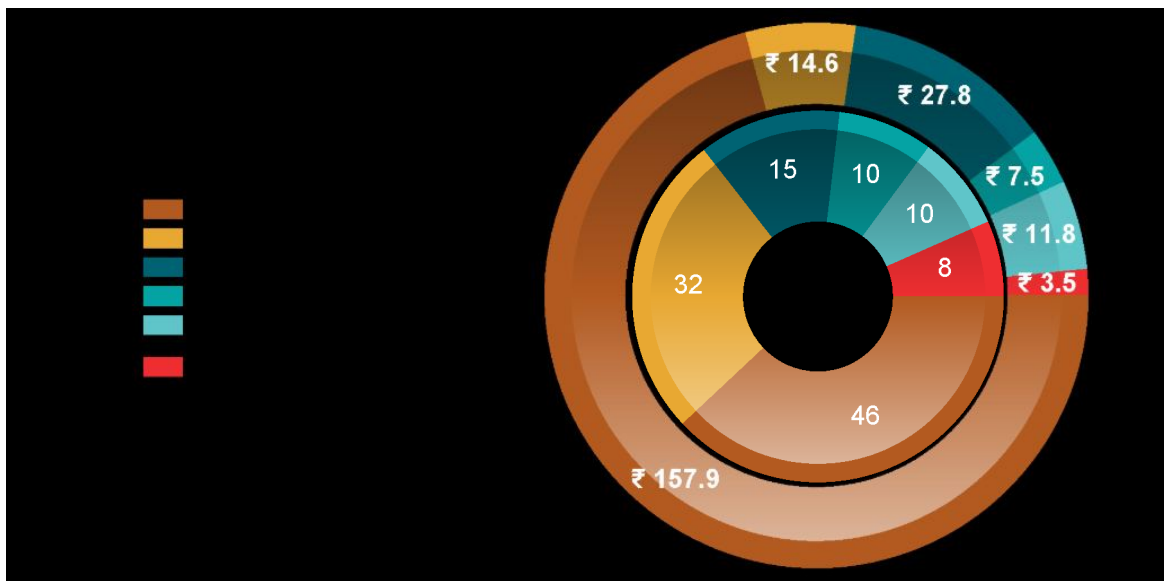


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

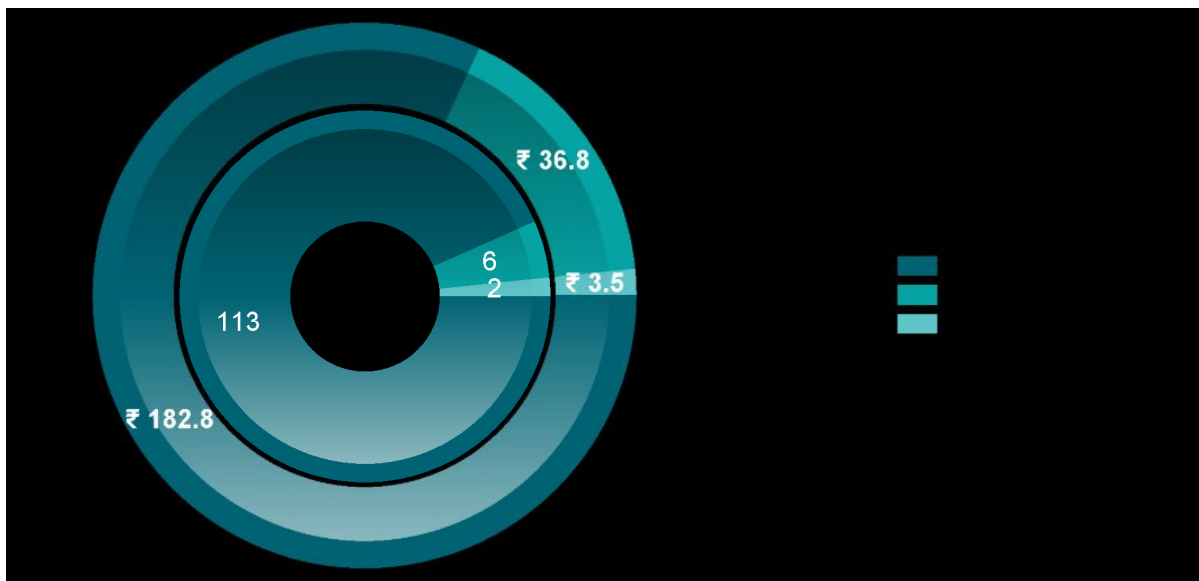

Cumulative Physical & Financial progress (%) : Project count

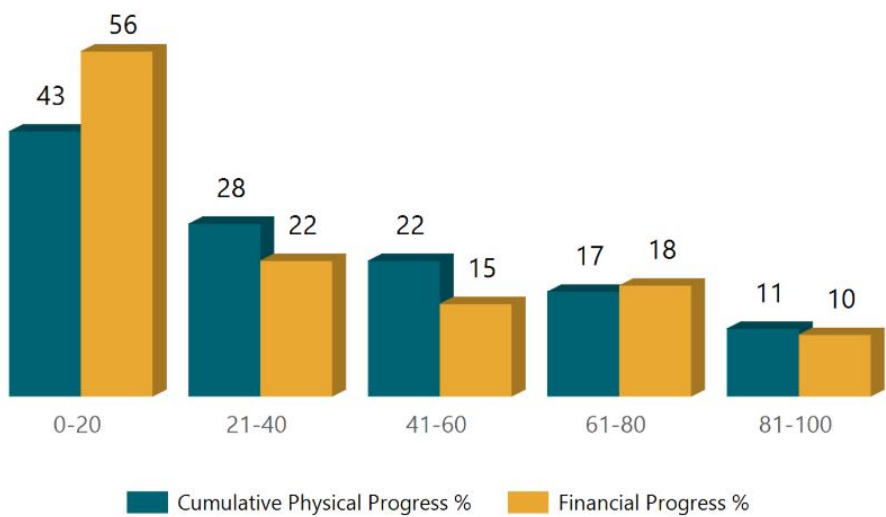

Cost Analytics : Major Sectors*

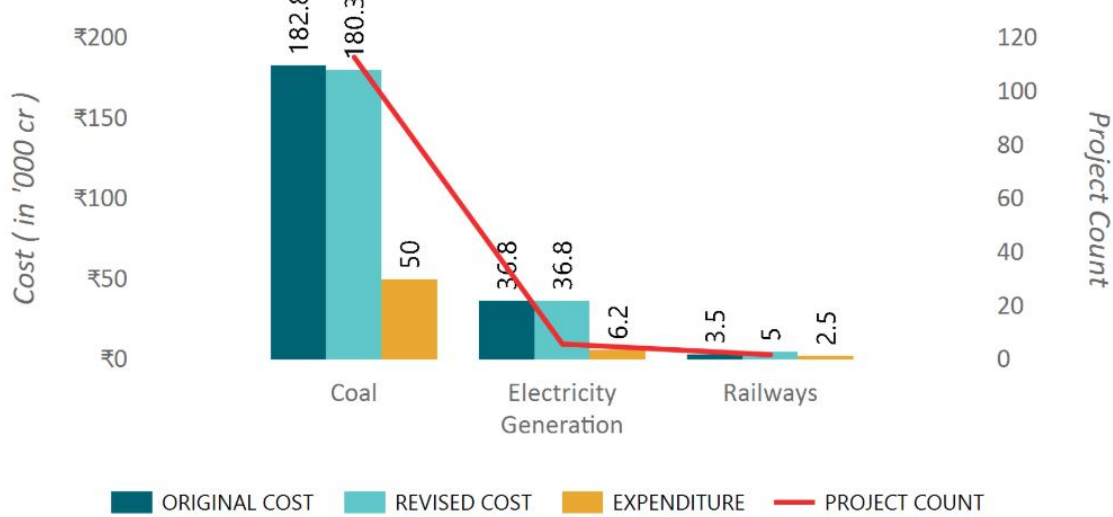

State Comparison : Major States*



Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	3,518	3.54
2	619032	JAYANT EXPN. [20 TO 38 MTPA]	25,560	25,560	257	2.02
3	400424	GEVRA OC [70 MTY]	11,816	11,816	6,960	78.48
4	400185	GOPALJI KANIHA OCP [10 TO 30 M]	8,416	6,108	1,777	35.69
5	400150	RPR MAGADH EXP OCP	6,964	6,964	2,298	39.42



Ministry of Petroleum & Natural Gas

JUNE 2026

105

Ongoing Projects

₹ 3,98,962

Original Cost
(crores)

₹ 4,33,241

Revised Cost
(crores)

₹ 4,19,391

(96.8% of Revised Cost)

Expenditure
(crores)

46 | ₹ 373,718

Mega Projects
Count | Original Cost (crores)

59 | ₹ 25,244

Major Projects
Count | Original Cost

4


Commissioned during month

0

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

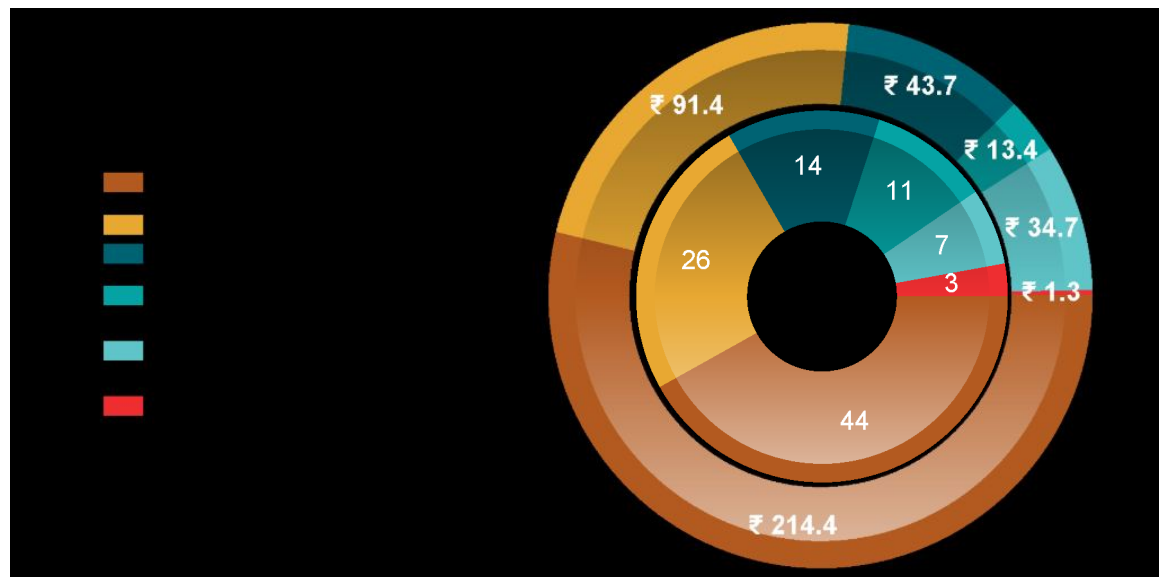


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

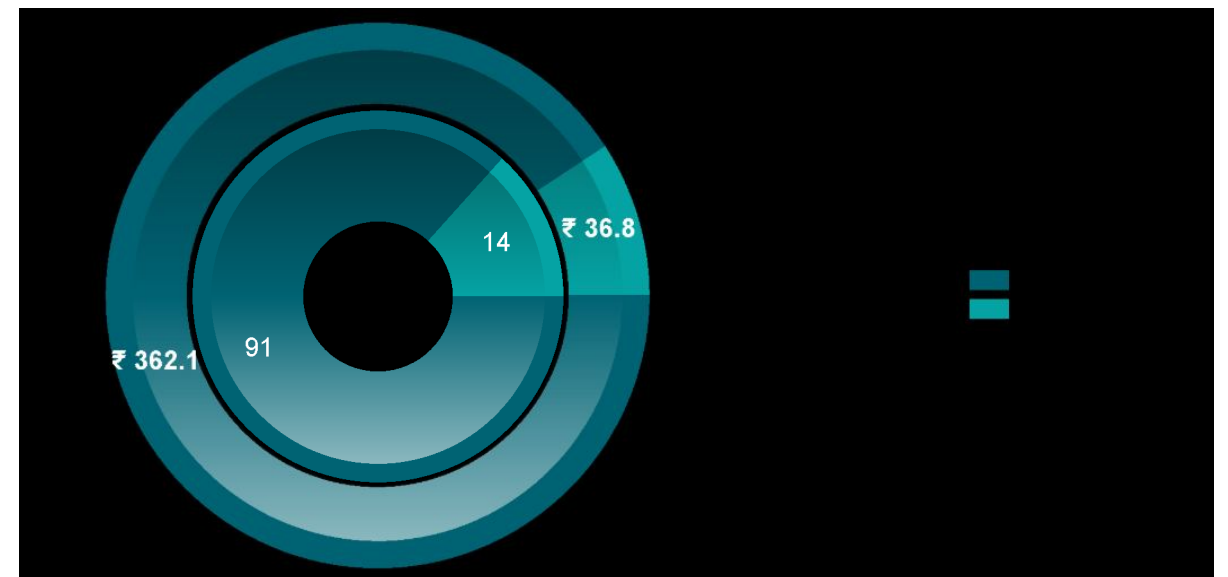


Cumulative Physical & Financial progress (%) : Project count

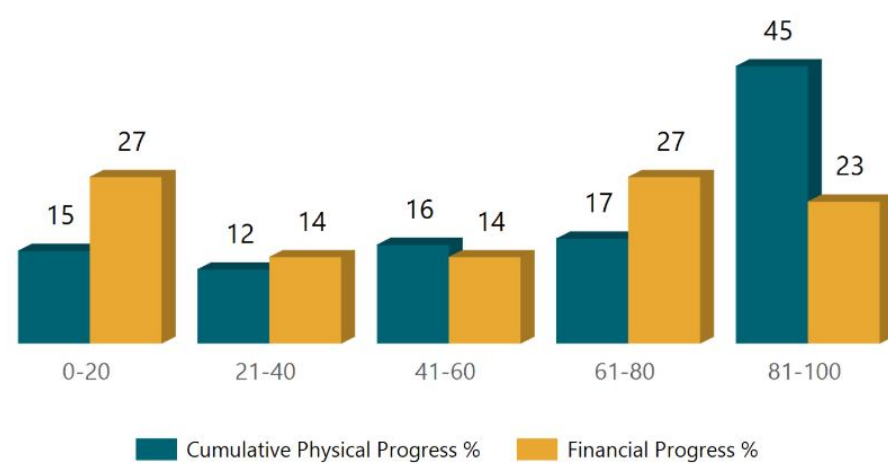

Cost Analytics : Major Sectors*

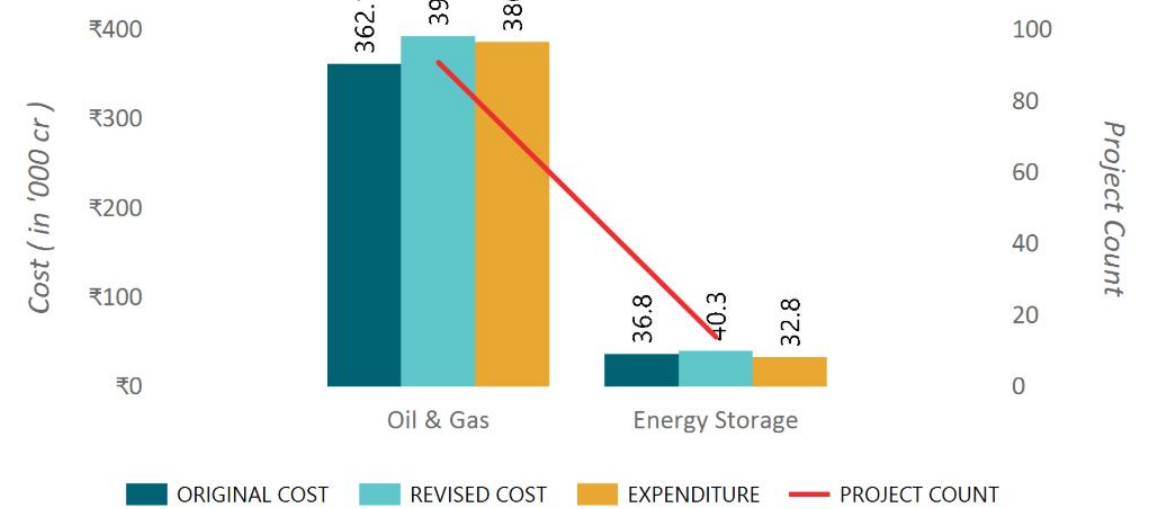

State Comparison : Major States*

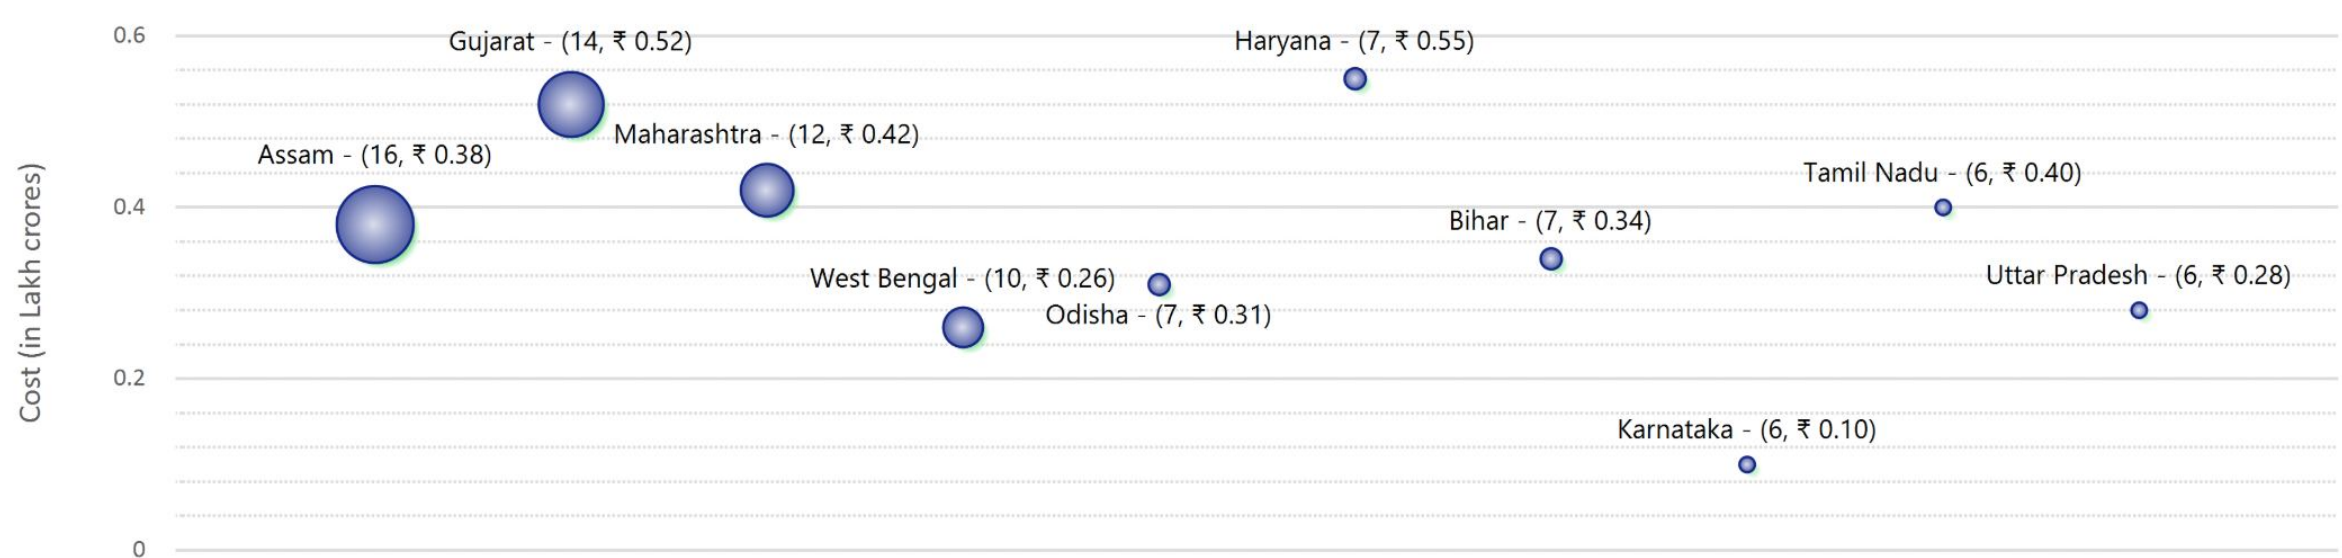

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)

Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	5,596	30.7
2	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	27,518	94
3	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,114	96.8
4	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,590	10.2
5	701329	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	18,936	17,825	75,183	89.2

Ministry of Power

JUNE 2026

98
Ongoing Projects

₹ 5,13,772
Original Cost
(crores)

₹ 5,70,744
Revised Cost
(crores)

₹ 2,03,450
(35.65% of Revised Cost)
Expenditure
(crores)


69 | ₹ 502,110
Mega Projects
Count | Original Cost (crores)

29 | ₹ 11,662
Major Projects
Count | Original Cost


3
Commissioned during month

0
Newly Added during month


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

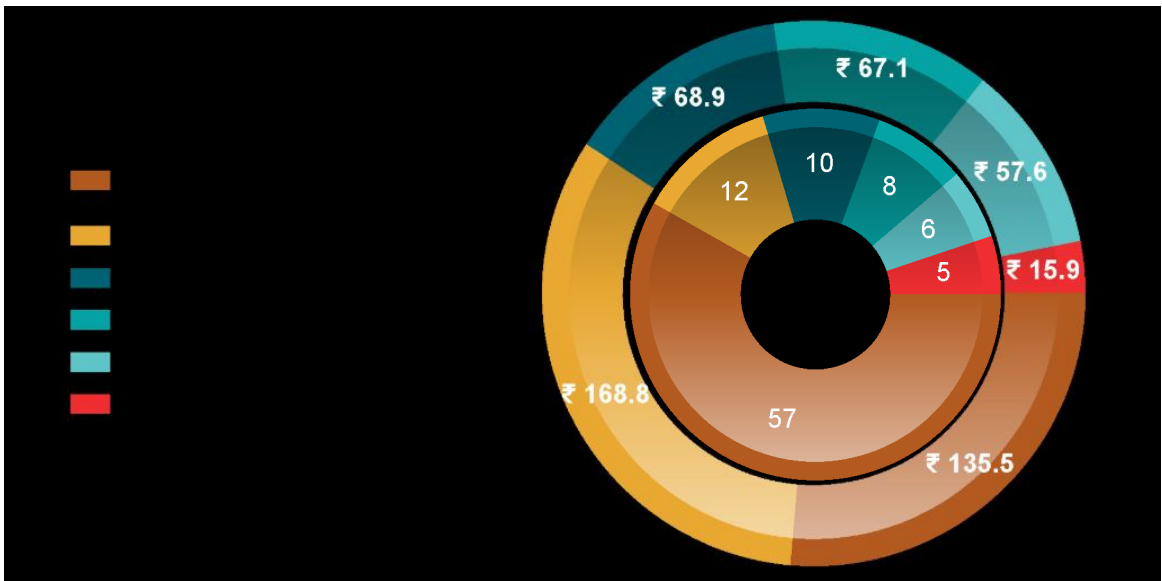


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

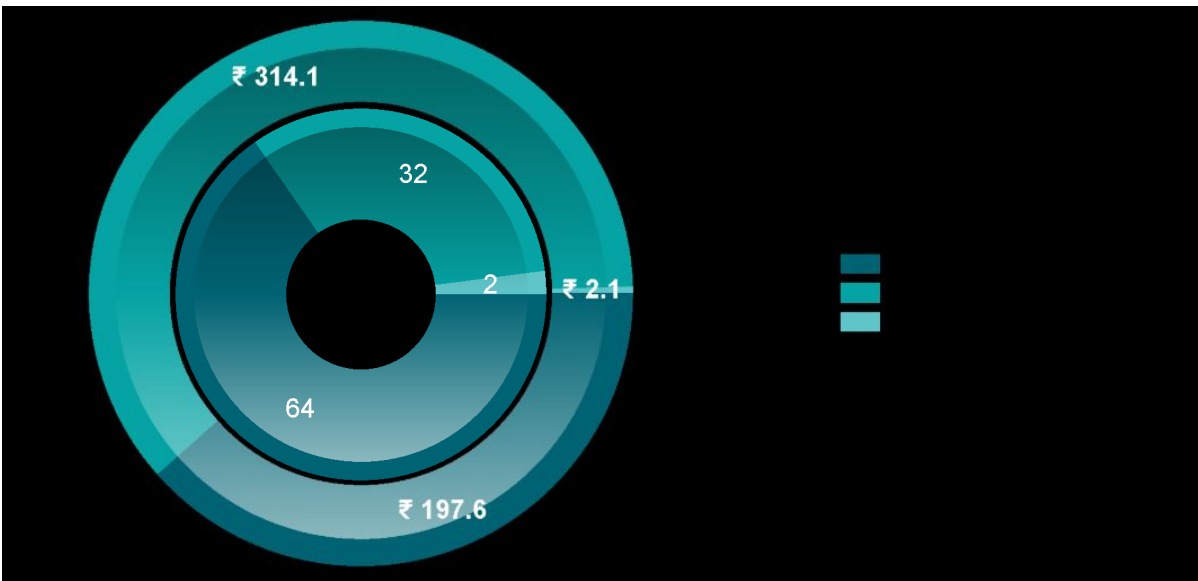


Cumulative Physical & Financial progress (%) : Project count

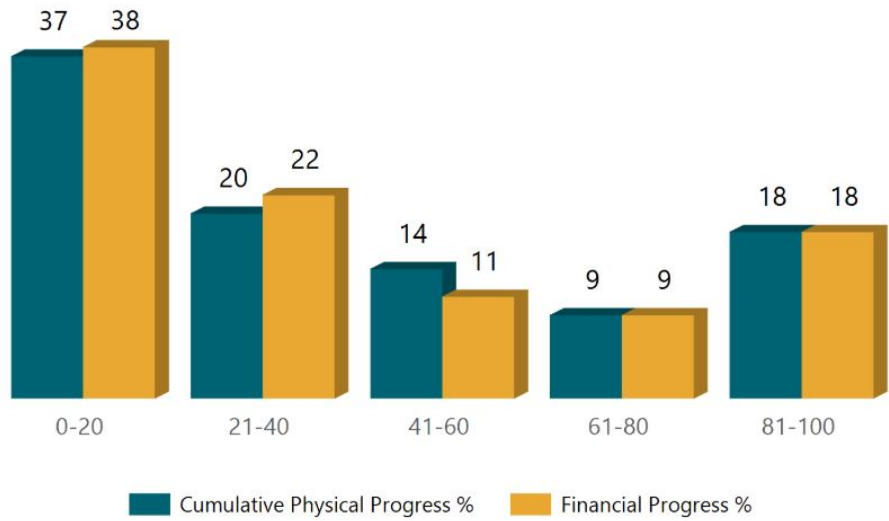

Cost Analytics : Major Sectors*

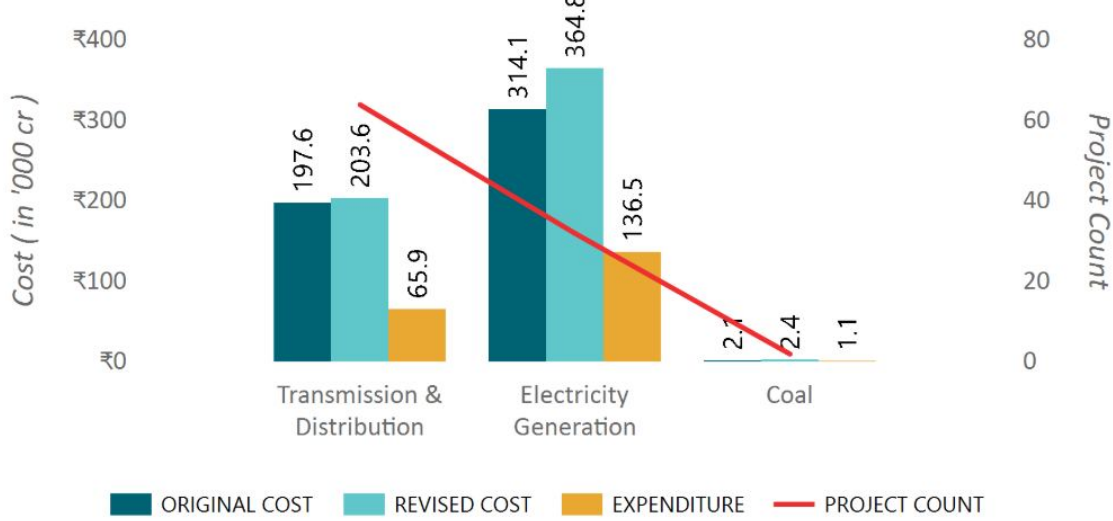


State Comparison : Major States*

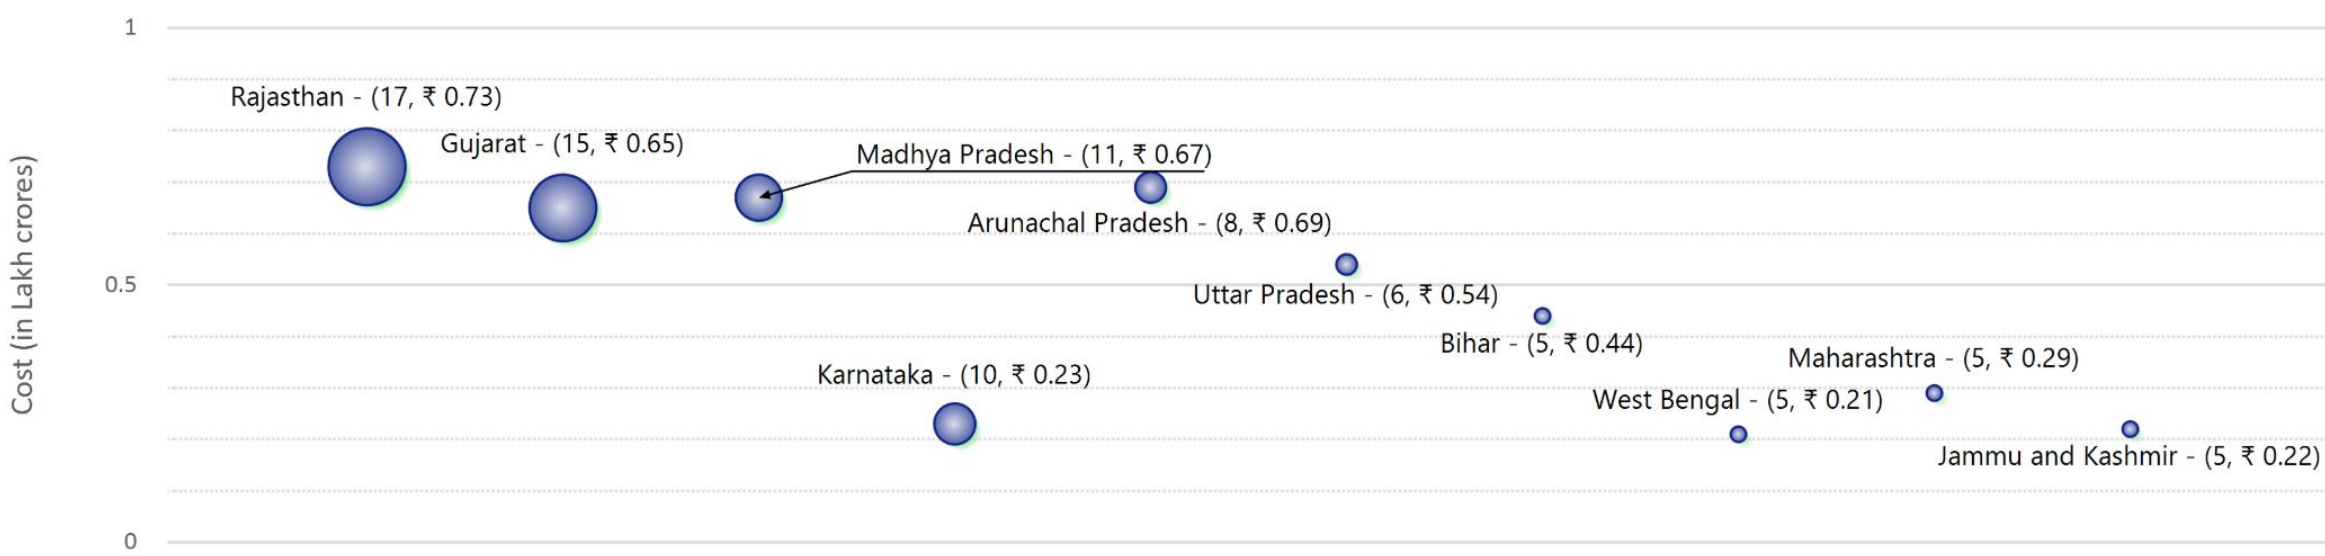

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	4,750	17.78
2	619051	NABINAGAR SUPER THERMAL POWER PROJECT, STAGE-II [3X800 MW]	29,948	29,948	3,100	13.65
3	619341	TELANGANA SUPER THERMAL POWER PROJECT , STAGE-II [3 X 800 MW]	29,345	29,345	730	0.78
4	619025	RAJASTHAN PART I POWER TRANSMISSION LIMITED	25,000	25,000	426	4
5	615347	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV NAME POWERGRID WEST CENTRAL TRANSMISSION LIMITED]	24,819	24,819	2,978	18.11



List of Tables






Table 1: Ministry-wise Ongoing Projects



Ministry-wise Ongoing Projects

JUNE 2026

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Logistics Infrastructure	1	763 763	430
		Real Estate	8	16507.91 16507.9	1742.34
		Total	9	17,270.91	2,172.34
2	Department of Higher Education	Education	30	15165.68 14945.9	8423.25
		Total	30	15,165.68	8,423.25
3	Department of Sports	Education	1	906.47 611.74	576.37
		Total	1	906.47	576.37
4	Department of Telecommunications	Telecommunication	15	161792.15 263714	79930.2
		Total	15	161,792.15	79,930.20
5	Department of Water Resources, River Development & GR	Waste & Water	8	4039.12 4039.12	1655.55
		Water Resources	32	98109.28 199840	143454
		Total	40	102,148.40	145,109.55
6	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	25	21345.07 22559.1	11209.2
		Total	25	21,345.07	11,209.20
7	Ministry of Coal	Coal	113	182823.26 180279	50030.4
		Electricity Generation	6	36781.81 36781.8	6166.01
		Railways	2	3485.86 5002.87	2505.92
		Total	121	223,090.93	58,702.33
8	Ministry of Health & Family Welfare	Healthcare	35	20308.19 24527	10433.5
		Total	35	20,308.19	10,433.50
9	Ministry of Housing & Urban Affairs	Construction	1	644 644	175.79
		Real Estate	4	33749.85 33816	15088
		Urban Public Transport	29	307834.71 326438	172730
		Waste & Water	16	3986.5 4085.78	3150.88
		Total	50	346,215.06	191,144.67
10	Ministry of Labour and Employment	Healthcare	9	2299.24 2496.24	1160.08
		Total	9	2,299.24	1,160.08
11	Ministry of Mines	Construction	1	255.37 255.37	98.92
		Metals & Mining	5	7989.36 12087.2	7351.9
		Total	6	8,244.73	7,450.82
12	Ministry of Petroleum & Natural Gas	Energy Storage	14	36838.3 40278.8	32754.4
		Oil & Gas	91	362124.04 392963	386636
		Total	105	398,962.34	419,390.40
13	Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	4117.61
		Shipping	6	14404.75 14445.4	10972
		Tourism, Hospitality & Wellness	1	573 1238.05	636.91
		Total	8	20,346.93	15,726.52
14	Ministry of Power	Coal	2	2083 2365	1053.41
		Electricity Generation	32	314074.05 364801	136477
		Transmission & Distribution	64	197615.23 203579	65919.5
		Total	98	513,772.28	203,449.91
15	Ministry of Railways	Railways	255	721177.95 868991	581963
		Total	255	721,177.95	581,963.00
16	Ministry of Road Transport & Highways	Roads & Highways	1022	969676.9 989066	448973
		Total	1022	969,676.90	448,973.00
17	Ministry of Steel	Metals & Mining	1	1700 1756.2	263.01
		Steel	17	17297.84 20536.1	10585.1
		Total	18	18,997.84	10,848.11
Total			1847	3,561,721.07	2,196,663.25




Table 2: State-wise Ongoing Projects



Ongoing Projects State-Wise

JUNE 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	7	26398.58 29147.8	17768.26
		Ministry of Railways	Railways	1	819 819	580.51
	PAN India	Department of Telecommunications	Telecommunication	3	79326.55 59529.4	26839.21
		Ministry of Railways	Railways	1	274.39 274.39	0.00
	Total			12	106818.52	45187.98
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 230	37.35
		Ministry of Road Transport & Highways	Roads & Highways	3	653.97 1081.48	0.00
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			6	62617.98	49254.19
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	3	7061.44 7061.44	1299.70
		Department of Higher Education	Education	1	305 305	67.73
		Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1958.12
		Department of Water Resources, River Development & GR	Water Resources	3	10901.5 57269.5	29230.08
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1224.86 1224.86	870.84
		Ministry of Housing & Urban Affairs	Waste & Water	1	172.22 172.22	88.86
		Ministry of Labour and Employment	Healthcare	1	384.27 384.27	253.37
		Ministry of Petroleum & Natural Gas	Energy Storage	1	2658.34 2810	2315.20
			Oil & Gas	4	36642.34 36702.3	33822.89
		Ministry of Power	Transmission & Distribution	4	15694.49 15694.5	3535.52
		Ministry of Railways	Railways	24	56748.36 64703	38621.46
		Ministry of Road Transport & Highways	Roads & Highways	78	76464.57 74274.4	33385.05
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			128	277158.69	194665.66
4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 592.61	551.30
		Department of Telecommunications	Telecommunication	1	1255.49 276.62	237.98
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6900.00
		Ministry of Power	Electricity Generation	6	64102.68 83892.9	31756.12
			Transmission & Distribution	2	4963.8 9338.7	8131.88
		Ministry of Railways	Railways	1	435 1250	887.87
		Ministry of Road Transport & Highways	Roads & Highways	13	9108.51 9108.51	1324.41
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			27	151477.22	99006.40
5	Assam	Department of Higher Education	Education	1	153.71 153.71	137.84
		Department of Telecommunications	Telecommunication	1	1255.49 276.62	237.98
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 256.16	44.70
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1712 2520	2660.15
		Ministry of Coal	Coal	2	449.23 449.23	218.46
		Ministry of Petroleum & Natural Gas	Energy Storage	3	10768.4 12947.4	11380.61
			Oil & Gas	13	26943.76 39952.9	29745.47
		Ministry of Power	Electricity Generation	1	6285.33 26075.5	26379.99
			Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Railways	Railways	9	19531.77 21246.8	13259.42
		Ministry of Road Transport & Highways	Roads & Highways	50	46497.7 47174.1	15525.95
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			85	180719.01	154385.16
6	Bihar	Department of Higher Education	Education	1	499.21 499.21	449.96

Ongoing Projects State-Wise

JUNE 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Department of Telecommunications	Telecommunication	3	3883.82 2718.14	1010.67
		Department of Water Resources, River Development & GR	Waste & Water	5	2351.43 2351.43	1310.08
			Water Resources	1	1622.27 2430.76	172.97
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3541.56 3541.56	1612.25
		Ministry of Health & Family Welfare	Healthcare	1	1264 1264	27.81
			Healthcare	7	1628 1878	930.01
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	13365.77 13365.8	5198.09
			Waste & Water	1	158.78 158.78	135.72
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 12407	11036.00
			Oil & Gas	6	23776.5 25641.2	76320.94
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	4117.61
		Ministry of Power	Electricity Generation	2	40387.09 43704.6	16706.66
			Transmission & Distribution	3	3119.63 3119.63	281.49
		Ministry of Railways	Railways	22	45121.2 49589.6	20368.59
		Ministry of Road Transport & Highways	Roads & Highways	68	87538.11 89462.4	37836.51
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
Total				128	305608.68	226732.20
7	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			2	61754.13	49216.84
8	Chhattisgarh	Department of Higher Education	Education	1	1188.97 1188.97	0.00
		Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1958.12
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 1109.33	869.21
		Ministry of Coal	Coal	14	34428.39 34428.4	12833.48
			Railways	1	1686.22 2438.53	792.73
		Ministry of Health & Family Welfare	Healthcare	3	975 972.85	536.99
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	2769.04 2769.04	559.54
		Ministry of Power	Electricity Generation	2	25321 25897	7074.85
		Ministry of Railways	Railways	18	34916.47 39751.6	21861.75
		Ministry of Road Transport & Highways	Roads & Highways	22	21163.16 22402.4	9479.64
		Ministry of Steel	Metals & Mining	1	1700 1756.2	263.01
			Steel	5	7180.39 9700.39	6393.55
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
Total				76	201072.2	111839.71
9	Dadra & Nagar Haveli and Daman & Diu	Ministry of Railways	Railways	1	108000 108000	90966.89
		Ministry of Road Transport & Highways	Roads & Highways	2	2107.8 2891.81	1172.46
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			5	171861.93	141356.19
10	Delhi	Department of Higher Education	Education	2	706.49 709.42	357.39
		Department of Telecommunications	Telecommunication	1	248.2 248.2	237.43
		Ministry of Health & Family Welfare	Healthcare	2	4799.19 4799.19	98.17
		Ministry of Housing & Urban Affairs	Real Estate	1	32850 32841	14370.45
			Urban Public Transport	4	51594.36 51594.4	22022.17
		Ministry of Power	Transmission & Distribution	3	3038 3038	2529.25
		Ministry of Railways	Railways	5	19348.46 20637.1	10863.11
		Ministry of Road Transport & Highways	Roads & Highways	4	8530.54 11101.5	9256.08



Ongoing Projects State-Wise

JUNE 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore	
10	PAN India	Department of Telecommunications	Telecommunication	1	645.13 645.13	407.15	
	Total			23	121760.37	60141.20	
11	Goa	Ministry of Railways	Railways	3	7696.49 8074.62	6674.35	
		Ministry of Road Transport & Highways	Roads & Highways	5	2476.3 2252.18	278.52	
	PAN India	Department of Telecommunications	Telecommunication	2	4387.13 4387.13	842.46	
	Total			10	14559.92	7795.33	
12	Gujarat	Department of Higher Education	Education	1	490.63 490.63	339.40	
		Department of Water Resources, River Development & GR	Water Resources	1	20718.17 33412.5	31943.15	
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1668.1 1914.1	1051.54	
		Ministry of Coal	Electricity Generation	4	5421.78 5421.78	2397.89	
		Ministry of Health & Family Welfare	Healthcare	3	1845 2477.48	2187.01	
		Ministry of Housing & Urban Affairs	Real Estate	1	539 539	623.44	
			Urban Public Transport	1	12020.32 12020.3	9166.71	
		Ministry of Labour and Employment	Healthcare	2	763.99 763.99	107.55	
		Ministry of Petroleum & Natural Gas	Energy Storage	3	19472.86 19420.4	16318.85	
			Oil & Gas	11	32704.12 32400	86580.28	
		Ministry of Ports, Shipping and Waterways	Shipping	2	4414.64 4455.25	2630.50	
			Tourism, Hospitality & Wellness	1	573 1238.05	636.91	
		Ministry of Power	Electricity Generation	1	339.35 339.35	370.00	
			Transmission & Distribution	14	64870.45 64870.4	12114.25	
		Ministry of Railways	Railways	27	189399.71 267208	240119.00	
		Ministry of Road Transport & Highways	Roads & Highways	34	38204.78 39075	19225.09	
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84	
	Total			110	455200.03	475028.41	
	13	Haryana	Department for Promotion of Industry & Internal Trade	Logistics Infrastructure	1	763 763	430.00
			Ministry of Health & Family Welfare	Healthcare	1	1299 1646.43	717.42
Ministry of Housing & Urban Affairs			Urban Public Transport	2	11683.71 11683.7	729.80	
			Waste & Water	1	278.01 278.01	228.49	
Ministry of Petroleum & Natural Gas			Energy Storage	1	9028 9028	7482.71	
			Oil & Gas	6	46284.07 49955.1	37673.10	
Ministry of Power			Transmission & Distribution	2	11326 11326	3693.04	
Ministry of Railways			Railways	4	53464 126368	125845.31	
Ministry of Road Transport & Highways		Roads & Highways	20	27779.95 30432.1	17996.90		
PAN India		Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84	
Total			40	223659.87	244013.61		
14	Himachal Pradesh	Department of Higher Education	Education	3	811.15 921.89	684.69	
		Ministry of Power	Electricity Generation	3	5113.04 11168.7	4233.79	
		Ministry of Railways	Railways	3	17005 17005.1	10786.04	
		Ministry of Road Transport & Highways	Roads & Highways	26	23587.87 27705.7	15260.66	
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84	
	Total			37	108271.19	80182.02	
15	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 500.91	484.52	
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 861.37	353.54	
		Ministry of Health & Family Welfare	Healthcare	3	2478 2810.84	1989.22	
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	1059.9 1059.9	323.40	
		Ministry of Power	Electricity Generation	4	22207.77 27945.1	16603.51	

Ongoing Projects State-Wise

JUNE 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
15	Jammu and Kashmir	Ministry of Power	Transmission & Distribution	1	218.6 218.6	3.72
		Ministry of Road Transport & Highways	Roads & Highways	36	33480.75 33631.9	15604.95
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			50	122485.45	84579.70
16	Jharkhand	Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1958.12
		Department of Water Resources, River Development & GR	Water Resources	2	5430.04 12010.3	6213.24
		Ministry of Coal	Coal	27	48656.67 48421	11920.78
			Railways	1	1799.64 2564.34	1713.19
		Ministry of Health & Family Welfare	Healthcare	2	500 958.9	336.00
		Ministry of Housing & Urban Affairs	Waste & Water	3	654.14 654.14	403.16
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 12407	11036.00
			Oil & Gas	2	633.07 633.07	332.89
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	4117.61
		Ministry of Power	Coal	2	2083 2365	1053.41
			Electricity Generation	2	33026 34660	21321.88
			Transmission & Distribution	1	1842.25 1842.25	1648.05
		Ministry of Railways	Railways	13	38167.71 39028.4	11435.06
		Ministry of Road Transport & Highways	Roads & Highways	35	39729.1 39718.4	18438.80
		Ministry of Steel	Steel	5	2340.76 3059.05	1629.15
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			102	259360.86	142774.18
17	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1701.81 1701.81	324.12
		Department of Water Resources, River Development & GR	Water Resources	1	770.16 1606.07	1515.60
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1143.4 1143.4	779.68
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	56804.24 61094.2	40189.40
			Waste & Water	1	162.73 162.73	79.50
		Ministry of Labour and Employment	Healthcare	2	428.92 428.92	111.57
		Ministry of Petroleum & Natural Gas	Energy Storage	1	678 1732	1155.32
			Oil & Gas	5	9662 12693.6	9924.23
		Ministry of Ports, Shipping and Waterways	Shipping	1	153.23 153.23	97.45
		Ministry of Power	Transmission & Distribution	10	23490.99 23491	8710.83
		Ministry of Railways	Railways	20	46557.93 52395.5	20413.77
		Ministry of Road Transport & Highways	Roads & Highways	71	75391.53 79644.5	47464.28
		Ministry of Steel	Steel	1	1043.63 1043.63	628.29
	PAN India	Department of Telecommunications	Telecommunication	3	65496.13 192387	49652.15
	Total			123	283484.7	181046.19
18	Kerala	Department for Promotion of Industry & Internal Trade	Real Estate	1	3805 3805	0.00
		Department of Higher Education	Education	2	2533.45 2744.4	696.00
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	484.57 484.57	227.50
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1957.05 1957.05	752.34
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	8505 11889	6056.26
		Ministry of Power	Transmission & Distribution	1	173.14 173.14	2.08
		Ministry of Railways	Railways	3	2846 5183.64	3679.44
		Ministry of Road Transport & Highways	Roads & Highways	21	55629.95 61868.6	42226.82
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			35	137688.29	102857.28



Ongoing Projects State-Wise

JUNE 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
19	Ladakh	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480 640	509.41
		Ministry of Health & Family Welfare	Healthcare	1	325 325	127.00
		Ministry of Road Transport & Highways	Roads & Highways	3	1184.27 1184.27	985.27
	PAN India	Department of Telecommunications	Telecommunication	1	645.13 645.13	407.15
	Total			6	2634.4	2028.83
20	PAN India	Department of Telecommunications	Telecommunication	1	645.13 645.13	407.15
	Total			1	645.13	407.15
21	Madhya Pradesh	Department of Higher Education	Education	1	496.28 496.28	97.35
		Department of Telecommunications	Telecommunication	3	3883.82 2718.14	1010.67
		Department of Water Resources, River Development & GR	Water Resources	3	23010.18 23323	11584.93
		Ministry of Coal	Coal	15	34550.26 34550.3	4005.46
		Ministry of Health & Family Welfare	Healthcare	2	650 650	262.41
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	14442.2 14442.2	9406.43
			Waste & Water	3	880.74 941.16	823.99
		Ministry of Mines	Metals & Mining	1	1856.36 3800	1009.90
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10088 10088	8672.35
			Oil & Gas	2	45159 45159	6106.50
		Ministry of Power	Electricity Generation	1	20446 20446	2141.47
			Transmission & Distribution	10	46260.32 46260.3	8614.76
		Ministry of Railways	Railways	17	52957.79 64553.6	51956.08
		Ministry of Road Transport & Highways	Roads & Highways	56	39929.41 37650	13864.82
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			119	356364.49	168773.96
22	Maharashtra	Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1958.12
		Department of Water Resources, River Development & GR	Water Resources	6	10857.15 20187.1	23649.57
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	398.75
		Ministry of Coal	Coal	26	12900.3 12900.3	3456.42
		Ministry of Health & Family Welfare	Healthcare	1	189 189	113.40
		Ministry of Housing & Urban Affairs	Urban Public Transport	9	60255.66 74569.4	36722.19
			Waste & Water	2	430.15 430.15	357.33
		Ministry of Labour and Employment	Healthcare	2	455.06 456.83	330.85
		Ministry of Petroleum & Natural Gas	Energy Storage	2	764.49 872.81	640.00
			Oil & Gas	10	41246.03 43994.3	16869.08
		Ministry of Ports, Shipping and Waterways	Shipping	1	6000 6000	5999.89
		Ministry of Power	Transmission & Distribution	5	29470.41 29470.4	3278.49
		Ministry of Railways	Railways	34	266393.54 357833	288698.68
		Ministry of Road Transport & Highways	Roads & Highways	90	72754.2 75303.7	27312.42
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			194	571117.77	459002.03
23	Manipur	Department of Sports	Education	1	906.47 611.74	576.37
		Department of Water Resources, River Development & GR	Water Resources	1	1449.44 1822.24	1848.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499 499	206.83
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6900.00
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Railways	Railways	1	14323 21885.9	16327.07
		Ministry of Road Transport & Highways	Roads & Highways	30	10790.98 10791	6734.14

Ongoing Projects State-Wise						JUNE 2026
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
23	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
		Total		38	104099.35	87387.17
24	Meghalaya	Department of Higher Education	Education	1	494.52 429.7	368.98
		Department of Telecommunications	Telecommunication	1	971.96 180.46	167.23
		Ministry of Health & Family Welfare	Healthcare	1	189 189	170.10
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6900.00
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Railways	Railways	2	9628.9 9646.9	1524.92
		Ministry of Road Transport & Highways	Roads & Highways	12	6148.96 5995.63	1870.46
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			21	93563.8	65796.28
25	Mizoram	Department of Higher Education	Education	1	474.23 474.23	167.55
		Ministry of Petroleum & Natural Gas	Energy Storage	1	225.71 225.71	30.84
			Oil & Gas	1	9265 9265	6900.00
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Road Transport & Highways	Roads & Highways	16	11295.22 11295.2	2582.81
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			22	88125.62	64475.79
26	Nagaland	Department of Higher Education	Education	1	275.63 275.63	263.25
		Ministry of Health & Family Welfare	Healthcare	1	325 325	155.00
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	9492.62 9492.62	6927.63
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Railways	Railways	2	8786.7 8786.7	6889.96
		Ministry of Road Transport & Highways	Roads & Highways	17	5178.71 5732.76	1785.96
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			26	90924.12	70816.39
27	Odisha	Department of Higher Education	Education	3	1882.56 1496.33	1027.18
		Department of Telecommunications	Telecommunication	3	7147.17 3937.81	1958.12
		Department of Water Resources, River Development & GR	Water Resources	3	4612.34 12314.5	13870.04
		Ministry of Coal	Coal	12	36569.58 34261.3	13781.82
			Electricity Generation	1	27212.96 27213	3518.17
		Ministry of Labour and Employment	Healthcare	1	164.6 164.6	16.44
		Ministry of Mines	Metals & Mining	3	5967 8121.17	6207.00
		Ministry of Petroleum & Natural Gas	Energy Storage	2	12886.34 15217	13351.20
			Oil & Gas	5	17956.1 16028.5	72551.00
		Ministry of Ports, Shipping and Waterways	Shipping	1	3004.63 3004.63	2244.12
		Ministry of Power	Electricity Generation	2	22974.75 23674	7339.63
			Transmission & Distribution	2	3065.19 3065.19	280.27
		Ministry of Railways	Railways	1	267.61 267.61	0.00
			Railways	29	42480.98 48238.2	33138.53
		Ministry of Road Transport & Highways	Roads & Highways	37	24529.15 27179.8	14872.29
	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Total			107	272475.09	233372.65
28	PAN India	Department of Telecommunications	Telecommunication	3	65496.13 192387	49652.15
	Puducherry	Department of Higher Education	Education	1	618.34 544.34	543.74

Ongoing Projects State-Wise						JUNE 2026
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
28	Puducherry	Ministry of Railways	Railways	1	713 981	645.24
		Ministry of Road Transport & Highways	Roads & Highways	4	7027.6 7051.29	4114.84
		Total		9	73855.07	54955.97
29	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Punjab	Department of Higher Education	Education	2	559.3 559.3	374.30
		Department of Water Resources, River Development & GR	Water Resources	2	3727.07 5177.86	4543.99
		Ministry of Health & Family Welfare	Healthcare	2	650 924.75	2.00
		Ministry of Housing & Urban Affairs	Waste & Water	2	545.53 553.64	374.66
		Ministry of Petroleum & Natural Gas	Oil & Gas	5	12693.36 12693.4	8406.70
		Ministry of Power	Transmission & Distribution	1	5969 5969	1880.23
		Ministry of Railways	Railways	4	15937.42 15937.8	10378.41
		Ministry of Road Transport & Highways	Roads & Highways	36	48277.52 53212.1	30958.42
		Total		56	150113.33	106135.55
30	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Rajasthan	Department for Promotion of Industry & Internal Trade	Real Estate	1	921.66 921.66	0.00
		Department of Telecommunications	Telecommunication	1	421.65 228.94	152.96
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	2874 2874	984.55
		Ministry of Coal	Electricity Generation	1	4147.07 4147.07	249.95
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	1184.89 1184.89	126.37
		Ministry of Petroleum & Natural Gas	Energy Storage	2	9489.05 9489.05	7717.81
			Oil & Gas	2	10599 10599	6785.30
		Ministry of Power	Transmission & Distribution	17	72773 72773	24166.82
		Ministry of Railways	Railways	22	85254.45 159925	149935.79
		Ministry of Road Transport & Highways	Roads & Highways	23	16620.81 14736.7	7706.33
		Total		76	266039.71	247042.72
31	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Sikkim	Department of Higher Education	Education	2	999.82 962.5	575.56
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 323.26	87.60
		Ministry of Health & Family Welfare	Healthcare	1	250 635.21	667.21
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6900.00
		Ministry of Power	Electricity Generation	2	6686.33 7576.15	6211.07
			Transmission & Distribution	1	4754.42 9129.32	8128.74
		Ministry of Railways	Railways	1	7877 11775	11090.47
		Ministry of Road Transport & Highways	Roads & Highways	8	3158.89 3287.17	105.09
		Total		19	95068.85	82982.58
32	PAN India	Department of Telecommunications	Telecommunication	1	645.13 645.13	407.15
	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1207 1207	314.15
		Ministry of Health & Family Welfare	Healthcare	1	1264 2021.51	522.72
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	63246 63246	33774.00
		Ministry of Mines	Metals & Mining	1	166 166	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	2	1507 2561	1538.28
			Oil & Gas	4	38385 46153	6859.00
		Ministry of Power	Transmission & Distribution	1	548 548	208.24
		Ministry of Railways	Railways	7	8370.7 11242.2	6926.80
		Ministry of Road Transport & Highways	Roads & Highways	42	54183.85 51303.4	24389.42
		Total		61	169522.68	75074.76

Ongoing Projects State-Wise						JUNE 2026
Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
33	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Telangana	Department for Promotion of Industry & Internal Trade	Real Estate	1	2360 2360	42.89
		Department of Higher Education	Education	1	262 262	216.10
		Department of Telecommunications	Telecommunication	2	3462.17 2489.2	857.71
		Department of Water Resources, River Development & GR	Water Resources	4	11670.14 24129.6	12143.40
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	398.75
		Ministry of Coal	Coal	7	2986.57 2986.57	1803.54
		Ministry of Health & Family Welfare	Healthcare	1	1028 1365.95	989.98
		Ministry of Housing & Urban Affairs	Construction	1	644 644	175.79
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	215 215	45.99
		Ministry of Power	Electricity Generation	1	29344.85 29344.8	729.63
			Transmission & Distribution	1	1368 1368	1231.20
		Ministry of Railways	Railways	11	19213.75 22977.8	15721.46
		Ministry of Road Transport & Highways	Roads & Highways	49	36602.98 39152.2	14528.78
		Total		83	171412.07	98102.06
34	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Tripura	Ministry of Petroleum & Natural Gas	Oil & Gas	2	9474.33 9396.51	6979.98
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5577.75
		Ministry of Road Transport & Highways	Roads & Highways	9	6260.76 6260.76	839.35
		Total		14	82600.55	62613.92
35	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Uttar Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	658 658	75.63
		Department of Higher Education	Education	1	246 246	209.68
		Department of Telecommunications	Telecommunication	5	10808.82 9643.14	1695.83
		Department of Water Resources, River Development & GR	Waste & Water	2	1532.96 1532.96	243.43
			Water Resources	3	22310.57 25667.1	13221.80
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3949.13 3949.13	1293.38
		Ministry of Coal	Coal	2	1328.09 1328.09	1294.59
		Ministry of Housing & Urban Affairs	Urban Public Transport	4	27511.5 27511.5	15212.43
			Waste & Water	2	704.2 734.95	659.17
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11068.45 11068.5	8967.90
			Oil & Gas	4	17302.12 17302.1	988.73
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	4117.61
		Ministry of Power	Electricity Generation	1	17195 17195	3646.01
			Transmission & Distribution	5	36697.81 36697.8	5059.42
		Ministry of Railways	Railways	26	95077.38 168712	148687.61
		Ministry of Road Transport & Highways	Roads & Highways	106	127489.74 122329	48276.34
		Total		170	441003.08	302866.40
36	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	Uttarakhand	Department of Higher Education	Education	1	650.85 650.85	391.87
		Department of Water Resources, River Development & GR	Water Resources	1	2584.1 2584.1	1307.15
		Ministry of Health & Family Welfare	Healthcare	2	650 1093.89	601.08
		Ministry of Housing & Urban Affairs	Real Estate	1	150.97 206	56.76
		Ministry of Labour and Employment	Healthcare	1	102.4 297.63	340.30
		Ministry of Power	Electricity Generation	2	6838.35 17312.4	13466.35
		Ministry of Railways	Railways	1	38953 38953	28828.18

Ongoing Projects State-Wise

JUNE 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
36	Uttarakhand	Ministry of Road Transport & Highways	Roads & Highways	38	22143.13 20991.8	7857.04
		Total		49	133826.93	102065.57
37	PAN India	Department of Telecommunications	Telecommunication	2	61754.13 188645	49216.84
	West Bengal	Department of Higher Education	Education	1	500 442	418.86
		Department of Telecommunications	Telecommunication	2	3462.17 2489.2	857.71
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 154.73	102.04
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1877.3 1877.3	656.55
		Ministry of Coal	Coal	10	12282.26 12282.2	2010.43
		Ministry of Mines	Construction	1	255.37 255.37	98.92
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 12407	11036.00
			Oil & Gas	9	16102.65 17047.2	11691.27
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	4117.61
			Shipping	1	832.25 832.25	0.00
		Ministry of Power	Electricity Generation	3	20091.84 21644.6	4876.34
			Transmission & Distribution	2	751.63 751.63	143.20
		Ministry of Railways	Railways	16	49559.1 60771	39116.73
		Ministry of Road Transport & Highways	Roads & Highways	23	15392.12 14807.2	7569.72
		Ministry of Steel	Steel	6	6733.06 6733.06	1934.13
		Total		81	205345.79	133846.35




Table 3: Completed Projects



Completed Projects During Month						JUNE 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	(Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
Ministry of Civil Aviation						
Aviation & Aviation Infrastructure						
1	Goa Airport Terminal Building Extension Project (Airport Authority of India [AAI]) 701105	Goa	11/2017 (12/2019)	(12/2021) (04/2026)	255.69 (255.69)	161.06
Total (1)					255.69	161.06
Ministry of Petroleum & Natural Gas						
Energy Storage						
2	Rajasthan Refinery Project (Ministry of Petroleum & Natural Gas) 701263	Rajasthan	10/2017 (10/2017)	(10/2022) (06/2026)	43129 (79459)	70293.57
3	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) 400035	Tripura	06/2022 (06/2022)	(09/2025) (06/2026)	656 (656)	546.57
Total (2)					43785	70840.14
Oil & Gas						
4	HP TDAE Unit in Mumbai Refinery (Hindustan Petroleum Corporation Limited) 709760	Maharashtra	06/2024 (06/2024)	(04/2026) (06/2026)	240 (240)	160.8
5	ATF Pipeline from Jawaharlal Nehru Port Trust to Navi Mumbai International Airport (Indian Oil Corporation Limited [IOCL]) 709782	Maharashtra	08/2022 (08/2022)	(08/2025) (06/2026)	165 (165)	103.36
Total (2)					405	264.16
Ministry of Power						
Transmission & Distribution						
6	Transmission Scheme for Solar Energy Zone in Ananthpuram 2500MW and Kurnool 1000MW (Power Grid Corporation of India Limited [POWERGRID]) 611967	Andhra Pradesh	09/2023 (09/2023)	(09/2025) (05/2026)	823 (-)	798.31
7	Transmission System for Kurnool Wind Energy Zone/ Solar Energy Zone Part-A and Part-B (Power Grid Corporation of India Limited [POWERGRID]) 900808	Multi-States (Telangana, Andhra Pradesh)	11/2022 (03/2023)	(11/2024) (05/2026)	3546.94 (-)	3546.94
8	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part H (Power Grid Corporation of India Limited [POWERGRID]) 611948	Rajasthan	10/2023 (10/2023)	(04/2025) (06/2026)	1910 (-)	1910
Total (3)					6279.94	6255.25
Ministry of Road Transport & Highways						
Roads & Highways						
9	Rehabilitation and Up-gradation from Km 170700 Bhadrachalam to Km 234567 Konta on NH-30 to Two lane with Paved Shoulder in the State of Andhra Pradesh on EPC mode. (MoRTH) 617907	Andhra Pradesh	12/2021 (09/2022)	(09/2024) (04/2026)	436.09 (-)	240.15
10	Construction of bypass road to Adoni town connecting NH-167 Hagari - Jadcharla road from km.62/700 to 71/400 in Kurnool District in the State of Andhra Pradesh. (MoRTH) 617990	Andhra Pradesh	03/2023 (02/2024)	(11/2025) (11/2025)	242 (-)	99.13
11	Widening to two lane with paved shoulder of Rampachodavaram - Koyyuru section of NH 516E from Km 43700 to Km 113820 in the State of Andhra Pradesh on EPC mode Job No. 737 (MoRTH) 618145	Andhra Pradesh	03/2022 (01/2023)	(01/2025) (04/2026)	568.12 (-)	324.96
12	Widening and Reconstruction of existing road to four lane from Km.56400 to Km 120300 i.e. from B.Kothapalli Junction to Gorantla excluding Kadiri Bypass from Km 70200 to Km 77105 of NH 716G in the State of Andhra Pradesh on EPC mode Job no. 742 (MoRTH) 618161	Andhra Pradesh	03/2022 (09/2023)	(12/2025) (03/2026)	839.98 (-)	415.11
13	Rehabilitation and upgradation of NH-167AD from Macherla to Dachepalli via Paluvai Junction, Rentachinthala, Gurazala from Km.0.000 to 43.659 to two lane with paved shoulders in the state of Andhra Pradesh job-729 (MoRTH) 618191	Andhra Pradesh	01/2022 (01/2023)	(01/2025) (02/2026)	403.22 (-)	256.17
14	Rehabilitation and Up-gradation of Pasarlupudi to Dhindi section from Km 105/170 to Km 126/510 of NH -214 New NH -216 to two lane with paved shoulder in the state of Andhra Pradesh under NHDP-IV (MoRTH) 618237	Andhra Pradesh	03/2017 (09/2017)	(09/2019) (01/2026)	263.45 (-)	158.8
15	Two laning with paved shoulders of Gondiguda to Araku upto Bhallaguda section of NH 516E (MoRTH) 618258	Andhra Pradesh	08/2020 (09/2021)	(09/2023) (12/2025)	296.66 (289.11)	275.38
16	Two laning with paved shoulders of Paderu to Gundiguda Section of NH 516E (MoRTH) 618259	Andhra Pradesh	08/2020 (03/2021)	(03/2023) (10/2025)	222.61 (-)	181.04
17	Six Laning of Vijayawada Bypass from Gollapudi to Chinnakani in Vijayawada - Gundugolanu Section from km. 30.00 to km. 47.881 Pkg-IV (NHAI) 618527	Andhra Pradesh	01/2020 (07/2021)	(01/2024) (05/2026)	1194.57 (1757.82)	862.83
18	Khammam-Devarapalle Pkg IV [4L Access Controlled Greenfield from Recherla village to Gurvaygudem village Design Chainage 105236 to 132664] (NHAI) 618748	Andhra Pradesh	11/2020 (09/2022)	(09/2024) (01/2026)	569.37 (752.02)	499.99



Completed Projects During Month

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	(Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
19	4L PS from Mandlem Existing Km. 38.000/Design Km.30.600 to Atmakur Existing Km.73.000/Design Km 66.115 of NH340C Package2 (NHAI) 618919	Andhra Pradesh	03/2023 (11/2023)	(11/2025) (11/2025)	887.28 (913.03)	550.42
20	6L Standalone Flyovers at Raha, Demow, Borghat, Kathiatali junctions and ROB at Jagiroad on stretches of NH 36 and NH 27 (NHAI) 618576	Assam	03/2022 (12/2022)	(06/2024) (10/2024)	280.75 (255.53)	212.27
21	Widening/Improvement to 4 -Lane with Paved Shoulder from Ch. 88.000km to Ch.99.930 km Design Ch.84.100km to Ch.96.000 km of Sagunbashi forest near Nichinta to starting of Krishnai Bypass Section of Bilasipura Guwahati road NH 17 on EPC Package-7 (NHIDCL) 618285	Assam	03/2021 (10/2023)	(10/2025) (08/2025)	286.72 (-)	220.81
22	Widening/Improvement to 4-Lane with Paved Shoulder from KM 113300 to Km 146230 Design Chainage 113830 to 145712 of Kwaram Taro Village - Dillai Section in Assam on EPC Package-6 (NHIDCL) 618327	Assam	09/2021 (07/2022)	(07/2024) (03/2025)	625.64 (-)	578.19
23	Construction of 4/6 Laning from existing Km 159.400 of NH-36 to existing Km 102.500 of NH-39 and upto end point of Assam portion [Design Km 118.050 to design Km 132.375] Total New Alignment length of 14.325 Km of Daboka - Dimapur Section Dimapur Bypass in the state of Assam under SARDP-NE 'Phase-A' on EPC mode Assam Portion (NHIDCL) 618330	Assam	03/2018 (11/2019)	(11/2022) (11/2025)	511.02 (-)	671.35
24	Widening / Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Kachukhana Harichara Paglagaunj to Dhubri - Phulbari Bridge approach Package-II of Srirampur - Dhubri Section of NH-127B from existing Km 28.050 to Km 55.060 Design Km 27.650 to Km 54.154, Design Length26.504 Km under JICA ODA Loan assistance Phase-V [Srirampur - Dhubri Pkg-2] (NHIDCL) 618372	Assam	03/2022 (01/2023)	(01/2025) (06/2025)	909.02 (-)	683.81
25	Rehabilitation & Widening work for 2 Lane with Paved Shoulder of Existing NH-80 from km 70.15 to Km 121.025 of Munger-Suttanganj -BhagatpurMirzachowki section on EPC Mode in the State of Bihar. (MoRTH) 617959	Bihar	03/2021 (02/2023)	(01/2025) (11/2025)	477.54 (-)	343.05
26	4L Elevated Highway and at grade improvements at Gopalganj Town from Km. 384.000 to Km. 386.750 on NH-27 (NHAI) 618570	Bihar	10/2021 (03/2022)	(08/2024) (05/2025)	325.57 (248.92)	241.89
27	4L of Galgalia - Bahadurganj section from Km 0.000 to Km 49.000 Package-I of NH327E (NHAI) 618582	Bihar	01/2021 (01/2022)	(01/2024) (02/2025)	1282.97 (1282.97)	816.12
28	4L of Bahadurganj Araria section from Km 49.000 to Km 94.000 Package-II of NH-327E (NHAI) 618583	Bihar	01/2021 (01/2022)	(01/2024) (01/2025)	1358.77 (1358.77)	812.28
29	Ara - Mohania Pkg-II (NHAI) 618774	Bihar	08/2020 (01/2021)	(07/2023) (11/2025)	984.63 (827.51)	798.25
30	4L of Aurangabad-Paithan (NHAI) 618779	Bihar	09/2022 (01/2023)	(07/2024) (12/2025)	1505 (349.96)	328.32
31	Aunta - Simaria including Ganga Bridge (NHAI) 618839	Bihar	01/2017 (08/2018)	(02/2022) (03/2026)	1309.47 (2107.68)	1209.46
32	4L of Bal. works of Patna - Gaya -Dobhi Pkg-II from km. 39.00 to km. 83.00 of Old NH-83 (NHAI) 618915	Bihar	09/2019 (11/2020)	(11/2022) (05/2025)	1637.29 (777.2)	764.68
33	4L of Bal. works of Patna - Gaya -Dobhi Pkg-III from km. 83.00 to km. 127.217 of Old NH-83 (NHAI) 618916	Bihar	09/2019 (11/2020)	(11/2022) (05/2025)	1077.46 (799.7)	803.33
34	Muzaffarpur - Sonbarsa Section of NH-77 from km 2.800 to km 89.000 (NHAI) 619320	Bihar	05/2011 (05/2011)	(11/2013) (03/2026)	2290.72 (2311.1)	2308.19
35	Strengthening and widening of existing 2 lane road to two lane paved shoulder from km 7.750 to 26.542 & km. 32.093 to 45.786 of NH-130 on EPC mode in the state of chhattisgarh.job No. 130-CG-2017-18-348 (MoRTH) 617973	Chhattisgarh	11/2017 (05/2019)	(11/2020) (06/2023)	188.8 (-)	107.79
36	Up-gradation of NH-930 Sherpar to Kohka from Km.67880 to Km.114860 to 2LPS in Chhattisgarh under EPC mode (MoRTH) 618064	Chhattisgarh	03/2020 (05/2022)	(05/2024) (12/2025)	278.97 (-)	210.82
37	Up-gradation of NH-130C Abhanpur to Paund from NH Km. 0000 to KM 40380 to two lane with paved shoulders in the State of Chhattisgarh on EPC mode. (MoRTH) 618078	Chhattisgarh	12/2020 (03/2022)	(09/2023) (08/2025)	193.16 (-)	116.5
38	Conversion of Partially Excavated Escape Tunnel to Uni-Directional 2L Tunnelincluding construction of cross passages and approach roads on either side of the tunnel from Km 12.732 to Km 14.568 of Kiratpur to Nerchowk Section of NH-21 (NHAI) 618849	Chhattisgarh	05/2022 (09/2022)	(03/2024) (04/2026)	444.21 (412.88)	394.73
39	6L Access Controlled Highway from DND Maharani Bagh - Jn. with Jaitpur - Pushta Road of NH-148NA from km. 0.00 to km. 9.00 in NCR (NHAI) 618578	Delhi	07/2020 (01/2022)	(07/2024) (04/2026)	1467.44 (2510.34)	1652.29

Completed Projects During Month

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	(Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
40	Vadodara Mumbai Expressway Ena -Kim Phase IB - Pkg VI [Km 217.500 to Km 254.430] (NHAI) 618464	Gujarat	05/2020 (12/2021)	(12/2023) (06/2025)	2271.86 (4297.28)	2991.42
41	Vadodara Mumbai Expressway Gandeva to Ena Phase IB - Pkg VII [Km 190.00 to Km 217.500] (NHAI) 618465	Gujarat	07/2020 (11/2021)	(11/2023) (01/2026)	1710.3 (3392.21)	2451.01
42	Ahmedabad - Dholera Pkg I from km. 0.00 to km. 22.00 [Sardar Patel Ring Road - Sindhrej Village] (NHAI) 618501	Gujarat	05/2020 (01/2022)	(01/2024) (01/2026)	1298 (1421.05)	1385.83
43	Ahmedabad - Dholera Pkg II from km. 22.00 to km. 48.52 [Sindhrej Village - Vejallka Village] (NHAI) 618502	Gujarat	05/2020 (01/2022)	(01/2024) (04/2026)	1415.34 (1729.69)	1785.68
44	Sanchoe - Santalpur from km 67.000 - km 99.000 of NH-754K AJ-RGBS- Package-3 (NHAI) 618614	Gujarat	02/2020 (08/2021)	(08/2023) (01/2024)	752.3 (765.25)	601.6
45	Pipli Bhavnagar-Package 1 from km 136.025 to km 169.328 (NHAI) 618699	Gujarat	03/2018 (02/2019)	(09/2021) (03/2024)	819.14 (1297.38)	975.85
46	4L Kodinar - Veraval Package VI from km. 222.400 to km. 230.00 Kodinar Bypass of NH-8E NH 51 new (NHAI) 618834	Gujarat	03/2022 (04/2022)	(09/2023) (05/2025)	162.73 (192.01)	189.95
47	4L of Bal Works of Talaja - Mahuva from 54.990 km. to 100.450 km. of Old NH-8E Package-II (NHAI) 618835	Gujarat	08/2020 (03/2021)	(09/2022) (05/2024)	698.4 (735.51)	726.01
48	6L of Chiloda-Naroda section from Km. 540.595 to Km. 555.595 of NH-8Package-VII (NHAI) 619067	Gujarat	11/2016 (05/2017)	(05/2019) (02/2026)	356.6 (463.03)	443.07
49	4L of Bal Works of Mahuva to Kagvadar from 100.450 Km. to 140.470 Km. of NH-8E Pkg- III (NHAI) 619147	Gujarat	08/2020 (03/2021)	(09/2022) (07/2024)	603.08 (628.49)	624.43
50	4L of Bhavnagar - Talaja Package-I from Km. 6.945 to Km. 54.990 of Old NH-8E (NHAI) 619148	Gujarat	03/2016 (02/2017)	(08/2019) (06/2024)	1185.66 (1343.16)	1316.53
51	Delhi-Amritsar-Katra Expressway Phase-I Pkg-III from Junction with Jind-Panipat road NH-352A near Gangana village to Junction with Jind-Karnal road NH-709A near Alewa village Km 60800 to Km 91400 (NHAI) 618484	Haryana	12/2020 (12/2021)	(12/2023) (11/2025)	1606.27 (1813.91)	1322.85
52	Delhi-Amritsar-Katra Expressway Phase-I Pkg-IV from Junction with Jind-Karnal road NH-709A near Alewa village to Junction with Ambala-Kaithal-Hissar road NH-152 near Kharak Pandwa village Km 91400 to Km 120250 (NHAI) 618485	Haryana	01/2021 (12/2021)	(12/2023) (11/2025)	1306.95 (1578.66)	1098.84
53	Rehabilitation and Upgradation to 2-lane/Intermediate lane configuration of Ashyari-Shri Kyari Section km 50.000 to km 75.000 of NH-707 in the state of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode. (MoRTH) 618050	Himachal Pradesh	08/2020 (09/2021)	(09/2023) (12/2025)	345.89 (359.56)	232.82
54	Construction & Upgradation to 2 lane with paved shoulder from Design Km. 31.449 Khellani Ex. Km 44.946 to Km 51.700 Prem Nagar Ex. Km 68617 of 20.251 Km length on Khellani - Kishtwar - Chattroo section of NH-244 in the UT of J&K on EPC Mode under NHO-Gen PKG- 1 (NHIDCL) 618396	Jammu and Kashmir	02/2021 (03/2021)	(09/2022) (11/2024)	486.45 (-)	300.52
55	4L from km 196.87 Sankha to km 219.6 Khajuri on NH-75 [Rehla / Garhwa Bypass] (NHAI) 618829	Jharkhand	09/2020 (10/2021)	(10/2023) (03/2025)	1129.48 (1129.48)	790.59
56	4L of Mehgama - Hansdiha from km. 41.900 to km. 93.000 of NH -133A Pkg-II (NHAI) 618946	Jharkhand	03/2022 (05/2023)	(05/2025) (05/2026)	1479.72 (1568.18)	1034.52
57	Balance work of Rehabilitation and upgrading to 2lane/2lane with paved shoulder configuration and strengthening from from Km 343.80 to 400.33 of Gowribidanur-Chik Ballapur section in the state of Karnataka Under Annual Plan 2021-22 under EPC Mode.-952 (MoRTH) 617954	Karnataka	03/2022 (02/2023)	(02/2025) (10/2025)	398.48 (-)	242.02
58	Challakere to Hariyur section from km 358.500 to km 414.205 of NH-150 A (NHAI) 618698	Karnataka	03/2018 (01/2021)	(01/2023) (12/2025)	1167.52 (1873.58)	1243.48
59	4L of Hubli - Hospet Section of NH-63 from Km 128.850 to Km 272.571 (NHAI) 619121	Karnataka	07/2016 (03/2017)	(03/2020) (03/2026)	2531.99 (3619.32)	3522.85
60	Hospet - Chitradurga from km. 299.00 to km. 418.750 (NHAI) 619144	Karnataka	03/2015 (02/2016)	(08/2018) (06/2026)	1519.72 (387.48)	331.26
61	Construction of Mihona bypass, Lahar bypass, Daboh bypass & Bhander Bypass total length 20.60 km to 2-lane with paved shoulder from on Mihona-Bhander-MP/UP border section of NH 552E in the State of Madhya Pradesh on EPC mode (MoRTH) 618045	Madhya Pradesh	03/2022 (06/2023)	(12/2024) (07/2025)	179.18 (-)	74.89
62	Indore - Gujarat / MP Border from km. Km 9.500 to Km 171.000 of NH-59 in MP (NHAI) 618625	Madhya Pradesh	12/2009 (08/2010)	(02/2013) (02/2026)	1175 (217.22)	191.43

Completed Projects During Month

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	(Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
63	4L of Sagar - Mohari from Km.8 to Km.50 Pkg-I (NHAI) 618665	Madhya Pradesh	03/2021 (04/2022)	(04/2024) (03/2026)	790.78 (660.38)	555.28
64	Indore - Harda Pkg-III [Nanasa to Pidgaon Section from km 95.000 to km 142.445] (NHAI) 618695	Madhya Pradesh	01/2020 (10/2021)	(10/2023) (04/2026)	1146.22 (1240.64)	758.23
65	Balance work of 4L of Nauradehi Sanctuary de-scoped stretch of Hiran River to Sindoor River from Km. 66.00 to 130.00 NH-12 New NH-45 (NHAI) 618701	Madhya Pradesh	01/2021 (07/2021)	(07/2023) (07/2025)	178.18 (153.15)	143.37
66	Rehabilitation & up-gradation for Talere Gaganbawada - kolhapur Road NH 166G stretch start from km. 0/00 to Km. 06/00 and km. 13/00 to km 19/440 of NH-166G, length 12.440 km in the State of Maharashtra. (MoRTH) 618099	Maharashtra	03/2024 (10/2024)	(04/2026) (10/2025)	164.13 (-)	115.51
67	Vadodara Mumbai Expressway Phase II - Pkg XI [Km. 77.000 to Km. 103.400] Ganjad - Talsari (NHAI) 618468	Maharashtra	06/2020 (05/2022)	(05/2024) (01/2026)	1524.71 (1913.95)	901.76
68	Tarsod - Fagne section of NH-6 (NHAI) 618638	Maharashtra	06/2016 (01/2019)	(07/2021) (04/2026)	2267.99 (2560.5)	2213.75
69	Chakur Loha Section of NH-361 from km 114.600 to km 187.80 (NHAI) 618652	Maharashtra	03/2018 (03/2019)	(03/2021) (02/2026)	1241.38 (3342.11)	1717.21
70	4L of existing 2/4L stretch from Lonand to Dive Ghat Km 166.400 to Km 220.900 of Mohol Alandi section of NH-965 Pkg - V (NHAI) 619209	Maharashtra	10/2021 (05/2022)	(05/2024) (03/2026)	1709.56 (2049.51)	1295.04
71	Up-gradation to 2-lane with paved shoulders of Ngopa - Pawlrang section of NH 102B of Aizawl - Imphal Economic Corridor from Existing Chainage km 32.796 to km 72.030 [Design Chainage km 31.280 to km 68.170] in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-2 Keifang-Tuivai Pkg-2 (NHIDCL) 618341	Mizoram	09/2021 (09/2023)	(02/2025) (06/2025)	523.78 (-)	426.69
72	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 250.00 Lunglei to km 298.00 on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-6 (NHIDCL) 618381	Mizoram	09/2019 (12/2019)	(06/2023) (05/2025)	768.76 (-)	168.78
73	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 298.00 to km 339.00 on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-7 (NHIDCL) 618382	Mizoram	09/2019 (10/2020)	(04/2024) (05/2025)	605.76 (750.32)	132.33
74	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 166. 000 to Km 208.000 Package-4 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-4 (NHIDCL) 618384	Mizoram	09/2019 (10/2019)	(04/2023) (04/2025)	899.45 (-)	191.68
75	6L of Varadharajula to Kumarajapet from km 0.000 to km 43.800 of NH-716B Pkg-I (NHAI) 618771	Multi-States (Andhra Pradesh, Tamil Nadu)	02/2021 (12/2022)	(12/2024) (02/2026)	1924.75 (1887.38)	1120.2
76	6L of Aurangabad to Bihar-Jharkhand border Chordaha section from km. 209.827 to Km. 249.525 of NH-19 PKG-02 (NHAI) 618532	Multi-States (Bihar, Jharkhand)	06/2021 (03/2022)	(03/2024) (04/2026)	1822.46 (738.11)	611.43
77	6L of Dhanara - Hatibena Section from Km 124.611 to km 146.50 of NH-130-CD Package OD-1 (NHAI) 618676	Multi-States (Chhattisgarh, Odisha)	02/2021 (03/2022)	(03/2024) (03/2026)	477.76 (638.32)	359.28
78	6L from Belgaum to Sankeshwar Bypass from Km. 515.000 to Km. 555.017 of NH-48 Pkg-I (NHAI) 618515	Multi-States (Maharashtra, Karnataka)	11/2021 (10/2022)	(04/2025) (03/2026)	1479.3 (1237.04)	1199.4
79	Mangloor to Telangana Maharashtra Border (NHAI) 618624	Multi-States (Maharashtra, Telangana)	03/2018 (04/2019)	(04/2021) (10/2025)	1082.65 (1323.12)	1011.7
80	4L of Rajura-Korpana-Adilabad Road upto M.S. Border from km 32.910 to km 89.090 of NH-353B (NHAI) 618938	Multi-States (Maharashtra, Telangana)	03/2022 (10/2022)	(10/2024) (03/2026)	1013.33 (1274.63)	699.33
81	4L Greenfield a Malout bypass from ch. Km 44.500 to ch. Km 35.500 on NH-07 and Ch. Km 0.000 to Km 6.984 on NH-09 bMandi Dabwali Bypass from Ch. 38.450 Km to Km 27.910 Pkg-02 (NHAI) 618760	Multi-States (Punjab, Haryana)	11/2021 (12/2022)	(07/2024) (01/2026)	646.42 (556.09)	571.11
82	4L Ambala - Kalaamb from Km. -0.800 to Km. 33.015 of old NH-72 (NHAI) 618935	Multi-States (Punjab, Haryana)	10/2022 (06/2023)	(06/2025) (02/2026)	1183.7 (1190.34)	706.54
83	4L of left out existing road section from Lalgopalganj Km 161.450 to Nawabganj Km 180.200 in Prayagraj (NHAI) 618755	Multi-States (Rajasthan, Uttar Pradesh)	03/2024 (04/2025)	(03/2026) (04/2026)	159.53 (100.74)	93.24
84	Akshardham - DL/UP Border Pkg-01 (NHAI) 619122	Multi-States (Uttar Pradesh, Delhi)	09/2020 (06/2022)	(12/2024) (08/2024)	1479.22 (1476.75)	1399.88
85	4L from Km 219.600 Khajuri to Km 260.483 Wyndhamganj on NH-75 Sec-V (NHAI) 618828	Multi-States (Uttar Pradesh, Jharkhand)	03/2022 (09/2023)	(09/2025) (05/2026)	1436.49 (1465.55)	959.96



Completed Projects During Month

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	(Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
86	Construction of Rudrapur Bypass Section from Km. 0.000 to 20.640 in the state of Uttar Pradesh & Uttarakhand (NHAI) 618912	Multi-States (Uttar Pradesh, Uttarakhand)	03/2023 (01/2024)	(01/2026) (03/2026)	1051.73 (1117.17)	670.74
87	4L/2L PS of Govindpur Raiganj - Chas - WB border section of from km. 0.00 to km. 56.889 of Old NH-32 (NHAI) 619104	Multi-States (West Bengal, Jharkhand)	03/2016 (12/2017)	(12/2019) (09/2025)	1139.65 (1154.8)	1064.7
88	Widening of existing single lane to intermediate lane road from Mokokchung to Chare via Dikhu in the state of Nagaland on EPC mode (MoRTH) 618002	Nagaland	02/2021 (06/2023)	(06/2025) (11/2025)	192.93 (-)	110.98
89	Construction of 4/6 Laning from Km 132.375 to Km 153.058 Total New Alignment length of 20.683 Km of Daboka-Dimapur Section Dimapur Bypass Nagaland Portion of NH-36 & 39 in the State of Nagaland on EPC basis under PhaseA of SARDP-NE (NHIDCL) 618329	Nagaland	02/2017 (09/2017)	(09/2020) (09/2025)	819.39 (-)	635
90	Construction of bypass to Nayagarh town from km 235.469 to 252.482 of NH-57 including land acquisition in the state of Odisha. (MoRTH) 617924	Odisha	01/2022 (05/2023)	(04/2025) (02/2026)	300.33 (-)	103.64
91	Balance work of Panikoili Rimoli Section of new NH-20 from Km 0.00 to Km. 163.000 (NHAI) 618819	Odisha	09/2020 (03/2021)	(03/2022) (12/2023)	183.03 (200.79)	185.4
92	4-L of Rajamunda to Barkote Section of NH-23 from km. 287.200 to km. 337.185 (NHAI) 618913	Odisha	10/2017 (12/2018)	(06/2021) (07/2025)	609.63 (630.97)	608.19
93	6L of Bhubaneswar - Jagatpur - Chandikhole Section of NH-16 (NHAI) 619075	Odisha	01/2009 (12/2011)	(06/2014) (04/2026)	639.3 (632.89)	579.23
94	Delhi-Amritsar-Katra Expressway Phase-I Pkg-VII from Junction with Patiala-Bathinda road NH-7 near Bhawanigarh to Junction with Ludhiana-Malerkotla SH-11 near Bhogiwal village Km 188830 to km 225770 (NHAI) 618487	Punjab	12/2020 (07/2022)	(07/2024) (02/2026)	1759.82 (1774.32)	1695.83
95	Construction of Two lane with Paved Shoulder for Fatehpur Bypass Design Km 0.000 to Km 7.400 , Mandawa Bypass Design Km 20.925 to Km 27.300 & Jhunjhunu Bypass Design Km 41.625 to Km 54.689 of NH-11 on EPC Mode in the state of Rajasthan . (MoRTH) 617891	Rajasthan	03/2022 (02/2023)	(08/2024) (09/2025)	186.29 (-)	78.06
96	Upgradation to Two Lane Paved Shoulder in km 33/0 to 126/520 of NH-23 Old NH-11B Kothun-Lalsot-Karoli-Dholpur road in the state of Rajasthan under EPC mode Length-93.52 Km. (MoRTH) 617900	Rajasthan	12/2021 (09/2022)	(09/2024) (05/2026)	150.11 (-)	12.25
97	Up-gradation to 2 lane with Paved shoulder from Charbhujia at Design km 0.00 existing km 150.00 to Neechli Oden Nathdwara at Design ch. Km 88.800 existing km 55.950 of NH-162E on EPC mode. (MoRTH) 618093	Rajasthan	02/2022 (09/2023)	(09/2025) (04/2025)	838.43 (-)	43.9
98	Upgradation of two lane paved shoulder from Shahpura existing km. 0.00 Design Ch. 000 to Thanagazi existing Km.37352 Design Ch. 36810 of NH-248A on EPC mode in the State of Rajasthan. (MoRTH) 618118	Rajasthan	03/2022 (02/2023)	(07/2024) (07/2025)	174.34 (-)	100.48
99	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-14 Ch. 388.420 to Ch. 419.000 [Junction with NH- 76 to Junction with NH-12 near village Ummedpura] (NHAI) 618456	Rajasthan	11/2019 (05/2021)	(05/2023) (03/2025)	1119.35 (1194.17)	1114.19
100	4L Greenfield spur from Delhi-Vadodara Greenfield expressway near Bandikui to Jaipur (NHAI) 619063	Rajasthan	03/2022 (11/2022)	(11/2024) (10/2025)	1636.15 (2170.39)	1283.3
101	Dindigul Bypass - Samyanallore from km. 373.275 to km. 426.00 (NHAI) 618562	Tamil Nadu	06/2005 (07/2006)	(01/2009) (07/2025)	579 (295.5)	141.09
102	Trichy 135.800 to Karur 218.000 section of NH-67 - Trichy Bypass (NHAI) 618743	Tamil Nadu	12/2006 (01/2008)	(07/2010) (06/2026)	876.88 (360.88)	336.71
103	4L of Vadugapatti to Therkuvenganallur Rajapalyam section from km 36.000 to km 71.600 of NH-744 (NHAI) 618745	Tamil Nadu	02/2022 (04/2023)	(04/2025) (06/2026)	1317.6 (1137.16)	954.04
104	Tuticorin - Tirunelveli from km. 0.00 to km. 47.250 (NHAI) 618773	Tamil Nadu	11/2009 (04/2010)	(04/2012) (06/2014)	449.85 (452.48)	2.8
105	Four Laning of Trichy - Dindigul from km. 333.00 to km. 421.273 of NH-45 (NHAI) 618874	Tamil Nadu	12/2006 (01/2008)	(07/2010) (06/2026)	1003.11 (435.81)	377.7
106	4L of Sethiyathope -Cholapuram section from Km. 65.960 to Km. 116.440 section of NH45 C Pkg-II (NHAI) 618897	Tamil Nadu	03/2017 (08/2018)	(08/2020) (11/2025)	2356.19 (2356.9)	1697.35
107	Salem - Ulundurpet section from km 0.313 to km 136.670 of NH-68 (NHAI) 618943	Tamil Nadu	12/2006 (01/2008)	(01/2011) (11/2025)	861.23 (1019.85)	940.44
108	Thumbipadi-Namakkal from km. 180.00 to km. 248.625 Package No. NS-2/BOT/TN-02 (NHAI) 619083	Tamil Nadu	06/2005 (08/2006)	(02/2009) (06/2026)	255.53 (395.43)	392.41

Completed Projects During Month

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	(Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
109	Start of Karur Bypass - Dindigul from km. 292.600 to km. 305.600 Contract Package No. NS2/BOT/TN-4 (NHA) 619084	Tamil Nadu	08/2005 (10/2006)	(04/2009) (12/2025)	461.54 (515.03)	222.72
110	Rehabilitation & upgradation of NH - 167 from design km 187.723 to 234.434 Miryalaguda to Kodad section to two lane with paved shoulder on EPC mode in the state of Telangana (MoRTH) 617992	Telangana	03/2018 (09/2018)	(09/2020) (01/2026)	322.81 (322.81)	154.47
111	Widening to 2/4 Lane with paved shoulders from Km 182.120 to Km 227.600 of NH 167 on Haggari-Jadcherla Road on EPC mode under NHO in the state of Telangana (MoRTH) 617996	Telangana	10/2016 (02/2017)	(02/2019) (04/2024)	298 (-)	238.2
112	Rehabilitation and upgradation to two lane with paved shoulders from Km 0/000 to 72/6 of NH-365 Nakrekal to Tanamcherla section under NHDP IV in the state of Telangana under EPC mode (MoRTH) 618026	Telangana	06/2017 (11/2017)	(10/2019) (05/2025)	605.08 (-)	585.2
113	Widening & strengthening of existing carriageway in 2 lane with paved shoulders from km 25/0 to 59/2 design Ch km 25.467 to 59.200 of NH - 353C on EPC mode in the state of Telangana (MoRTH) 618132	Telangana	02/2018 (06/2018)	(06/2020) (01/2025)	206.13 (-)	318.62
114	Widening to Two lane with Paved shoulders from km.40/410 to 84/037 of Thirumanlagiri-- Suryapet Section of NH-365B earstwhile section of SH-16 (MoRTH) 618142	Telangana	01/2017 (05/2017)	(05/2019) (08/2023)	244.54 (-)	147.48
115	widening to two lane with Paved shoulders from Km.0/970 to Km.40/410 of Jangaon - Thirumal giri of NH- 365B in the state of Telangana on EPC mode under NHO Annual Plan 2016-17 (MoRTH) 618143	Telangana	03/2017 (11/2017)	(10/2019) (10/2023)	197 (-)	3.24
116	Rehabilitation & Upgradation of Road from Km 0.00 to Km 18.600 Total length- 18.600 km of Kumarghat-Kailashahar section on NH-208 to 2-lane with Paved shoulder on EPC bais under NHO (NHIDCL) 618386	Tripura	02/2020 (07/2020)	(01/2022) (12/2024)	277.5 (302.03)	273.04
117	Construction of four-lane elevated viaduct from km.4634 to km.6345 on NH-24A including Retaining wall, service lane, at grade road and improvement of junctions, on EPC mode (MoRTH) 618008	Uttar Pradesh	03/2021 (03/2022)	(09/2023) (09/2024)	185.09 (269.81)	200.32
118	Improvement and upgradation to two lane with Paved Shoulder configuration from existing km 55.00 to km 90.00 Design length 34.76 of NH-227A near Chhaphia Village to near Sikriganj in the State of UP on EPC Mode. (MoRTH) 618110	Uttar Pradesh	11/2021 (11/2022)	(05/2024) (05/2025)	307.11 (-)	136.8
119	6L Greenfield Kanpur - Lucknow Expressway Pkg II from km. 28.500 to km. 73.744 (NHA) 618498	Uttar Pradesh	12/2021 (11/2022)	(05/2025) (02/2026)	2471.56 (2489)	1439.5
120	6L of Agra Bypass Northern connecting Km. 174.500 of NH-2 new NH-19 to Km. 141.000 of Yamuna Expressways (NHA) 618553	Uttar Pradesh	01/2022 (02/2023)	(02/2025) (01/2026)	957.62 (1034.42)	759.58
121	Strengthening of existing 4L Ayodhya Bypass Section from design Km. 121 600 to Km. 144020 of NH 28 New NH 27Pkg-3 (NHA) 618565	Uttar Pradesh	03/2023 (09/2023)	(03/2025) (11/2025)	526.45 (281.13)	270.75
122	4L Spur of Panipat - Shamli connecting NH-709AD Panipat Shamli Muzaffarnagar and NH-709A Karnal Meerut bypassing Shamli district UP (NHA) 618770	Uttar Pradesh	10/2021 (10/2022)	(10/2024) (05/2025)	516.16 (273.42)	247.21
123	2L PS of Raebareli - Jagdishpur with 4L Jagdishpur Bypass Spur (NHA) 618854	Uttar Pradesh	02/2021 (01/2022)	(01/2024) (11/2025)	706.41 (752.52)	534.31
124	Improvement and Up-Gradation of Existing Road to 2/4L PS from Km 40.000 to 88.750, start of Khutar bypass to start of Shahjahanpur bypass of NH 731Pkg-I (NHA) 618855	Uttar Pradesh	03/2022 (02/2023)	(02/2025) (03/2026)	838.68 (838.68)	616.56
125	4L from Mathura Bypass Start at Existing Km. 154.20 of NH-44 to Gaju Village at Km 32.982 of NH-530B Pkg-IB (NHA) 618864	Uttar Pradesh	01/2022 (03/2023)	(03/2025) (01/2026)	1722.11 (1820.77)	1057.04
126	4L from Gaju Village at Km. 32.982 to Devinagar Bypass End at Km. 208.000 of NH-530B Pkg-1C. (NHA) 618865	Uttar Pradesh	12/2021 (01/2023)	(01/2025) (04/2025)	1384.79 (1496.44)	862.65
127	4L Prayagraj Greenfield By-pass from design Km 50860 near Nibi Kala Uperhar to design Km 64763 on NH-19 near Khodaypur Kasgaon including Interchange loop at NH-19 (NHA) 618959	Uttar Pradesh	08/2023 (12/2023)	(03/2025) (02/2026)	1017.99 (427.54)	412.74
128	Reconstruction of existing 2 L/IL to 2L with paved shoulder from existing km 52.200 to 92.880 of NH- (MoRTH) 617970	Uttarakhand	10/2016 (06/2017)	(06/2019) (09/2023)	282.08 (-)	352.53
129	Rehabilitation and upgradation to 2 lane with paved shoulder configuration from km 122.00 Dharasu Bend to km 147.230 Silkyara Bend of NH-94 in the state of Uttarakhand (MoRTH) 617975	Uttarakhand	03/2017 (11/2017)	(11/2019) (01/2026)	237.79 (-)	196.69
	Total (121)				104751.18	80525.34

Completed Projects During Month

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	(Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
	Ministry of Steel					
	Steel					
130	Revamping of old sub-systems of Blast Furnace 3 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) 617253	Jharkhand	08/2023 (10/2023)	(07/2025) (05/2026)	513.82 (-)	415.18
	Total (1)				513.82	415.18

Note: Cumulative Expenditure is as per last reporting by Central Line Ministries/ Departments on the PAIMANA-CRIP portal, this may not be the actual completion cost.




Table 4: Newly Added Projects



Newly Added Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
	Department of Telecommunications				
	Telecommunication				
1	Amended BharatNet Program - KTK, GOA, PY (Department of Telecommunications) (108841)	PAN India	08/2023 (06/2025)	06/2028 (-)	3742 (-)
2	Amended BharatNet Program - UP (East) (Department of Telecommunications) (222253)	Uttar Pradesh	08/2023 (02/2025)	02/2028 (-)	5008 (-)
3	Amended BharatNet Program - UP (West) (Department of Telecommunications) (708687)	Uttar Pradesh	08/2023 (02/2025)	02/2028 (-)	1917 (-)
	Total (3)				10667
	Ministry of Road Transport & Highways				
	Roads & Highways				
4	Improvement and Widening to 2-lane with Paved Shoulder of NH-13 & 15 Old NH-52 from Existing Km 745.60 Design Km 0.000 to Existing km 770.600 Design Km 24.819 Brahmakund T-junction to Kamlang T-Junction, Existing Length 25.00 Km, Design Length 24.819 Km in the state of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (619248)	Arunachal Pradesh	12/2023 (06/2026)	06/2028 (-)	441.41 (-)
5	Balance Works of Rehabilitation and Up gradation of NH-43 New NH-30 from Krm 162120 to Krm 173500 Length 11.380 Km. Keshkal Bypass 4-Lane with Paved shoulder in the State Of Chhattisgarh under NHDP-IV through Engineering, Procurement & Construction EPC Basis (MoRTH) (619039)	Chhattisgarh	06/2025 (06/2026)	06/2028 (-)	307.96 (-)
6	Balance Work Estimate of Rehabilitation and Up-gradation of NH- 43 from Km. 468.600 to Km. 531.250 Pathalgaon to kunkuri Section to two-lane with paved shoulder in the State of Chhattisgarh on SBD mode under NHO under Annual plan 2025-26 (MoRTH) (619347)	Chhattisgarh	03/2026 (06/2026)	06/2028 (-)	201.16 (-)
7	4 Lane with Paved Shoulder from Dareota Village to Kalar Bala NH 205, Design Chainage -Km 33185 to Km 41000, Design Length-7.815 Km Package-IIB (NHAI) (618892)	Himachal Pradesh	06/2025 (06/2026)	06/2028 (06/2028)	992.85 (-)
8	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Donoreshan village to junction with NH-20 in Bongabar village from km 288.600 to km 325.500 Pkg -11 (NHAI) (618729)	Jharkhand	03/2023 (07/2026)	07/2028 (-)	1856.12 (-)
9	6L Greenfield Varanasi- Ranchi- Kolkata Highway from junction with NH-20 in Bongabar village to junction with NH-30 in Lepo village from km 325.500 to km 358.500 Pkg -12 (NHAI) (618733)	Jharkhand	03/2023 (07/2026)	07/2028 (-)	1525.52 (-)
10	Capacity Augmentation in the stretch of Pimpri Sado Vadape section of NH848 Km. 460900 to Km. 537000 by Construction of Slip/Service Road on either side at various locations total length 25.140 Km LHSRHS, Flyover 2 x 25m at Borivali Junction Km. 528550 & LVUP 1 x 15m at Sherekarpada Km. 528800 (NHAI) (619204)	Maharashtra	12/2025 (04/2026)	10/2027 (10/2027)	372.03 (-)
11	Construction of 6 Lane Elevated corridor from KM 612582 to KM 617540 including construction of Service Roads in Kolhapur City on NH -48 in the State of Maharashtra on EPC mode under NHO (NHAI) (619298)	Maharashtra	02/2026 (06/2026)	06/2029 (06/2029)	1039 (-)
12	Construction of a 6-Lane Elevated Corridor from Km 593766 to Km 596620 Including Construction of Service Roads in Kagal City on NH-48 in the State of Maharashtra on EPC Mode. (NHAI) (619299)	Maharashtra	03/2026 (06/2026)	06/2028 (06/2028)	357.99 (-)
13	Construction of Four Lane Nagpur-Katol section of NH-353J including Mitigation Structures from Design Ch. 37000 to Ch. 45990 Tiger Corridor-I Mitigation Structures from Design Ch. 37000 to Ch. 45990 Tiger Corridor-I in the State of Maharashtra on EPC Mode (NHAI) (619300)	Maharashtra	01/2026 (06/2026)	12/2027 (12/2027)	300.68 (-)
14	Development of 6-lane Greenfield Southern Ludhiana Bypass from intersection with NH-44 near Village Rajgarh to intersection with Delhi Katra Expressway NE-5 near Village Ballawal, km 0000 to km 25240 (NHAI) (618648)	Punjab	11/2024 (03/2026)	03/2028 (03/2028)	1424.55 (-)
15	Upgradation of 6 laned Jaipur- Kishangarh section of NH-48 from km 274100 to 363885 involving construction of flyovers and Service road in Rajasthan On Engineering, Procurement & Construction EPC Mode (NHAI) (619270)	Rajasthan	03/2026 (07/2026)	01/2029 (-)	910.91 (-)
16	Construction of Elevated Corridor at Kherwara Town on Udaipur Ratanpur Shamlaji Section of NH-48 in Udaipur District in the State of Rajasthan on EPC mode (NHAI) (619271)	Rajasthan	03/2026 (07/2026)	01/2029 (-)	363.89 (-)
17	2L PS Greenfield bypass Ialganj ajhara, mohanganj and Raniganj on Raebareli - Jaunpur Section Design km 0.00 to Km 53177 of NH-31 (NHAI) (618842)	Uttar Pradesh	12/2024 (06/2026)	06/2028 (-)	1280.68 (-)
	Total (14)				11374.75




Table 5: Ongoing Projects

North Eastern Region



Ongoing Projects of North-East Region							JUNE 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (06/2026)	1712 (2520)	2660.15	99.3
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	206.83	52.64
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	06/2026 (06/2027)	323.26 (323.26)	87.6	36.12
	Total (3)				2534.26	2954.58	
	Ministry of Coal						
	Coal						
4	TIRAP OCP (INVALID CO.) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.66	5.26
5	TIKAK EXTENSION OCP (INVALID CO.) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	112.8	89.73
	Total (2)				449.23	218.46	
	Department of Higher Education						
	Education						
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (08/2024)	592.61 (592.61)	551.3	80
7	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 (153.71)	137.84	97.97
8	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (10/2026)	494.52 (429.7)	368.98	96
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (03/2022)	474.23 (474.23)	167.55	4
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	263.25	98
11	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	283.56	37.6
12	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (03/2026)	314.06 (351.74)	292	96
	Total (7)				2990.52	2064.48	
	Department of Sports						
	Education						
13	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081)	Manipur	06/2022 (01/2022)	08/2024 (08/2026)	906.47 (611.74)	576.37	97.25
	Total (1)				906.47	576.37	
	Ministry of Power						
	Electricity Generation						
14	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	4749.66	17.78
15	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	105.5	6.33
16	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	78.38	5.1
17	700 MW Tato-II HE Project (North Eastern Electric Power Corporation Limited) (611716)	Arunachal Pradesh	09/2025 (09/2025)	09/2031 (-)	8146.21 (8146.21)	253.97	6.54
18	Kalai-II Hydro Electric Project [1200 MW] (THDC India Limited) (619311)	Arunachal Pradesh	04/2026 (04/2026)	10/2032 (-)	14105.83 (14105.8)	188.62	0
19	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	26379.99	97.84
20	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	4519.87	73.48
21	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (11/2026)	938.29 (1828.11)	1691.2	97.34
	Total (8)				70789.01	37967.19	

Ongoing Projects of North-East Region							JUNE 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Transmission & Distribution							
22	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	3.14	1.56
23	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	8128.74	83.8
24	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Mizoram, Meghalaya, Nagaland, Tripura, Assam, Manipur)	12/2014 (03/2016)	12/2018 (03/2027)	5111.33 (6700)	5577.75	99.1
Total (3)					10075.13	13709.63	
Ministry of Petroleum & Natural Gas							
Energy Storage							
25	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	235.27	85.5
26	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	109.34	79.8
27	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Assam	01/2019 (01/2019)	07/2024 (10/2026)	10228 (12407)	11036	92.9
28	LPG Bottling Plant at Mualkhang (MinistryofPetroleumNaturalGas) (617829)	Mizoram	07/2024 (07/2024)	10/2028 (03/2028)	225.71 (225.71)	30.84	33
Total (4)					10994.11	11411.45	
Oil & Gas							
29	Group Gathering Station, Lakwagaon (Ministry of Petroleum & Natural Gas) (619316)	Assam	10/2025 (10/2025)	10/2027 (10/2027)	495.59 (495.59)	20.04	7.8
30	Coke Drum Structure Package (Ministry of Petroleum & Natural Gas) (617836)	Assam	12/2022 (12/2022)	12/2025 (09/2026)	635.28 (635.28)	543	70.8
31	Pipeline Rehabilitation Project, Phase-II (Ministry of Petroleum & Natural Gas) (617827)	Assam	12/2024 (12/2024)	12/2029 (12/2029)	680 (680)	12.65	29
32	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	12/2020 (12/2020)	03/2024 (06/2026)	430.76 (430.76)	348.57	94.5
33	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	01/2018 (01/2018)	02/2020 (06/2026)	682.9 (726.93)	599.83	94.4
34	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	07/2020 (07/2020)	07/2024 (03/2027)	12366 (25313)	20127.1	86.2
35	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	04/2023 (04/2023)	12/2024 (12/2026)	293.5 (293.5)	81.84	99
36	DCU Revamp Project (NRL) (709864)	Assam	08/2021 (08/2021)	07/2024 (03/2027)	370 (370)	310.38	78.6
37	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	09/2023 (09/2023)	05/2026 (09/2026)	198.7 (198.7)	103.59	62.5
38	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2027)	481.03 (481.03)	238.7	54.8
39	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (MinistryofPetroleumNaturalGas) (709779)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768 (740)	225.2	59.4
40	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (MinistryofPetroleumNaturalGas) (709776)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277 (323.09)	234.57	84.2
41	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Mizoram, Manipur, Nagaland, Arunachal Pradesh, Sikkim, Assam, Meghalaya, Tripura)	04/2020 (04/2020)	03/2024 (07/2026)	9265 (9265)	6900	88
42	Augmentation/ Revamping of Dimapur Depot, Dimapur (MinistryofPetroleumNaturalGas) (709786)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 (227.62)	27.63	41.6
43	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022 (03/2022)	05/2024 (08/2026)	209.33 (131.51)	79.98	70.5
Total (15)					27380.71	29853.08	
Ministry of Health & Family Welfare							
Healthcare							
44	Establishment of new GMC West Garo Hills [Tura] (Medical Education, Ministry of Health and Family Welfare) (706989)	Meghalaya	NA (01/1900)	01/1900 (-)	189 (189)	170.1	0
45	Establishment of new GMC Mon (Medical Education, Ministry of Health and Family Welfare) (707067)	Nagaland	NA (01/1900)	01/1900 (-)	325 (325)	155	0

Ongoing Projects of North-East Region							JUNE 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
46	Establishment of new GMC Gangtok <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707039)	Sikkim	10/2018 (12/2018)	12/2026 (-)	250 (635.21)	667.21	92
Total (3)					764	992.31	
Ministry of Railways							
Railways							
47	Furkating-New Tinsukia[194 Km] <i>(Northeast Frontier Railway [NFR])</i> (618986)	Assam	09/2025 (09/2025)	06/2029 (-)	3633.58 (3633.58)	0	0
48	Harmuty-Murkongselek Branch Line Electrification Project <i>(GM/C/ NFR)</i> (706942)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
49	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project <i>(GM/C/ NFR)</i> (706940)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
50	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km <i>(Northeast Frontier Railway [NFR])</i> (705572)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3831.06	95.16
51	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh <i>(Central Organisation for Railway Electrification [CORE])</i> (706922)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
52	Jiribam-Imphal new line project <i>(Northeast Frontier Railway [NFR])</i> (705391)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	16327.07	73.05
53	Byrnihat-Shillong New Rail Line- 108 km <i>(Northeast Frontier Railway [NFR])</i> (705396)	Meghalaya	04/2011 (03/2010)	03/2021 (03/2027)	8324.28 (8342.28)	266.12	2.04
54	Murkongselek-Pasighat <i>(Northeast Frontier Railway [NFR] - II)</i> (705401)	Multi-States (Assam, Arunachal Pradesh)	02/2011 (03/2023)	03/2025 (12/2026)	435 (1250)	887.87	72
55	Tetlia-Byrnihat New Railway Line <i>(Northeast Frontier Railway [NFR])</i> (705394)	Multi-States (Assam, Meghalaya)	08/2010 (03/2007)	11/2011 (06/2027)	1304.62 (1304.62)	1258.8	86.16
56	Lumding Furkating Doubling Project 140 km <i>(Northeast Frontier Railway [NFR])</i> (616701)	Multi-States (Assam, Nagaland)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	141.06	12.5
57	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] <i>(Northeast Frontier Railway [NFR] - II)</i> (705392)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2029)	6663 (6663)	6748.9	46.5
58	Sivok-Rangpo New Rail Line <i>(Indian Railway Construction International Limited [IRCON])</i> (705432)	Sikkim	10/2009 (05/2010)	05/2015 (12/2027)	7877 (11775)	11090.47	80
Total (12)					50056.05	40943.08	
Ministry of Road Transport & Highways							
Roads & Highways							
59	Construction of 2-lane road of Potin to Pangin section of NH-13 from Km 163.59 to Km 206.66 Package-5 on EPC Mode in the State of Arunachal Pradesh under Arunachal Pradesh Package of Roads and Highways of SARDP-NE [Job No SARDP-NE/P-P/Pkg-A/NH-13/Ar.Pr./PWD/2018-19/116] <i>(MoRTH)</i> (617892)	Arunachal Pradesh	03/2019 (11/2020)	11/2023 (07/2026)	450.65 (450.65)	345.01	96.61
60	4-Laning of Itanagar to Banderdewa section of NH-415from km 40430 to km 51735 Package-Bon EPC Mode in the state of Arunachal Pradesh Job NO. 415/Ar. P/2020-21/031 <i>(MoRTH)</i> (618033)	Arunachal Pradesh	06/2020 (12/2021)	12/2024 (07/2026)	496.47 (496.47)	171.91	51.37
61	Construction of Balance work of 2-Lane with PS of Joram Koloriang Road from existing Km122.600 to km138.00 [Design Km108.724 to Km123.714] in Arunachal Pradesh on EPC Mode under SARDP-NE Pkg-7 <i>(NHIDCL)</i> (618433)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (04/2026)	184.89 (184.89)	0	99.69
62	Roing-Hunli Road Greenfield Alignment Project <i>(NHIDCL)</i> (618434)	Arunachal Pradesh	02/2017 (03/2018)	03/2022 (10/2026)	1718.59 (1718.59)	189.24	82.32
63	Construction of 2-Laning with hard shoulders of Demwe-Brahmakund section of NH-13 from Ch.0.00 km to 18.464 km on EPC under SARDP-NE NHO-NE - Balance Work <i>(NHIDCL)</i> (618445)	Arunachal Pradesh	08/2020 (06/2025)	12/2027 (12/2027)	353.9 (353.9)	0	19.55
64	Improvement and Widening to 2 lane with paved Shoulder of NH-15 old NH-52 from Existing Km 770.600 Design Km 24.819 to Existing km 805.750 Design Km 59.885 Kamlang T-Junction to Chowkham, Existing Length 35.150 Km, Design Length-35.066 Km in the state of Arunachal Pradesh on EPC mode Pkg-2 <i>(NHIDCL)</i> (619014)	Arunachal Pradesh	12/2023 (02/2026)	02/2028 (02/2028)	316.73 (316.73)	0	11.74
65	Improvement and Widening to 2-lane with Paved Shoulder of NH-13 & 15 Old NH-52 from Existing Km 745.60 Design Km 0.000 to Existing km 770.600 Design Km 24.819 Brahmakund T-junction to Kamlang T-Junction, Existing Length 25.00 Km, Design Length 24.819 Km in the state of Arunachal Pradesh on EPC mode Pkg-1 <i>(NHIDCL)</i> (619248)	Arunachal Pradesh	12/2023 (06/2026)	06/2028 (-)	441.41 (441.41)	0	0
66	Construction of Intermediate Lane of Pango to Jorging Road from 0000 to Design Km Design Km 40000 Design Length 40.00 Km, Pkg-I, Greenfield Alignment in the State of Arunachal Pradesh on EPC mode Pkg-1 <i>(NHIDCL)</i> (618405)	Arunachal Pradesh	01/2024 (01/2025)	07/2027 (07/2027)	898.19 (898.19)	0	39.8

Ongoing Projects of North-East Region							JUNE 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
67	Construction of Intermediate Lane Road with hard shoulder from design chainage Km 0.000 to Km 53.040 Existing Length68.500 Km & Total Design length 53.04 km of Tato to Monigong section of NH-913 Frontier Highway on Nafra Bomdila to Vijaynagar along China border in state of Arunachal pradesh on EPC mode (NHIDCL) (618404)	Arunachal Pradesh	12/2023 (05/2025)	11/2027 (11/2027)	625.61 (625.61)	0	21.97
68	Construction of Intermediate Lane Road with hard shoulder from design Km 0.000 to Km 17.387 Total length 17.387 km of Hunli to lthun Bridge section on NH-913 Frontier Highway in State of Arunachal Pradesh on EPC mode under NHO-NE (NHIDCL) (618403)	Arunachal Pradesh	02/2024 (01/2025)	01/2027 (01/2027)	275.5 (275.5)	0	54.11
69	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang from Design Km 0.000 to Km 53.000 Design Length 53.000 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Package-I (NHIDCL) (618402)	Arunachal Pradesh	02/2024 (03/2025)	02/2028 (03/2028)	1262.43 (1262.43)	245.19	18.1
70	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang Package-III from design Km 60.000 to Km 121.500 Design Length 61.500 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Pkg-3 (NHIDCL) (618401)	Arunachal Pradesh	02/2024 (07/2025)	07/2028 (07/2028)	1418.67 (1418.67)	0	1.7
71	Construction of 4-Lane Panchgram Bypass from Design Chainage km 15500 on NH-37 Old NH-53 at Kalinagar Pt.-I Village to Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Package-2 (NHIDCL) (618308)	Assam	03/2023 (08/2024)	02/2027 (02/2027)	676.18 (728.97)	0	57.17
72	Widening/Improvement to 4-Laning and Greenfield alignment with Paved shoulder of Silchar-Badarpur Churaibari section of NH-37 & NH-8 from Design chainage 38.600 End point of proposed Badarpur Bypass to Km. 62.800 Start point of proposed Nilambazar/Cheragi Bypass in the state of Assam on HAM Mode Package-4 (NHIDCL) (618309)	Assam	02/2024 (08/2025)	08/2027 (08/2027)	1319.55 (1319.55)	0	25.16
73	Widening/Improvement to 4-L of Karimgani - sutarkandi section of NH 37 from design Ch 0020 Start of proposed Karimganj Bypass from NH -8 to design Chainage Km 14380 near Sutarkandi Spur Connectivity to Indo/Bangladesh Border on Silchar-Churaibari in the State of Assam on HAM Mode Package-7 (NHIDCL) (618310)	Assam	02/2024 (02/2025)	02/2027 (02/2027)	791.79 (791.79)	0.06	41.88
74	Widening/Improvement to 4-Lane with Paved shoulder for existing as well as Greenfield alignment of Badarpur Churaibari section of NH-8 from Design chainage 87.700 Chandkhira to Km. 106.500 Churaibari section Assam-Tripura border in the state of Assam on HAM Mode Package-6 (NHIDCL) (618311)	Assam	03/2024 (03/2025)	03/2027 (03/2027)	870 (870)	0	40.99
75	Widening/Improvement to 4-Lane with Paved Shoulder from existing road and Greenfield alignment form Design Ch. 62.800 start of proposed Nilambazar/Cheragi Bypass to Design Ch. 87.700 near Chandkhira Village of NH-8 on Silchar-Churaibari in the state of Assam on HAM Mode Package-5 (NHIDCL) (618312)	Assam	02/2024 (04/2025)	10/2027 (10/2027)	1258.13 (1258.13)	0	14.04
76	Widening/Improvement of Existing 2 lane to 4-Laning of Karimganj-Silchar section of NH-37 from Design Ch 0.000 near Silchar ISBT to Design Ch 15.970 near Kalinagar Pt I on NH-37 in Assam on HAM Mode Pkg-1 (NHIDCL) (618313)	Assam	03/2024 (09/2025)	09/2027 (09/2027)	1181.55 (1181.55)	0	41.26
77	4-Laning of Dhanehari Lailapur / Vairengte section from Existing Chainage km 12920 to km 43000 of NH 306 Design Chainage km 20000 to km 49360 on Silchar - Vairengte Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode. Project Length 29.360 km under NHO-NE Package-2 (NHIDCL) (618314)	Assam	03/2023 (02/2024)	08/2026 (08/2026)	1716.21 (1716.21)	970.37	81.65
78	4-Laning of Silchar - Dhanehari section from Existing Chainage km 263800 of NH 37 to km 12920 of NH 306 Design Chainage km 0000 to km 20000 on Silchar - Vairengte - Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode Package-1 (NHIDCL) (618315)	Assam	02/2023 (01/2024)	07/2026 (07/2026)	1256.9 (1256.9)	575.03	59.65
79	Dillai to Lahorijan Package-7 (NHIDCL) (618325)	Assam	11/2021 (01/2023)	07/2024 (04/2026)	204.1 (204.1)	142.21	0
80	Widening/Improvement to 4-Lane with Paved Shoulder from KM 38500 to Km 51246 Design Chainage 38500 to 50959 with proposed Daboka Bypass of Daboka-Parokhaowa of NH 29 on EPC under NHO-NE Package-1 (NHIDCL) (618326)	Assam	01/2023 (11/2023)	11/2025 (06/2026)	516.88 (516.88)	0	99.7
81	Improvement to 4-Lane with Paved Shoulder from existing km 260000 Design Ch.4560 km to existing km Ch.233000 D. Ch.24560 of Silchar near Nutan Dayapur village - Budha Nagar Section Length-20.00 Km of NH-37 under Package Silchar-Jiribam Pkg-1 in the state of Assam on HAM Mode (NHIDCL) (618331)	Assam	01/2024 (01/2025)	01/2028 (01/2028)	957.95 (957.95)	165.23	47.27
82	Construction and up gradation to 4-Lane of existing two lane with paved shoulder from Hapachara to Tulungia road of NH-117 of existing Km 0.00 to km 14.050 and Design Km 0.000 to km 14.660 under BMP on EPC mode (NHIDCL) (618289)	Assam	03/2020 (06/2020)	12/2022 (03/2026)	224.85 (224.85)	209.94	97.76
83	Widening/Improvement to 4-Lane with Paved Shoulder from Ch.5.580 Km to Ch.25.633 Km Design Ch.0.000 Km to Ch.17.737km Km 901.100 to Km 921.145 of old NH-31 of Bilasipara- Guwahati road NH-17 Section Near Chirakuta to near Mowatari, before Chapar Bypass in the state of Assam on HAM mode Package-1 (NHIDCL) (618288)	Assam	02/2024 (02/2025)	08/2027 (08/2027)	1081.15 (1081.15)	0	32.59

Ongoing Projects of North-East Region							
JUNE 2026							
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
84	Widening/Improvement to 4-Lane with paved Shoulder from Ch. 25.633 Km to Ch. 52.470 Km Design Ch. 21.850 Km to Ch.48.670 Km for Package-2 of Bilasipura- Guwahati road NH-17 Section Near Mowatari, before Chapar Bypass to Tulungia junction with NH-17 in the state of Assam on HAM mode under NHO-NE Package-2 (NHIDCL) (618287)	Assam	11/2023 (12/2024)	06/2027 (06/2027)	1338.61 (1338.61)	0	12.45
85	Construction of New 2-Lane Bridge with its approaches from km 0000 to Km 4385 across River Brahmaputra on NH-17 at Jogighopa in Assam on EPC mode (NHIDCL) (618286)	Assam	09/2021 (11/2021)	11/2024 (12/2026)	746.76 (746.76)	426.91	81.07
86	Widening/Improvement to 4-Lane with paved shoulder from Km 99930 to Km 143680 Design Chainage 96000 to 139750 of Paikan to Dhupdhara Sahar of Bilasipura-Guwahati Road on NH-17 in the state of Assam on EPC mode under Bharatmala Pariyojana in Economic Corridors Project Length 43.750km under NHO-NE Package-8 (NHIDCL) (618284)	Assam	03/2023 (12/2023)	12/2026 (12/2026)	1457.59 (1457.59)	926.96	85.87
87	4-L Bilasipara-Guwahati Package-9 (NHIDCL) (618283)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1000.27 (1000.27)	490.64	59.78
88	4-L Bilasipara-Guwahati Package-10 (NHIDCL) (618282)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1264.9 (1264.9)	603.33	64.48
89	Construction of 2 lane Major Bridge including approaches over Brahmaputra between Majuli on North Bank and Jorhat on South Bank from km. 11.690 to km. 19.715 length of bridge 6,812.5m Package - II on NH-715K in the state of Assam Job no. 715/AS/2020-21/213 (MoRTH) (618160)	Assam	03/2025 (12/2025)	12/2027 (12/2027)	1019.17 (1019.17)	0	3.25
90	Construction of new 2 Lane with paved shoulders of NH Standards from km 0.080 to km 11.690 L11.610 km in Majuli and from km 19.715 to km 27.484 L 7.769 km in Jorhat on the newly declared NH 715K and construction of 1.10 km flyover on NH-715 with its approaches and service roads L1.10 km, Total Length 20.479 km in the State of Assam Job No. 715K/AS/2023-24/256 (MoRTH) (618159)	Assam	02/2024 (09/2025)	03/2027 (03/2027)	382.1 (382.1)	26.05	6.3
91	Construction of 2 lane Barpeta Bypass from Km 77900Baradi to Km 86150 Deurikuchi Length8.25Km on NH-427 in the state of Assam under EPC ModeJob No.427/AS/2022-23/245 (MoRTH) (618034)	Assam	03/2023 (02/2025)	08/2026 (08/2026)	173.65 (173.65)	11.38	20
92	Construction of 4 lane Gauripur Bypass Starting bfrom Km 852.56 of NH-31Dumardoha Pt-II and Terminating at Km 862.17 Baladmara via. Khudimari Pt.-II, Fulkumari, Charaldanga, Sajuakuti,Geramari Pt.-III and finally meeting at km 862.17 of NH-17New/ NH-31Old in the State of Assam under EPC Mode Job no. 31/AS/ 2023-24/265 (MoRTH) (617896)	Assam	03/2024 (04/2025)	10/2026 (10/2026)	421.15 (421.15)	0	20.8
93	Construction of Mangaldoi Bypass NH-15 starting at Ch 26400 and terminating at Ch 41505 under Rangia NH Division L 15.105 Km in the State of Assam. Job No. 15/AS/2021-22/234 (MoRTH) (617895)	Assam	03/2022 (04/2023)	04/2025 (12/2026)	535.03 (535.03)	209.27	75.82
94	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 453.000 to Km 490.800, under SARDP- NE , under EPC Mode in the state of Assam Pkg-IV Structures & Toll Plaza (NHIDCL) (618444)	Assam	01/2024 (02/2024)	08/2024 (07/2026)	279.01 (279.01)	398.54	94.73
95	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 463.00 to Km 477.000 14.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-II Road Works (NHIDCL) (618443)	Assam	01/2024 (02/2024)	08/2024 (03/2026)	438.44 (438.44)	0	95.86
96	Earthwork in Formation, Road Work, Construction of Bridges, Blanketing, P. Way Linking works including Supply of P. Way Fittings and Track Ballast in connection with Construction of Railway Siding from Jogighopa Railway Station to MMLP at Jogighopa from Ch. 00 to 3760 on Item Rate basis Package -3, Railway Siding from Jogighopa Railway Station to MMLP (NHIDCL) (618454)	Assam	02/2020 (12/2020)	06/2022 (09/2024)	693.97 (693.97)	41.78	93.23
97	Development of External Trunk Connectivity and Internal Infrastructure Works at Multi Model Logistics ParkMMLP at Jogighopa in the State of Assam on EPC Mode Package-I Road and Utility Works (NHIDCL) (618455)	Assam	02/2020 (09/2020)	04/2022 (09/2024)	693.97 (693.97)	310.1	100
98	Guwahati Ring Road in the State of Assam (NHAI) (618934)	Assam	08/2024 (01/2026)	01/2030 (01/2030)	5729.47 (5729.47)	328.42	0
99	2L with ES of Yagyi - Kalewa section from Milepost 40/0 to Milepost 115/5 in Myanmar (NHAI) (618958)	Assam	12/2017 (05/2018)	06/2023 (07/2027)	1200.14 (1200.14)	0	52
100	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 501.800 to Km 514.800 13.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-II Road Works (NHIDCL) (619013)	Assam	10/2014 (10/2024)	01/2026 (07/2026)	508.76 (542.87)	111.01	73.88
101	Construction of 4-Lane Badarpur Bypass from Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village to Design Chainage km 38600 on NH-37 Old NH-44 at Kandigram Chaitha Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Pkg-3 (NHIDCL) (619057)	Assam	02/2023 (02/2024)	08/2026 (08/2026)	574.26 (574.26)	318.82	71.09

Ongoing Projects of North-East Region							JUNE 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
102	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 514.800 to Km 534.800 20.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (619060)	Assam	10/2014 (10/2024)	09/2025 (07/2026)	344.71 (619.7)	54.48	72
103	Balance work of 4L of NarimbangloJatinga Junction- Harangajoroad section from Km 0.000 to Km 49.230 of NH-27 (NHAI) (619089)	Assam	03/2022 (01/2023)	01/2026 (07/2026)	1909.98 (2745.74)	1386.87	94.59
104	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 477.000 to Km 490800 13.800 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (618442)	Assam	01/2024 (02/2024)	08/2024 (06/2026)	358.72 (358.72)	398.28	100
105	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 501.800 11.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618441)	Assam	01/2016 (10/2024)	09/2025 (07/2026)	467.79 (476.5)	0	87.33
106	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 534.800, under SARDP- NE on EPC Mode in the state of Assam Pkg- IV Structures & Toll Plaza (NHIDCL) (618440)	Assam	01/2016 (10/2024)	10/2025 (07/2026)	187.09 (100.22)	0	58.19
107	Widening/Improvement to 2-Lane Lane with Paved Shoulder from km 16900 Bogapani to km 27150 Golai Goan on existing Dibrugarh to Ledo section with proposed Digboi Bypass Green Field and Brownfield 2-LanePS of NH-315 OLD NH-38 in Tinsukia District under NHO- NE Package-4 (NHIDCL) (618339)	Assam	01/2023 (12/2023)	12/2025 (12/2026)	356.65 (356.65)	80.08	20.45
108	Widening/Improvement to 4-Lane with Paved Shoulder from km 626030 Nalani hulla Gaon to km 650450 Chotahapjan on existing Tinsukhia -Makum Bypass of NH-15 OLD NH-37 and Strengthening of existing NH-315 OLD NH-38 from Km 0000 Chotahapjan to Km 16900 Bogapani section 2-Lane PS in Assam on EPCMode under NHO-NE Package-3 (NHIDCL) (618340)	Assam	01/2023 (05/2023)	05/2025 (10/2026)	458.59 (458.59)	249.84	88.99
109	Construction of Balance Work of 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 453000 to Km 463000 10.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618439)	Assam	01/2024 (02/2024)	08/2024 (06/2026)	478.3 (478.3)	0	96.79
110	4-Laning of NH-37 Section between Demow to End of Moran Bypass From Km. 534.800 to Km. 561.700 including Emergency Landing Facility ELF under SARDP-NE, Phase 'A' in the State of Assam on EPC mode (NHIDCL) (618438)	Assam	01/2016 (01/2023)	07/2024 (08/2025)	385.57 (385.57)	685.73	100
111	Construction of Balance Work of 4-Laning of NH-37 Section between End of Moran Bypass to Bogibeel junction near Lapetketa Km. 561.700-Km. 580.875 under SARDP-NE, Phase 'A' in the State of Assam on EPC mode Pkg-I Road works & Toll Plaza (NHIDCL) (618437)	Assam	01/2016 (09/2024)	03/2025 (08/2025)	274.34 (274.34)	96.67	100
112	4-Laning of Jamugurihat to end of Biswanath Chariali By-Pass from Km 182.000 to Km 208.000 of NH-52 on EPC mode in state of Assam under SARDP-NE (NHIDCL) (618436)	Assam	03/2015 (12/2016)	06/2019 (07/2025)	599 (599)	434.89	100
113	4-Laning from Rangagara to Kaliabor Tiniali from km 297.00 to km 315.315 of NH-37 on EPC basis under SARDP-NE in state of Assam (NHIDCL) (618435)	Assam	01/2016 (10/2017)	04/2020 (07/2026)	386.51 (386.51)	360.25	97.13
114	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 156.489 near P. Leikul to km 176.410 near Borowapu on EPC mode under NHO-NE Assam portion Package-10 (NHIDCL) (618351)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	890.33 (693.15)	604.86	90.5
115	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 136.500 near Hejaichak to km 156.489 near P. Leikul Package-9 on EPC mode under NHO-NE Package-9 (NHIDCL) (618352)	Assam	03/2023 (08/2023)	08/2025 (07/2026)	860.37 (614.43)	559.69	87.5
116	Widening & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 116.480 near Hangrum to km 136.500 near Hejaichak Package-8 on EPC mode under NHO-NE Package 8 (NHIDCL) (618353)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	904.04 (904.04)	557.37	85.2
117	Wideinig & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 96.870 near Jiri River to km 116.550 near Hangrum Package-7 on EPC mode Package7 (NHIDCL) (618354)	Assam	12/2023 (03/2024)	03/2026 (12/2026)	846.82 (846.82)	0	90.36
118	Construction of 4-Lane Bridge including approaches over River Brahmaputra between Dhubri on North Bank,Assam and Phulbari on south Bank,Meghalaya on NH-127B under JICA ODA Loan assistance Phase-III (NHIDCL) (618373)	Assam	05/2019 (12/2020)	09/2028 (09/2028)	4997.04 (4997.04)	3033.59	77.14
119	Widening/Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Srirampur near Bhairiguri Village to Kachukhana Harichara Paglagaunj Package-I of Srirampur - Dhubri Section of NH-127B from existing Km 0.000 to Km 28.050 Design Km 0.000 to Km 27.650, Design Length27.650 Km under JICA ODA Loan assistance Phase-V -Balance work (NHIDCL) (618371)	Assam	03/2022 (11/2024)	11/2026 (11/2026)	613.89 (613.89)	384.24	89.5

Ongoing Projects of North-East Region							JUNE 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
120	Widening/Improvement to 2 lane with earthen shoulder of Choithar to Marrem Khullen section of NH-202 of Imphal Ukhrlul Jessami Economic Corridor from Design Chainage km 53.110 to km 95.700 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-5 (NHIDCL) (618306)	Manipur	03/2023 (05/2025)	03/2027 (08/2027)	564.05 (564.05)	172.98	14.5
121	Widening/Improvement to 2 lane with earthen shoulder of Marrem Khullen to Jessami section of NH-202 of Imphal - Ukhrlul - Jessami Economic Corridor from Design Chainage km 95.700 to km 140.180 in the State of Manipur on EPC mode under Bharatmala Pariyojana under NHO-NE Package-6 (NHIDCL) (618305)	Manipur	03/2023 (12/2024)	12/2026 (08/2027)	554.66 (554.66)	221.02	24.43
122	Widening/Improvement to 2 Lane with earthen shoulder of Jessami to Laynen bridge Nagaland border section of NH-29 of Imphal -Ukhrlul - Jessami Economic Corridor from km 0.000 to km 11.009 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-7 (NHIDCL) (618304)	Manipur	03/2023 (12/2024)	06/2026 (02/2027)	164.89 (164.89)	127.59	26.67
123	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 0.000 to Km 16.900 of NH-202 in the state of Manipur on EPC mode Package-1 (NHIDCL) (618303)	Manipur	03/2020 (07/2020)	06/2022 (08/2026)	222.77 (222.77)	0	88.96
124	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 16.900 to Km 30.970 of NH-202 in the state of Manipur on EPC mode Package-2 (NHIDCL) (618302)	Manipur	03/2020 (07/2020)	06/2022 (08/2026)	256.04 (256.04)	0	98.12
125	Improvement of existing road to 2 laning with Hard Shoulders of Maram -Peren section Package-1A, length- 22.340Km from Design Chainage 0.000 km to 22.340 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618416)	Manipur	02/2021 (06/2021)	12/2022 (03/2027)	226.32 (226.32)	189.26	75.08
126	Improvement of existing road to 2 laning with Hard Shoulders of Maram-Peren section Package-1B, length- 17.660 km from Design Chainage 22.340 km to 40.000 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618415)	Manipur	02/2021 (06/2021)	12/2022 (03/2026)	188.36 (188.36)	0	100
127	Construction of 2-laning with Hard shoulder road of Ukhrlul - Tolloi - Tadubi section of NH-102A from Design Chainage 81.870 km to 105.825 km in the State of Manipur on EPC mode under NHO-TSP Package -4 (NHIDCL) (618389)	Manipur	09/2021 (08/2022)	02/2024 (08/2026)	310.76 (310.76)	255.6	97
128	Construction of 2-laning with Hard shoulder road of Ukhrlul - Tolloi - Tadubi section of NH-102A from Design Chainage 50.850 km to 81.870 km in the State of Manipur on EPC mode under NHO-TSP Package -3 (NHIDCL) (618388)	Manipur	09/2021 (07/2023)	01/2025 (07/2026)	315.56 (315.56)	251.46	91.11
129	Construction of 2-laning with Hard shoulder of Ukhrlul Tolloi - Tadubi section of NH-102A from Design Chainage km 9450 to km 50850 in the State of Manipur on EPC mode under NHO-NE Package-2 (NHIDCL) (618387)	Manipur	03/2023 (03/2024)	03/2026 (12/2026)	578.98 (578.98)	267.11	80.02
130	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 starting from km 80.630 near Mandeu to km 96.870 near Jiri River on EPC Mode Package-6 (NHIDCL) (618358)	Manipur	09/2021 (11/2021)	05/2023 (12/2025)	311.18 (311.18)	231.08	87.3
131	Widening to 2-Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 15.940 km to 33.120 Km Existing Chainage Km 15.946 to Km 33.395 Total length17.180 Km in the State of Manipur on EPC mode PKG-2 - Balance Works & Rectification works (NHIDCL) (618338)	Manipur	03/2021 (03/2025)	03/2026 (08/2026)	195.14 (195.14)	161.96	92.99
132	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 in Manipur starting from km 54.180 near Azuram to km 80.630 near Mandeu on EPC Mode Package 5 (NHIDCL) (618357)	Manipur	09/2021 (11/2021)	05/2023 (01/2026)	477.86 (477.86)	330.12	84.87
133	Widening to 2 lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 169570 Near Nungkao village under Tamenglong District to km 205974 near Jiribam Bridge under Jiribam district under NHO-NE PKG-7 (NHIDCL) (618333)	Manipur	01/2023 (12/2023)	12/2025 (12/2026)	760.16 (760.16)	424.3	92.52
134	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 131.280 to km 169.570 on EPC mode in Manipur under NHO-TSP PKG-6 (NHIDCL) (618334)	Manipur	12/2021 (02/2023)	02/2025 (09/2026)	504.76 (504.76)	325.89	95.2
135	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from Km 101280 Near Khongsang Village to Km 131280 near Puilon Kambiron Village on EPC Mode in Manipur PKG-5 (NHIDCL) (618335)	Manipur	12/2021 (11/2022)	05/2024 (08/2026)	410.68 (410.68)	345.66	90.61
136	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 66.110 km to 101.280 Km Existing Chainage km 67.496 to km 103.557 on EPC Mode in Manipur PKG-4 (NHIDCL) (618336)	Manipur	09/2021 (06/2022)	12/2023 (07/2026)	579.63 (579.63)	404.8	85.98
137	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 33.000 km to 66.390 Km Existing Chainage from km 33.395 to km 67.496 on EPC Mode in Manipur PKG-3 (NHIDCL) (618337)	Manipur	03/2021 (09/2021)	03/2023 (03/2026)	467 (467)	593.44	86.33

Ongoing Projects of North-East Region							JUNE 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
138	Widening/Improvement of existing 2-lane to 4-Lane Divided Highway from Kuraopokpi to Sekmai section of Imphal-Kohima Road Design Ch. km 287.00 to 297.700 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5A (NHIDCL) (618301)	Manipur	09/2020 (02/2025)	08/2026 (08/2026)	228.97 (228.97)	114.62	48.31
139	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Taphukuki to Daili section of Imphal-Kohima road NH-02 Design Chainage from Km 262175 to Km 274610 in the state of Manipur on EPC mode Pkg-4A (NHIDCL) (618300)	Manipur	09/2020 (10/2020)	04/2022 (08/2026)	379.39 (379.39)	312.58	91.39
140	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Daili to Kuraopokpi section of Imphal-Kohima road NH-02 Design Chainage from Km 274610 to Km 287000 in the state of Manipur on EPC mode Pkg-4B (NHIDCL) (618299)	Manipur	09/2020 (12/2024)	06/2026 (01/2027)	268.98 (268.98)	0	56.16
141	Widening/Improvement of existing 2-Lane road to 4-Lane Divided Highway from Sekmai to Nilakuthi section of Imphal-Kohima Road Design Chainage from Km 297700 to Km 308729 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5B (NHIDCL) (618298)	Manipur	03/2021 (07/2021)	01/2023 (09/2026)	211.7 (211.7)	254.22	93.54
142	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur in the state of Manipur from km 31.430 at Old Tamenglong to km 43.480 ending near Phelong on EPC Mode Package-3 (NHIDCL) (618356)	Manipur	03/2021 (06/2021)	12/2022 (04/2026)	234.08 (234.08)	201.13	98.5
143	Construction of 2 -Lane with paved shoulders road from Tamenglong-Tousem-Lisang-Mahur Road NH-137 starting near Dialong Village from km 10.000 at Dialong to km 31.430 near Old Tamenglong , near Barak River on EPC Mode Package-2 (NHIDCL) (618355)	Manipur	07/2021 (09/2021)	03/2023 (03/2026)	483.87 (483.87)	372.1	95.28
144	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from Design Chainage 69.875 Km to 121.769 Km in the State of Manipur on EPC mode Package-3 (NHIDCL) (618344)	Manipur	03/2021 (08/2021)	08/2023 (12/2026)	673.27 (673.27)	563.27	84.72
145	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section from Km 48.587 to Km 69.875 in the State of Manipur on EPC mode under NHO Package-2B (NHIDCL) (618345)	Manipur	06/2020 (08/2020)	08/2022 (08/2026)	365.53 (365.53)	195.73	88.2
146	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 32.835 to km 48.587 in the State of Manipur on EPC mode under NHO Package-2A (NHIDCL) (618346)	Manipur	04/2020 (07/2020)	06/2022 (07/2026)	232.99 (232.99)	155.44	100
147	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 13.747 to km 32.835 in the State of Manipur on EPC mode under NHO Package-1B (NHIDCL) (618347)	Manipur	04/2020 (07/2020)	06/2022 (07/2026)	241.52 (241.52)	164.85	100
148	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from km 130.000 to km 141.029 Package-4B in the State of Manipur on EPC Mode (NHIDCL) (618348)	Manipur	06/2020 (11/2025)	11/2026 (11/2026)	177.76 (177.76)	97.93	7.45
149	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from Design Chainage km 118850 to km 130000 Package-4A in the State of Manipur on EPC Mode (NHIDCL) (618349)	Manipur	04/2020 (08/2025)	08/2026 (08/2026)	204.12 (204.12)	0	24.66
150	Improvement/Widening to 2-L with Paved Shoulder/ 4-Laning of NH-40 section from Km 151330 to Km 163400 design Km 63.530 to Km 71.520 including Dawki Bridge of length 368 m between Shillong-Dawki under JICA ODA Loan assistance Phase-II Pkg-5 -Balance work (NHIDCL) (618374)	Meghalaya	07/2020 (05/2024)	11/2026 (11/2026)	284.21 (284.21)	170.81	41.92
151	Improvement/Widening to 2-Lane with Paved Shoulder from design Km 45.760 to Km 63.530 between Shillong-Dawki under JICA ODA Loan assistance Phase-II - Balance work Pkg-4 (NHIDCL) (618375)	Meghalaya	07/2020 (04/2024)	04/2026 (10/2026)	445.51 (445.51)	42.39	53.21
152	Improvement/Widening to 2-Lane with Paved Shoulder between Shillong-Dawki road up to Bangladesh Border from design Km 10.670 to Km 37.550 under JICA ODA Loan assistance Phase-II -Balance Work-Pkg-2 (NHIDCL) (618376)	Meghalaya	07/2020 (02/2024)	08/2026 (12/2026)	525.67 (525.67)	0	51.02
153	Improvement/Widening to 2-L with Paved Shoulder/4-L from Km 81740 to Km 93490 design Km 0000 to Km 10670 of NH-40 New NH-106 & 206 section & 4-L from design Km 0.00 to Km 0.930 of NH-44 section between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance Work Pkg-1 (NHIDCL) (618377)	Meghalaya	07/2020 (10/2023)	10/2025 (06/2026)	351.12 (351.12)	0	100
154	Rehabilitation and Up-gradation of Nongstoin Wahkaji section of Project Road Km 0000 to Km 43060 to Intermediate Lane with earthen shoulder under SARDP-NE Phase-A in the State of Meghalaya on EPC mode. Job No- SARDP-NE ong-Don-Maw/MG/2020-21/294 (MoRTH) (617885)	Meghalaya	08/2020 (02/2022)	08/2023 (07/2026)	302.88 (302.88)	187.77	99.1
155	Rehabilitation and up gradation of Nongstoin-Rambrai-Kyrshai road up to Meghalaya-Assam border from Km 0.335 to km 34.039 to 2-Lane under NHO - NE in the State of Meghalaya Package-1 (NHIDCL) (618418)	Meghalaya	09/2021 (05/2022)	05/2024 (12/2026)	359.86 (359.86)	299.18	83.02

Ongoing Projects of North-East Region							JUNE 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
156	Construction of 2-Lane with paved shoulders of Shillong Western Bypass starting from NH-06 near Ladumsaw existing Km 60.900 of old NH40 to NH106 old NH 44E Package-III, from km 24700 to km 38256 under SARDP-NE PHASE A in the state of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618419)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	562.48 (562.48)	254.54	52
157	Construction of 2 lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw existing km 60.900 of old NH-40 to NH-106 old NH-44E, Package-II km 12800 to km 24700 under SARDP-NE Phase A in the State of Meghalaya on EPC Mode (NHIDCL) (618420)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	686.03 (686.03)	435.15	49.82
158	Improvement/Widening of New NH-217 Dainadubi-Darugiri section to Two lane with paved shoulder in Meghalaya from design Km 0000 to Km 40840 existing Km 8600 to Km 53000 of Old NH-62 under BMP Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618295)	Meghalaya	03/2023 (03/2025)	03/2027 (03/2027)	705.83 (705.83)	0	45.52
159	Improvement and Widening of National Highway No. 127B Darugiri - Songsak - Williamnagar Junction Section to two lane with paved shoulder from design Km 0000 to Km 36635 Design length 36.635 Km existing Km 112000 to Km 151060 of NH-1278 under Bharatmala Pariyojana Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618294)	Meghalaya	03/2023 (09/2025)	09/2027 (09/2027)	801.07 (801.07)	176.12	26.08
160	Construction of 2-Lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw Existing km 60.900 of old NH-40 to NH106 old NH-44E, km 0000 to km 12800 Package-I under SARDP-NE PHASE A in the State of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618421)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	620.3 (620.3)	304.5	73.13
161	Improvement and Widening two lannig with paved Shoulder of NH 127B from km 31.500 Goeragre to km 63.224 Package-II in state of Meghalaya (MoRTH) (618076)	Meghalaya	12/2023 (05/2025)	05/2027 (-)	504 (350.67)	0	2.5
162	2-laning of Zorinpui - Longmasu section of NH-502A from km 0.000 to km 28.244 in the State of Mizoram on EPC mode under NHO-NE, stretch of IMBR (NHIDCL) (618452)	Mizoram	02/2023 (12/2024)	12/2026 (07/2027)	781.85 (781.85)	48.14	4.71
163	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 339.00 to km 380.00 Siaha on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-8 (NHIDCL) (618383)	Mizoram	09/2019 (03/2020)	09/2023 (06/2026)	637.06 (637.06)	101.89	99.82
164	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 125. 000 to Km 166 Package-3 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-3 (NHIDCL) (618380)	Mizoram	09/2019 (10/2019)	04/2023 (06/2026)	867.09 (867.09)	159.55	97.51
165	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 208. 000 to Km 250.000 Package-5 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-5 (NHIDCL) (618379)	Mizoram	09/2019 (10/2019)	04/2023 (06/2026)	752.89 (752.89)	125.64	95.35
166	4-Laning of Vairengte - Chhimluang section Package-3 of NH-306 from Existing Chainage km 43000 to Km 59700 Design Chainage km 46000 to km 60850 on Silchar - Vairengte- Sairang road in the State of Mizoram under Bharatmala Pariyojna under NHO-NE. Package-1&2 in Assam state (NHIDCL) (618316)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	491.39 (491.39)	237.85	17.86
167	4-Laning of chhimluang-Kolasib from section pkg-4 of NH-306 & NH-6 existing chainage km 59700 to km 86000 design chainage km 61000 to km 77500 on Silchar-vairengte-sairang road in the state of Mizoram under Bharatmala Pariyojna on EPC mode Vairengte - Sairang Pkg-4 (NHIDCL) (618317)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	561.91 (561.91)	0	17.12
168	4-Laning of Kolasib - Sethawn section Package-5 of NH-6 from Existing Chainage km 86000 to km 107850 Design Chainage km 77500 to km 95500 on silchar - voirengte - sairang road under Bharatmala Pariyojna on EPC mode under NHO-NE Vairengte - Sairang Pkg-5 (NHIDCL) (618318)	Mizoram	11/2021 (07/2025)	07/2027 (06/2027)	720.4 (720.4)	247.14	11.86
169	4-Laning of Sethawn - N. Kawnpui section Package-6 of NH-6 from Existing Chainage km 107850 to km 126315 Design Chainage km 95500 to km 111850 on Silchar-Vairengte- Sairang road, Vairengte - Sairang Pkg-6 (NHIDCL) (618319)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	595.65 (595.65)	173.14	6.72
170	Up-gradation to 2 lane with paved shoutders of Pawlrang - Rulchawm section- of NH-102B of Aizawl - Imphal Economic Corridor from Existing Chainage km 72.030 to km 104.129 including 2.459 km re-alignment section from Tuivai River to Rulchawm connecting km 48.150 of NH-6 [Design Chainage km 68.170 to km 98.579] in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-3 Keifang- Tuivai Pkg-3 (NHIDCL) (619010)	Mizoram	12/2021 (11/2023)	05/2025 (07/2026)	500.88 (500.88)	442.08	99.52
171	Construction of 4-Laning of N. Kawnpui N. Mualvum Mualkhang via Khamrang Village section Package-7 of NH-6 from Existing Chainage km 127200 to km 142000 Design Chainage km 111850 to km 123400 on Silchar - Vairengte - Sairang road in the State of Mizoram on EPC mode (NHIDCL) (618320)	Mizoram	02/2024 (10/2025)	10/2028 (-)	866.32 (866.32)	0	18.9
172	Construction of 4-Laning of West Serawlg-Sairang section of NH-6 from Existing Chainage km 142000 to km 158900 Design Chainage km 123400 to km 136260 on Silchar - Vairengte - Sairang road in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-8 (NHIDCL) (618321)	Mizoram	02/2024 (11/2025)	11/2028 (-)	875.79 (875.79)	0	13.95

Ongoing Projects of North-East Region

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
173	Construction of Twin Tube Uni-directional Aizawl Bypass Tunnel of 2.5 km and its approaches of 2.1 km from km 10.600 to km 15.200 on Sarrang - Phaibawk section of NH-6 in the State of Mizoram on EPC Mode under NHO-NE Package-2 (NHIDCL) (618323)	Mizoram	01/2024 (12/2025)	12/2028 (-)	1313.28 (1313.28)	0	0
174	Construction of 2-lane Aizawl Bypass from km 15.200 to km 34.500 Package-3 on Sairang - Phaibawk section of NH-6 in the State of Mizoram under Bharatmala Pariyojna on EPC Mode under NHO-NE (NHIDCL) (618324)	Mizoram	02/2023 (10/2025)	11/2028 (-)	720.72 (720.72)	0	15.1
175	Balance work of widening to two laning/re-alignment and geometric improvement from Km. 11000 to Km. 114618 with rectification of damaged stretches and provision of protection works in vulnerable location of NH-44 in the State of Mizoram. (MoRTH) (619321)	Mizoram	10/2025 (05/2026)	05/2028 (-)	170.96 (170.96)	0	2
176	Construction of 2-laning with hard shoulder configuration of Chhumkhum to Tlabung from Design Chainage Km 37.420 to Km 74.950 of NH-302 in Mizoram under Bharatmala Pariyojana on EPC mode [Pkg-B] (NHIDCL) (618363)	Mizoram	06/2021 (07/2021)	01/2023 (12/2026)	740.58 (740.58)	494.49	61.34
177	Construction of 2-laning with hard shoulder of Lunglei to Chhumkhum from Design Chainage Km 0.000 to Km 37.420 of NH-302 [Lunglei-Tlabung] Package-A (NHIDCL) (618362)	Mizoram	03/2021 (06/2021)	12/2022 (11/2026)	698.45 (698.45)	552.89	64.78
178	Widening/Improvement to 4-Lane with Paved Shoulder from km 55000 Nagabang Gamsuk to km 82514 Oyan in the State of Assam and Arunachal Pradesh on EPC mode under Bharatmala Pariyojna of Length 27.514 Km Package-3 (NHIDCL) (618359)	Multi-States (Assam, Arunachal Pradesh)	03/2023 (09/2024)	03/2027 (03/2027)	665.47 (665.47)	373.06	96.7
179	Construction of 2-lane with Paved shoulder of Kohima-Bypass Road connecting NH- 39 New NH-02, NH150New NH-02, NH7-61 New NH-29 and NH-39 New NH-02 from Design km 21.000 to km 32.268 [Design length11.268 km] in the state of Nagaland Under SARDP-NE on EPC Mode Package- 3 (NHIDCL) (618291)	Nagaland	07/2020 (06/2023)	06/2025 (12/2026)	159.85 (342.29)	123.42	39.54
180	Construction of 2-lane with Paved shoulder of Kohima- Bypass Road Connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29, NH-39New NH-02 from Design Km 32.00 to Design Km 43.454Design Length-11.454 Km in the State of Nagaland under SARDP-NE on EPC Mode Package-IV (NHIDCL) (618290)	Nagaland	07/2020 (10/2020)	04/2022 (12/2026)	202.36 (202.36)	102.12	46.77
181	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon MTM Road from existing Km 20.456 to Km 41.065 Design Km. 20 to Km. 40.0 Design Length-20.000 Km in the State of Nagaland under SARDP-NE Phase-A Pkg-2 Balance work (NHIDCL) (618423)	Nagaland	03/2018 (08/2023)	08/2025 (03/2026)	215.79 (215.79)	173.12	100
182	Construction of 2-lane with hard shoulders of Merangkong-Tamlu-Mon road Wakching Twon portion on EPC basis from existing Chainage Km 59000 to Km 73640 [Design Km. 59000 to Km, 72450] Design length - 13.450 Km under SARDP-NE package-V Balance work (NHIDCL) (618422)	Nagaland	03/2021 (09/2023)	09/2025 (07/2026)	161.73 (161.73)	101.21	99.75
183	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting New NH-02 and New NH-29 from Design Km 10.500 to design Km 21.000 [Design Length- 10.500 km] including TUNNEL of 500m at Ch. 11.000 in the state of Nagaland Under SARDP-NE on EPC Mode Package-2 (NHIDCL) (618292)	Nagaland	07/2020 (10/2020)	10/2022 (10/2027)	277.44 (277.44)	198.97	69.76
184	Widening to Existing single lane /intermediate lane to 2 lane from Km185.00 to Km 220.00 of NH-61 New NH-02 in the state of Nagaland. (MoRTH) (618072)	Nagaland	03/2021 (07/2022)	07/2024 (03/2026)	297.25 (297.25)	155.15	100
185	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29 and NH-39New NH-02 from design Km 0.00 to Km 10.500 in the State of Nagaland under SARDP-NE on EPC Mode Package-1 -Balance work (NHIDCL) (618293)	Nagaland	07/2020 (11/2023)	11/2026 (11/2026)	232.29 (350.88)	116.76	27.24
186	Balance work of Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 old NH-150 from existing km 98.380 near Chizami vill. to km120.367 Nagaland/Manipur Border [Design km 95.700 to design km 117.200] [Design Length 21.500 km] in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode Package-V under NHO (NHIDCL) (618296)	Nagaland	03/2020 (11/2023)	11/2025 (07/2026)	330.8 (330.8)	0	98.39
187	Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 Old NH-150 from existing Km 30.474 Near Kidwema road Chakahabama to existing Km 53.220 Near Kikruma Village Design Km 29.60 to Km 51.50 Design length-21.90 Km in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode under NHO Package-II -Balance work (NHIDCL) (618297)	Nagaland	03/2020 (01/2024)	01/2026 (12/2026)	355.79 (355.79)	0	43.13
188	4-Laning of Balance work of Dimapur-Kohima Road from design km 152.490 to km 166.700 Existing km 156.000 to km 172.900 Excluding Dimapur & Kohima Bypass under SARDP-NE Package-III (NHIDCL) (618328)	Nagaland	03/2016 (09/2023)	09/2025 (07/2026)	562.98 (794.75)	535.96	84.32
189	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-I Design Chainage 0000 Km to 34795 Km, in the State of Nagaland on EPC mode under NH O-NE (NHIDCL) (618364)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	430.24 (430.24)	0	87

Ongoing Projects of North-East Region

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
190	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-III Design Chainage 69875 Km to 106816 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618365)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	497.18 (497.18)	0	85.67
191	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-II Design Chainage 34795 Km to 69875 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618366)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	442.54 (442.54)	0	58.5
192	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon Road on EPC Basis from existing road Km. 76.640 to Km 98.065 Design chainage Km. 63.800 to Km. 86.835 Design Length-23.035 Km in the state of Nagaland under SARDP-NE PKG-IV Balance work (NHIDCL) (619059)	Nagaland	03/2018 (09/2023)	09/2025 (12/2026)	323.98 (323.98)	143.39	79.03
193	Widening of existing Single lane / Intermediate lane road to 2 lane from Km 101 to Km 125 of NH 61 (MoRTH) (617886)	Nagaland	06/2020 (06/2024)	06/2026 (03/2027)	252.2 (252.2)	0	44.46
194	Construction of 2 laning with Hard shoulder of Peren-Dimapur section on NH 129A from Design Km 146.208 to Km 163.592 Length- 17.384 km in the state of Nagaland on EPC mode under NHO-TSP Package-III (NHIDCL) (618413)	Nagaland	02/2021 (06/2023)	06/2025 (07/2026)	177.77 (199.02)	0	95.62
195	Construction of Balance work for 2-lane with hard shoulder of Peren- Dimapur section on NH-129A from Design Km 126.775 to Km 146.208 Length 19.433 Km in the state of Nagaland on EPC mode under NHO-TSP Package-II (NHIDCL) (618414)	Nagaland	01/2021 (09/2023)	09/2025 (09/2025)	258.52 (258.52)	135.86	96.53
196	Realignment of NH-717A from Design Ch.0.00 Km 77.800 of NH-10 to Design Ch.2.00 Km 3.100 of NH-717A with two lane paved shoulder including Major Bridge of 680 m in the State of Sikkim on EPC Mode-COS work (NHIDCL) (618428)	Sikkim	01/2021 (04/2021)	04/2023 (05/2026)	264.84 (380.94)	70.7	100
197	Construction/Up gradation of Existing road to 2 Lane with Paved Shoulder including Geometric Improvement from Ranipool to Pakyong Balance work from Km 2.000 to 16.167 of NH-717-A on EPC basis under SARDP-NE Phase A in the State of Sikkim (NHIDCL) (618426)	Sikkim	03/2018 (01/2023)	07/2024 (12/2026)	264.84 (380.94)	0.17	87.03
198	Construction of two lane with paved shoulder Gangtok Bypass Road from Ranipool to Burtuk Ch 0.00 Km to 23.316 L23.316 Km in the State of Sikkim (MoRTH) (618071)	Sikkim	10/2021 (05/2022)	05/2024 (12/2026)	385.15 (342.89)	0	90
199	Construction & Upgradation of existing road to 2-lane with paved shoulder from New Rolep Bridge at km 37.600 to Chochenpheri at km 52.00 in the section of Rongli to Chochenpheri of NH 717B Pkg-II C (NHIDCL) (618446)	Sikkim	10/2020 (05/2021)	05/2024 (09/2026)	493.42 (478.79)	0.03	79.13
200	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Helipad near Menla at Km 82000 to Menla at Km 94030 of Rhenock-Menla Spur NH-717B Package-IIIB on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618447)	Sikkim	01/2021 (02/2021)	02/2024 (05/2027)	410.6 (379.3)	0	82.64
201	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Chochenpheri at Km 52000 to Helipad near Menla at Km 82000 of Rhenock-Menla Spur NH-717B Package-IIIA on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618448)	Sikkim	10/2020 (12/2020)	12/2023 (05/2027)	816.79 (786.6)	32.28	64.31
202	Construction & Upgradation of existing road to 2-lane with paved shoulder from km27.200 End of Rongli bypass to km37.600New Rolep Bridge of Rhenok-Menla spur NH-717B on EPC Mode under SARDP-NE Phase-A in Sikkim Pkg-II B (NHIDCL) (618449)	Sikkim	07/2020 (10/2020)	04/2023 (09/2026)	230.45 (244.91)	0	86.19
203	Rehabilitation & Upgradation of existing road to 2-lane with paved shoulder including geometric improvement of section from start of Rabangla km33.600 to km58.840 under SARDP-NE Phase A Pkg- IV (NHIDCL) (618450)	Sikkim	07/2020 (10/2020)	05/2022 (12/2026)	292.8 (292.8)	1.91	65.15
204	Improvement & widening of existing NH-08 to 4-lane with Paved Shoulder from Champak Nagar to Khayerpur section design Km 242500 to Km 261610 in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618350)	Tripura	12/2023 (09/2024)	09/2026 (03/2027)	920.66 (920.66)	0	48.3
205	Improvement and Widening to 2-lane with paved shoulder of road from design Km 72.000 Pati Chhari to design Km 107.654 Harina Total length 35.654 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-4 (NHIDCL) (618367)	Tripura	01/2024 (12/2024)	12/2026 (06/2027)	726.9 (726.9)	259.36	9.33
206	Improvement and Widening to 2-lane with paved shoulder of road from design Km 36.000 Rangamati to design Km 72.000 Pati Chhari Total length 36.000 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-3 (NHIDCL) (618368)	Tripura	01/2024 (09/2024)	09/2026 (05/2027)	670.9 (670.9)	0	14.5
207	Improvement and Widening to 2-lane with paved shoulder of road from existing Km 438.170 Khowai Chowmuhani to existing Km 439.410 South Pulinpur of NH-08 and from design Km 0.000 South Pulinpur to design Km 36.00 near Rangamati of NH 208 on Khowai Teliamura- Harina section Total length 37.24 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-2 (NHIDCL) (618369)	Tripura	01/2024 (09/2024)	09/2026 (03/2027)	657.21 (657.21)	0	60.5

Ongoing Projects of North-East Region

JUNE 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
208	Improvement and Widening to 2-lane with paved shoulder of road from Km 101.300 to km 127.319 Total Length 26.019 Km i.e. the Khowai Teliamura-Amarpur-Harina-Sabroom section of NH 208 in the state of Tripura on EPC under JICA ODA Loan Phase VI Package-1 (NHIDCL) (618370)	Tripura	01/2024 (07/2024)	07/2026 (04/2027)	431.78 (431.78)	0	63.15
209	Construction of 4-Lane with paved shoulder Agartala bypass Western side, length 25.402 km connecting NH-8 near Amtali to NH-108B near Lembuchhera in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618417)	Tripura	03/2023 (03/2024)	03/2027 (03/2027)	2026.05 (2026.05)	487.38	9.2
210	Rehabilitation and up-gradation of road from km 16.077 to km 43.935 total length 27.858 km of Lalchara-Kanchanpur section via Shivbari on NH-44A to 2 lane with paved shoulder in the state of Tripura on EPC Mode Pkg-2 under BharatMala Pariyojana Manu-Simlung -2 (NHIDCL) (618307)	Tripura	02/2022 (01/2023)	01/2025 (01/2026)	456.88 (456.88)	0	54.56
211	Rehabilitation and up-gradation of road from design km 25.250 to km 36.460 Total lengh 11.210 km of Kailashahar-Kurti Bridge section on NH-208A to 2-lane with paved shoulder on EPC basis under NHO Package-III- Balance Work (NHIDCL) (618385)	Tripura	02/2020 (09/2024)	03/2026 (03/2026)	174.43 (174.43)	0	41.9
212	Melaghar-Srimantapur section on NH-08 Spur from Km 23 to Km 34.500 11.5 Km and overlay from Km 20.30 to Km 22.00 1.7 Km Total Length 13.2 Km (NHIDCL) (618411)	Tripura	01/2023 (05/2023)	11/2024 (08/2026)	195.95 (195.95)	92.61	72.48
Total (154)					97774.26	30395.11	
Department of Telecommunications							
Telecommunication							
213	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (06/2026)	971.96 (180.46)	167.23	99.84
214	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597)	Multi-States (Assam, Arunachal Pradesh)	12/2020 (10/2021)	04/2023 (09/2026)	1255.49 (276.62)	237.98	99.6
215	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (709856)	Multi-States (Assam, Meghalaya, Arunachal Pradesh, Nagaland, Mizoram, Tripura, Sikkim, Manipur)	05/2023 (05/2023)	08/2024 (06/2026)	645.13 (645.13)	407.15	92.1
216	BharatNet (Department of Telecommunications [DoT]) (706775)	Multi-States (Meghalaya, Assam, Mizoram, Tripura, Manipur, Nagaland, Sikkim, Arunachal Pradesh)	07/2017 (10/2011)	08/2023 (03/2027)	61109 (188000)	48809.69	99.98
Total (4)					63981.58	49622.05	
Department of Water Resources, River Development & GR							
Water Resources							
217	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55.44
218	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997 (04/1997)	12/2019 (12/2026)	1449.44 (1822.24)	1848.17	99
Total (2)					1705.6	1892.87	




Table 6: All Ongoing Projects



All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport (Airport Authority of India [AAI]) (612786) (-) (-)	Andhra Pradesh	03/2023 (01/2024)	01/2026 (07/2026)	265.91 (265.91)	153.62	75
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. (Airport Authority of India [AAI]) (701107) (-) (-)	Andhra Pradesh	06/2020 (09/2020)	09/2022 (10/2026)	611.8 (611.8)	527.74	88.25
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. (Airport Authority of India [AAI]) (701121) (-) (-)	Andhra Pradesh	12/2022 (08/2023)	08/2025 (06/2026)	347.15 (347.15)	189.48	94.5
4	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724) (-) (-)	Assam	12/2016 (03/2018)	03/2025 (06/2026)	1712 (2520)	2660.15	99.3
5	Development of New Civil Enclave at Bihta (Airport Authority of India [AAI]) (612183) (-) (-)	Bihar	08/2024 (04/2025)	03/2027 (-)	1413 (1413)	9.56	2.86
6	Development of New Civil Enclave and associated works at Darbhanga Airport (Airport Authority of India [AAI]) (612194) (-) (-)	Bihar	07/2024 (07/2024)	07/2026 (11/2026)	911.66 (911.66)	400.62	69.8
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna (Airport Authority of India [AAI]) (701101) (-) (-)	Bihar	10/2018 (10/2018)	05/2026 (08/2026)	1216.9 (1216.9)	1202.07	99.19
8	Development of Keshod Airport. (Airport Authority of India [AAI]) (619054) (-) (-)	Gujarat	01/2024 (07/2025)	01/2027 (-)	363.1 (363.1)	102.3	41.5
9	Development of Dholera International Greenfield Airport , Gujarat (Airport Authority of India [AAI]) (701126) (-) (-)	Gujarat	06/2022 (07/2022)	06/2026 (06/2026)	1305 (1551)	949.24	87
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. (Airport Authority of India [AAI]) (611047) (-) (-)	Jammu and Kashmir	10/2023 (12/2023)	06/2026 (11/2026)	861.37 (861.37)	353.54	55.35
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport (Airport Authority of India [AAI]) (612787) (-) (-)	Karnataka	06/2023 (01/2024)	01/2026 (06/2026)	320.47 (320.47)	160.21	85
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. (Airport Authority of India [AAI]) (612788) (-) (-)	Karnataka	06/2023 (02/2024)	02/2026 (06/2026)	322.45 (322.45)	220.72	95
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 (Airport Authority of India [AAI]) (612789) (-) (-)	Kerala	06/2023 (02/2024)	09/2025 (12/2026)	484.57 (484.57)	227.5	64.5
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh (Airport Authority of India [AAI]) (400010) (-) (-)	Ladakh	07/2018 (09/2018)	09/2021 (07/2026)	480 (640)	509.41	83.4
15	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718) (-) (-)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499 (499)	206.83	52.64
16	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, Jewar [earlier MOPA, without ASMGCS], HIAL & BIAL (Airport Authority of India [AAI]) (611570) (-) (-)	Multi-States (Karnataka, Maharashtra, Telangana, Uttar Pradesh)	12/2020 (10/2022)	09/2025 (08/2026)	500.48 (500.48)	398.75	80
17	Development of New Greenfield Airport at Bundi, Kota Rajasthan. (Airport Authority of India [AAI]) (618977) (-) (-)	Rajasthan	08/2025 (10/2025)	10/2027 (11/2027)	1507 (1507)	71.13	13.3
18	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. (Airport Authority of India [AAI]) (701127) (-) (-)	Rajasthan	06/2022 (05/2023)	03/2026 (06/2026)	480 (480)	348.01	100
19	Construction of New Integrated Passenger Terminal Building at Udaipur Airport (Airport Authority of India [AAI]) (701128) (-) (-)	Rajasthan	06/2023 (11/2023)	03/2026 (09/2026)	887 (887)	565.41	74.71

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
20	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793) (-) (-)	Sikkim	11/2023 (12/2023)	06/2026 (06/2027)	323.26 (323.26)	87.6	36.12
21	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAI]) (611602) (-) (-)	Tamil Nadu	05/2018 (06/2023)	07/2025 (12/2026)	1207 (1207)	314.15	43.5
22	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAI]) (701113) (-) (-)	Uttar Pradesh	07/2024 (07/2024)	07/2027 (07/2027)	2869.65 (2869.65)	677.21	31
23	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAI]) (701122) (-) (-)	Uttar Pradesh	06/2024 (07/2024)	07/2026 (11/2026)	579 (579)	217.42	43.22
24	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAI]) (611495) (-) (-)	West Bengal	08/2024 (09/2024)	03/2027 (03/2027)	1549 (1549)	507.8	39.68
25	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCB Airport Kolkata. (Airport Authority of India [AAI]) (612791) (-) (-)	West Bengal	03/2023 (12/2023)	10/2025 (08/2026)	328.3 (328.3)	148.75	71.4
Total (25)					21345.07	11209.22	
Ministry of Coal							
Coal							
26	TIKAK EXTENSION OCP (INVALID CO.) (615820) (-) (-)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 (159.77)	112.8	89.73
27	TIRAP OCP (INVALID CO.) (615821) (-) (-)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 (289.46)	105.66	5.26
28	PORDA CHINTAPANI OCP [10 MTY] (South Eastern Coalfields Limited [SECL]) (400144) (-) (-)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	2310.12 (2310.12)	117.37	11.81
29	BAROUD OC EXPANSION [3.0-10.0M] (South Eastern Coalfields Limited [SECL]) (400149) (-) (-)	Chhattisgarh	08/2020 (08/2020)	03/2029 (-)	2309.8 (2309.8)	1007.09	55.95
30	DIPKA EXPANSION OCP [40 MTY] (South Eastern Coalfields Limited [SECL]) (400354) (-) (-)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	5241.4 (5241.4)	2939.33	39.34
31	GEVRA OC [70 MTY] (SECL - CIL) (400424) (-) (-)	Chhattisgarh	03/2016 (03/2016)	03/2023 (03/2027)	11816.4 (11816.4)	6960.23	78.48
32	AMERA OC RCE [1.0 MTY] (SECL - CIL) (613798) (-) (-)	Chhattisgarh	02/2015 (02/2015)	03/2026 (-)	335.97 (335.97)	91.76	42.47
33	AMGAON OC RCE [1.0 MTY] (SECL - CIL) (613799) (-) (-)	Chhattisgarh	07/2015 (07/2015)	03/2026 (-)	316.11 (316.11)	192.9	78.86
34	JAGANNATHPUR OC RCE PROJECT (SECL - CIL) (613800) (-) (-)	Chhattisgarh	07/2016 (07/2016)	03/2025 (03/2027)	459.49 (459.49)	278.71	96.15
35	MAHAMAYA OCP [1.50 MTY] (SECL - CIL) (613801) (-) (-)	Chhattisgarh	05/2018 (05/2018)	03/2026 (03/2028)	410.26 (410.26)	188.6	54.6
36	KATKONA RO UG MINE (SECL - CIL) (615191) (-) (-)	Chhattisgarh	01/2023 (01/2023)	03/2029 (-)	329.21 (329.21)	62.01	2.01
37	PELMA OC MDO (SECL - CIL) (616234) (-) (-)	Chhattisgarh	10/2022 (10/2022)	03/2033 (-)	1725.04 (1725.04)	16.71	40.34
38	KUSMUNDA OC EXPANSION PROJECT (SECL - CIL) (617287) (-) (-)	Chhattisgarh	11/2024 (11/2024)	03/2030 (-)	4516.88 (4516.88)	837.14	23.75
39	MANIKPUR OC EXPANSION PROJECT (SECL - CIL) (617288) (-) (-)	Chhattisgarh	01/2025 (01/2025)	03/2029 (-)	382.61 (382.61)	138.83	21.29
40	RPR FOR DURGAPUR OCP 10 MTY (SECL - CIL) (619171) (-) (-)	Chhattisgarh	09/2025 (09/2025)	03/2032 (-)	2415.91 (2415.91)	2.35	0.01

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
41	MADANNAGAR OCP 12 MTY - MDO (SECL - CIL) (619172) (-) (-)	Chhattisgarh	12/2024 (12/2024)	03/2033 (-)	1859.19 (1859.19)	0.45	0
42	HURA C OCP (ECL - CIL) (400018) (-) (-)	Jharkhand	08/2022 (08/2022)	03/2029 (-)	859.41 (859.41)	455.95	63.3
43	KONAR EXPANSION OCP (CCL - CIL) (400073) (-) (-)	Jharkhand	01/2022 (01/2022)	03/2032 (-)	674.65 (674.65)	172.3	50.78
44	KARO EXPANSION OCP (CCL - CIL) (400074) (-) (-)	Jharkhand	01/2022 (01/2022)	03/2029 (-)	849.31 (849.31)	208.28	23.28
45	SANGHMITRA OC (CCL - CIL) (400136) (-) (-)	Jharkhand	03/2024 (03/2024)	03/2032 (-)	2660 (2660)	17.4	16.77
46	CHANDRAGUPT OCP (CCL - CIL) (400138) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	973.5 (973.5)	772.12	25.11
47	KOTRE BASANTPUR PACHMO OCP (Ministry of Coal) (400139) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	861.06 (625.4)	456.48	45.78
48	Pachwara South Coal Block (NLC India Limited) (400142) (-) (-)	Jharkhand	03/2016 (11/2019)	09/2028 (-)	2242.9 (2242.9)	1422.51	87
49	RPR MAGADH EXP OCP (Ministry of Coal) (400150) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2028 (-)	6964.33 (6964.33)	2298.45	39.42
50	NORTH URIMARI EXPANSION OCP (Ministry of Coal) (400151) (-) (-)	Jharkhand	07/2021 (07/2021)	03/2029 (-)	634.3 (634.3)	598.32	68.9
51	EPR ROHINI - KARKETTA OCP (Ministry of Coal) (400153) (-) (-)	Jharkhand	01/2021 (01/2021)	03/2028 (-)	995.57 (995.57)	85.34	24.02
52	EPR PUNDI OCP (Ministry of Coal) (400154) (-) (-)	Jharkhand	11/2020 (11/2020)	03/2027 (-)	639.6 (639.6)	236.58	11.24
53	EPR ASHOK OC (Ministry of Coal) (400155) (-) (-)	Jharkhand	05/2021 (05/2021)	03/2031 (-)	2821.07 (2821.07)	186.02	27.74
54	EPR AMRAPALI OCP (CCL - CIL) (400156) (-) (-)	Jharkhand	02/2020 (02/2020)	03/2028 (-)	4983.57 (4983.57)	1811.77	43.69
55	RAJRAPPA RCE OCP (CCL - CIL) (400160) (-) (-)	Jharkhand	12/2009 (12/2009)	03/2016 (03/2027)	510.85 (510.85)	489.2	75.61
56	CHITRA EAST OC (ECL - CIL) (400172) (-) (-)	Jharkhand	08/2018 (08/2018)	03/2026 (03/2028)	513.99 (513.99)	274.28	53.03
57	JHARKHAND-LAIYO OCP (Ministry of Coal) (400352) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2031 (-)	654.87 (654.87)	0.43	32.45
58	MOONIDIH XV SEAM UG (BCCL - CIL) (400425) (-) (-)	Jharkhand	08/2011 (08/2011)	03/2019 (09/2026)	1230.27 (1230.27)	796.31	84.02
59	AMALAGAMATED NTST KUJAMA OCP 8.5MTY (Bharat Coking Coal Limited (BCCL)) (611864) (-) (-)	Jharkhand	01/2023 (01/2023)	03/2030 (-)	4011.85 (4011.85)	414.97	30.92
60	MURAI DIH UG PROJECT (BCCL - CIL) (613808) (-) (-)	Jharkhand	02/2011 (02/2011)	04/2014 (12/2026)	339.87 (339.87)	191.14	70.47
61	TAPIN SOUTH EXPN (CCL - CIL) (615349) (-) (-)	Jharkhand	11/2020 (11/2020)	03/2028 (-)	230.41 (230.41)	40.02	23.67
62	SIRKA OC (CCL - CIL) (615822) (-) (-)	Jharkhand	05/2020 (05/2020)	03/2028 (-)	222.82 (222.82)	280.03	56.47
63	TETARIAKHAR OC (CCL - CIL) (615843) (-) (-)	Jharkhand	11/2019 (11/2019)	03/2025 (03/2027)	243.52 (243.52)	50.82	30.06

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
64	CHUPERBHITA SIMLONG OCP MDO 6 (ECL - CIL) (616225) (-) (-)	Jharkhand	12/2023 (12/2023)	03/2037 (-)	979.08 (979.08)	0	0.05
65	JARANGDIH EXPN. OCP 1.5 MTY (CCL - CIL) (616236) (-) (-)	Jharkhand	02/2020 (02/2020)	03/2029 (-)	414.37 (414.37)	85.6	32.83
66	BLOCK E OCP (BCCL - CIL) (616253) (-) (-)	Jharkhand	03/2024 (03/2024)	03/2029 (-)	5850.83 (5850.83)	20.32	4.18
67	Revised Jharia Master Plan for Dealing with Fire, Subsidence & Rehabilitation of affected families in Jharia Coalfield- Reg. (Bharat Coking Coal Limited [BCCL]) (617416) (-) (-)	Jharkhand	06/2025 (07/2025)	12/2028 (-)	5940.47 (5940.47)	327.78	31
68	North Dhadu Western Part OCP (NLC India Limited [NLCIL]) (617764) (-) (-)	Jharkhand	10/2023 (12/2023)	03/2029 (-)	1354.2 (1354.2)	228.36	40
69	AMADAND OCP[4.0MTY] (SECL - CIL) (400148) (-) (-)	Madhya Pradesh	03/2016 (03/2016)	03/2021 (03/2027)	869.44 (869.44)	324.92	75.15
70	BLOCK B EXPANSION [3.5 TO 8.0 (NCL - CIL) (400162) (-) (-)	Madhya Pradesh	07/2019 (07/2019)	03/2023 (03/2027)	998.71 (998.71)	684.46	51.08
71	NIGAH I EXPANSION [15 TO 25 MTP (NCL - CIL) (400321) (-) (-)	Madhya Pradesh	11/2020 (11/2020)	03/2025 (03/2028)	1729.68 (1729.68)	968.37	53.73
72	KANCHAN OC EXP (SECL - CIL) (613802) (-) (-)	Madhya Pradesh	12/2014 (12/2014)	03/2026 (03/2028)	371.04 (371.04)	150.83	58.2
73	JHIRIA WEST OCP [1.5 MTY] (SECL - CIL) (613803) (-) (-)	Madhya Pradesh	01/2024 (01/2024)	03/2029 (-)	366.94 (366.94)	36.68	41.29
74	RPR TAWA-III UG 0.84 MTY (WCL - CIL) (613804) (-) (-)	Madhya Pradesh	12/2021 (12/2021)	03/2027 (-)	314.09 (314.09)	17.9	17.78
75	AMALGAMATED DHANKASA & JAMUNIA (WCL - CIL) (615185) (-) (-)	Madhya Pradesh	09/2022 (09/2022)	03/2027 (-)	399.2 (399.2)	117	67.13
76	RPR OF VISHNUPURI UG TO OC (WCL - CIL) (615187) (-) (-)	Madhya Pradesh	11/2022 (11/2022)	03/2029 (-)	220.62 (220.62)	0	11.2
77	URDHAN EXPANSION OC COST PLUS (WCL - CIL) (615194) (-) (-)	Madhya Pradesh	07/2022 (01/2023)	03/2031 (-)	206.88 (206.88)	50.69	2.02
78	SHARDA UG MINE (WCL - CIL) (615195) (-) (-)	Madhya Pradesh	07/2022 (09/2023)	03/2028 (-)	166.25 (166.25)	5.93	9.39
79	GANDHIGRAM UG MINE (WCL - CIL) (615206) (-) (-)	Madhya Pradesh	08/2019 (08/2019)	03/2026 (03/2027)	414.15 (414.15)	22.16	56.88
80	JAYANT EXPN. [20 TO 38 MTPA] (NCL - CIL) (619032) (-) (-)	Madhya Pradesh	02/2025 (02/2025)	03/2032 (-)	25560.48 (25560.5)	256.7	2.02
81	RPR FOR RAMPUR BATURA OCP (SECL - CIL) (619053) (-) (-)	Madhya Pradesh	05/2025 (05/2025)	03/2030 (-)	1604.69 (1604.69)	75.23	0.3
82	BHATADI EXPANSION OC (WCL - CIL) (400033) (-) (-)	Maharashtra	02/2020 (05/2022)	03/2028 (-)	580.61 (580.61)	112.17	33.91
83	AMALGAMATED YEKONA I & YEKONA (WCL - CIL) (400177) (-) (-)	Maharashtra	08/2015 (08/2015)	03/2025 (03/2027)	727.28 (727.28)	564.25	80.77
84	DINESH[MAKARDHOKRA-III] OC (WCL - CIL) (400178) (-) (-)	Maharashtra	02/2020 (02/2020)	03/2027 (-)	822.88 (822.88)	791.48	40.63
85	DHUPTALA OC [SASTI UG TO OC] (WCL - CIL) (400353) (-) (-)	Maharashtra	02/2019 (10/2021)	03/2028 (-)	711.01 (711.01)	174.66	19.02

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
86	SAONER UG MINE -1 EXPANSION 1. (WCL - CIL) (615184) (-) (-)	Maharashtra	01/2022 (01/2022)	03/2028 (-)	228.64 (228.64)	157.02	69.33
87	SASTI EXPANSION OPENCAST (WCL - CIL) (615186) (-) (-)	Maharashtra	08/2020 (08/2020)	03/2026 (03/2027)	319.04 (319.04)	153.78	32.21
88	NEW MAJRI UG TO OC 3 MTY COST (WCL - CIL) (615188) (-) (-)	Maharashtra	05/2019 (09/2022)	03/2027 (-)	402.27 (402.27)	67.81	24.17
89	MAKARDHOKRA EXPN OC 4.9 MTY (WCL - CIL) (615189) (-) (-)	Maharashtra	06/2022 (06/2022)	03/2026 (03/2027)	361.87 (361.87)	104.17	12.2
90	SINGHORI DEEP OC MIN 2.0 MTY (WCL - CIL) (615190) (-) (-)	Maharashtra	05/2022 (05/2022)	03/2029 (-)	335.75 (335.75)	53.34	9.64
91	GOKUL EXTENSION OC MINE (WCL - CIL) (615192) (-) (-)	Maharashtra	04/2021 (04/2021)	03/2026 (03/2027)	309.58 (309.58)	62.31	8.44
92	KOLGAON EXPANSION DEEP OC MINE (WCL - CIL) (615199) (-) (-)	Maharashtra	01/2023 (09/2023)	03/2027 (-)	198.71 (198.71)	25.08	2.82
93	BALLARPUR NORTH WEST OC MINE (WCL - CIL) (615330) (-) (-)	Maharashtra	12/2022 (12/2022)	03/2029 (-)	360.81 (360.81)	26.97	5.35
94	GADEGAON OC 3 MTY (WCL - CIL) (615331) (-) (-)	Maharashtra	10/2023 (10/2023)	03/2030 (-)	497.41 (497.41)	86.72	2.19
95	GHONSA EXPANSION DEEP OC MINE (WCL - CIL) (615914) (-) (-)	Maharashtra	03/2021 (04/2021)	03/2029 (-)	184.71 (184.71)	15.72	12.98
96	AMLG GAURI PAUNI EXPANSION OC (WCL - CIL) (615916) (-) (-)	Maharashtra	04/2024 (04/2024)	03/2030 (-)	1225.21 (1225.21)	91.83	4.21
97	GAURIDEEP/GAURI CENTRAL OCP 7. (WCL - CIL) (615917) (-) (-)	Maharashtra	08/2023 (06/2024)	03/2030 (-)	973.07 (973.07)	1.55	2.31
98	RPR OF BHANEGAON OC (WCL - CIL) (615918) (-) (-)	Maharashtra	02/2017 (09/2022)	03/2028 (-)	405.2 (405.2)	43.1	16.06
99	N. EXTN. MUNGOLI NIRGUDA D OCP (WCL - CIL) (615919) (-) (-)	Maharashtra	06/2024 (06/2024)	03/2029 (-)	1024.91 (1024.91)	218.36	27.92
100	NILJAI EXPANSION DEEP OCP (WCL - CIL) (615982) (-) (-)	Maharashtra	08/2016 (08/2016)	03/2022 (03/2027)	319.75 (319.75)	196.82	79.83
101	UKNI DEEP OC MINE -COST PLUS (WCL - CIL) (616044) (-) (-)	Maharashtra	11/2018 (01/2019)	03/2021 (03/2027)	237.06 (237.06)	168.2	94.57
102	AMALGAMATED INDER-KAMPTEE DEEP (WCL - CIL) (616050) (-) (-)	Maharashtra	09/2018 (09/2018)	03/2024 (03/2027)	235.9 (235.9)	128.23	98.97
103	ADASA UG TO OC MINE (WCL - CIL) (616223) (-) (-)	Maharashtra	11/2018 (11/2018)	03/2024 (03/2027)	316 (316)	209.29	86.49
104	AMAL GONDEGAON GHATROHANA EXPN (WCL - CIL) (616229) (-) (-)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	668.54 (668.54)	2.95	2.55
105	WAGHODA UG MINE [1.02 MTY] (WCL - CIL) (617233) (-) (-)	Maharashtra	01/2024 (01/2025)	03/2030 (-)	379.3 (379.3)	0	0.11
106	KOLARPIMPRI EXPANSION OC [2.5 (WCL - CIL) (617278) (-) (-)	Maharashtra	06/2024 (02/2025)	03/2030 (-)	630.37 (630.37)	0.61	0.4
107	SAONER-III EXPN UG MINE 1.54 (WCL - CIL) (619055) (-) (-)	Maharashtra	08/2025 (08/2025)	03/2032 (-)	444.42 (444.42)	0	0
108	BINA KAKRI AMALGAMATION EXPANS (WCL - CIL) (400369) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020 (08/2020)	03/2024 (03/2027)	836.42 (836.42)	914.9	92.05

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
109	KHADIA EXPANSION [10 TO 16 MTP (NCL - CIL) (615183) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021 (06/2021)	03/2025 (03/2027)	491.67 (491.67)	379.69	57.12
110	SUBHADRA OCP (Mahanadi Coalfields Limited [MCL]) (400165) (-) (-)	Odisha	05/2021 (05/2021)	04/2032 (-)	1693.81 (1693.81)	1331.36	46.27
111	SIARMAL OCP (Mahanadi Coalfields Limited [MCL]) (400166) (-) (-)	Odisha	02/2021 (02/2021)	03/2029 (-)	5194.95 (5194.95)	3491.08	60.66
112	BALARAM EXPANSION OCP (Mahanadi Coalfields Limited [MCL]) (400183) (-) (-)	Odisha	08/2020 (08/2020)	03/2029 (-)	3504.21 (3504.21)	961.2	58.23
113	GOPALJI KANIHA OCP [10 TO 30 M (MCL - CIL) (400185) (-) (-)	Odisha	04/2022 (04/2022)	03/2030 (-)	8416.19 (6107.87)	1776.83	35.69
114	INTEGRATED LAKHANPUR-BELPAHAR- (Mahanadi Coalfields Limited [MCL]) (400187) (-) (-)	Odisha	05/2018 (05/2018)	03/2027 (-)	2434.75 (2434.75)	2030.9	82.5
115	BHARATPUR RE-ORGANIZATION OCP (Mahanadi Coalfields Limited [MCL]) (400392) (-) (-)	Odisha	11/2018 (11/2018)	03/2029 (-)	2838.86 (2838.86)	1713.38	53.04
116	Naini Coal Mine (Singareni Collieries Company Limited [SCCL]) (615857) (-) (-)	Odisha	03/2020 (03/2020)	03/2026 (-)	494.3 (494.3)	491.33	80
117	INTEGRATED KULDA GARJANBAHAL O (MCL - CIL) (616226) (-) (-)	Odisha	04/2023 (04/2023)	03/2033 (-)	3563.5 (3563.5)	652.7	10.24
118	BHUBANESWARI EXPN OCP 50 MTY (MCL - CIL) (616231) (-) (-)	Odisha	03/2024 (03/2024)	03/2033 (-)	5366.27 (5366.27)	477.43	33.96
119	HINGULA II OC EXPN PH III 15 M (MCL - CIL) (616232) (-) (-)	Odisha	11/2022 (11/2022)	03/2029 (-)	1561.85 (1561.85)	279.32	31.05
120	BALABHADRA OCP (MCL - CIL) (616233) (-) (-)	Odisha	04/2023 (04/2023)	03/2030 (-)	978.44 (978.44)	251.55	18.21
121	Talabira II & III OCP - FMC (NLC India Limited [NLCIL]) (618982) (-) (-)	Odisha	10/2022 (05/2023)	06/2026 (12/2026)	522.45 (522.45)	324.74	73.65
122	Jawahar Khani Open Cast Mine (Singareni Collieries Company Limited [SCCL]) (615818) (-) (-)	Telangana	12/2021 (12/2021)	03/2025 (03/2027)	297.88 (297.88)	50.39	20
123	Kalyanikhani Opencast Project (Singareni Collieries Company Limited [SCCL]) (615858) (-) (-)	Telangana	03/2016 (05/2017)	03/2026 (-)	384.32 (384.32)	301.56	76
124	Godavarikhani Coal Mine - 5 (Singareni Collieries Company Limited [SCCL]) (615860) (-) (-)	Telangana	07/2019 (05/2019)	03/2025 (03/2026)	607.04 (607.04)	200.83	71
125	Indaram Opencast Project (Singareni Collieries Company Limited [SCCL]) (615861) (-) (-)	Telangana	08/2017 (12/2022)	03/2025 (03/2026)	424.81 (424.81)	408.29	81
126	Goleti Opencast Mine (Singareni Collieries Company Limited [SCCL]) (615862) (-) (-)	Telangana	07/2021 (08/2021)	03/2026 (-)	345.6 (345.6)	111.94	33
127	Venkatesh Khani Coal Mine (Singareni Collieries Company Limited [SCCL]) (615863) (-) (-)	Telangana	10/2020 (06/2020)	03/2026 (-)	484.5 (484.5)	477.14	97
128	Kakatiyakhani OC - 2 Project (Singareni Collieries Company Limited [SCCL]) (615865) (-) (-)	Telangana	08/2017 (09/2017)	03/2025 (03/2026)	442.42 (442.42)	253.39	63
129	MOHANPUR EXPANSION OC -PHASE I (ECL - CIL) (400173) (-) (-)	West Bengal	11/2020 (11/2020)	03/2026 (03/2030)	888.99 (888.99)	143.29	31.52
130	BONJEMEhari EXPANSION OCP (Eastern Coal Fields Limited [ECL]) (400180) (-) (-)	West Bengal	08/2021 (08/2021)	03/2026 (03/2030)	570.11 (570.11)	88.96	17.13
131	NAKRAKONDA KUMARDIH- B OCP (ECL - CIL) (400181) (-) (-)	West Bengal	08/2018 (08/2018)	03/2029 (-)	502.68 (502.67)	88.9	28.58

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
132	TILABONI UG (ECL - CIL) (400186) (-) (-)	West Bengal	01/2023 (01/2023)	03/2029 (-)	749.08 (749.07)	53.97	12.14
133	JHANJRA EXPANSION UG (Eastern Coal Fields Limited [ECL]) (400312) (-) (-)	West Bengal	04/2020 (04/2020)	03/2029 (-)	1210.12 (1210.12)	633.57	52.04
134	SONEPUR BAZARI EXPANSION OCP [(Eastern Coal Fields Limited [ECL]) (400315) (-) (-)	West Bengal	07/2021 (07/2021)	03/2029 (-)	5365.88 (5365.88)	628.22	18.5
135	ITAPARA OCP (ECL - CIL) (612816) (-) (-)	West Bengal	12/2023 (12/2023)	03/2030 (-)	929.1 (929.1)	132.43	8.41
136	SHYAMSUNDARPUR UG INCLUDING SA (ECL - CIL) (613793) (-) (-)	West Bengal	04/2020 (04/2020)	03/2026 (03/2028)	483.65 (483.65)	96.8	16.79
137	PARASEA-BELBAID UG PROJECT (ECL - CIL) (613794) (-) (-)	West Bengal	01/2023 (01/2023)	03/2028 (-)	389.1 (389.1)	132.48	22.26
138	PARASCOLE JAMBAD OCP (ECL - CIL) (616230) (-) (-)	West Bengal	11/2024 (11/2024)	03/2037 (-)	1193.55 (1193.55)	11.81	0.23
Total (113)					182823.26	50030.39	
Electricity Generation							
139	50 MW Wind Power Project (NLC India Limited) (617299) (-) (-)	Gujarat	07/2022 (01/2024)	06/2025 (12/2026)	383.84 (383.84)	328.54	52
140	600 MW Khavda Solar Power Project (NLC India Limited [NLCIL]) (617730) (-) (-)	Gujarat	08/2023 (06/2024)	06/2026 (12/2026)	3335.85 (3335.85)	2000.62	60
141	200 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (618991) (-) (-)	Gujarat	07/2022 (03/2024)	12/2026 (-)	1221.41 (1221.41)	66.07	0
142	100 MW SPP part of SECI 150 MW Hybrid (NLC India Limited [NLCIL]) (618992) (-) (-)	Gujarat	07/2022 (04/2024)	12/2026 (-)	480.68 (480.68)	2.66	1.2
143	NLC Talabira Thermal Power Project (NLC India Limited) (400231) (-) (-)	Odisha	01/2017 (01/2024)	03/2030 (-)	27212.96 (27213)	3518.17	3.54
144	810 MW Solar Power Project - Rajasthan (NLC India Limited [NLCIL]) (618981) (-) (-)	Rajasthan	10/2024 (09/2025)	03/2028 (-)	4147.07 (4147.07)	249.95	0
Total (6)					36781.81	6166.01	
Railways							
145	Dharamjaigarh-Korba (Railway) (400203) (-) (-)	Chhattisgarh	05/2018 (03/2017)	12/2026 (08/2026)	1686.22 (2438.53)	792.73	43.7
146	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] (Ministry of Coal) (400416) (-) (-)	Jharkhand	02/2018 (05/2022)	06/2025 (06/2027)	1799.64 (2564.34)	1713.19	71
Total (2)					3485.86	2505.92	
Ministry of Power							
Coal							
147	Tubed Coal Mine (Damodar Valley Corporation) (400192) (-) (-)	Jharkhand	07/2016 (10/2016)	05/2026 (05/2026)	1581 (1581)	616.91	36.5
148	Badam Coal Mining project of NTPC (National Thermal Power Corporation [NTPC]) (603293) (-) (-)	Jharkhand	02/2019 (09/2019)	12/2056 (04/2027)	502 (784)	436.5	67.86
Total (2)					2083	1053.41	
Electricity Generation							
149	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182) (-) (-)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31876.39 (31876.4)	4749.66	17.78
150	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698) (-) (-)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1938.85 (1938.85)	105.5	6.33

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
151	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699) (-) (-)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1750.07 (1750.07)	78.38	5.1
152	700 MW Tato-II HE Project (North Eastern Electric Power Corporation Limited) (611716) (-) (-)	Arunachal Pradesh	09/2025 (09/2025)	09/2031 (-)	8146.21 (8146.21)	253.97	6.54
153	Kalai-II Hydro Electric Project [1200 MW] (THDC India Limited) (619311) (-) (-)	Arunachal Pradesh	04/2026 (04/2026)	10/2032 (-)	14105.83 (14105.8)	188.62	0
154	Buxar Thermal Power Project [1320 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602579) (-) (-)	Bihar	03/2019 (06/2019)	01/2024 (05/2026)	10439.09 (13756.6)	13606.72	94.94
155	Nabinagar Super Thermal Power Project, Stage-II [3x800 MW] (National Thermal Power Corporation [NTPC]) (619051) (-) (-)	Bihar	11/2024 (03/2025)	07/2030 (09/2030)	29948 (29948)	3099.94	13.65
156	Lara Super Thermal Power Project Stage-II [2 x 800 MW] (National Thermal Power Corporation [NTPC]) (611930) (-) (-)	Chhattisgarh	08/2023 (08/2023)	06/2028 (11/2028)	15530 (16106)	5279.03	32.3
157	Sipat Super Thermal Power Project, Stage-III [1x800 MW] (National Thermal Power Corporation [NTPC]) (617188) (-) (-)	Chhattisgarh	09/2024 (09/2024)	09/2029 (11/2029)	9791 (9791)	1795.82	21.3
158	Bagodara Solar Power Project (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (709747) (-) (-)	Gujarat	03/2021 (05/2021)	12/2025 (12/2025)	339.35 (339.35)	370	51.86
159	Dhaultasidh Hydro Electric Project [66 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602582) (-) (-)	Himachal Pradesh	10/2020 (05/2021)	11/2025 (03/2027)	687.97 (1561.21)	1159.67	79.59
160	Luhri Stage-I Hydro Electric Project [210 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (602593) (-) (-)	Himachal Pradesh	11/2020 (11/2020)	01/2026 (02/2030)	1810.56 (4681.64)	1958.25	52.13
161	Sunni Dam Hydro Electric Project [382 MW] (Satluj Jal Vidyut Nigam [SJVN] Thermal Limited) (611586) (-) (-)	Himachal Pradesh	01/2023 (01/2023)	04/2028 (12/2029)	2614.51 (4925.87)	1115.87	34.58
162	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW (National Hydroelectric Power Corporation Limited [NHPC]) (602525) (-) (-)	Jammu and Kashmir	10/2014 (02/2018)	04/2020 (12/2026)	8112.12 (12728)	9313.54	82.05
163	Kiru HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (602532) (-) (-)	Jammu and Kashmir	03/2019 (02/2020)	09/2023 (12/2026)	4287.59 (5409)	3948.67	87
164	Rattle HE Project - 850 MW, Rattle Hydroelectric Power Corporation Limited. (National Hydroelectric Power Corporation Limited [NHPC]) (602535) (-) (-)	Jammu and Kashmir	02/2021 (01/2022)	02/2026 (11/2028)	5281.94 (5281.94)	1639.83	31.29
165	Kwar HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (605155) (-) (-)	Jammu and Kashmir	05/2022 (11/2022)	11/2026 (03/2028)	4526.12 (4526.12)	1701.47	36.52
166	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] (National Thermal Power Corporation [NTPC]) (400261) (-) (-)	Jharkhand	11/2017 (11/2017)	03/2023 (04/2027)	18668 (20302)	19207.59	90.5
167	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand (Damodar Valley Corporation) (611509) (-) (-)	Jharkhand	04/2023 (11/2024)	03/2029 (-)	14358 (14358)	2114.29	13.5
168	Gadarwara Super Thermal Power Project, Stage-II [2x800 MW] (National Thermal Power Corporation [NTPC]) (618976) (-) (-)	Madhya Pradesh	11/2024 (05/2025)	03/2030 (05/2030)	20446 (20446)	2141.47	10
169	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (05/2026)	6285.33 (26075.5)	26379.99	97.84
170	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion (National Thermal Power Corporation [NTPC]) (602961) (-) (-)	Odisha	08/2022 (09/2022)	05/2027 (05/2028)	11843.75 (12543)	6779.45	53.5
171	Darlipali Super Thermal Power Project, Stage-II [1x800 MW] (National Thermal Power Corporation [NTPC]) (619056) (-) (-)	Odisha	11/2025 (11/2025)	01/2031 (05/2031)	11131 (11131)	560.18	2.45
172	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181) (-) (-)	Sikkim	03/2019 (03/2020)	03/2024 (12/2027)	5748.04 (5748.04)	4519.87	73.48

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
173	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156) (-) (-)	Sikkim	03/2021 (08/2021)	05/2024 (11/2026)	938.29 (1828.11)	1691.2	97.34
174	Telangana Super Thermal Power Project , Stage-II [3 x 800 MW] (National Thermal Power Corporation [NTPC]) (619341) (-) (-)	Telangana	03/2026 (03/2026)	01/2032 (-)	29344.85 (29344.8)	729.63	0.78
175	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] (National Thermal Power Corporation [NTPC]) (612142) (-) (-)	Uttar Pradesh	03/2024 (03/2024)	02/2030 (04/2030)	17195 (17195)	3646.01	23.8
176	Tapovan-Vishnugad HEP [4x130 MW] (National Thermal Power Corporation [NTPC]) (602185) (-) (-)	Uttarakhand	11/2006 (11/2006)	03/2013 (04/2029)	2978 (10907.3)	7766.24	75.81
177	Vishnugad Pipalkoti Hydro Electric Project [444 MW] (THDC India Limited) (602195) (-) (-)	Uttarakhand	08/2008 (01/2014)	12/2022 (06/2028)	3860.35 (6405.08)	5700.11	81
178	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal (Damodar Valley Corporation) (400062) (-) (-)	West Bengal	01/2023 (02/2025)	06/2029 (-)	17673 (17673)	2120.39	11.5
179	Rammam-III HEPP [3x40 MW] (National Thermal Power Corporation [NTPC]) (602184) (-) (-)	West Bengal	09/2014 (09/2014)	09/2019 (03/2029)	1381.84 (2865.56)	1617.53	57.1
180	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 (Damodar Valley Corporation) (602538) (-) (-)	West Bengal	06/2019 (02/2021)	01/2024 (05/2026)	1037 (1106)	1138.42	97
Total (32)					314074.05	136477.31	
Transmission & Distribution							
181	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617183) (-) (-)	Andhra Pradesh	03/2025 (03/2025)	12/2027 (-)	2886 (2886)	739.68	41.68
182	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375) (-) (-)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 (209.38)	3.14	1.56
183	Transmission system for evacuation of Power from REZ in Rajasthan [20 GW] under phase-III Part-D Phase-II (Power Grid Corporation of India Limited [POWERGRID]) (615336) (-) (-)	Delhi	11/2023 (10/2024)	02/2026 (12/2026)	284 (284)	78.5	33.63
184	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (612139) (-) (-)	Gujarat	12/2023 (12/2023)	12/2025 (12/2026)	4231 (4231)	3175.78	70.87
185	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (612855) (-) (-)	Gujarat	05/2024 (05/2024)	05/2026 (06/2026)	697 (697)	573.07	82
186	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615342) (-) (-)	Gujarat	10/2024 (10/2024)	07/2026 (04/2027)	329 (329)	51.98	18
187	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] (Power Grid Corporation of India Limited [POWERGRID]) (615343) (-) (-)	Gujarat	11/2024 (11/2024)	11/2026 (-)	501 (501)	25.05	8.67
188	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345) (-) (-)	Gujarat	10/2024 (10/2024)	10/2026 (10/2027)	4766 (4766)	2111.34	36.57
189	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069) (-) (-)	Gujarat	02/2025 (02/2025)	02/2027 (-)	466 (466)	143.48	37
190	Augmentation of Banaskantha [Raghnesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182) (-) (-)	Gujarat	03/2025 (03/2025)	03/2027 (-)	172 (172)	58.48	39
191	Augmentation of Transformation Capacity at Bhuj-II PS [GIS] (Power Grid Corporation of India Limited [POWERGRID]) (617391) (-) (-)	Gujarat	02/2025 (02/2025)	11/2026 (06/2027)	488.29 (488.29)	9.76	4.5

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
192	Jamnagar Transmission Limited (Adani Transmission Limited) (617405) (-) (-)	Gujarat	NA (10/2024)	10/2026 (-)	4000 (4000)	553	19
193	Provision of ICT Augmentation & Bus Reactor at Bhuj-II PS (Power Grid Corporation of India Limited [POWERGRID]) (617801) (-) (-)	Gujarat	03/2025 (03/2025)	12/2026 (06/2027)	581.74 (581.74)	17.45	6
194	KPSIII HVDC Transmission Limited (Adani Transmission Limited) (619026) (-) (-)	Gujarat	NA (12/2025)	12/2029 (-)	19000 (19000)	20	1
195	Transmission System for Reliable Power Supply to Dholera (Power Grid Corporation of India Limited [POWERGRID]) (619029) (-) (-)	Gujarat	09/2024 (09/2024)	03/2026 (12/2026)	319.42 (319.42)	63.88	31
196	Khavda IVA Power Transmission Limited (Adani Transmission Limited) (619049) (-) (-)	Gujarat	08/2024 (08/2024)	08/2026 (-)	4500 (4500)	2332.7	60
197	Transmission Scheme for evacuation of Power from Ratle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179) (-) (-)	Jammu and Kashmir	07/2024 (07/2024)	07/2026 (06/2027)	218.6 (218.6)	3.72	1.7
198	Implementation of Transmission Systems in the State of Jharkhand consisting of 400/220/132/33 kV transmission lines and substations under Jharkhand Consultancy Project (Power Grid Corporation of India Limited [POWERGRID]) (617326) (-) (-)	Jharkhand	02/2012 (02/2012)	03/2026 (08/2026)	1842.25 (1842.25)	1648.05	96.3
199	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140) (-) (-)	Karnataka	12/2023 (12/2023)	12/2025 (09/2026)	4445 (4445)	3958.72	92.35
200	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672) (-) (-)	Karnataka	01/2025 (01/2025)	06/2027 (-)	1354 (1354)	284.34	34.6
201	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068) (-) (-)	Karnataka	02/2025 (02/2025)	06/2027 (-)	288 (288)	20.16	18
202	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184) (-) (-)	Karnataka	03/2025 (03/2025)	09/2027 (-)	3453 (3453)	483.42	21.31
203	Transmission System Strengthening at Davanagere for Integration of RE Generation [SPV Name - POWERGRID Davanagere Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617803) (-) (-)	Karnataka	09/2025 (09/2025)	09/2027 (-)	379 (379)	17.06	2.5
204	Transmission System Strengthening for integration of additional RE Potential at Davanagere [0.25 GW] and Bellary [2.75 GW] (Power Grid Corporation of India Limited [POWERGRID]) (619228) (-) (-)	Karnataka	02/2026 (02/2026)	02/2028 (-)	1111 (1111)	13.44	1
205	Augmentation of 1x500 MVA 400/220kV ICT [3rd] at Thrissur VSC HVDC Station in Kerala (Power Grid Corporation of India Limited [POWERGRID]) (619028) (-) (-)	Kerala	08/2025 (08/2025)	08/2027 (-)	173.14 (173.14)	2.08	1.5
206	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344) (-) (-)	Madhya Pradesh	10/2024 (10/2024)	10/2026 (06/2027)	3674 (3674)	1637.5	45.5
207	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346) (-) (-)	Madhya Pradesh	08/2024 (08/2024)	08/2026 (02/2027)	2708 (2708)	1570.64	70.96
208	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272) (-) (-)	Madhya Pradesh	06/2024 (06/2024)	12/2026 (-)	370 (370)	129.5	52.14
209	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279) (-) (-)	Madhya Pradesh	06/2025 (06/2025)	12/2027 (-)	558 (558)	180.9	15.11

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
210	Augmentation of Transformation Capacity and Implementation of Line Bays at Mandsaur S/S for RE Interconnection [SPV Name- POWERGRID Mandsaur I RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617802) (-) (-)	Madhya Pradesh	10/2025 (10/2025)	03/2028 (-)	319 (319)	16.3	2.5
211	Mahan Transmission Limited (Adani Transmission Limited) (619024) (-) (-)	Madhya Pradesh	03/2025 (03/2025)	04/2027 (-)	3125.32 (3125.32)	317.79	18
212	Transmission System for Evacuation of power from Potential RE Zone in Khavda Area of Gujarat under phase IV 7GW-Part E4 (Power Grid Corporation of India Limited [POWERGRID]) (611966) (-) (-)	Maharashtra	11/2023 (11/2023)	07/2025 (05/2026)	224.41 (224.41)	224.41	100
213	WRNES Talegaon Power Transmission Limited (Adani Transmission Limited) (619027) (-) (-)	Maharashtra	NA (05/2025)	01/2028 (-)	2000 (2000)	18	5
214	Network Expansion Scheme in Maharashtra for removal of Transmission constraints in Pune Region-I [765/400kV AIS Pune East] (Power Grid Corporation of India Limited [POWERGRID]) (619227) (-) (-)	Maharashtra	03/2026 (03/2026)	03/2028 (-)	1420 (1420)	7.95	0.5
215	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	03/2025 (03/2025)	03/2027 (09/2027)	5550 (5550)	1595.07	24.88
216	Transmission System for Integration of Ananthapur 2 REZ Phase 1 for 4.5 GW. SPV Name Anantapuram 2 REZ Transmission Ltd (Sterlite Power) (617806) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	08/2024 (03/2025)	03/2027 (-)	4535.99 (4535.99)	1057.57	50
217	Inter-Regional Strengthening between SR Grid and ER Grid (Power Grid Corporation of India Limited [POWERGRID]) (619030) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	02/2026 (02/2026)	08/2028 (-)	2722.5 (2722.5)	143.2	1.77
218	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223) (-) (-)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4754.42 (9129.32)	8128.74	83.8
219	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709) (-) (-)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (03/2027)	5111.33 (6700)	5577.75	99.1
220	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271) (-) (-)	Multi-States (Bihar, Odisha, West Bengal)	09/2024 (09/2024)	03/2026 (09/2026)	342.69 (342.69)	137.07	29.73
221	Inter-regional [NR-WR] Transmission System strengthening to relieve the loading of 765 kV Vindhyachal-Varanasi D/c line (Power Grid Corporation of India Limited [POWERGRID]) (617807) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	10/2025 (10/2025)	10/2027 (-)	2368 (2368)	138.29	2.03
222	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270) (-) (-)	Multi-States (Bihar, West Bengal)	11/2024 (11/2024)	05/2026 (06/2027)	408.94 (408.94)	6.13	1.5
223	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735) (-) (-)	Multi-States (Delhi, Rajasthan)	12/2022 (12/2022)	03/2025 (12/2026)	331 (331)	227.16	67.5
224	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D Phase I [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132) (-) (-)	Multi-States (Delhi, Rajasthan)	02/2024 (02/2024)	08/2025 (09/2026)	2423 (2423)	2223.59	90.51
225	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347) (-) (-)	Multi-States (Gujarat, Maharashtra)	11/2024 (11/2024)	05/2029 (-)	24819 (24819)	2978.28	18.11
226	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339) (-) (-)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024 (11/2024)	11/2026 (04/2027)	5969 (5969)	1880.23	30.6
227	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Siwani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340) (-) (-)	Multi-States (Haryana, Rajasthan)	11/2024 (11/2024)	11/2026 (06/2027)	5357 (5357)	1812.81	34.01
228	Inter-Regional Strengthening between SR Grid and WR Grid (Power Grid Corporation of India Limited [POWERGRID]) (617808) (-) (-)	Multi-States (Karnataka, Maharashtra)	10/2025 (10/2025)	10/2027 (-)	1007 (1007)	49.85	2.5

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
229	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138) (-) (-)	Multi-States (Karnataka, Telangana)	02/2024 (02/2024)	02/2026 (08/2026)	1368 (1368)	1231.2	93.76
230	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (12/2026)	2227 (2227)	1024.42	46.71
231	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (04/2027)	3251 (3251)	2048.13	44.33
232	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [Rajasthan V Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025 (03/2025)	03/2027 (06/2027)	5028 (5028)	1263.53	31.49
233	RAJASTHAN PART I POWER TRANSMISSION LIMITED (Adani Transmission Limited) (619025) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	01/2025 (01/2025)	07/2029 (-)	25000 (25000)	426.05	4
234	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133) (-) (-)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023 (12/2023)	12/2025 (12/2026)	3271 (3271)	2731.29	73.17
235	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670) (-) (-)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024 (12/2024)	12/2026 (06/2027)	5846 (5846)	1753.81	37.67
236	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949) (-) (-)	Rajasthan	10/2023 (10/2023)	04/2025 (05/2026)	1160 (1160)	1148.4	99.67
237	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134) (-) (-)	Rajasthan	12/2023 (12/2023)	12/2025 (12/2026)	4741 (4741)	3887.62	77.65
238	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332) (-) (-)	Rajasthan	08/2024 (08/2024)	08/2026 (03/2027)	3279 (3279)	1790.99	52.83
239	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615335) (-) (-)	Rajasthan	08/2024 (08/2024)	08/2026 (03/2027)	1382 (1382)	590.11	48.83
240	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615337) (-) (-)	Rajasthan	08/2024 (08/2024)	02/2026 (09/2026)	369 (369)	228.78	82.1
241	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615338) (-) (-)	Rajasthan	11/2024 (11/2024)	11/2026 (06/2027)	2735 (2735)	1100.29	43
242	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617181) (-) (-)	Rajasthan	03/2025 (03/2025)	12/2026 (06/2027)	404 (404)	29.61	16.4
243	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Tarnsmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616671) (-) (-)	Tamil Nadu	01/2025 (01/2025)	12/2026 (03/2027)	548 (548)	208.24	20.49
244	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex (Power Grid Corporation of India Limited [POWERGRID]) (617269) (-) (-)	Uttar Pradesh	12/2024 (12/2024)	06/2026 (12/2026)	212.81 (212.81)	9.98	11.17
	Total (64)				197615.23	65919.46	

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Housing & Urban Affairs							
Construction							
245	Construction of One Tower of Office Complex and another Tower of Residential quarters consisting of 10Nos. Type-V, 10Nos. Type-VI & 1No.Type-VII Quarters i/c internal water supply, sanitary installation and all development and bulk services, Horticulture works on EPC Mode-I basis i/c comprehensive operation and maintenance of Civil, E&M services for 7 years after completion of original construction work for Ranga Reddy, Secunderabad, Medchal, Audit-I, Audit-II Commissionerates of Central Tax at Khajaguda, Serilingampally, Hyderabad. (Central Public Works Department - CPWD) (617412) (-) (-)	Telangana	03/2024 (11/2024)	09/2027 (-)	644 (644)	175.79	23
Total (1)					644	175.79	
Real Estate							
246	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System (ministry of housing and urban affairs) (707229) (-) (-)	Andaman & Nicobar	07/2021 (11/2021)	05/2023 (10/2025)	209.88 (230)	37.35	97
247	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi (National Buildings Construction Corporation [NBCC]) (400188) (-) (-)	Delhi	07/2016 (05/2018)	12/2025 (12/2025)	32850 (32841)	14370.45	46.7
248	Rehabilitation in Junavadaj Area Smart City Project (ministry of housing and urban affairs) (701719) (-) (-)	Gujarat	02/2016 (06/2016)	07/2022 (07/2026)	539 (539)	623.44	98.5
249	Green Building Development Project (ministry of housing and urban affairs) (701766) (-) (-)	Uttarakhand	11/2019 (08/2019)	11/2023 (12/2026)	150.97 (206)	56.76	40.05
Total (4)					33749.85	15088	
Urban Public Transport							
250	Patna Metro Rail Project (Patna Metro Rail Corporation Ltd. [PMRCL]) (702627) (-) (-)	Bihar	02/2019 (02/2019)	02/2024 (06/2027)	13365.77 (13365.8)	5198.09	50.05
251	Delhi Metro Rail Phase-IV [2 Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (617207) (-) (-)	Delhi	03/2024 (03/2024)	03/2029 (-)	8399.81 (8399.81)	156.69	4.29
252	Delhi Metro Rail Phase V A (Delhi Metro Rail Corporation Limited [DMRC]) (619031) (-) (-)	Delhi	01/2026 (01/2026)	12/2028 (-)	12014.91 (12014.9)	253.96	5.63
253	DMRTS Phase - IV [3 Priority Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (702632) (-) (-)	Delhi	07/2019 (07/2019)	03/2025 (12/2026)	24948.65 (24948.7)	21041.39	82.2
254	Surat Metro Rail Project (Gujarat Metro Rail Corporation Limited [GMRL]) (702630) (-) (-)	Gujarat	03/2019 (03/2019)	03/2024 (03/2027)	12020.32 (12020.3)	9166.71	81.1
255	Metro connectivity from Millennium City Centre to Cyber City with Spur to Dwarka Expressway, Gurugram. (Gurugram Metro Rail Limited [GMRL]) (619022) (-) (-)	Haryana	07/2023 (08/2024)	07/2027 (-)	5452.72 (5452.72)	159.67	4.3
256	Bangalore Metro Rail Project - PHASE-3 (Bengaluru Metro Rail) (612878) (-) (-)	Karnataka	NA (06/2026)	05/2031 (-)	15611 (15611)	0	0
257	Construction of Bangalore Metro Rail Project Phase 2. (Bengaluru Metro Rail) (702635) (-) (-)	Karnataka	02/2014 (02/2016)	03/2021 (09/2026)	26405.14 (30695.1)	29812.97	95.6
258	Construction Bangalore Metro Rail Project Phase-2A & 2B (Bengaluru Metro Rail) (702665) (-) (-)	Karnataka	06/2021 (01/2019)	06/2026 (06/2026)	14788.1 (14788.1)	10376.43	66
259	Kochi Metro Rail Phase 2 Development Project (CSPCC Projects) (702664) (-) (-)	Kerala	11/2022 (11/2022)	11/2026 (11/2026)	1957.05 (1957.05)	752.34	38
260	Bhopal Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702625) (-) (-)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (06/2028)	6941.4 (6941.4)	4362.43	62.5
261	Indore Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702626) (-) (-)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (12/2028)	7500.8 (7500.8)	5044	65.19
262	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617225) (-) (-)	Maharashtra	10/2023 (10/2023)	01/2027 (-)	910.18 (960.18)	309.65	47.17

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
263	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617226) (-) (-)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	2954.53 (2954.53)	88.81	6.2
264	Thane Integral Ring Metro Rail Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617327) (-) (-)	Maharashtra	09/2024 (09/2024)	09/2029 (-)	12200.1 (12200.1)	95.64	9.49
265	Pune Metro Rail Project Phase-2 Corridor 2A Vanaz to Chandani Chowk and Corridor 2B Ramwadi to Wagholi/Vitthalwadi (Maharashtra Metro Rail Corporation Limited [MMRCL]) (618971) (-) (-)	Maharashtra	07/2025 (07/2025)	07/2029 (-)	3626.24 (3626.24)	4.48	1.88
266	Pune Metro Rail Project Phase-2 Line-4 Kharadi to Khadakwasla with Spur Line 4A Nal Stop - Warje - Manikbaug (Maharashtra Metro Rail Corporation Limited [MMRCL]) (618985) (-) (-)	Maharashtra	12/2025 (12/2025)	12/2030 (-)	9857.85 (9857.85)	7.41	1.3
267	New Suburba Station Development Project (ministry of housing and urban affairs) (701745) (-) (-)	Maharashtra	04/2018 (03/2019)	07/2022 (-)	262.76 (262.76)	17.62	6
268	Kalyan Station Precinct Imporvement Project (ministry of housing and urban affairs) (701991) (-) (-)	Maharashtra	04/2018 (07/2020)	07/2023 (06/2026)	600 (723.7)	523.76	84
269	Mumbai Metro Line 3 (Mumbai Metro Rail Corporation Limited [MMRC]) (702637) (-) (-)	Maharashtra	07/2013 (06/2016)	03/2023 (08/2025)	23136 (37276)	33648.26	97.86
270	Nagpur Metro Rail Phase II Development Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (702658) (-) (-)	Maharashtra	12/2022 (12/2022)	12/2027 (-)	6708 (6708)	2026.56	40.86
271	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] (Delhi Metro Rail Corporation Limited [DMRC]) (617206) (-) (-)	Multi-States (Delhi, Haryana)	01/2025 (01/2025)	01/2029 (-)	6230.99 (6230.99)	570.13	3.02
272	Rajasthan Metro Rail Project Phase 1C from Badi Chaupar to Transport Nagar via Galta Gate (Jaipur Metro Rail Corporation) (612066) (-) (-)	Rajasthan	10/2025 (09/2023)	04/2027 (-)	980.08 (980.08)	103.03	0
273	Jaipur Metro Phase 1D Project from Mansarovar to Ajmer Road Chauraha (Jaipur Metro Rail Corporation) (612068) (-) (-)	Rajasthan	05/2026 (12/2023)	03/2026 (-)	204.81 (204.81)	23.34	12.48
274	Chennai Metro Rail Phase-II Development Project (Chennai Metro Rail Limited [CMRL]) (702668) (-) (-)	Tamil Nadu	10/2024 (11/2020)	08/2029 (-)	63246 (63246)	33774	53.36
275	Extension of Aqua Line Metro Corridor from Noida Sector-142 station to Botanical Garden, Noida of Noida Metro Rail Corporation (Noida Metro Rail Corporation Ltd. [NMRCL]) (616221) (-) (-)	Uttar Pradesh	03/2026 (03/2026)	03/2030 (-)	2254.35 (2254.35)	0	0
276	LUCKNOW METRO RAIL PROJECT PHASE-1B EAST WEST CORRIDOR (Uttar Pradesh metro rail corporation [UPMRC]) (619052) (-) (-)	Uttar Pradesh	09/2025 (05/2026)	04/2031 (-)	5801.05 (5801.05)	0	1.5
277	Kanpur Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702628) (-) (-)	Uttar Pradesh	05/2019 (11/2019)	05/2024 (03/2027)	11076.48 (11076.5)	9131.15	82.5
278	Agra Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702629) (-) (-)	Uttar Pradesh	05/2019 (12/2020)	05/2024 (06/2027)	8379.62 (8379.62)	6081.28	72.5
	Total (29)				307834.71	172729.8	
Waste & Water							
279	ESR - 8 nos., distribution system - 216 Km, new house service connections - 38760 nos. upgrading of feeder mains, pumping station etc. - Phase II (Ministry of Housing & Urban Affairs) (702674) (-) (-)	Andhra Pradesh	02/2017 (07/2018)	03/2023 (08/2026)	172.22 (172.22)	88.86	82
280	Muzaffarpur Storm Water Drainage Phase-I Project (Ministry of Housing & Urban Affairs) (702699) (-) (-)	Bihar	11/2016 (02/2019)	10/2023 (06/2026)	158.78 (158.78)	135.72	85
281	Sewerage Management Scheme Part-3 Implementation (Ministry of Housing & Urban Affairs) (702734) (-) (-)	Haryana	03/2017 (11/2017)	09/2023 (09/2026)	278.01 (278.01)	228.49	88
282	Dhanbad Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702741) (-) (-)	Jharkhand	02/2017 (12/2018)	03/2023 (06/2026)	216.55 (216.55)	129.16	76
283	SAAP-3 Water Supply Infrastructure SAAP-3 Project (Ministry of Housing & Urban Affairs) (702742) (-) (-)	Jharkhand	02/2017 (12/2018)	10/2023 (06/2026)	159.31 (159.31)	87.5	67

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
284	Augmentation and Strenghthning of Urban Water Supply Phase 1 - SAAP 3 (Ministry of Housing & Urban Affairs) (702746) (-) (-)	Jharkhand	02/2017 (12/2018)	03/2023 (06/2026)	278.28 (278.28)	186.5	81
285	Belgavi Improvement in Sewerage System Project (Ministry of Housing & Urban Affairs) (702760) (-) (-)	Karnataka	12/2015 (10/2016)	07/2023 (06/2026)	162.73 (162.73)	79.5	80
286	Indore Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702793) (-) (-)	Madhya Pradesh	12/2016 (11/2017)	03/2023 (06/2026)	287.17 (287.17)	252.5	99
287	Satna Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702808) (-) (-)	Madhya Pradesh	11/2015 (12/2016)	03/2024 (08/2026)	191.56 (215.89)	200.32	96
288	Singrauli Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702810) (-) (-)	Madhya Pradesh	05/2016 (11/2017)	03/2023 (06/2026)	402.01 (438.1)	371.17	90
289	Kalyan-Dombivali Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702833) (-) (-)	Maharashtra	07/2016 (09/2019)	10/2023 (08/2026)	194.2 (194.2)	136.56	75
290	Pune Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702851) (-) (-)	Maharashtra	03/2017 (07/2017)	03/2023 (08/2026)	235.95 (235.95)	220.77	96
291	Jalandhar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (703021) (-) (-)	Punjab	11/2016 (08/2020)	08/2023 (08/2026)	258.53 (266.64)	161.02	90
292	Patiala Water Supply Infrastructure Part-2 Project (Ministry of Housing & Urban Affairs) (703057) (-) (-)	Punjab	11/2016 (08/2020)	10/2023 (08/2026)	287 (287)	213.64	99
293	Jhansi Water Supply Infrastructure Phase-II Project (Ministry of Housing & Urban Affairs) (702949) (-) (-)	Uttar Pradesh	03/2017 (06/2019)	07/2023 (08/2026)	561.74 (561.74)	506.52	95
294	Lucknow Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702958) (-) (-)	Uttar Pradesh	NA (05/2019)	03/2023 (08/2026)	142.46 (173.21)	152.65	95
Total (16)					3986.5	3150.88	
Ministry of Mines							
Construction							
295	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata (Central Public Works Department [CPWD]) (617280) (-) (-)	West Bengal	04/2019 (02/2020)	08/2026 (-)	255.37 (255.37)	98.92	64
Total (1)					255.37	98.92	
Metals & Mining							
296	Expansion of Malanjhand Copper Project (Hindustan Copper Limited [HCL]) (400426) (-) (-)	Madhya Pradesh	09/2011 (04/2015)	04/2020 (03/2029)	1856.36 (3800)	1009.9	26
297	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonne Per Annum (National Aluminium Company Limited [NALCO]) (400141) (-) (-)	Odisha	04/2017 (04/2017)	12/2022 (06/2026)	4103 (5677.4)	4985.07	95.2
298	Pottangi Bauxite Mines Project (National Aluminium Company Limited [NALCO]) (400299) (-) (-)	Odisha	05/2018 (05/2018)	03/2025 (11/2026)	1381 (1960.77)	770.23	52.2
299	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (National Aluminium Company Limited [NALCO]) (709831) (-) (-)	Odisha	11/2017 (11/2019)	05/2025 (06/2026)	483 (483)	451.7	93.1
300	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (National Aluminium Company Limited [NALCO]) (709832) (-) (-)	Tamil Nadu	09/2017 (12/2017)	03/2025 (03/2026)	166 (166)	135	66.73
Total (5)					7989.36	7351.9	
Department of Higher Education							
Education							
301	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008) (-) (-)	Andhra Pradesh	09/2019 (12/2023)	06/2027 (-)	305 (305)	67.73	44.5
302	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898) (-) (-)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (08/2024)	592.61 (592.61)	551.3	80

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
303	Tezpur University Projects (Tezpur University) (606112) (-) (-)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 (153.71)	137.84	97.97
304	Additional Campus of NITPatna (NIT Patna) (606013) (-) (-)	Bihar	07/2022 (08/2022)	07/2024 (01/2026)	499.21 (499.21)	449.96	98.6
305	Phase B Construction of Permanent Campus of IIT Bhilai (Indian Institute of Technology, Bhilai) (617877) (-) (-)	Chhattisgarh	05/2025 (01/2026)	10/2028 (-)	1188.97 (1188.97)	0	0
306	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis (National Institute of Technology Delhi) (612851) (-) (-)	Delhi	09/2009 (11/2022)	09/2025 (01/2026)	333.49 (336.42)	327.26	99.9
307	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886) (-) (-)	Delhi	09/2024 (03/2025)	10/2026 (-)	373 (373)	30.13	13
308	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Central University of Gujarat) (612916) (-) (-)	Gujarat	12/2020 (02/2021)	03/2025 (03/2026)	490.63 (490.63)	339.4	86
309	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099) (-) (-)	Himachal Pradesh	09/2018 (08/2020)	10/2023 (06/2026)	392.51 (454.78)	338.83	98.3
310	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128) (-) (-)	Himachal Pradesh	03/2023 (03/2024)	03/2026 (07/2026)	166.66 (166.66)	122.26	84
311	Construction of Permanent Campus of Central University of Himachal Pradesh at Dehra, District - Kangra, [H.P.] on Engineering. Procurement and Construction [EPC Mode 1] Basis. (Central University, Himachal Pradesh) (612894) (-) (-)	Himachal Pradesh	03/2021 (08/2022)	11/2024 (03/2026)	251.98 (300.45)	223.6	86
312	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098) (-) (-)	Jammu and Kashmir	03/2019 (10/2020)	06/2023 (11/2025)	424.93 (500.91)	484.52	96
313	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431) (-) (-)	Kerala	07/2017 (03/2020)	06/2022 (06/2026)	1006.45 (1217.4)	686.2	86.5
314	Phase B of Construction of Permanent Campus of IIT Palakkad (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (617878) (-) (-)	Kerala	05/2025 (01/2026)	10/2028 (-)	1527 (1527)	9.8	0
315	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] (Indian Institute of Technology, Indore) (611957) (-) (-)	Madhya Pradesh	12/2023 (04/2024)	02/2027 (-)	496.28 (496.28)	97.35	65
316	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885) (-) (-)	Meghalaya	09/2009 (09/2014)	03/2022 (10/2026)	494.52 (429.7)	368.98	96
317	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876) (-) (-)	Mizoram	09/2009 (06/2014)	12/2029 (03/2022)	474.23 (474.23)	167.55	4
318	Establishment of NIT Nagaland (NIT Nagaland) (613013) (-) (-)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 (275.63)	263.25	98
319	IISER BERHAMPUR (Indian Institutes of Science Education and Research, Behrampur) (610315) (-) (-)	Odisha	10/2018 (09/2019)	03/2021 (06/2026)	1229.32 (843.09)	874.09	98.5
320	Construction of IIT Bhubaneswar -Phase III (Indian Institute of Technology, Bhubaneshwar) (611961) (-) (-)	Odisha	02/2024 (05/2024)	11/2026 (-)	454.27 (454.27)	101.36	9.2
321	1000 seater Boys hostel, 500 seater Girls hostel, 1.5 MLD Sewage Treatment Plant and Faculty Residence - 72 nos. Flats (NIT Rourkela) (619033) (-) (-)	Odisha	09/2023 (01/2024)	06/2026 (-)	198.97 (198.97)	51.73	47
322	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] (National Institute of Technology, Puducherry) (612877) (-) (-)	Puducherry	09/2009 (07/2013)	12/2024 (05/2026)	618.34 (544.34)	543.74	99.5

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
323	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I <i>(Indian intitue of Management, Amritsar)</i> (605292) (-) (-)	Punjab	10/2019 (07/2020)	06/2023 (11/2026)	348.31 (348.31)	293.24	91.7
324	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment <i>(Central University of Punjab)</i> (617221) (-) (-)	Punjab	08/2024 (04/2025)	10/2027 (-)	210.99 (210.99)	81.06	48
325	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim <i>(Sikkim University)</i> (609736) (-) (-)	Sikkim	08/2020 (01/2022)	01/2025 (03/2026)	314.06 (351.74)	292	96
326	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District <i>(NIT Sikkim)</i> (612883) (-) (-)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 (610.76)	283.56	37.6
327	Construction of Precast housing and hostels at IIT Hyderabad <i>(Indian Institute of Technology, Hyderabad)</i> (609996) (-) (-)	Telangana	09/2022 (11/2022)	10/2024 (01/2026)	262 (262)	216.1	89.11
328	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] <i>(Banaras Hindu University)</i> (606479) (-) (-)	Uttar Pradesh	06/2020 (06/2020)	09/2022 (03/2026)	246 (246)	209.68	99
329	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal <i>(National Institute of Technology Uttarakhand)</i> (611963) (-) (-)	Uttarakhand	06/2020 (04/2024)	09/2027 (-)	650.85 (650.85)	391.87	62
330	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur <i>(Indian Institute of Technology, Kharagpur)</i> (609019) (-) (-)	West Bengal	06/2018 (04/2019)	03/2023 (03/2026)	500 (442)	418.86	97
Total (30)					15165.68	8423.25	
Department of Sports							
Education							
331	National Sports University [NSU], Imphal [Manipur] <i>(Department of Sports & Youth Affairs)</i> (400081) (-) (-)	Manipur	06/2022 (01/2022)	08/2024 (08/2026)	906.47 (611.74)	576.37	97.25
Total (1)					906.47	576.37	
Ministry of Petroleum & Natural Gas							
Energy Storage							
332	Construction of LPG Facilities at Kamardanga, Assam <i>(Hindustan Petroleum Corporation Limited)</i> (709754) (-) (-)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 (156.36)	109.34	79.8
333	Setting up of new rail fed POL facility at Kamardanga, Assam <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (709755) (-) (-)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 (384.04)	235.27	85.5
334	Capacity Augmentation of Kandla LPG Import Terminal [KLIT] from 0.6 MMTPA to 2.5 MMTPA <i>(Ministry of Petroleum & Natural Gas)</i> (617839) (-) (-)	Gujarat	05/2023 (05/2023)	07/2026 (07/2026)	356.86 (304.4)	163.79	67.5
335	Andheri Residential Towers, Mumbai <i>(Ministry of Petroleum & Natural Gas)</i> (604833) (-) (-)	Maharashtra	06/2017 (06/2017)	05/2025 (06/2026)	281.35 (389.67)	279.72	83
336	Setting up of 50 MW [plus/minus 5 percent] Wind Power Plant for Captive Consumption at MR <i>(MinistryofPetroleumNaturalGas)</i> (619313) (-) (-)	Maharashtra	05/2023 (05/2023)	04/2027 (04/2027)	483.14 (483.14)	360.28	65.9
337	LPG Bottling Plant at Mualkhang <i>(MinistryofPetroleumNaturalGas)</i> (617829) (-) (-)	Mizoram	07/2024 (07/2024)	10/2028 (03/2028)	225.71 (225.71)	30.84	33
338	Srikakulam Angul Gas Pipeline Project <i>(Ministry of Petroleum & Natural Gas)</i> (701343) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	09/2019 (09/2019)	07/2022 (06/2026)	2658.34 (2810)	2315.2	98.1
339	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip <i>(Ministry of Petroleum & Natural Gas)</i> (701349) (-) (-)	Multi-States (Assam, Bihar, Jharkhand, Odisha, West Bengal)	01/2019 (01/2019)	07/2024 (10/2026)	10228 (12407)	11036	92.9
340	New Mundra Panipat Crude Oil Pipeline <i>(Ministry of Petroleum & Natural Gas)</i> (400078) (-) (-)	Multi-States (Gujarat, Haryana, Rajasthan)	12/2021 (12/2021)	12/2024 (06/2026)	9028 (9028)	7482.71	94.1
341	Kandla Gorakhpur LPG Pipeline <i>(Ministry of Petroleum & Natural Gas)</i> (400012) (-) (-)	Multi-States (Gujarat, Madhya Pradesh, Uttar Pradesh)	12/2018 (12/2018)	12/2021 (06/2026)	10088 (10088)	8672.35	95.7

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
342	Multi Product Pipeline from Irugur to Devangonchi (Department of Water Resources, River Development & GR) (400301) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	11/2012 (11/2012)	02/2017 (09/2026)	678 (1732)	1155.32	84.3
343	Petrochemical evacuation marketing terminal at Barmer, Rajasthan (Hindustan Petroleum Corporation Limited [HPCL]) (709759) (-) (-)	Rajasthan	12/2023 (12/2023)	12/2026 (12/2026)	461.05 (461.05)	235.1	95.8
344	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] (Ministry of Petroleum & Natural Gas) (400043) (-) (-)	Tamil Nadu	01/2022 (01/2022)	05/2026 (03/2027)	829 (829)	382.96	79.6
345	Grass-root Terminal at Mirzapur, Uttar Pradesh (Ministry of Petroleum & Natural Gas) (604852) (-) (-)	Uttar Pradesh	09/2022 (09/2022)	11/2026 (11/2026)	980.45 (980.45)	295.55	76.5
Total (14)					36838.3	32754.43	
Oil & Gas							
346	KG-DWN-98/2 Cluster - II Development Project - NELP Block (Ministry of Petroleum Natural Gas) (400120) (-) (-)	Andhra Pradesh	03/2016 (03/2016)	06/2020 (06/2026)	34012 (34012)	33113.74	96.8
347	Provision of four bitumen tanks with capacity of 5 TMT each at Visakh Refinery (Ministry of Petroleum and Natural Gas) (619226) (-) (-)	Andhra Pradesh	09/2025 (09/2025)	03/2028 (03/2028)	258.34 (258.34)	7.12	15.7
348	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery (Hindustan Petroleum Corporation Limited) (709752) (-) (-)	Andhra Pradesh	09/2021 (09/2021)	06/2024 (02/2027)	160 (220)	152.82	93.5
349	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791) (-) (-)	Assam	07/2020 (07/2020)	07/2024 (03/2027)	12366 (25313)	20127.1	86.2
350	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863) (-) (-)	Assam	01/2018 (01/2018)	02/2020 (06/2026)	682.9 (726.93)	599.83	94.4
351	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858) (-) (-)	Assam	12/2020 (12/2020)	03/2024 (06/2026)	430.76 (430.76)	348.57	94.5
352	Coke Drum Structure Package (Ministry of Petroleum & Natural Gas) (617836) (-) (-)	Assam	12/2022 (12/2022)	12/2025 (09/2026)	635.28 (635.28)	543	70.8
353	Group Gathering Station, Lakwagaon (Ministry of Petroleum & Natural Gas) (619316) (-) (-)	Assam	10/2025 (10/2025)	10/2027 (10/2027)	495.59 (495.59)	20.04	7.8
354	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Ministry of Petroleum Natural Gas) (709776) (-) (-)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277 (323.09)	234.57	84.2
355	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Ministry of Petroleum Natural Gas) (709779) (-) (-)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768 (740)	225.2	59.4
356	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847) (-) (-)	Assam	01/2023 (01/2023)	04/2026 (04/2027)	481.03 (481.03)	238.7	54.8
357	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850) (-) (-)	Assam	09/2023 (09/2023)	05/2026 (09/2026)	198.7 (198.7)	103.59	62.5
358	DCU Revamp Project (NRL) (709864) (-) (-)	Assam	08/2021 (08/2021)	07/2024 (03/2027)	370 (370)	310.38	78.6
359	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865) (-) (-)	Assam	04/2023 (04/2023)	12/2024 (12/2026)	293.5 (293.5)	81.84	99
360	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar (Ministry of Petroleum Natural Gas) (617304) (-) (-)	Bihar	10/2023 (10/2023)	03/2027 (03/2027)	340.15 (340.15)	179.55	55
361	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA (Ministry of Petroleum & Natural Gas) (701324) (-) (-)	Bihar	01/2020 (01/2020)	04/2023 (08/2026)	14810 (16724)	74990.3	91.6
362	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery (Ministry of Petroleum Natural Gas) (709777) (-) (-)	Bihar	01/2022 (01/2022)	04/2025 (06/2027)	389.35 (340)	130.89	64.6

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
363	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts (Bharat Petroleum Corporation Limited [BPCL]) (709792) (-) (-)	Bihar	12/2022 (12/2022)	03/2030 (03/2030)	3638 (3638)	489.42	33.5
364	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts (Bharat Petroleum Corporation Limited [BPCL]) (709793) (-) (-)	Bihar	12/2022 (12/2022)	06/2030 (06/2030)	3919 (3919)	518.13	30.2
365	City Gas Distribution [CGD] Project in Kondagaon, Bastar, Sukma, Narayanpur, Bijapur & Dantewada GA (Ministry of Petroleum & Natural Gas) (617819) (-) (-)	Chhattisgarh	06/2022 (06/2022)	06/2030 (06/2030)	557.04 (557.04)	10.33	2.2
366	Redevelopment of Sobhasan Complex (Oil and Natural Gas Corporation Limited [ONGC]) (400087) (-) (-)	Gujarat	08/2021 (08/2021)	03/2027 (03/2027)	885.63 (1347.61)	1037.37	94.3
367	Redevelopment of Santhal Field [Onshore-Mehsana Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (400167) (-) (-)	Gujarat	02/2017 (02/2017)	03/2026 (12/2026)	1162.56 (1162.56)	1117.8	96.8
368	Redevelopment of Linch Field (MinistryofPetroleumNaturalGas) (400169) (-) (-)	Gujarat	04/2021 (04/2021)	03/2025 (07/2026)	631.03 (845.42)	617.84	92.1
369	Petrochemical and Lube Integration Project at Gujarat Refinery (Ministry of Petroleum & Natural Gas) (701329) (-) (-)	Gujarat	09/2020 (09/2020)	08/2024 (11/2026)	18936 (17825)	75182.67	89.2
370	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery (MinistryofPetroleumNaturalGas) (709778) (-) (-)	Gujarat	01/2022 (01/2022)	08/2025 (12/2026)	328.29 (344.36)	227.48	87
371	Commercial Polymer Flooding Project in Bechraji field (Oil and Natural Gas Corporation Limited [ONGC]) (709838) (-) (-)	Gujarat	01/2022 (01/2022)	11/2024 (05/2027)	621.4 (739.02)	251.74	48.2
372	Restoration of Gas Terminal, Phase-I [Part-A], Hazira (Oil and Natural Gas Corporation Limited [ONGC]) (709840) (-) (-)	Gujarat	05/2022 (05/2022)	02/2025 (07/2026)	249.43 (249.43)	218.03	97.5
373	Old Pipe Line Replacement [OPRP] Group-A (Oil and Natural Gas Corporation Limited [ONGC]) (709841) (-) (-)	Gujarat	07/2021 (07/2021)	07/2025 (07/2026)	173.03 (169.84)	167.98	94.5
374	Kalol Redevelopment Project, Ahmedabad Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709842) (-) (-)	Gujarat	08/2022 (08/2022)	03/2027 (03/2027)	1487.41 (1487.41)	945.45	65
375	Revamping of SV Stations, Gas Terminal & Kribhco Terminal (Oil and Natural Gas Corporation Limited [ONGC]) (709845) (-) (-)	Gujarat	11/2022 (11/2022)	08/2026 (08/2026)	837.34 (837.34)	451.61	70.1
376	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad (Ministry of Petroleum & Natural Gas) (604853) (-) (-)	Haryana	06/2019 (06/2019)	12/2022 (07/2027)	2281.94 (3200)	1921.56	65.3
377	Poly Butadiene Rubber plant at Panipat (Indian Oil Corporation Limited [IOCL]) (611917) (-) (-)	Haryana	03/2022 (03/2022)	03/2025 (12/2026)	1459 (2531.44)	1643.7	88.7
378	Change of service of existing Mundra-Panipat Pipeline [Panipat - Churwa section] from Crude oil to Product (IOCL) (619196) (-) (-)	Haryana	05/2025 (05/2025)	04/2027 (03/2027)	359 (359)	40.86	39.6
379	Capacity Expansion of Panipat Refinery from 15 to 25 MMTPA (Ministry of Petroleum & Natural Gas) (701289) (-) (-)	Haryana	02/2021 (02/2021)	09/2024 (12/2026)	34627 (36225)	27518.03	94
380	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. (MinistryofPetroleumNaturalGas) (709783) (-) (-)	Haryana	12/2020 (12/2020)	06/2023 (06/2026)	165.13 (247.69)	186.64	91.8
381	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts (MinistryofPetroleumNaturalGas) (709773) (-) (-)	Jammu and Kashmir	03/2022 (03/2022)	09/2034 (09/2034)	538 (538)	4.3	0.6
382	Development of Jharia CBM Block [Phase-1] (Oil and Natural Gas Corporation Limited [ONGC]) (610984) (-) (-)	Jharkhand	11/2019 (11/2019)	01/2024 (07/2026)	431 (431)	267.59	66.1
383	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] (MinistryofPetroleumNaturalGas) (709785) (-) (-)	Jharkhand	02/2023 (02/2023)	02/2026 (03/2027)	202.07 (202.07)	65.3	58.1

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
384	Power System Upgradation Project (Ministry of Petroleum Natural Gas) (612790) (-) (-)	Karnataka	10/2023 (10/2023)	11/2025 (09/2026)	385 (385)	268.2	88.7
385	Demo Bio-ATF Project (Ministry of Petroleum & Natural Gas) (616879) (-) (-)	Karnataka	03/2024 (03/2024)	01/2027 (01/2027)	364 (364)	85.56	51.1
386	Revamping/ Augmentation of facilities at existing port terminal at Mangalore (Ministry of Petroleum & Natural Gas) (709774) (-) (-)	Karnataka	01/2022 (01/2022)	12/2025 (06/2027)	463 (500.62)	321.59	85
387	Augmentation of CCKPL and IDPL Pipelines capacity along with setting up of Palakkad TOP (Ministry of Petroleum & Natural Gas) (617838) (-) (-)	Kerala	09/2024 (09/2024)	08/2028 (08/2028)	1130 (1130)	306.1	43.2
388	Setting up Polypropylene Unit at Kochi Refinery (Ministry of Petroleum Natural Gas) (709799) (-) (-)	Kerala	12/2023 (12/2023)	10/2027 (10/2027)	4460 (4850)	893.86	40.5
389	C2/C3 Vijaipur Pata Pipeline (Ministry of Petroleum & Natural Gas) (617830) (-) (-)	Madhya Pradesh	05/2024 (05/2024)	01/2027 (01/2027)	1792 (1792)	510.5	70.8
390	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery (Ministry of Petroleum Natural Gas) (709798) (-) (-)	Madhya Pradesh	05/2023 (05/2023)	05/2028 (05/2028)	43367 (43367)	5596	30.7
391	500 KTA PDHPP Project, Usar (Ministry of Petroleum & Natural Gas) (400168) (-) (-)	Maharashtra	04/2021 (04/2021)	04/2025 (06/2027)	8797 (11256)	8741.88	91.6
392	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery (Ministry of Petroleum and Natural Gas) (616933) (-) (-)	Maharashtra	12/2024 (12/2024)	03/2028 (03/2028)	4679 (4679)	288.53	12.3
393	Petro Resid Fluidized Catalytic Cracking [PRFCC] Unit and its associated facilities at Mumbai Refinery (Ministry of Petroleum & Natural Gas) (619223) (-) (-)	Maharashtra	05/2025 (05/2025)	09/2029 (09/2029)	13626 (13626)	81.87	6.1
394	Augmentation of DUPL-DPPL Pipeline (Ministry of Petroleum & Natural Gas) (619224) (-) (-)	Maharashtra	06/2025 (06/2025)	03/2028 (03/2028)	844 (844)	0.61	7.3
395	Installation of Compression facility at GAIL Usar (Ministry of Petroleum & Natural Gas) (619225) (-) (-)	Maharashtra	04/2025 (04/2025)	04/2027 (04/2027)	260.2 (260.2)	0	0
396	ONGC-BP Redevelopment Phase-1 Scheme of Mumbai High Field (Ministry of Petroleum & Natural Gas) (619328) (-) (-)	Maharashtra	11/2025 (11/2025)	03/2027 (03/2027)	3713.4 (3908)	1557.5	53.2
397	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts (Ministry of Petroleum Natural Gas) (709771) (-) (-)	Maharashtra	03/2022 (03/2022)	09/2031 (09/2031)	865 (865)	84.85	3.4
398	Construction of Additional Tankages and Allied Facilities at JNPT Terminal (Ministry of Petroleum Natural Gas) (709780) (-) (-)	Maharashtra	04/2022 (04/2022)	08/2026 (08/2026)	341.43 (436.14)	304.75	72.4
399	POL & LOBS Installations with Receipt Pipelines at Rasayani (Bharat Petroleum Corporation Limited [BPCL]) (709797) (-) (-)	Maharashtra	05/2023 (05/2023)	05/2026 (09/2026)	2585 (2585)	1416.51	85.4
400	Visakh Raipur Pipeline Project (Ministry of Petroleum and Natural Gas) (616254) (-) (-)	Multi-States (Andhra Pradesh, Chhattisgarh, Odisha)	09/2024 (09/2024)	09/2027 (09/2027)	2212 (2212)	549.21	37.1
401	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346) (-) (-)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura, West Bengal)	04/2020 (04/2020)	03/2024 (07/2026)	9265 (9265)	6900	88
402	Pipeline Rehabilitation Project, Phase-II (Ministry of Petroleum & Natural Gas) (617827) (-) (-)	Multi-States (Assam, Bihar, West Bengal)	12/2024 (12/2024)	12/2029 (12/2029)	680 (680)	12.65	29
403	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (Ministry of Petroleum & Natural Gas) (701330) (-) (-)	Multi-States (Gujarat, Haryana, Punjab, Rajasthan)	07/2011 (07/2011)	06/2024 (03/2027)	7392 (7392)	6362.31	90.2
404	Gurdaspur Jammu Pipeline (Gas Authority of India Limited [GAIL]) (612853) (-) (-)	Multi-States (Jammu and Kashmir, Punjab)	07/2023 (07/2023)	07/2026 (07/2026)	521.9 (521.9)	319.1	84.6

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
405	Kochi - Koottanad - Bangalore - Mangalore Pipeline Phase-II (Ministry of Petroleum & Natural Gas) (701228) (-) (-)	Multi-States (Karnataka, Kerala, Tamil Nadu)	06/2009 (06/2009)	12/2012 (09/2026)	2915 (5909)	4856.3	97
406	City Gas Distribution Maharashtra Natural Gas Limited (Ministry of Petroleum & Natural Gas) (701338) (-) (-)	Multi-States (Karnataka, Maharashtra)	01/2006 (01/2006)	06/2031 (06/2031)	5535 (5535)	4392.58	47
407	Dhamra Haldia Pipeline Project (Ministry of Petroleum & Natural Gas) (701344) (-) (-)	Multi-States (Odisha, West Bengal)	03/2020 (03/2020)	11/2022 (09/2026)	1030.65 (1125)	924.4	94.3
408	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (Bharat Petroleum Corporation Limited [BPCL]) (709794) (-) (-)	Multi-States (Punjab, Rajasthan)	12/2022 (12/2022)	06/2030 (06/2030)	3207 (3207)	422.99	31
409	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum & Natural Gas) (709786) (-) (-)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 (227.62)	27.63	41.6
410	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (Ministry of Petroleum & Natural Gas) (604859) (-) (-)	Odisha	07/2020 (07/2020)	01/2024 (08/2026)	13805 (11783)	70820.19	94.6
411	City Gas Distribution [CGD] Project in Gajapati, Kandhamal, Boudh, & Sonepur GA (Ministry of Petroleum & Natural Gas) (617818) (-) (-)	Odisha	02/2022 (02/2022)	12/2031 (12/2031)	514.91 (514.91)	24.9	5.9
412	CUF POL Depot at Sadashibpur [Meramundali], Odisha (Ministry of Petroleum & Natural Gas) (709800) (-) (-)	Odisha	04/2021 (04/2021)	03/2026 (06/2026)	393.54 (393.54)	232.3	83.5
413	Life Extension of 48 well platforms of Mumbai High & Heera Fields (Oil and Natural Gas Corporation Limited [ONGC]) (400119) (-) (-)	Offshore	12/2015 (12/2015)	04/2018 (10/2026)	3190.69 (3375.9)	3123.2	90
414	PRP-VIII [Group-A] (Ministry of Petroleum & Natural Gas) (616950) (-) (-)	Offshore	09/2024 (09/2024)	02/2026 (12/2026)	1486.4 (1486.4)	618.99	59.6
415	Pipeline Replacement Project- PRP-IX (Ministry of Petroleum & Natural Gas) (619314) (-) (-)	Offshore	08/2025 (08/2025)	05/2027 (05/2027)	6684 (6175)	864.28	21.2
416	Daman Upside Development Project (Oil and Natural Gas Corporation Limited [ONGC]) (709839) (-) (-)	Offshore	06/2022 (06/2022)	10/2025 (12/2026)	4144.41 (6406.9)	6284.81	99.9
417	MHN TCPP PGC BGC Project [MTPBP] (Ministry of Petroleum & Natural Gas) (709848) (-) (-)	Offshore	06/2022 (06/2022)	05/2026 (12/2026)	2329.45 (2354.23)	1929.54	95.5
418	PRP-VIII Group B [NH & BS Asset] (Ministry of Petroleum & Natural Gas) (709849) (-) (-)	Offshore	06/2024 (06/2024)	02/2026 (12/2026)	2379.84 (3165.53)	2923.49	98.7
419	Integrated Development of 4 Contract Areas under DSF-II (Ministry of Petroleum & Natural Gas) (709851) (-) (-)	Offshore	05/2023 (05/2023)	04/2027 (04/2027)	6183.79 (6183.79)	2023.95	43.9
420	2G Ethanol Biorefinery at Bathinda (Ministry of Petroleum & Natural Gas) (400171) (-) (-)	Punjab	05/2020 (05/2020)	02/2023 (12/2026)	1421.46 (1421.46)	1293.34	94
421	City Gas Distribution Project at Pathankot District (Ministry of Petroleum & Natural Gas) (709770) (-) (-)	Punjab	03/2022 (03/2022)	09/2033 (09/2033)	151 (151)	8.96	2
422	CBR 9 MMTPA Project (Chennai Petroleum Corporation Limited [CPCL]) (604795) (-) (-)	Tamil Nadu	09/2021 (09/2021)	06/2025 (10/2028)	31580 (36354)	1590.07	10.2
423	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore (Chennai Petroleum Corporation Limited [CPCL]) (709750) (-) (-)	Tamil Nadu	01/2024 (01/2024)	09/2025 (12/2026)	205 (205)	114.87	74.8
424	City Gas Distribution Projects at the Nilgiris and Erode districts (Bharat Petroleum Corporation Limited [BPCL]) (709796) (-) (-)	Tamil Nadu	12/2022 (12/2022)	03/2030 (03/2030)	3685 (3685)	297.76	25.5
425	ATF Pipeline from BPCLs Malkapur POL Installation to Hyderabad International airport (Ministry of Petroleum & Natural Gas) (617822) (-) (-)	Telangana	03/2025 (03/2025)	09/2027 (09/2027)	215 (215)	45.99	26.1
426	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837) (-) (-)	Tripura	03/2022 (03/2022)	05/2024 (08/2026)	209.33 (131.51)	79.98	70.5

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
427	Kanpur LPG Bottling Plant (Ministry of Petroleum Natural Gas) (619191) (-) (-)	Uttar Pradesh	09/2025 (09/2025)	09/2027 (09/2027)	202 (202)	130.8	60
428	Bulk Loading Hub- Kanpur (Ministry of Petroleum Natural Gas) (619312) (-) (-)	Uttar Pradesh	09/2025 (09/2025)	09/2027 (09/2027)	186 (186)	95.21	60
429	Revamping / Augmentation of Facilities at Mathura Bitumen Plant (Ministry of Petroleum Natural Gas) (709781) (-) (-)	Uttar Pradesh	04/2022 (04/2022)	06/2027 (12/2026)	260.12 (260.12)	24.1	55.7
430	City Gas Distribution Projects at Lakhimpur Kheri , Sitapur, Bahraich, Shrivasti, Balrampur, Siddharth Nagar & Maharajganj districts (Bharat Petroleum Corporation Limited [BPCL]) (709795) (-) (-)	Uttar Pradesh	12/2022 (12/2022)	06/2030 (06/2030)	16654 (16654)	738.62	19
431	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] (Ministry of Petroleum & Natural Gas) (617302) (-) (-)	West Bengal	03/2017 (03/2017)	12/2020 (09/2026)	1740 (2493.15)	2375.1	95.2
432	Siliguri-Jhapa Pipeline Project (Indian Oil Corporation Limited [IOCL]) (617828) (-) (-)	West Bengal	09/2024 (09/2024)	03/2029 (03/2029)	267 (267)	2.41	14.3
433	Siliguri Marketing Terminal [SMT] Capacity Augmentation Project (Ministry of Petroleum & Natural Gas) (617837) (-) (-)	West Bengal	11/2021 (11/2021)	12/2025 (10/2026)	484 (484)	315.4	88.3
434	Haldia Panagarh Pipeline Project (Hindustan Petroleum Corporation Limited) (709753) (-) (-)	West Bengal	11/2022 (11/2022)	11/2025 (08/2026)	1010 (1107)	865.19	97.2
435	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts (Ministry of Petroleum Natural Gas) (709772) (-) (-)	West Bengal	03/2022 (03/2022)	06/2031 (06/2031)	609 (609)	63.62	2.9
436	City Gas Distribution Projects at Alipurduar and Cooch Behar (Bharat Petroleum Corporation Limited [BPCL]) (709791) (-) (-)	West Bengal	12/2022 (12/2022)	03/2030 (03/2030)	1017 (1017)	232.5	43.7
	Total (91)				362124.04	386636.12	
	Ministry of Health & Family Welfare						
	Healthcare						
437	AIIMS Darbhanga (PMSSY AND Institute of NATIONAL Importance) (701172) (-) (-)	Bihar	09/2020 (09/2020)	09/2024 (-)	1264 (1264)	27.81	0
438	Establishment of new GMC Saran [Chhapara] (Medical Education, Ministry of Health and Family Welfare) (706965) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	189 (189)	113.4	0
439	Establishment of new GMC Samastipur (Medical Education, Ministry of Health and Family Welfare) (706966) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	189 (189)	113.4	0
440	Establishment of new GMC Sitamarhi (Medical Education, Ministry of Health and Family Welfare) (707016) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	250 (250)	150	0
441	Establishment of new GMC Jhanjharpur (Medical Education, Ministry of Health and Family Welfare) (707017) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	250 (250)	150	0
442	Establishment of new GMC Siwan (Medical Education, Ministry of Health and Family Welfare) (707018) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	250 (250)	150	0
443	Establishment of new GMC Buxar (Medical Education, Ministry of Health and Family Welfare) (707019) (-) (-)	Bihar	NA (01/1900)	01/1900 (-)	250 (250)	150	0
444	Establishment of new GMC Jamui (Medical Education, Ministry of Health and Family Welfare) (707020) (-) (-)	Bihar	03/2019 (10/2022)	10/2025 (-)	250 (500)	103.21	50
445	Establishment of new GMC Korba (Medical Education, Ministry of Health and Family Welfare) (707044) (-) (-)	Chhattisgarh	02/2023 (10/2023)	12/2026 (-)	325 (322.85)	178.49	54
446	Establishment of new GMC Mahasamund (Medical Education, Ministry of Health and Family Welfare) (707045) (-) (-)	Chhattisgarh	10/2023 (10/2023)	05/2026 (-)	325 (325)	322.5	82
447	Establishment of new GMC Kanker (Medical Education, Ministry of Health and Family Welfare) (707046) (-) (-)	Chhattisgarh	02/2020 (09/2024)	03/2027 (-)	325 (325)	36	59

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
448	Setting up IT Infrastructure including Network Security and Hosting at AIIMS, New Delhi (PMSSY AND Institute of NATIONAL Importance) (617882) (-) (-)	Delhi	09/2025 (09/2025)	09/2026 (-)	358.19 (358.19)	53.73	35
449	Redevelopment of Residential colonies at Ayur Vigyan Nagar and West Ansari Nagar campuses of AIIMS, New Delhi (PMSSY AND Institute of NATIONAL Importance) (617883) (-) (-)	Delhi	10/2016 (06/2022)	06/2027 (-)	4441 (4441)	44.44	57
450	AIIMS Rajkot (PMSSY AND Institute of NATIONAL Importance) (701170) (-) (-)	Gujarat	01/2019 (01/2019)	03/2026 (12/2026)	1195 (1195)	793.03	93.85
451	Establishment of new GMC Panchmahal (Medical Education, Ministry of Health and Family Welfare) (707049) (-) (-)	Gujarat	09/2022 (09/2022)	03/2026 (-)	325 (663.5)	457.34	87.5
452	Establishment of new GMC Porbandar (Medical Education, Ministry of Health and Family Welfare) (707050) (-) (-)	Gujarat	04/2022 (10/2022)	09/2024 (-)	325 (618.98)	936.64	81
453	AIIMS Majra Rewari Haryana (PMSSY AND Institute of NATIONAL Importance) (701173) (-) (-)	Haryana	02/2019 (02/2019)	12/2026 (12/2026)	1299 (1646.43)	717.42	64.85
454	AIIMS Kashmir at Awantipora Jammu & Kashmir (PMSSY AND Institute of NATIONAL Importance) (701167) (-) (-)	Jammu and Kashmir	01/2019 (03/2019)	12/2025 (12/2026)	1828 (2160.84)	1594.22	78
455	Establishment of new GMC Udhampur (Medical Education, Ministry of Health and Family Welfare) (707051) (-) (-)	Jammu and Kashmir	09/2019 (01/2022)	03/2027 (-)	325 (325)	222	75
456	Establishment of new GMC Handwara [Distt. Kupwara] (Medical Education, Ministry of Health and Family Welfare) (707052) (-) (-)	Jammu and Kashmir	NA (01/1900)	01/1900 (-)	325 (325)	173	0
457	Establishment of new GMC Koderma (Medical Education, Ministry of Health and Family Welfare) (707021) (-) (-)	Jharkhand	09/2023 (02/2024)	08/2026 (-)	250 (504.8)	271	40
458	Establishment of new GMC Chaibasa [Singbhum] (Medical Education, Ministry of Health and Family Welfare) (707022) (-) (-)	Jharkhand	06/2018 (03/2023)	09/2025 (-)	250 (454.1)	65	57
459	Establishment of new GMC Leh (Medical Education, Ministry of Health and Family Welfare) (707057) (-) (-)	Ladakh	NA (01/1900)	01/1900 (-)	325 (325)	127	0
460	Establishment of new GMC Rajgarh (Medical Education, Ministry of Health and Family Welfare) (707058) (-) (-)	Madhya Pradesh	12/2021 (11/2022)	04/2024 (-)	325 (325)	179	84
461	Establishment of new GMC Mandla (Medical Education, Ministry of Health and Family Welfare) (707059) (-) (-)	Madhya Pradesh	08/2023 (10/2023)	04/2026 (-)	325 (325)	83.41	43
462	Establishment of new GMC Gondia (Medical Education, Ministry of Health and Family Welfare) (706988) (-) (-)	Maharashtra	NA (01/1900)	01/1900 (-)	189 (189)	113.4	0
463	Establishment of new GMC West Garo Hills [Tura] (Medical Education, Ministry of Health and Family Welfare) (706989) (-) (-)	Meghalaya	NA (01/1900)	01/1900 (-)	189 (189)	170.1	0
464	Establishment of new GMC Mon (Medical Education, Ministry of Health and Family Welfare) (707067) (-) (-)	Nagaland	NA (01/1900)	01/1900 (-)	325 (325)	155	0
465	Establishment of new GMC Kapurthala (Medical Education, Ministry of Health and Family Welfare) (707069) (-) (-)	Punjab	11/2019 (07/2027)	12/2028 (-)	325 (550)	0	0
466	Establishment of new GMC Hoshiarpur (Medical Education, Ministry of Health and Family Welfare) (707070) (-) (-)	Punjab	01/2020 (03/2026)	12/2028 (-)	325 (374.75)	2	1
467	Establishment of new GMC Gangtok (Medical Education, Ministry of Health and Family Welfare) (707039) (-) (-)	Sikkim	10/2018 (12/2018)	12/2026 (-)	250 (635.21)	667.21	92
468	ALL India Institute of Medical Sciences-AIIMS Madurai (PMSSY AND Institute of NATIONAL Importance) (701168) (-) (-)	Tamil Nadu	12/2018 (12/2018)	08/2022 (10/2026)	1264 (2021.51)	522.72	52
469	AIIMS Bibinagar (PMSSY AND Institute of NATIONAL Importance) (701171) (-) (-)	Telangana	12/2018 (07/2022)	06/2026 (06/2026)	1028 (1365.95)	989.98	87.32

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
470	Establishment of new GMC Rudrapur (Medical Education, Ministry of Health and Family Welfare) (707086) (-) (-)	Uttarakhand	10/2022 (02/2024)	12/2026 (-)	325 (325)	274	60
471	Establishment of new GMC Pithoragarh (Medical Education, Ministry of Health and Family Welfare) (707087) (-) (-)	Uttarakhand	08/2021 (04/2023)	12/2026 (-)	325 (768.89)	327.08	84
	Total (35)				20308.19	10433.53	
	Ministry of Labour and Employment						
	Healthcare						
472	Construction of 350 beds + 50 Super Specialty beds ESIC Hospital Sheelanagar, Visakhapatnam, Andhra Pradesh (Employee's State Insurance Company [ESIC]) (612167) (-) (-)	Andhra Pradesh	02/2021 (04/2023)	10/2025 (06/2026)	384.27 (384.27)	253.37	94
473	350 Bedded [Upgradable to 500 beds] ESI Hospital at Sanand (Employee's State Insurance Company [ESIC]) (612186) (-) (-)	Gujarat	06/2022 (04/2023)	03/2026 (05/2027)	558.12 (558.12)	55.81	21.5
474	Demolition, Construction and upgradation of ESI Hospital, Kalol, Gujarat from 50 beds to 150 beds. (Employee's State Insurance Company [ESIC]) (612211) (-) (-)	Gujarat	08/2022 (10/2023)	10/2025 (11/2026)	205.87 (205.87)	51.74	50
475	Construction of 200 bed ESI Hospital at Bommasandra, Karnataka (Employee's State Insurance Company [ESIC]) (612745) (-) (-)	Karnataka	02/2015 (10/2024)	01/2027 (05/2027)	278 (278)	80.52	34
476	Construction of 100 bed ESI Hospital and Staff Quarters [32 Nos.] at Harohalli, Karnataka (Employee's State Insurance Company [ESIC]) (612748) (-) (-)	Karnataka	07/2019 (03/2025)	02/2027 (-)	150.92 (150.92)	31.05	25.9
477	Construction of 200 Bedded ESIC Hospital at Butibori, Nagpur, Maharashtra. (Employee's State Insurance Company [ESIC]) (612213) (-) (-)	Maharashtra	10/2013 (08/2022)	08/2025 (09/2026)	194.93 (196.7)	114.39	67
478	Upgradation & Extension of ESIC Hospital and Construction of PG Hostel / Staff Housing for ESIC Hospital at Andheri, Mumbai (Employee's State Insurance Company [ESIC]) (616691) (-) (-)	Maharashtra	12/2008 (06/2009)	08/2025 (09/2026)	260.13 (260.13)	216.46	89
479	Construction of 100 Bedded ESI Hospital at Duburi, Odisha. (Employee's State Insurance Company [ESIC]) (612513) (-) (-)	Odisha	12/2010 (02/2025)	06/2027 (-)	164.6 (164.6)	16.44	7.2
480	CONSTRUCTION OF 300 BEDDED HOSPITAL AT HARIDWAR (Employee's State Insurance Company [ESIC]) (612259) (-) (-)	Uttarakhand	02/2021 (12/2021)	10/2024 (07/2026)	102.4 (297.63)	340.3	89
	Total (9)				2299.24	1160.08	
	Ministry of Ports, Shipping and Waterways						
	Inland Waterways						
481	Jal Marg Vikas Project (Inland Waterways Authority of India [IWAI]) (701565) (-) (-)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	01/2018 (02/2018)	12/2023 (12/2025)	5369.18 (5061.15)	4117.61	83.72
	Total (1)				5369.18	4117.61	
	Shipping						
482	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust) (609424) (-) (-)	Gujarat	10/2022 (03/2024)	03/2027 (09/2027)	4243.64 (4243.64)	2481	60
483	Replacement and revamping of pipeline projects in oil jetty area, Kandla (Deendayal Port Trust [DPT]) (701570) (-) (-)	Gujarat	09/2021 (09/2021)	09/2023 (03/2025)	171 (211.61)	149.5	92
484	Mechanization of Berth No.14 for handling Containers and other cargo on DBFOT basis - Phase II (New Mangalore Port Authority) (617804) (-) (-)	Karnataka	12/2023 (06/2024)	03/2027 (-)	153.23 (153.23)	97.45	95
485	Rewas Port Project (Reliance Industries Ltd) (400382) (-) (-)	Maharashtra	12/2019 (01/2020)	03/2023 (-)	6000 (6000)	5999.89	88
486	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574) (-) (-)	Odisha	05/2022 (01/2023)	12/2027 (10/2028)	3004.63 (3004.63)	2244.12	74
487	Integrated development of Outer Container Terminal and berth No. 1 though 5 NSD at KDS, SMPK on DBFOT basis through PPP mode (Syama Prasad Mookerjee Port Kolkata) (619229) (-) (-)	West Bengal	03/2025 (02/2027)	08/2028 (-)	832.25 (832.25)	0	0
	Total (6)				14404.75	10971.96	

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Tourism, Hospitality & Wellness							
488	National Maritime Heritage Complex [NMHC] Phase-I <i>(Indian Port Rail & Ropeway Corporation Ltd. [IPRCL])</i> (707215) (-) (-)	Gujarat	02/2019 (01/2022)	03/2024 (03/2026)	573 (1238.05)	636.91	78.92
	Total (1)				573	636.91	
Department for Promotion of Industry & Internal Trade							
Logistics Infrastructure							
489	Integrated Multi Modal Logistics Hub at Nangal Chaudhary in Haryana - Other Trunk Infrastructure Development Phase 1 <i>(National Highways & Infrastructure Development Corporation Ltd. [NHIDCL])</i> (707410) (-) (-)	Haryana	05/2018 (12/2021)	12/2023 (05/2028)	763 (763)	430	60
	Total (1)				763	430	
Real Estate							
490	Orvakal Industrial Area <i>(NICDC)</i> (617727) (-) (-)	Andhra Pradesh	08/2024 (10/2025)	10/2028 (-)	2786 (2786)	278.6	12.81
491	Kopparthy Industrial Area <i>(NICDC)</i> (617729) (-) (-)	Andhra Pradesh	08/2024 (10/2025)	10/2028 (-)	2136 (2136)	39.75	5.23
492	Krishnapatnam Node - Phase 1 - Roads and Services Development <i>(National Industrial Corridor Development Corporation)</i> (701658) (-) (-)	Andhra Pradesh	12/2020 (02/2024)	02/2027 (-)	2139.44 (2139.44)	981.35	45.43
493	Tumakuru Node - Phase 1 - Roads and Services Development <i>(National Highways & Infrastructure Development Corporation Ltd. [NHIDCL])</i> (701657) (-) (-)	Karnataka	12/2020 (02/2023)	09/2026 (09/2027)	1701.81 (1701.81)	324.12	25.67
494	Development of Palakkad Node under extension of CBIC to Kochi <i>(National Industrial Corridor Development Corporation)</i> (701668) (-) (-)	Kerala	08/2024 (10/2025)	04/2029 (-)	3805 (3805)	0	5.25
495	Development of Jodhpur Pali Marwar Industrial Area JPMIA in Rajasthan <i>(National Industrial Corridor Development Corporation)</i> (603210) (-) (-)	Rajasthan	08/2024 (01/2026)	07/2028 (-)	921.66 (921.66)	0	4.67
496	Development of Zaheerabad Node under Hyderabad Nagpur Industrial Corridor <i>(National Industrial Corridor Development Corporation)</i> (601812) (-) (-)	Telangana	08/2024 (02/2026)	02/2029 (-)	2360 (2360)	42.89	3.58
497	IMC at Prayagraj <i>(National Industrial Corridor Development Corporation)</i> (707419) (-) (-)	Uttar Pradesh	08/2024 (04/2026)	06/2027 (-)	658 (658)	75.63	22.54
	Total (8)				16507.91	1742.34	
Ministry of Steel							
Metals & Mining							
498	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul <i>(National Mineral Development Corporation Limited [NMDC])</i> (615202) (-) (-)	Chhattisgarh	08/2021 (07/2022)	12/2028 (03/2028)	1700 (1756.2)	263.01	18.3
	Total (1)				1700	263.01	
Steel							
499	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617243) (-) (-)	Chhattisgarh	07/2024 (08/2024)	07/2026 (-)	198.62 (198.62)	129.24	82.13
500	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617255) (-) (-)	Chhattisgarh	10/2023 (12/2023)	06/2026 (09/2026)	471.83 (471.83)	257.18	70.5
501	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617256) (-) (-)	Chhattisgarh	11/2023 (01/2024)	10/2025 (09/2026)	884.1 (884.1)	618.87	93.74
502	NMDC Slurry Pipeline Project Phase-1 <i>(National Mineral Development Corporation Limited [NMDC])</i> (706811) (-) (-)	Chhattisgarh	11/2015 (09/2020)	06/2023 (05/2026)	2907 (5427)	3639.5	95.2
503	SCREENING PLANT-III AT KIRANDUL <i>(National Mineral Development Corporation Limited [NMDC])</i> (709826) (-) (-)	Chhattisgarh	01/2009 (10/2021)	01/2026 (07/2027)	2718.84 (2718.84)	1748.76	83.15
504	New Sinter Plant at BSL, SAIL <i>(Steel Authority of India Limited [SAIL])</i> (400174) (-) (-)	Jharkhand	03/2015 (10/2015)	10/2027 (06/2027)	1034.01 (1752.3)	1014.95	63.76
505	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617249) (-) (-)	Jharkhand	01/2025 (02/2025)	01/2027 (-)	211.94 (211.94)	59.72	50.4

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
506	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617250) (-) (-)	Jharkhand	01/2025 (02/2025)	10/2026 (04/2027)	207.13 (207.13)	86.62	51.82
507	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617254) (-) (-)	Jharkhand	03/2024 (04/2024)	06/2026 (04/2027)	260.37 (260.37)	125.6	50.16
508	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617257) (-) (-)	Jharkhand	11/2023 (12/2023)	11/2026 (11/2027)	627.31 (627.31)	342.26	66.11
509	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. <i>(National Mineral Development Corporation Limited [NMDC])</i> (400121) (-) (-)	Karnataka	11/2014 (06/2024)	08/2026 (-)	1043.63 (1043.63)	628.29	65
510	Rebuilding of COB 4 at Durgapur Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (612781) (-) (-)	West Bengal	09/2023 (09/2023)	12/2026 (09/2027)	916.78 (916.78)	234.05	35.36
511	Installation of New Bar Mill at Durgapur Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617242) (-) (-)	West Bengal	07/2024 (08/2024)	06/2027 (-)	2115.44 (2115.44)	828.94	66.02
512	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617246) (-) (-)	West Bengal	09/2024 (10/2024)	06/2026 (10/2027)	758.09 (758.09)	286.36	41.68
513	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617248) (-) (-)	West Bengal	11/2024 (12/2024)	07/2026 (11/2026)	227.96 (227.96)	103.97	74.55
514	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617251) (-) (-)	West Bengal	07/2024 (12/2024)	05/2026 (08/2026)	196.4 (196.4)	65.5	32.21
515	Stamp Charge Battery No.12 Battery Proper at IISCO Steel Plant <i>(Steel Authority of India Limited [SAIL])</i> (617338) (-) (-)	West Bengal	01/2025 (02/2025)	07/2028 (-)	2518.39 (2518.39)	415.31	26.7
Total (17)					17297.84	10585.12	
Ministry of Railways							
Railways							
516	Nadikudi - Srikalahasti New Line <i>(South Central Railway [SCR] - II)</i> (400298) (-) (-)	Andhra Pradesh	03/2012 (12/2016)	05/2027 (03/2028)	2312 (5932)	3119.31	55.02
517	GUNTAKAL WEST-MALLAPPA GATE RAIL OVER RAIL - ROR TRACK <i>(South Central Railway [SCR] - II)</i> (611754) (-) (-)	Andhra Pradesh	07/2023 (07/2023)	07/2026 (-)	293.3 (293.3)	272.72	0.24
518	Kurnool - Setting up facilities for coach midlife rehabilitation workshop <i>(WPO/Patna)</i> (611927) (-) (-)	Andhra Pradesh	01/2014 (10/2017)	12/2023 (-)	560.72 (560.72)	276.66	65
519	Flyover between Pendurthi and Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB 73 of 2023 24 NR <i>(East Coast Railway [ECOR] - II)</i> (612827) (-) (-)	Andhra Pradesh	04/2023 (05/2024)	04/2027 (-)	183.65 (183.65)	17.25	16
520	3rd & 4th line between Vadlapudi -Gate Jn. cabin and Tie line between Gate Junction to Gangavaram port <i>(East Coast Railway [ECOR] - II)</i> (616697) (-) (-)	Andhra Pradesh	04/2023 (03/2024)	06/2026 (-)	154.28 (154.28)	69.59	80
521	Tiupati Katpadi 104.39 kms <i>(South Central Railway [SCR] - II)</i> (617210) (-) (-)	Andhra Pradesh	04/2025 (04/2025)	03/2029 (-)	1215.56 (1215.56)	62.2	0.06
522	3rd Line between Gudur Renigunta 83.17 Km <i>(South Central Railway [SCR] - II)</i> (617216) (-) (-)	Andhra Pradesh	10/2024 (10/2024)	03/2027 (-)	877.34 (877.34)	206.02	0.17
523	Nidadavolu-Duvvada 3rd & 4th Lines <i>(South Central Railway [SCR] - II)</i> (619326) (-) (-)	Andhra Pradesh	04/2026 (04/2026)	01/2032 (-)	9889.24 (9889.24)	0	0.01
524	Kurnool Coach Midlife Rehabilitation Project <i>(South Central Railway [SCR] - II)</i> (705253) (-) (-)	Andhra Pradesh	05/2016 (07/2014)	12/2020 (12/2026)	563 (560.72)	959.27	75.01
525	Kotapalli - Narasapur New Line <i>(South Central Railway [SCR] - II)</i> (705436) (-) (-)	Andhra Pradesh	03/2009 (09/2013)	03/2028 (03/2028)	2501 (2501)	1417.7	30.02
526	Guntur-Guntakal Doubling Project <i>(South Central Railway [SCR] - II)</i> (705633) (-) (-)	Andhra Pradesh	03/2017 (11/2017)	12/2025 (12/2026)	3733 (4295)	5552.65	94.05

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
527	Vijaywada-Gudur 3rd Line (RVNL - II) (705648) (-) (-)	Andhra Pradesh	08/2016 (04/2018)	11/2024 (03/2026)	6654 (6654)	6213.64	96
528	Furkating-New Tinsukia[194 Km] (Northeast Frontier Railway [NFR]) (618986) (-) (-)	Assam	09/2025 (09/2025)	06/2029 (-)	3633.58 (3633.58)	0	0
529	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572) (-) (-)	Assam	09/2016 (09/2016)	03/2026 (03/2026)	4060 (4961)	3831.06	95.16
530	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922) (-) (-)	Assam	09/2020 (09/2018)	09/2020 (06/2024)	890.36 (889.36)	391.73	89
531	Mariani-Jorhat, Tinsukia-Dangri and Makum - TirapTrack Electrification Project (GM/C/ NFR) (706940) (-) (-)	Assam	09/2018 (01/2022)	05/2024 (-)	183.99 (183.99)	0	0
532	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942) (-) (-)	Assam	09/2018 (01/2022)	05/2024 (-)	237.52 (237.52)	0	0
533	Sakri -Hasanpur [via Harnagar - Kusheshwar Asthan] New Railway line (East Central Railway [ECR] - I) (400254) (-) (-)	Bihar	12/2023 (08/1997)	12/2024 (03/2027)	735.2 (735.2)	589.37	84.2
534	Construction of Bulb line at Nabinagar Ankorah of East Central Railway (East Central Railway [ECR] - I) (617231) (-) (-)	Bihar	06/2024 (06/2024)	06/2028 (-)	611.74 (611.74)	0	0
535	Doubling of Narkatiaganj Raxaul Sitamarhi Darbhanga & Sitamarhi Muzaffarpur 256 KM (East Central Railway [ECR] - I) (617239) (-) (-)	Bihar	11/2024 (11/2025)	11/2029 (03/2030)	4079.95 (4079.95)	9.93	0
536	Khagaria-Kusheshwar Asthan [42Km] new line project (East Central Railway [ECR] - I) (705364) (-) (-)	Bihar	04/2019 (12/1998)	12/2024 (03/2027)	614 (1384.16)	491.56	55.7
537	Hajipur-Sagauli New line (East Central Railway [ECR] - I) (705366) (-) (-)	Bihar	10/2007 (10/2004)	03/2020 (06/2027)	2067 (2087)	2182.46	75.6
538	Araria Supaul New BG Line (East Central Railway [ECR] - I) (705368) (-) (-)	Bihar	06/2018 (03/2009)	03/2024 (01/2027)	1605 (2514)	1725.95	46.9
539	Fatuha-Islampur incl. MM for extn.of NL from Neora to Daniawan , Daniawan to Biharsharif, Biharsharif to Barbiga , Barbiga to Shekhpura (East Central Railway [ECR] - I) (705373) (-) (-)	Bihar	08/2002 (03/2002)	03/2023 (08/2025)	1473 (2882)	2712.19	98.2
540	Jogbani-Biratnagar New Rail Line project (Indian Railway Construction International Limited [IRCON]) (705450) (-) (-)	Bihar	06/2010 (01/2011)	03/2022 (12/2026)	402 (486)	369.48	86.5
541	Samastipur-Darbhanga Doubling Railway Project (East Central Railway [ECR] - I) (705526) (-) (-)	Bihar	11/2015 (12/2015)	03/2025 (10/2025)	519 (519)	412.58	100
542	Sagauli-Valmiknagar (East Central Railway [ECR] - I) (705527) (-) (-)	Bihar	03/2018 (03/2017)	12/2025 (12/2025)	1216 (2222)	2102.51	93
543	Muzaffarpur-Sugauli (East Central Railway [ECR] - I) (705528) (-) (-)	Bihar	03/2018 (03/2017)	06/2024 (06/2026)	1586 (1586)	1509.67	99
544	Rampur Dumra-Tal-Rajendrapul Additional Bridge and Railway Line Doubling (Indian Railway Construction International Limited [IRCON]) (706759) (-) (-)	Bihar	03/2016 (05/2017)	12/2024 (12/2025)	2373.64 (1700.24)	1581.96	98.5
545	Barauni-Bachwara [16 km] - 3rd & 4th line incl. Barauni yard remodelling [32 km] (East Central Railway [ECR] - I) (706860) (-) (-)	Bihar	10/2022 (08/2025)	08/2025 (10/2026)	645 (645)	54.13	56.9
546	JHAJHA - BATIA (East Central Railway [ECR] - I) (900874) (-) (-)	Bihar	03/2023 (03/2023)	03/2028 (01/2030)	588.18 (588.18)	2.38	0.1
547	Kharsia-Dharamjaygarh with Spur line [East Corridor-Phase 1] (Indian Railway Construction International Limited [IRCON]) (400220) (-) (-)	Chhattisgarh	03/2016 (01/2014)	09/2018 (12/2026)	3055 (3798.06)	2790.19	95.15
548	Doubling of Kirandul-Jagdalpur Line [150 km] (East Coast Railway [ECor] - I) (400291) (-) (-)	Chhattisgarh	02/2013 (03/2013)	03/2020 (04/2027)	1589 (1798)	1691.27	96.17

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
549	Gauge Conversion of Kendri-Dhamtari including Abhanpur - Rajim Branch line 67.20 Kms - 2nd Material Modification to Raipur Titlagarh doubling. (SECR) (602792) (-) (-)	Chhattisgarh	07/2011 (05/2021)	02/2025 (06/2026)	1171 (1171)	448.77	100
550	4th line between Nipania Bhatapara 14.4 Km (South East Central Railway [SECR] - II) (612815) (-) (-)	Chhattisgarh	12/2022 (05/2024)	03/2027 (-)	170.49 (170.49)	9.98	15
551	KHARSIA- NAYA RAIPUR-PARMALKASA 5th and 6th Line [278KM] (CAO/C/SECR) (617200) (-) (-)	Chhattisgarh	04/2025 (04/2025)	03/2031 (-)	7853.84 (7853.84)	0.64	0
552	Dallirajhara - Rowghat New Rail Line Project, Phase-I (Rail Vikas Nigam Limited) (617374) (-) (-)	Chhattisgarh	07/2009 (11/2009)	03/2025 (02/2026)	1516.45 (1881.26)	2154.73	98
553	Dallirajhra- Rowghat New Railway Line - Phase I [95 km] (Rail Vikas Nigam Limited) (705433) (-) (-)	Chhattisgarh	07/2009 (12/2009)	09/2025 (12/2025)	1628 (1628)	1440.85	82
554	Gevra Road-Pendra Road New Railway Line [135 km] (Indian Railway Construction International Limited [IRCON]) (705444) (-) (-)	Chhattisgarh	04/2014 (04/2014)	03/2022 (12/2026)	4970 (7448.52)	5327.55	83.36
555	Boridand - Ambikapur Doubling Line Project (South East Central Railway [SECR] - II) (706854) (-) (-)	Chhattisgarh	06/2022 (04/2022)	06/2030 (06/2030)	1376 (1576.72)	312.72	30
556	4TH LINE - BHATAPARA-HATHBAND [8.8 KM] [PB-72/NR/2022-23] (SECR) (709815) (-) (-)	Chhattisgarh	09/2022 (05/2024)	01/2027 (12/2027)	177.03 (177.03)	12.3	18
557	4TH LINE - BHILAI-BHILAI NAGAR [8.8 KM] [PB-72/NR/2022-23] (SECR) (709816) (-) (-)	Chhattisgarh	09/2022 (05/2024)	02/2027 (02/2027)	177.34 (177.34)	32.49	11
558	4TH LINE RAJNANDGAON-DONGARHGARH [31.2 KM] [PB-72/NR/2022-23] (SECR) (709818) (-) (-)	Chhattisgarh	09/2022 (05/2024)	01/2027 (01/2027)	328.34 (328.34)	96.2	36
559	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (709819) (-) (-)	Chhattisgarh	09/2022 (05/2025)	12/2026 (12/2026)	167.64 (167.64)	28.01	11
560	Redevelopment of New Delhi Railway Station and construction of associated infrastructure (Rail Land Development Authority) (613785) (-) (-)	Delhi	01/2023 (06/2024)	12/2028 (-)	4744 (4744)	355.8	6
561	Development of New Bijwasan Railway Terminal (Northern Railways) (617379) (-) (-)	Delhi	02/2008 (03/2013)	03/2020 (12/2026)	446.21 (446.21)	565.7	80
562	Anand Vihar-Tilak Bridge 3rd & 4th line (CAO/C/NR) (705583) (-) (-)	Delhi	03/2013 (03/2013)	03/2023 (12/2027)	667 (667)	333.72	23
563	Chandargaon - Cansaulium Rail Flyover Project [16 Km] (South Western Railway [SWR] - II) (706865) (-) (-)	Goa	NA (04/2026)	03/2031 (-)	1892 (1892)	0	0
564	Kosamba Umapada 70 Km (PCE/WR) (611918) (-) (-)	Gujarat	07/2023 (07/2022)	03/2027 (-)	468 (468)	44.62	9
565	New Broad Gauge line between Naliya to Jakhau Port (Western Railway [WR] - II) (611943) (-) (-)	Gujarat	02/2023 (02/2023)	01/2028 (02/2028)	410.26 (410.26)	11.3	5
566	Petlad-Bhadran 22.5 km (CAOCWR WR mor) (611945) (-) (-)	Gujarat	05/2022 (05/2022)	05/2030 (05/2030)	307.11 (307.11)	18.9	17
567	Samlaya Timba Road 54 km (PCE/WR) (611970) (-) (-)	Gujarat	02/2023 (02/2023)	03/2030 (03/2030)	670.17 (670.17)	47.46	12
568	Samni Jambusar 24 km (PCE/WR) (611971) (-) (-)	Gujarat	05/2022 (05/2022)	03/2030 (03/2030)	350 (349.93)	80.49	31
569	Western Railway Samakhiali Gandhidham Quadrupiling 53 Kms (Western Railway [WR] - II) (611974) (-) (-)	Gujarat	08/2023 (08/2023)	12/2026 (12/2027)	1430 (1430)	582.1	45
570	Dahod Creation of Infrastructure facilities for 9000 HP Electric locomotives Manufacturing at (PCE/WR) (611977) (-) (-)	Gujarat	05/2022 (02/2023)	02/2025 (-)	487 (487)	222.88	53

All Ongoing Projects							JUNE 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
571	Dahod Rolling Stock Workshop Provision of Infrastructure for CBS at (PCE/WR) (611978) (-) (-)	Gujarat	11/2022 (03/2023)	03/2025 (-)	158 (158)	51.87	10
572	Sabarmati Setting up of Maintenance Facilities for Train Sets Phase ii (Western Railway [WR] - II) (611979) (-) (-)	Gujarat	01/2023 (04/2023)	06/2025 (05/2026)	250 (250)	185.02	88
573	4th LINE BETWEEN BAREJADI NANDEJ-SANAND-AHMEDABAD BYPASS (Western Railway WR - II) (612072) (-) (-)	Gujarat	02/2023 (02/2023)	03/2027 (07/2028)	961.67 (961.67)	524.6	22
574	Redevelopment of Ahmedabad railway station and associated infrastructure on engineering, procurement and construction mode (Rail Land Development Authority) (613786) (-) (-)	Gujarat	01/2023 (11/2023)	03/2028 (-)	2379 (2379)	984.21	32.5
575	Kosamba Umarpada GC PROJECT (Ministry of Railways-) (616983) (-) (-)	Gujarat	07/2023 (07/2023)	06/2027 (-)	467.58 (467.58)	70.54	16
576	Desalpar-Hajipir-Luna and Vayor-Lakhpat New Line (Western Railway [WR] - II) (617880) (-) (-)	Gujarat	09/2025 (09/2025)	09/2028 (-)	2526.47 (2526.47)	0	0
577	Devbhumi Dwarka [Okha] - Kanalus Doubling (Western Railway [WR] - II) (618972) (-) (-)	Gujarat	12/2025 (12/2025)	12/2028 (-)	1456.77 (1456.77)	0.28	0
578	Miyagam-Karjan-Dabhoi-Samlaya [GC] (Western Railway [WR] - II) (705458) (-) (-)	Gujarat	01/2017 (01/2017)	03/2021 (12/2026)	483.88 (1039.13)	723.52	45
579	Modasa-Shamlaji Road Railway Line Project (Western Railway WR - II) (706757) (-) (-)	Gujarat	09/2012 (04/2008)	03/2025 (03/2026)	262 (262)	387.82	64
580	Rajkot - Kanalus Doubling Project [111.2 Kms] (Western Railway WR - II) (706763) (-) (-)	Gujarat	10/2021 (12/2021)	10/2026 (06/2026)	1080.58 (1080.58)	969.78	82
581	NADIAD-PETLAD [37.26 KM] (Railway) (709812) (-) (-)	Gujarat	05/2022 (10/2023)	06/2030 (06/2030)	461.91 (461.91)	186.9	8
582	NEW BG LINE INTERSECTION [5 NOS] BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD [16.51 KM] (Western Railway [WR] - II) (709813) (-) (-)	Gujarat	10/2022 (07/2025)	06/2028 (10/2027)	437.21 (437.21)	117.95	22
583	Bhiwani - Dobh Bahali Doubling Project [42.30 Km] (North Western Railway [NWR]) (611884) (-) (-)	Haryana	02/2023 (02/2023)	02/2028 (02/2028)	471 (471)	273.41	73
584	Koderma-Arigada Doubling 133.38 Km of East Central Railway (East Central Railway [ECR] - I) (617832) (-) (-)	Jharkhand	06/2025 (06/2025)	12/2029 (-)	2887.11 (2887.11)	0.1	0
585	Parasnath-Madhuban-Giridih new line (East Central Railway [ECR] - I) (705747) (-) (-)	Jharkhand	03/2019 (03/2019)	03/2024 (03/2026)	902.86 (902.86)	0	0.1
586	Gomoh - Flyover for DN trains (East Central Railway [ECR] - I) (705765) (-) (-)	Jharkhand	01/2018 (01/2018)	03/2026 (03/2026)	686 (686)	634.71	66.7
587	Lodhma - Piska - Link Line bypassing Hatia/Ranchi with Y connection (South Eastern Railway [SER] - I) (705785) (-) (-)	Jharkhand	08/2021 (03/2019)	06/2026 (05/2027)	473 (473)	349.31	10
588	Pradhan Kuntha Jn Line Doubling Project (East Central Railway [ECR] - I) (706837) (-) (-)	Jharkhand	11/2022 (11/2022)	11/2027 (11/2027)	349.22 (349.22)	145.57	72
589	Construction of New BG line between Hassan to Belur [27 Km] (South Western Railway [SWR] - II) (400023) (-) (-)	Karnataka	03/2019 (12/2025)	04/2028 (03/2030)	749 (749)	3.43	0.5
590	Yeshvanthpur - Channasandra Doubling Project [21.70 Km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703585) (-) (-)	Karnataka	04/2019 (10/2019)	03/2024 (03/2026)	314.1 (683.57)	173.5	56.8
591	New Railway Line between Ginigera and Raichur [165.57 km] (South Western Railway [SWR] - II) (705434) (-) (-)	Karnataka	03/2008 (05/2009)	03/2019 (03/2027)	2565 (3034.98)	2412.11	71
592	Bangalore-Satyamanglam New Line Project [260 Km] - Part Hejjala - Chamarajanagar [142 Km] (South Western Railway [SWR] - II) (705464) (-) (-)	Karnataka	02/1999 (07/2026)	12/2031 (-)	1382.78 (1382.78)	0	0

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
593	Gadag-Wadi New Railway Line [257 km] (South Western Railway [SWR] - II) (705490) (-) (-)	Karnataka	04/2013 (08/2017)	03/2027 (12/2027)	2842 (6700)	1604.89	36.5
594	Kadur - Chickamagalur - Sakleshpur [93km] (South Western Railway [SWR] - II) (705492) (-) (-)	Karnataka	01/2014 (11/2016)	06/2025 (12/2025)	825 (825)	789.58	84.8
595	Hubli-Ankola New Line Project [164.44 km] (South Western Railway [SWR] - II) (705493) (-) (-)	Karnataka	01/1999 (01/2000)	03/2005 (03/2030)	5174 (5174)	180.48	4.7
596	Bagalkot-Kudachi New Railway Line [142 km] (South Western Railway [SWR] - II) (705495) (-) (-)	Karnataka	10/2013 (11/2012)	03/2027 (01/2027)	1378 (1649)	809.24	36.5
597	Tumkur-Chitradurga-Davangere New Rail Line Project [191 km] (South Western Railway [SWR] - II) (705496) (-) (-)	Karnataka	10/2013 (01/2017)	03/2019 (12/2027)	1876 (1876)	602.36	16
598	Bangalore-Whitefield-Bangalore City-Krishnarajapuram [23.08 km] - Quadrupling (South Western Railway [SWR] - II) (705663) (-) (-)	Karnataka	02/2018 (06/2022)	02/2026 (02/2026)	493 (493)	337.37	85.9
599	SHIMOGA - SHIKARIPURA - RANEBENNUR [96 Km] (South Western Railway [SWR] - II) (705761) (-) (-)	Karnataka	09/2019 (02/2023)	12/2027 (06/2028)	1454 (1454)	102.64	13.9
600	Construction of New BG line between Hassan [Alur] to Belur [Km 27.34] (CAOC/SWR SWR mor) (705762) (-) (-)	Karnataka	06/2019 (09/2022)	04/2027 (12/2027)	748.86 (748.86)	3.64	0
601	Bangalore Suburban Railway Project (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (705941) (-) (-)	Karnataka	10/2020 (10/2020)	12/2026 (03/2030)	15767 (15767)	3277.99	20.02
602	Belgaum-Dharwad via Kittur [73.10Km] (South Western Railway [SWR] - II) (706835) (-) (-)	Karnataka	09/2020 (03/2025)	12/2027 (03/2029)	1591 (1591)	0.38	0
603	Kumbalam-Turavur doubling project [15.59 Km] (Ministry of Railways) (705638) (-) (-)	Kerala	04/2023 (04/2023)	03/2027 (03/2027)	813 (802.8)	151.83	35
604	Ernakulam-Kumbalam doubling project [7.71 Km] (SR-ERS) (705639) (-) (-)	Kerala	04/2023 (04/2023)	03/2028 (02/2027)	601 (595.39)	313.97	28
605	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho (North Central Railway) (705480) (-) (-)	Madhya Pradesh	01/2007 (03/1998)	03/2027 (12/2027)	8914 (8914)	6889.55	74
606	Satna-Rewa Railway Line Doubling Project (West Central Railway [WCR] - II) (705659) (-) (-)	Madhya Pradesh	11/2015 (08/2017)	03/2026 (03/2026)	500 (584)	573.8	88
607	Doubling of Katni - Singrauli Railway Line [261 km] (Indian Railway Construction International Limited [IRCON]) (705660) (-) (-)	Madhya Pradesh	03/2016 (03/2017)	12/2025 (12/2025)	2445 (4377)	3368.46	81.25
608	Katni Grade Separator/Bye Pass (Indian Railway Construction International Limited [IRCON]) (705661) (-) (-)	Madhya Pradesh	03/2016 (09/2017)	09/2024 (09/2026)	1248 (1248)	1850.38	95
609	Indore - Budni New Railway Line [198 kms] (RVNL - II) (705763) (-) (-)	Madhya Pradesh	08/2019 (10/2020)	09/2030 (09/2030)	7474 (7474)	2879.62	41
610	Nimach-Ratlam Doubling [133 Km] (Western Railway [WR] - II) (705933) (-) (-)	Madhya Pradesh	10/2021 (10/2021)	10/2027 (10/2027)	1095.88 (1095.88)	1284.91	100
611	DHULE [BORVIHIR] - NARDANA NEW LINE [50.60 KMS] (Central Railway) (400019) (-) (-)	Maharashtra	01/2019 (04/2023)	12/2026 (09/2027)	492.76 (1170.83)	560.32	38
612	Wardha-Nanded Via Yavatmal New BG Line (Central Railway [CR] - II) (400271) (-) (-)	Maharashtra	12/2017 (04/2008)	03/2025 (12/2026)	3445 (3445)	3002.93	50
613	AURANGABAD-ANKAI - DOUBLING PROJECT 98.25 Km (South Central Railway [SCR] - II) (611751) (-) (-)	Maharashtra	05/2023 (05/2023)	03/2027 (-)	960.64 (960.64)	1375.55	2.03
614	Gauge Conversion of Pachora-Jamner with Extension upto Malkapur [Bodwad] [84.34 Kms] (Central Railway [CR] - II) (612845) (-) (-)	Maharashtra	08/2022 (01/2026)	07/2028 (-)	955.39 (955.39)	13.99	10

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
615	Redevelopment of Chhatrapati Shivaji Maharaj Terminus [CSMT] and construction of associated infrastructure (Rail Land Development Authority) (613015) (-) (-)	Maharashtra	04/2023 (07/2023)	03/2027 (-)	1813 (1813)	873.99	25
616	Gondia-Balharshah [Chanda Fort] Doubling [240 Km] (South East Central Railway) (617201) (-) (-)	Maharashtra	04/2025 (04/2025)	03/2031 (-)	4373.04 (4373.04)	1.79	2
617	Doubling between Parbhani Parli Vajjanath stations 64.71 Km (South Central Railway [SCR] - II) (617215) (-) (-)	Maharashtra	12/2023 (12/2023)	03/2028 (-)	769.93 (769.93)	197.62	0.2
618	Babupeth - Sasti New Rail Line [13.114 KMs] (CentralRailway) (617361) (-) (-)	Maharashtra	10/2024 (10/2024)	03/2028 (-)	362.81 (362.81)	0.48	0
619	Double Chord line Between Nilaje-Kopar (CentralRailway) (617364) (-) (-)	Maharashtra	01/2025 (01/2025)	07/2028 (-)	338.33 (205)	55.83	60
620	Ahmednagar - Beed - Parli - Vajjnath New Broad Gauge Line Railway Project [261.3 km] (Central Railway [CR] - II) (705356) (-) (-)	Maharashtra	01/1999 (10/2002)	03/2026 (03/2026)	2538.67 (4957.27)	5233.2	93
621	Baramati Lonand New Line Project (Central Railway) (705357) (-) (-)	Maharashtra	03/2016 (03/1999)	03/2027 (03/2027)	138.48 (1843.9)	1039.72	60
622	Wadsa-Gadchiroli (South East Central Railway) (705479) (-) (-)	Maharashtra	05/2017 (03/2012)	03/2027 (03/2027)	1886 (1886)	846.22	68
623	Wardha - Yavatmal Nanded Railway Line Project (Central Railways) (705497) (-) (-)	Maharashtra	02/2008 (04/2013)	12/2026 (-)	3445.34 (4030.69)	4053.03	47
624	3rd Line Kalyan - Kasara [67.35 Kilometres] (Central Railway) (705498) (-) (-)	Maharashtra	09/2015 (09/2015)	12/2026 (12/2026)	792.89 (1395.79)	1088.38	73
625	3rd Line Wardha - Sewagram - Nagpur (Central Railway [CR] - II) (705500) (-) (-)	Maharashtra	09/2015 (05/2016)	12/2025 (10/2026)	540.02 (916.53)	842.78	88
626	3rd Line Wardha - Ballarshah [132 Kilometres] (Central Railway [CR] - II) (705502) (-) (-)	Maharashtra	03/2016 (12/2016)	12/2025 (02/2026)	1384.72 (2033.59)	1841.71	86
627	Doubling of Daund Manmad Line [247.6 km] (Central Railway) (705504) (-) (-)	Maharashtra	10/2017 (03/2017)	12/2025 (03/2026)	2081.27 (3267.06)	3111.8	92
628	4th Line Wardha - Nagpur [78.7 Kilometres] (Central Railway [CR] - II) (705505) (-) (-)	Maharashtra	04/2017 (05/2018)	12/2025 (10/2026)	637.95 (1214.69)	1061.23	88
629	3rd Line Manmad - Jalgaon [160 Kilometres] (Central Railway [CR] - II) (705506) (-) (-)	Maharashtra	05/2017 (04/2018)	12/2024 (11/2025)	1035.16 (1870)	1843.54	100
630	Solapur-tuljapur-Osmanabad (Central Railway) (705735) (-) (-)	Maharashtra	08/2018 (12/2023)	03/2027 (03/2028)	904.92 (3295.74)	1277.63	22
631	Nagpur- Nagbhir Railway Line Gauge Conversion Project (MRIDC) (705799) (-) (-)	Maharashtra	10/2019 (04/2020)	12/2025 (12/2025)	1400 (1400)	1472	80
632	Mumbai Urban Transport Project [MUTP] - PHASE II (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706779) (-) (-)	Maharashtra	05/2008 (04/2008)	03/2014 (12/2027)	8087 (8087)	7559.14	90
633	Mumbai Urban Transport Project [MUTP] Phase-IIIA (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706780) (-) (-)	Maharashtra	04/2019 (04/2019)	12/2027 (12/2027)	33690 (33690)	3854.46	25
634	Mumbai Urban Transport Project Phase-III (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706781) (-) (-)	Maharashtra	11/2016 (12/2016)	03/2022 (12/2026)	10947 (10947)	6880.48	75
635	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391) (-) (-)	Manipur	03/2013 (12/2007)	12/2026 (06/2029)	14323 (21885.9)	16327.07	73.05
636	Byrnihat-Shillong New Rail Line- 108 km (Northeast Frontier Railway [NFR]) (705396) (-) (-)	Meghalaya	04/2011 (03/2010)	03/2021 (03/2027)	8324.28 (8342.28)	266.12	2.04

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
637	Marikuppam - Kuppam New Line Project [23.70 Km] (South Western Railway [SWR] - II) (705491) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	04/2012 (10/2018)	06/2026 (06/2026)	297 (297)	147.99	21.5
638	Rayadurg-Tumkur via Kalyandurg New Line [207 km] (South Western Railway [SWR] - II) (705494) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	03/2008 (07/2010)	09/2015 (02/2028)	2496 (2496)	1943.23	73
639	Renigunta, Wadi & Gooty Bypass Railway Project (South Central Railway [SCR] - II) (705610) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	04/2016 (04/2016)	12/2025 (03/2026)	302 (543)	636.74	89.04
640	Doubling between Mudkhed Medchal & Mahbubnagar Dhone section 417.88 Km (South Central Railway [SCR] - II) (617212) (-) (-)	Multi-States (Andhra Pradesh, Maharashtra, Telangana)	08/2023 (08/2023)	03/2029 (08/2029)	4686.09 (4686.09)	640.06	21
641	Vizianagaram - Titlagarh 3rd line [272 Km including By - pass line of 7.68 KM] (RVNL - II) (400253) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	06/2016 (11/2016)	12/2025 (12/2026)	4803 (6669.91)	6260.17	99
642	Doubling of Kottavalasa-Koraput Rail Line [189 KM] (East Coast Railway [ECOR] - II) (705512) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	12/2015 (01/2016)	03/2022 (03/2028)	2500 (2500)	2217.87	73
643	Tindivanam-Nagari New Line Project [184.5 km] (Ministry of Railways) (400275) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	07/2008 (10/2008)	09/2025 (03/2028)	3631 (3631)	1335.29	16.85
644	Doubling between Motumari Vishnupuram - 88.81 Km and Rail over Rail - RoR at Motumari - 10.877 Km (South Central Railway [SCR] - II) (616857) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	02/2024 (03/2025)	03/2029 (-)	1595.55 (1595.55)	264.89	2.05
645	Doubling of Guntur Bibinagar 239 Km (South Central Railway [SCR] - II) (617211) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	08/2023 (08/2023)	03/2029 (-)	2853.23 (2853.23)	357.74	2.6
646	Rail Connectivity to Errupalem Amravati Namburu 57 Km (South Central Railway [SCR] - II) (617214) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	11/2024 (11/2024)	03/2027 (-)	2047.4 (2047.4)	208.57	0.17
647	Kazipet-Vijayawada 3rd line with electrification [220 km] (South Central Railway [SCR] - II) (705612) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	03/2013 (08/2014)	02/2025 (12/2025)	1953 (3363)	5192.51	95.02
648	Vijayawada - Kazipet Bypass line (South Central Railway [SCR] - II) (705632) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	04/2016 (04/2016)	01/2025 (12/2025)	647 (904)	1249.39	93.6
649	Murkongselek-Pasighat (Northeast Frontier Railway [NFR] - II) (705401) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (03/2023)	03/2025 (12/2026)	435 (1250)	887.87	72
650	Tetlia-Byrnihat New Railway Line (Northeast Frontier Railway [NFR]) (705394) (-) (-)	Multi-States (Assam, Meghalaya)	08/2010 (03/2007)	11/2011 (06/2027)	1304.62 (1304.62)	1258.8	86.16
651	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701) (-) (-)	Multi-States (Assam, Nagaland)	02/2024 (01/2025)	02/2028 (-)	2123.7 (2123.7)	141.06	12.5
652	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR] - II) (705392) (-) (-)	Multi-States (Assam, Nagaland)	08/2015 (02/2016)	03/2025 (12/2029)	6663 (6663)	6748.9	46.5
653	New Delhi- Howrah Speed Booster[160Kmph] Project (PCE/NCR) (705794) (-) (-)	Multi-States (Bihar, Delhi, Jharkhand, Uttar Pradesh, West Bengal)	09/2019 (09/2019)	03/2024 (-)	6684.81 (6684.81)	127.03	0
654	Multi tracking of Son Nagar-Andal 374.53 rkm & 814.38 tkm (East Central Railway [ECR] - I) (616699) (-) (-)	Multi-States (Bihar, Jharkhand)	08/2023 (08/2023)	03/2028 (-)	12333.57 (12333.6)	882.77	18
655	Koderma-Tilaiya New Line (East Central Railway [ECR] - I) (705375) (-) (-)	Multi-States (Bihar, Jharkhand)	11/2004 (03/2002)	02/2025 (02/2026)	1626 (2486.62)	2221.76	95.6
656	Pirpainti - Jasidih [100.52 Km] New BG line (Eastern Railway [ER] - I) (705385) (-) (-)	Multi-States (Bihar, Jharkhand)	03/2014 (03/2022)	03/2028 (03/2028)	2555 (2555)	1117.17	61.9
657	NER Provision of Automatic Block Signalling on Gorakhpur Cantt[Excl] Chhapra Gramin & Burhwal Jn [Excl] Sitapur Jn section of high density routes (North Eastern Railway [NER]) (611669) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	05/2022 (06/2023)	03/2027 (03/2028)	380.47 (380.47)	258.65	25
658	Gorakhpur-Valmikinagar Doubling project (NER) (617224) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	08/2023 (03/2024)	12/2027 (-)	1120 (1120)	442.7	32

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
659	Chhapra-Ballia Patch Doubling (North Eastern Railway [NER]) (705562) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	03/2013 (12/2015)	02/2025 (05/2026)	963 (1046)	918.18	96
660	Katihar Kumedpur & Katihar Mukuria BG Doubling Project (Northeast Frontier Railway [NFR]) (617245) (-) (-)	Multi-States (Bihar, West Bengal)	08/2022 (08/2022)	08/2026 (02/2027)	942.64 (942.64)	656.16	66
661	Gondia - Dongargarh 4th line [84 Km] (South Eastern Central Railway) (618978) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	10/2025 (10/2025)	10/2030 (-)	2222.53 (2222.53)	0.35	1
662	Rajnandgaon - Nagpur [Kalumna] Third Railway Line [228.30 km] (South East Central Railway [SECR] - II) (705617) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	09/2016 (12/2016)	12/2024 (06/2026)	3545 (3545)	3678.97	96
663	Sardega - Bhalumuda New Double line [37.24 Km] (SECR) (617390) (-) (-)	Multi-States (Chhattisgarh, Odisha)	09/2024 (09/2024)	03/2028 (-)	1281.81 (1281.81)	130.14	5
664	Jagdulpur-Koraput (East Coast Railway [ECOR] - II) (705511) (-) (-)	Multi-States (Chhattisgarh, Odisha)	12/2015 (03/2016)	03/2024 (12/2026)	1547 (1547)	1403.9	92.55
665	Jharsuguda-Bilaspur Fourth Railway Line [206 km] (SECR) (705616) (-) (-)	Multi-States (Chhattisgarh, Odisha)	09/2016 (09/2016)	10/2024 (03/2026)	2140 (2979)	2302.69	97
666	Mumbai-Ahmedabad High Speed Rail Project- 508 km (National High Speed Rail Corporation [NHSRC]) (705728) (-) (-)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	03/2015 (09/2017)	08/2027 (12/2029)	108000 (108000)	90966.89	60.87
667	Raising of speed to 160 kmph/200 kmph on existing New Delhi-Mumbai route incl. Vadodara-Ahmedabad (PCEWR) (705793) (-) (-)	Multi-States (Delhi, Gujarat, Madhya Pradesh, Maharashtra, Rajasthan)	09/2019 (09/2019)	03/2024 (03/2026)	6806.44 (8095.12)	9480.86	66.32
668	Hospet - Tinaighat - Vasco Rail Doubling Project (RVNL - II) (705650) (-) (-)	Multi-States (Goa, Karnataka)	03/2010 (07/2012)	03/2027 (12/2027)	5060 (5060)	5511.03	86.14
669	Hospet-Hubli-Vasco da Gama Line Electrification Project (RVNL) (706950) (-) (-)	Multi-States (Goa, Karnataka)	07/2015 (05/2018)	03/2023 (06/2026)	744.49 (1122.62)	1163.32	99.7
670	Western Dedicated Freight Corridor (DFCCIL) (705237) (-) (-)	Multi-States (Gujarat, Haryana, Maharashtra, Rajasthan, Uttar Pradesh)	02/2008 (01/2012)	03/2022 (12/2025)	51101 (124005)	124623	96
671	New line Dahod-Indore via Sardarpur, Jabuwa and Dhar (Western Railway [WR] - II) (705453) (-) (-)	Multi-States (Gujarat, Madhya Pradesh)	06/2012 (06/2012)	02/2027 (02/2027)	456.07 (3516.77)	4166.4	55
672	Chhota Udaipur - Dhar New Line Project [157 km] (Western Railway [WR] - II) (705454) (-) (-)	Multi-States (Gujarat, Madhya Pradesh)	11/2008 (01/2014)	12/2025 (12/2025)	1794 (1794)	1828.91	80.5
673	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (Western Railway) (611452) (-) (-)	Multi-States (Gujarat, Maharashtra)	09/2019 (03/2023)	12/2025 (12/2026)	311 (311)	263.42	93
674	Taranga Hill-Abu Road via Ambaji (North Western Railway [NWR]) (400022) (-) (-)	Multi-States (Gujarat, Rajasthan)	07/2022 (07/2022)	07/2030 (07/2030)	2798 (2798)	2616.51	45
675	LUNI- SAMDARI- BHILDI DOUBLING (North Western Railway [NWR]) (616842) (-) (-)	Multi-States (Gujarat, Rajasthan)	02/2024 (02/2024)	07/2027 (-)	3085.59 (3085.59)	962.77	36
676	Chandigarh-Baddi New Rail Line- 36 km (Northen Railway [NR]) (705424) (-) (-)	Multi-States (Haryana, Himachal Pradesh)	02/2018 (02/2018)	12/2026 (12/2026)	1540 (1540.13)	606.07	44
677	Rewari - Kathuwas Doubling Project [27.72 Km] (North Western Railway [NWR]) (611861) (-) (-)	Multi-States (Haryana, Rajasthan)	02/2023 (12/2022)	06/2027 (06/2027)	352 (352)	342.83	80
678	Nangal Dam-Talwara New Broad Gauge Line [84 KM] and Taking Over Siding Mukerian-Talwara [29 KM] (Northen Railway [NR]) (705410) (-) (-)	Multi-States (Himachal Pradesh, Punjab)	03/1983 (05/1985)	12/2025 (12/2027)	2018 (2018)	2398.08	85.5
679	Bhanupalli-Bilaspur-Beri New Railway Line Project (RVNL - II) (705428) (-) (-)	Multi-States (Himachal Pradesh, Punjab)	03/2009 (04/2015)	12/2026 (12/2027)	13447 (13447)	7781.89	64
680	Doubling of Hatia [Ranchi]-Bondamunda Rail Line - 159 km (South Eastern Railway - JH) (705628) (-) (-)	Multi-States (Jharkhand, Odisha)	03/2016 (02/2017)	06/2025 (06/2026)	3029 (3029.04)	2649.22	94

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
681	Buramara-Chakulia new line [59.96 km] (South Eastern Railway [SER] - I) (616588) (-) (-)	Multi-States (Jharkhand, Odisha, West Bengal)	08/2024 (12/2024)	12/2029 (-)	1459.13 (1459.13)	9.16	0
682	Chandil - Anara - Damodar - 3rd line [121.26 km] (CAO/C/SER) (616227) (-) (-)	Multi-States (Jharkhand, West Bengal)	09/2024 (07/2025)	09/2029 (-)	1932.01 (1932.01)	3.97	0
683	KHARAGPUR-ADITYAPUR THIRD RAIL LINE- 132 KM (RVNL - I) (705668) (-) (-)	Multi-States (Jharkhand, West Bengal)	09/2016 (01/2018)	03/2025 (06/2026)	3250 (3250)	3294.29	98
684	Baiyyappanahalli - Hosur Doubling Project [48 km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703586) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	04/2019 (02/2019)	03/2024 (01/2026)	498.7 (748.7)	713.85	88.3
685	Trivandrum- Kanyakumari (Southern Railway [SR] - I) (705635) (-) (-)	Multi-States (Kerala, Tamil Nadu)	08/2017 (03/2016)	03/2025 (06/2028)	1432 (3785.45)	3213.64	58
686	Ratlam-Mhow-Khandwa-Akola Gauge Conversion (Western Railway [WR] - II) (705457) (-) (-)	Multi-States (Madhya Pradesh, Maharashtra)	04/2008 (03/2010)	03/2027 (09/2028)	1656.25 (6499.86)	4606.71	83
687	Itarsi - Nagpur Third Railway Line [280 km] (Central Railway [CR] - II) (705507) (-) (-)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016 (09/2016)	03/2027 (12/2027)	2449.91 (2506.68)	2195.77	55
688	RATLAM- DUNGARPUR VIA BANSWARA NEW LINE PROJECT (North Western Railway [NWR]) (617406) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	10/2015 (05/2023)	03/2028 (-)	2417.24 (2417.24)	7.7	8
689	Gwalior - Seopurkala with extension to Kota [Gauge Conversion] (North Central Railway) (705419) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	03/2011 (07/2018)	03/2025 (02/2026)	2913 (2913)	2270.23	95
690	Nimach-Badi Sadri New Rail Line Project (Western Railway [WR] - II) (705764) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	04/2017 (09/2021)	03/2026 (06/2026)	495 (825)	294.57	60
691	Mathura-Jhansi Third Railway Line [274 Km] (RVNL - II) (705667) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	12/2015 (03/2018)	12/2024 (12/2026)	5961 (5961)	5195.18	96.71
692	Jhansi - Bina Third Railway Line [153 Km] (CAO/C/NCR) (705598) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	09/2016 (03/2018)	03/2022 (03/2026)	2002 (2002)	1960.31	98
693	Jhansi-Khairar-Manikpur & Khirar-Bhimsen (North Central Railway) (705608) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2018 (04/2019)	03/2026 (03/2026)	4330 (4330)	3102.72	73
694	Third Line [new] between Kazipet - Balharshah with electrification [201.04 Km] (South Central Railway [SCR] - II) (705613) (-) (-)	Multi-States (Maharashtra, Telangana)	09/2016 (10/2016)	01/2025 (11/2025)	2595 (3071)	4154.83	94.8
695	Narayangarh-Bhadrak 3rd line (South Eastern Railway [SER] - I) (705629) (-) (-)	Multi-States (Odisha, West Bengal)	03/2019 (03/2017)	12/2025 (01/2027)	2400 (3425.32)	2713.19	82
696	Nagapattinam-Tiruturaipundi and Karaikal-Peralam New Line (Ministry of Railways) (400223) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	07/2008 (01/2019)	03/2027 (03/2028)	713 (981)	645.24	81
697	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432) (-) (-)	Multi-States (Sikkim, West Bengal)	10/2009 (05/2010)	05/2015 (12/2027)	7877 (11775)	11090.47	80
698	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass Line Project (Eastern Railway [ER] - I) (602797) (-) (-)	Multi-States (Uttar Pradesh, West Bengal)	08/2017 (12/2017)	03/2027 (03/2027)	461.64 (461.64)	296.61	33
699	Jharsuguda-Barpali-Sardega Ph II Works- Rail Connectivity for Coal Loading Bulb at Barpali. (South Eastern Railway [SER] - I) (400006) (-) (-)	Odisha	10/2021 (10/2021)	10/2025 (12/2026)	808.99 (808.99)	743.46	40
700	Proposed 6 nos Road Over Bridge [ROB] at different locations under MCL Talcher Under Deposit Scheme. (East Coast Railway [ECOR] - II) (400045) (-) (-)	Odisha	08/2022 (07/2022)	03/2025 (01/2025)	168.32 (168.32)	69.85	82
701	Doubling of Lingaraj SILO connectivity of NTPC line and augmentation of NTPC exchange yard and NTPC Block Cabin. (East Coast Railway [ECOR] - II) (400047) (-) (-)	Odisha	08/2022 (06/2022)	12/2024 (12/2026)	210 (210)	41.17	53
702	Doubling of lines connecting the loading spurs in Talcher Yard. (East Coast Railway [ECOR] - II) (400048) (-) (-)	Odisha	09/2022 (06/2022)	12/2024 (06/2027)	186.21 (186.21)	105.07	88

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
703	Brundamal-Jharsuguda- flyover connection for joining downline (East Coast Railway [ECoR] - II) (400232) (-) (-)	Odisha	01/2014 (01/2014)	12/2026 (12/2026)	297 (297)	237.83	67
704	3rd & 4th line between Sarla - Sason [8 km] [PB 73/2023-24/NR] (East Coast Railway [ECoR] - II) (612834) (-) (-)	Odisha	04/2023 (04/2023)	12/2025 (-)	252 (252)	117.97	92
705	Rourkela-Bondamunda A-Cabin 5th line [9.6 km] (CAO/C/SER) (615915) (-) (-)	Odisha	09/2022 (12/2023)	03/2026 (11/2026)	244.99 (244.99)	146.07	45
706	Bangriposi-Gorumahisani new line [85.60 km] (CAO/C/SER) (616586) (-) (-)	Odisha	08/2024 (09/2025)	12/2029 (-)	2269.49 (2269.49)	7.14	0
707	Badampahar-Kendujhargarh new line [82.06 km] (CAO/C/SER) (616587) (-) (-)	Odisha	08/2024 (09/2025)	12/2029 (-)	1875.72 (1875.72)	2.35	0
708	Flyover between Siju and Paradeep coaching Yard to avoid Surface crossing of trains (East Coast Railway [ECoR] - II) (616694) (-) (-)	Odisha	04/2023 (10/2025)	07/2028 (-)	200.77 (200.77)	37.26	5.5
709	Paradeep - Badabandha 3rd & 4th Line / 18.51kms (East Coast Railway [ECoR] - II) (616695) (-) (-)	Odisha	08/2023 (04/2025)	11/2028 (-)	300.15 (300.15)	2.47	10.5
710	Naupada-Gunupur - New line upto Theruvali [73.62 km] (Indian Railway) (616839) (-) (-)	Odisha	08/2024 (04/2026)	12/2029 (-)	1165.89 (1165.89)	0	0
711	New Line between Junagarh - Nabarangpur [116.21 Km] (Indian Railway) (618995) (-) (-)	Odisha	08/2024 (08/2025)	08/2030 (-)	2864.51 (2864.51)	1.06	0
712	Khurda-Bolangir New Broad Gauge Rail Link [301km] (East Coast Railway [ECoR] - II) (705358) (-) (-)	Odisha	03/1994 (03/2001)	12/2026 (12/2026)	3792 (5089)	5789.53	92.5
713	Talcher-Bimlagarh New Railway Line (East Coast Railway [ECoR] - II) (705359) (-) (-)	Odisha	03/2004 (12/2004)	03/2025 (03/2029)	1928 (1928)	2127.3	57
714	Bhadrak-Nergundi Third Line (East Coast Railway [ECoR] - II) (705510) (-) (-)	Odisha	10/2015 (04/2015)	11/2024 (01/2026)	1284 (1284)	1379.6	95.8
715	Koraput - Singapur Railway Doubling (East Coast Railway [ECoR] - II) (705513) (-) (-)	Odisha	12/2015 (12/2015)	12/2027 (03/2028)	2362 (2362)	2007.83	67.67
716	Jarapada- Budhapank with flyover at Talcher road 3rd and 4th Line (East Coast Railway [ECoR] - II) (705514) (-) (-)	Odisha	11/2015 (12/2015)	11/2018 (03/2028)	1000 (810.02)	478.83	59
717	3rd & 4th Railway Line Project from Salegaon to Budhapank via Rajathgarh. (East Coast Railway [ECoR] - II) (705515) (-) (-)	Odisha	07/2013 (12/2015)	03/2026 (03/2026)	1173 (2092)	2138.09	90
718	Jeypore-Navarangpur New Rail Line Project (East Coast Railway [ECoR] - II) (705741) (-) (-)	Odisha	07/2017 (04/2023)	07/2028 (12/2029)	748 (748)	15.91	2.13
719	Khurda Road - Balangir Electrification of Railway Track Project (Ministry of Railways) (706898) (-) (-)	Odisha	09/2018 (09/2019)	03/2021 (-)	267.61 (267.61)	0	0
720	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION/12.76kms (East Coast Railway [ECoR] - II) (709811) (-) (-)	Odisha	09/2022 (05/2025)	09/2027 (09/2027)	190 (189.93)	3.4	5
721	Jaynagar-Bijalpura, incl. extn. Bet, Bijalpura-Bardibas [Nepal] (East Central Railway [ECR] - I) (705362) (-) (-)	Offshore	08/2015 (03/2011)	03/2022 (03/2026)	819 (819)	580.51	75
722	North Region Video Surveillance Project (RCIL) (705298) (-) (-)	PAN India	06/2020 (04/2023)	03/2024 (-)	274.39 (274.39)	0	48
723	Ludhiana Mullanpur 21Km Doubling Railway project (CAO/C/INR) (607653) (-) (-)	Punjab	NA (10/2022)	06/2024 (02/2027)	234.78 (234.78)	61.39	99
724	Ludhiana- Killa Raipur Railway Doubling Project (Railway) (705783) (-) (-)	Punjab	03/2019 (12/2022)	03/2025 (02/2027)	237.64 (238)	137.05	57

All Ongoing Projects							JUNE 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
725	Devgarh Madariya - Nathdwara Gauge Conversion [82.54 Km] part of Marwar - Mavli Gauge Conversion [152 Km] (North Western Railway [NWR]) (611855) (-) (-)	Rajasthan	01/2023 (01/2023)	01/2027 (-)	968.92 (968.92)	745.15	73
726	Maintenance cum workshop depot for Vande Bharat Sleeper Trains as per conditions under WTA 527 (WPO/Patna) (611929) (-) (-)	Rajasthan	09/2022 (06/2023)	12/2024 (-)	166.86 (166.86)	0	0
727	PUSHKAR- MERTA CITY NEW LINE (North Western Railway [NWR]) (616841) (-) (-)	Rajasthan	02/2024 (02/2024)	12/2026 (12/2028)	799.64 (799.64)	224.71	8
728	AJMER- CHANDERIYA DOUBLING (North Western Railway [NWR]) (616843) (-) (-)	Rajasthan	02/2024 (02/2024)	06/2027 (03/2028)	1634.79 (1634.79)	489.56	22
729	SADULPUR - CHURU DOUBLING PROJECT (North Western Railway [NWR]) (617403) (-) (-)	Rajasthan	01/2024 (01/2024)	06/2026 (-)	468.64 (468.64)	197.84	95
730	POKHRAN - RAMDEVRA New Line (North Western Railway [NWR]) (617404) (-) (-)	Rajasthan	04/2025 (04/2025)	03/2028 (-)	189.21 (189.21)	55.58	2
731	NATHDWARA- NATHDWARA TOWN NL (North Western Railway [NWR]) (617408) (-) (-)	Rajasthan	03/2019 (04/2024)	03/2027 (-)	166.33 (166.33)	112.55	15
732	Dholpur - Sirmuttra Gauge Conversion (North Central Railway) (705482) (-) (-)	Rajasthan	03/2022 (04/2020)	02/2019 (02/2027)	747 (747)	509.8	49.7
733	Gudha-Thatha Mithri Construction of Railway Track Project (North Western Railway [NWR]) (705752) (-) (-)	Rajasthan	04/2019 (04/2019)	11/2026 (11/2026)	819.48 (967.06)	405.39	95
734	Sawai Madhopur-Jaipur Railway Line Project (North Western Railway [NWR]) (705912) (-) (-)	Rajasthan	02/2024 (04/2023)	03/2027 (-)	1203.89 (1203.89)	240.33	19
735	Agra Fort-Bandikui Doubling Line Project (CAO/C/NCR) (705919) (-) (-)	Rajasthan	06/2022 (02/2021)	06/2027 (06/2027)	1390 (1390)	529.92	56
736	Dedicated Test Track for RDSO /Phase-II Project (North Western Railway [NWR]) (706836) (-) (-)	Rajasthan	11/2021 (01/2022)	03/2026 (-)	466.42 (466.42)	538.22	98
737	Sawaimadhopur Bye Pass Line Project (North Western Railway [NWR]) (706866) (-) (-)	Rajasthan	12/2022 (01/2023)	03/2026 (05/2027)	304 (304)	93.09	77
738	Phase II extension of MRTS from Velachery to St Thomas Mount (Ministry of Railways) (400280) (-) (-)	Tamil Nadu	11/2007 (11/2008)	07/2025 (09/2025)	734 (734.01)	486.53	99.9
739	Redevelopment of Chennai Egmore Station (Ministry of Railways) (613002) (-) (-)	Tamil Nadu	05/2022 (10/2022)	03/2026 (-)	842 (842)	340	0
740	Coach Production Factory Upgradation Project (CPM/ICF) (705244) (-) (-)	Tamil Nadu	12/2017 (07/2018)	12/2021 (-)	520 (520)	192.25	0
741	Doubling between Bhadrachalam Road and Dornakal (South Central Railway [SCR] - II) (616856) (-) (-)	Telangana	08/2023 (04/2025)	04/2029 (-)	770.12 (770.12)	87.94	0.06
742	Railway Manufacturing Unit (RVNL - II) (617409) (-) (-)	Telangana	07/2016 (02/2023)	12/2026 (03/2026)	521.36 (521.36)	492.12	91
743	Kazipet Wagon Overhauling Project (RVNL) (705252) (-) (-)	Telangana	09/2017 (07/2017)	12/2023 (-)	385 (385)	0	0
744	Manoharabad-Kothapalli New Rail Line [151 km] (South Central Railway [SCR] - II) (705437) (-) (-)	Telangana	07/2016 (01/2017)	03/2027 (12/2027)	1160 (2781)	3073.41	72.02
745	Bahraich-Shravasti-Balrampur-Siddharthnagar -Santkabir nagar (North Eastern Railway [NER]) (400204) (-) (-)	Uttar Pradesh	10/2018 (03/2017)	10/2030 (10/2030)	4939.78 (4939.78)	1086.23	13.1
746	Sahjanwa-Dohrighat (North Eastern Railway [NER]) (400205) (-) (-)	Uttar Pradesh	08/2019 (03/2017)	03/2029 (03/2029)	1319.75 (1319.75)	544.89	4.2

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
747	Varanasi-Pt. Deen Dayal Upadhyaya multitracking 15km including construction of new Rail-cum-Road Bridge across Ganga River. (Northern Railways) (617213) (-) (-)	Uttar Pradesh	10/2024 (10/2025)	10/2029 (-)	2464.46 (2464.46)	96.98	3.93
748	Anandnagar - Ghugli via Maharajganj New line 52.7 km (Construction NER) (617252) (-) (-)	Uttar Pradesh	10/2023 (11/2023)	03/2028 (-)	958.27 (958.27)	640.17	24
749	Chunar-Chopan doubling project (North Central Railway) (617284) (-) (-)	Uttar Pradesh	08/2023 (01/2025)	03/2028 (-)	1423.96 (1423.96)	151.57	18.5
750	Surface triangle line bet. Bhadura stn and new crossing stn Karma (East Central Railway [ECR] - I) (617333) (-) (-)	Uttar Pradesh	10/2022 (05/2024)	02/2027 (-)	199.96 (199.96)	7.67	0.6
751	Doubling between Jaunpur Jn - Zaffarabad 6.28 km (M/S SRC company Infra Private Limited) (617370) (-) (-)	Uttar Pradesh	03/2023 (02/2025)	01/2027 (-)	180.66 (180.66)	65.54	27.55
752	Burhwal Gonda 3rd line (North Eastern Railway [NER]) (705567) (-) (-)	Uttar Pradesh	11/2017 (07/2019)	03/2025 (05/2026)	1016 (1118)	1058.77	88.5
753	Janghai-Pratapgarh- Amethi (CAO/C/II/INR) (705588) (-) (-)	Uttar Pradesh	11/2017 (03/2017)	03/2025 (03/2026)	722 (1194)	1729.27	70
754	Lalitpur-Birari with flyover at Lalitpur- 16 Km (North Central Railway) (705766) (-) (-)	Uttar Pradesh	03/2017 (11/2017)	12/2024 (01/2026)	304.44 (356)	283.67	86
755	Allahabad-Bamhraul Flyover Construction & 4th Railway Line Project (North Central Railway) (705771) (-) (-)	Uttar Pradesh	04/2019 (10/2020)	03/2026 (03/2026)	494 (494)	410.3	80
756	Mughalsarai-Allahabad, 3rd line (North Central Railway) (705772) (-) (-)	Uttar Pradesh	12/2015 (03/2016)	12/2026 (03/2027)	2649 (2649.44)	2024.65	74
757	Aligarh -Daud Khan Flyover Construction & 3rd Railway Line Project (CAO/C/NCR) (705774) (-) (-)	Uttar Pradesh	04/2019 (09/2020)	01/2025 (03/2027)	758 (779.49)	511.12	83
758	Bhandai - Flyover for Etawah bound down train- 10 Km (North Central Railway [NCR] - II) (705777) (-) (-)	Uttar Pradesh	07/2020 (04/2021)	02/2026 (02/2027)	250.18 (250.18)	163.27	9
759	Bhatni-Aurnihar with electrification excluding Indara-Mau (RVNL - I) (705780) (-) (-)	Uttar Pradesh	03/2018 (03/2017)	12/2024 (06/2026)	2529 (2529.46)	2171.72	96.7
760	Barabanki-Malhour 3rd & 4th Railway Line Project (Ministry of Railways) (705782) (-) (-)	Uttar Pradesh	01/2019 (04/2017)	03/2025 (08/2026)	407 (407)	417.22	78
761	Allahabad division - Aligarh - Harduaganj Flyover (North Central Railway) (705918) (-) (-)	Uttar Pradesh	04/2020 (02/2021)	10/2026 (03/2027)	1457 (1457)	400.19	36
762	Rishikesh-Karnaprayag New Rail Line- 125 km (RVNL - II) (705429) (-) (-)	Uttarakhand	11/2016 (08/2018)	12/2025 (12/2028)	38953 (38953)	28828.18	77.5
763	Kalinarayanpur-Krishnanagar Doubling Alongwith Krishnanagar - Chapra New Line And Naihati-Ranaghat 3rd Line. (Eastern Railway [ER] - I) (400247) (-) (-)	West Bengal	07/2015 (11/2005)	02/2027 (03/2028)	1000 (1000)	1066.85	76
764	Tarakeshwar-Bishnupur New Line [82.47 km] (Eastern Railway [ER] - I) (400273) (-) (-)	West Bengal	03/2001 (02/2008)	03/2019 (02/2026)	1189 (1542)	1390.59	96.9
765	Dum Dum Airport-New Garia via Rajarhat-Construction of Metro Railway (RVNL - II) (400277) (-) (-)	West Bengal	03/2010 (10/2011)	12/2025 (12/2027)	8964 (8964)	8984.66	87
766	Construction of Balurghat-Hilli new BG Line (Northeast Frontier Railway [NFR]) (612096) (-) (-)	West Bengal	12/2010 (12/2010)	03/2027 (03/2027)	1209 (1181.57)	518.15	18
767	SER Upgradation of maintenance infrastructure at Shalimar into Vande Bharat Chair Car maintenance cum workshop depot. (South Eastern Railway - JH) (617345) (-) (-)	West Bengal	03/2024 (12/2024)	10/2026 (-)	226.87 (226.87)	86.69	50
768	Joka-BBD Bag new metro project (RVNL - II) (705730) (-) (-)	West Bengal	03/2010 (04/2010)	12/2026 (12/2029)	4835 (10362)	5098.73	51

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
769	Noapara-Barasat via Bimanbandar - Construction of Metro railway [18 km] (Metro Railway, Kolkata) (706776) (-) (-)	West Bengal	11/2010 (03/2010)	08/2026 (03/2029)	4830 (4830)	3350.62	32.2
770	Baranagar-Barrackpore and Dakshineshwar- Construction of Metro Railway (RVNL - II) (706777) (-) (-)	West Bengal	03/2010 (03/2010)	12/2026 (12/2030)	2298 (2734)	429.56	17
	Total (255)				721177.95	581963.35	
	Ministry of Road Transport & Highways						
	Roads & Highways						
771	Rehabilitation and up-gradation and completion of balance works of the section from Km 107.760 km to 129.445 km After Middle strait to Humphrey, Km 130.600 to 138.300 After Humphrey to Kadamtala of NH-4 Intermediate/2-Lane with hard shoulder in the Union Territory of Andaman & Nicobar Islands on EPC basis Package- IIIA (NHIDCL) (619184) (-) (-)	Andaman & Nicobar	02/2018 (03/2024)	09/2025 (12/2026)	207.45 (376.48)	0	81.32
772	Rehabilitation and up-gradation and completion of balance work of section from Km 155.00 to Km 181.00 End of Jarwa to Rangat of NH -4 Total length 26 Km to Intermediate Lane/2-lane with hard shoulders in the UT of A&N Islands on EPC basis - Package-III.B Balance work (NHIDCL) (619185) (-) (-)	Andaman & Nicobar	02/2018 (05/2024)	10/2025 (03/2027)	183.56 (333.12)	0	50.15
773	Construction of Balance works of Major Bridge over Middle Strait Creek between Km.106.590 to km108.553 of NH-04 connecting South Andaman & Baratang Island in the Union Territory of Andaman & Nicobar Islands on EPC basis (NHIDCL) (619186) (-) (-)	Andaman & Nicobar	03/2015 (05/2024)	02/2026 (12/2026)	262.96 (371.88)	0	12.98
774	Tadipatri Bypass Km 0000 to Km 6285 of 4-Lane on NH-67 in Anantapuramu district of AP state under NHO on EPC Mode under Annual Plan 2022-23 (MoRTH) (617949) (-) (-)	Andhra Pradesh	03/2023 (03/2024)	03/2026 (03/2026)	159.66 (159.66)	75.64	100
775	Gudivada Town 2 RoB, and Road improvement NH-165 (MoRTH) (617984) (-) (-)	Andhra Pradesh	03/2022 (05/2023)	05/2025 (03/2027)	317.22 (317.22)	0	75.2
776	Widening to two lane with paved shoulders from Km 0/0 to 64/020 Pamaru to Akiveedu (MoRTH) (617985) (-) (-)	Andhra Pradesh	03/2020 (11/2021)	11/2023 (05/2027)	529.54 (588.65)	0	74.41
777	Kurnool/Kadapa Border-Jammalamadugu section of NH-167K i.e. Design Ch. Km 248010 to km 269900 to 2 (MoRTH) (617986) (-) (-)	Andhra Pradesh	03/2023 (12/2024)	12/2026 (12/2026)	292.63 (292.63)	0	95.77
778	Nandyala-Kurnool/Kadapa Border section of NH-167K i.e. Km 186/000 to Km 250/000Design Ch.186000 to 248010 to 2LPS (MoRTH) (617987) (-) (-)	Andhra Pradesh	10/2024 (09/2025)	09/2027 (09/2027)	691.81 (691.81)	0	46.45
779	Sangameswaram - Atmakuru section from Km 96 to Km 124 & Velegodu- Nandyal section including Nandyal Bypass from Km 143/6 to 185/9 NH-167K (MoRTH) (617988) (-) (-)	Andhra Pradesh	10/2024 (07/2025)	07/2027 (07/2027)	776.17 (644.14)	0	35.6
780	Rehabilitation and up-gradation of NH-167 from Km 14/900 to Km70/000 Design Ch. 14/900 to 69/700 Chintakunta to Adoni section to two lane with paved shoulders in the State of Andhra Pradesh under Corridor Approach through Engineering, Procurement (MoRTH) (617991) (-) (-)	Andhra Pradesh	11/2016 (05/2017)	05/2019 (12/2026)	290.15 (290.15)	141.83	91.9
781	4-laning of Puttaparthi-Koduru Section of NH-342 (MoRTH) (618013) (-) (-)	Andhra Pradesh	10/2022 (11/2023)	11/2025 (08/2026)	1318.59 (909.19)	464.06	90.19
782	Rehabilitation and Up-gradation of existin of road from 2-lane to 2-lane with paved shoulders from km. 0.00 to km 53.590 total length-53.590 km of Raychoti to Vempalli section of NH-440 in the State of Andhra Pradesh on EPC mode. (MoRTH) (618037) (-) (-)	Andhra Pradesh	12/2021 (05/2022)	05/2024 (09/2026)	439.82 (359.52)	213.04	86.54
783	Gorantla - Hindupur section from Km 120/300 to 165/000 of NH716G in the State of Andhra Pradesh (MoRTH) (618052) (-) (-)	Andhra Pradesh	10/2024 (08/2025)	08/2027 (08/2027)	808.7 (808.7)	0	28.78
784	Muddanur to B. Kothapalli section of NH-716G from Km. 0/000 to Km. 56/500 56.500 Km in the State of Andhra Pradesh on EPC mode Job no. 741 (MoRTH) (618053) (-) (-)	Andhra Pradesh	10/2024 (08/2025)	08/2027 (08/2027)	1019.97 (1019.97)	0	30.55
785	Kondamodu to Perecherla Section Design Ch. Km 000 to Km 49917 of NH-167AG to to 4LPS (MoRTH) (618101) (-) (-)	Andhra Pradesh	10/2024 (04/2025)	04/2027 (04/2027)	881.61 (881.61)	0	37.95

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
786	Rehabilitation and upgradation from Km 22300 to 58635 of MudireddyPalle to Kadapa/Nellore Border via porumamilla Section of NH 167 Two Lane with paved Shoulder in (MoRTH) (618103) (-) (-)	Andhra Pradesh	03/2022 (10/2024)	04/2026 (07/2026)	279.29 (279.29)	168.7	90.33
787	Rehabilitation and upgradation of NH 326A from km 0/0 to 41/979 excluding km 2/255 to 3/372 and km 36/820 to 38/275 Odisha border to Narasamapeta to two lane with paved Shoulders in the State of Andhra Pradesh under NHO on EPC Mode (MoRTH) (618125) (-) (-)	Andhra Pradesh	03/2018 (09/2018)	03/2020 (10/2025)	228.32 (228.32)	0	100
788	Widening of Existing Road to Two Lane with Paved Shoulder Configuration from Km 0.00 to 26.000 & Km 45.200 To 59.622 Of NH 365BB in the State of Andhra Pradesh Under Annual Plan 2023-24 through EPC Mode (MoRTH) (618193) (-) (-)	Andhra Pradesh	01/2024 (04/2025)	12/2026 (12/2026)	368.63 (368.63)	62.43	22.55
789	Rehabilitation and upgradation of New NH 544DD from design Chainage Km. 56/000 to 102/20 of Kalyandrg - Molakalmuru Section (MoRTH) (618194) (-) (-)	Andhra Pradesh	03/2018 (08/2018)	02/2020 (09/2025)	294.13 (285.29)	312.4	98.52
790	Rehabilitation and Up-gradation of Dhindi - Digamarru section from Km 126/510 to Km 135/740 of NH -214 New NH -216 and digamarru -Losari section from Km 0/000 tp Km 34/230 of NH-214 A New Nh-216 to two lane with paved shoulder in the state of AP-NH (MoRTH) (618236) (-) (-)	Andhra Pradesh	02/2016 (05/2016)	05/2018 (11/2023)	316.06 (288.76)	222.43	100
791	Rehabilitation and Up-gradation of Thimmapuram to Gurajanapalli section from Km 26/150 to Km 41/161 of NH - 214 New NH - 216 to two lane with paved shoulder in the state of Andhra Pradesh under NHDP-IV (MoRTH) (618238) (-) (-)	Andhra Pradesh	08/2016 (01/2017)	07/2018 (09/2026)	350.61 (432.91)	233.93	98.2
792	Rehabilitation & Upgradation of NH214 New NH-216 from Km 34/230 to Km 84/550 Losari to Machavaram Section to two lane with paved shoulder in the state of Andhrapradesh under NHDP-IV through Engineering, Procurement& Construction EPC mode. (MoRTH) (618239) (-) (-)	Andhra Pradesh	03/2016 (09/2016)	09/2018 (07/2025)	445.22 (459.37)	0	98.6
793	Construction of Paderu bypass Km 0000 to Km 13000 of 2- lane with paved shoulder on NH-516E (MoRTH) (618254) (-) (-)	Andhra Pradesh	03/2023 (01/2025)	07/2026 (12/2026)	244.43 (244.43)	21.96	13
794	Two laning with paved shoulders of Lambasingi to Paderusection of NH 516E (MoRTH) (618255) (-) (-)	Andhra Pradesh	04/2020 (11/2023)	11/2025 (03/2027)	361.24 (358.05)	145.94	43.22
795	Rehabilitation and Upgradation to 2-lane with paved should ders Sir, configuration of Chaprathipalem to Lambasingi section Km 165500 to Km 205000 of NH-516E in the State of Andhra Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode (MoRTH) (618256) (-) (-)	Andhra Pradesh	08/2020 (10/2022)	10/2024 (07/2026)	311.22 (311.22)	211.05	91.25
796	Rehabilitation and Upgradation to 2-lane with paved shoulders configuration of Koyyuru to Chaprathipalem section Km 120000 to Km 165500 of NH-516E in the State of Andhra Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode (MoRTH) (618257) (-) (-)	Andhra Pradesh	08/2020 (07/2022)	07/2024 (07/2026)	349.29 (349.29)	264.81	100
797	Construction of i Connecting Road from Z-Morh Tunnel to Zojila Tunnel Road Length 18.475km and ii 14.150 Km long 2-L Bi-directional single tube Zoji-la Tunnel across Zojila Pass on Sonamarg - Kargil section from Km 82 to Km 118 of NH-01 under PMDP (NHIDCL) (618412) (-) (-)	Andhra Pradesh	01/2018 (10/2020)	09/2026 (02/2028)	6808.69 (6808.69)	3549.07	68.8
798	Bangalore Chennai Expressway Phase-II Pkg-II from km.96.000 to Km 127.000 Baireddypalle to Bangarupalem section (NHAI) (618475) (-) (-)	Andhra Pradesh	02/2021 (06/2023)	06/2025 (10/2026)	2548.04 (2548.04)	1327.64	93.32
799	Bangalore Chennai Expressway Phase-II Pkg-III from km.127.000 to Km 156.000 Bangarupalem to Gudipala section (NHAI) (618476) (-) (-)	Andhra Pradesh	11/2020 (10/2022)	10/2024 (08/2026)	1407.33 (1407.33)	868.61	99.46
800	Construction of 6 lane elevated corridor including its approaches from Km. 629880 to Km. 634470 Design Chainage of NH-16 in Ranasthalam Town portion in the state of Andhra Pradesh on EPC Mode under NHO. (NHAI) (618524) (-) (-)	Andhra Pradesh	07/2024 (03/2025)	03/2027 (08/2027)	257.98 (192.85)	55.83	35.63
801	Construction of flyover at Gammon Junction at Km.903.265 on NH16 including vent at Diwancheruvu junction at Km.902.308 Blackspot ID No.AP03299 in Andhra Pradesh on EPC mode under NHO (NHAI) (618525) (-) (-)	Andhra Pradesh	03/2025 (10/2025)	10/2027 (10/2027)	326.61 (223.29)	43.67	18.79

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
802	6L of Gundugolanu Design km 1023.280 to Kalaparru Design km 1050.680 of NH-5 New NH-16 (<i>NHAI</i>) (618526) (-) (-)	Andhra Pradesh	10/2018 (01/2020)	07/2021 (08/2026)	665.59 (665.59)	643.95	95.73
803	6L of Anandapuram Pendurthi Anakapalli Section from km. 681.000 to km. 731.780 of NH-16 (<i>NHAI</i>) (618579) (-) (-)	Andhra Pradesh	01/2018 (01/2019)	07/2021 (07/2026)	2527 (2957.25)	2376.08	100
804	Nandigama Bypass and Kanchikacherla bypass (<i>NHAI</i>) (618629) (-) (-)	Andhra Pradesh	11/2017 (03/2018)	06/2019 (09/2026)	416.07 (444.58)	387.77	98.47
805	4L of Kadapa China Orampadu section of NH-716 Package I of Kadapa-Renigunta section (<i>NHAI</i>) (618633) (-) (-)	Andhra Pradesh	12/2022 (03/2026)	03/2028 (03/2028)	1732.66 (1732.66)	105.77	2.3
806	6L Korlam-Kantakapalle Section of NH-130CD Road from Km 421.100 to Km 445.100 Pkg-3 (<i>NHAI</i>) (618682) (-) (-)	Andhra Pradesh	02/2021 (02/2022)	02/2024 (07/2026)	1112.7 (1127.63)	849.97	99.5
807	Renigunta - Poyya - Naidupeta km 124.60 to km 183.4 of NH 71 (<i>NHAI</i>) (618700) (-) (-)	Andhra Pradesh	03/2020 (01/2022)	01/2024 (09/2026)	1863.09 (2510.14)	1677.08	98.6
808	6L Access Controlled Greenfield Highway from Kodur Ch. 0000 to Vanavolu Ch. 24300 of [NH-544G] Package-1 (<i>NHAI</i>) (618712) (-) (-)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (03/2027)	912.94 (798.25)	357.89	86.63
809	6L Access Controlled Greenfield Highway from Yerragudipadu Ch. 129000 to Audireddipalle Ch. 160000 of [NH 544G] Package-6 (<i>NHAI</i>) (618713) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (11/2027)	1200.42 (1019.69)	282.03	45.04
810	6L Access Controlled Greenfield Highway from Nallacheruvu palli Ch. 96300 to Yerragudipadu Ch. 129000 of [NH-544G] Package-5 (<i>NHAI</i>) (618714) (-) (-)	Andhra Pradesh	02/2022 (02/2024)	02/2026 (06/2027)	1253.26 (1095.78)	388.46	65.04
811	6L Access Controlled Greenfield Highway from Odulapalle Ch. 72000 to Nallacheruvu-palli Ch. 96300 of [NH-544G]Package-4 (<i>NHAI</i>) (618715) (-) (-)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (04/2027)	1058.9 (946.1)	403.17	75.92
812	6L Access Controlled Greenfield Highway from Vankarakunta Ch. 45700 to Odulapalle Ch. 72000 of [NH-544G]Package-3 (<i>NHAI</i>) (618716) (-) (-)	Andhra Pradesh	12/2022 (03/2024)	03/2026 (03/2027)	992.91 (888.07)	320.05	77.21
813	6L Access Controlled Greenfield Highway from Vanavolu Ch. 24300 to Vankarakunta Ch. 45700 of [NH-544G] Package-2 (<i>NHAI</i>) (618717) (-) (-)	Andhra Pradesh	01/2023 (03/2024)	03/2026 (02/2027)	750.81 (626.91)	250.23	86.13
814	6L Access Controlled Greenfield Highway from Kavulakuntla Ch. 196000 to Narayanmpet Ch. 203500Package-09 (<i>NHAI</i>) (618718) (-) (-)	Andhra Pradesh	02/2023 (02/2025)	02/2027 (12/2027)	1092.18 (956.4)	200.13	47.73
815	6L Access Controlled Greenfield Highway from Mallapalle Ch. 176000 to Kavulakuntla Ch. 196000 Package-08 (<i>NHAI</i>) (618719) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (07/2027)	909.02 (751.81)	289.88	60.57
816	6L Access Controlled Greenfield Highway from Audireddipalle Ch. 160000 to Mallapalle Ch. 176000Package-07 (<i>NHAI</i>) (618720) (-) (-)	Andhra Pradesh	02/2023 (03/2024)	03/2026 (04/2027)	987.1 (848.06)	338.11	70.51
817	6L Access Controlled Greenfield Highway from Chandrasekharapuram Ch. 228000 to Polavaram Ch. 260000of [NH-544G] Package-11 (<i>NHAI</i>) (618721) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (08/2027)	1292.65 (1110.33)	337.78	60.8
818	Khammam-Devarapalle Pkg V [4L Access Controlled Greenfield from Gurvaygudem village to Devarapalle village Design Chainage 132664 to 162126 (<i>NHAI</i>) (618749) (-) (-)	Andhra Pradesh	12/2020 (09/2022)	09/2024 (07/2026)	711.94 (926.48)	566.96	100
819	4L PS Mydukur - Badvel from Km 585.820 to Km 630.960 of NH-67 (<i>NHAI</i>) (618759) (-) (-)	Andhra Pradesh	05/2022 (09/2023)	09/2025 (10/2026)	1063.57 (1103.87)	585.5	90.4
820	4L of Pileru to Kalur Section from Km 55.900 to Km 92.800 & Km 94.500 to Km 95.717 of NH-71Package-II (<i>NHAI</i>) (618777) (-) (-)	Andhra Pradesh	03/2022 (10/2023)	11/2025 (08/2026)	1877.47 (592.85)	246.41	98.84

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
821	4L of Madanapalle to Pileru Section from Km 0.000 to Km 55.900 of NH-71Package-I (NHAI) (618778) (-) (-)	Andhra Pradesh	02/2022 (01/2023)	01/2025 (07/2026)	1877.47 (1994.1)	1182.65	94.9
822	Development of 4L Road from Samarlakota to Achampeta Junction as part of Kakinada Port Connectivity to NH-16 Rajanagaram Junction in East Godavari District (NHAI) (618803) (-) (-)	Andhra Pradesh	09/2022 (08/2023)	08/2025 (12/2026)	645.63 (750.2)	680.06	92.1
823	Dedicated Port road to Krishnapatnam Port Package-I from Km. 0.000 to Km. 18.000 (NHAI) (618804) (-) (-)	Andhra Pradesh	03/2018 (12/2018)	12/2020 (03/2027)	348.72 (341.36)	303.73	78.95
824	6L Connectivity to Port Road from Sabbavaram Sheelanagar-NH516C (NHAI) (618805) (-) (-)	Andhra Pradesh	12/2024 (02/2026)	02/2028 (02/2028)	977.33 (977.33)	127.79	6.3
825	Improvement of 4L road to 6L road and 4L dedicated Port Roads for the Port connectivity road from Convent junction to Sheelanagar Junction (NHAI) (618806) (-) (-)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (12/2026)	685.99 (680.21)	478.52	79
826	4L Greenfield Road connecting North and South industrial cluster of Khandaleru Creek near Krishnapatnam port at Thamminapatnam to Mollur from Km 0.0 to Km 16.046, Part I & 6L extension of dedicated port road of NH-67 Km 18.0 to Km 19.3, Part II (NHAI) (618807) (-) (-)	Andhra Pradesh	08/2022 (09/2023)	09/2025 (01/2027)	609.43 (559.98)	552.88	81.81
827	4 Laning of NH-544D from Km 0.000 to km 37.000 of Anantapur- Muchukota section Pkg-1 (NHAI) (618826) (-) (-)	Andhra Pradesh	10/2022 (07/2023)	07/2025 (08/2026)	907.76 (905.98)	468.12	91.97
828	4 Laning of NH-544D from Km 37.000 to km 69.000 of Muchukota- Bugga section Pkg-2 (NHAI) (618827) (-) (-)	Andhra Pradesh	10/2022 (08/2023)	08/2025 (12/2026)	1097.57 (1055.23)	466.89	82.05
829	Access Controlled Highway of 4 Lane with Paved Shoulders from TN/AP Border Design Chainage Km 6151 to Puttur Design Chainage Km 81540 of NH-716 & 6 Lane with Paved Shoulders from Mallavaram to Renigunta (NHAI) (618920) (-) (-)	Andhra Pradesh	03/2024 (12/2024)	12/2026 (03/2027)	1346.82 (1260.37)	188.66	39.57
830	Six Laning of Vijayawada Bypass from Chinna Avutapalli to Gollapudi in Vijayawada - Gundugolanu Section from km. 0.00 to km. 30.00 Pkg-III (NHAI) (619076) (-) (-)	Andhra Pradesh	01/2020 (02/2021)	02/2023 (09/2026)	1581.24 (1883.71)	1024.75	98.2
831	4 L of China Orampadu-Renigunta section of NH-716 Package-II of Kadapa-Renigunta section (NHAI) (619102) (-) (-)	Andhra Pradesh	12/2022 (03/2026)	03/2028 (03/2028)	1500.11 (1500.11)	120.46	0
832	6L Jakkuva Korlam Section of NH-130CD Road from km 396.800 to km 421.100 Pkg 2 (NHAI) (619111) (-) (-)	Andhra Pradesh	02/2021 (03/2022)	03/2024 (07/2026)	840.51 (840.51)	573.89	99.5
833	6L Kantakapalle Sabbavaram Section of NH-130CD Road from Km 445.100 to Km 464.662 Pkg-4 (NHAI) (619112) (-) (-)	Andhra Pradesh	02/2021 (10/2022)	10/2024 (12/2026)	1012.57 (1012.57)	702.32	84
834	6L Access Controlled Greenfield Highway from Narayanmpet Ch. 203500 to Chandrasekharpuram Ch. 228000Package-10 (NHAI) (619123) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (07/2027)	813.66 (678.21)	223.05	66.12
835	6L Access Controlled Greenfield Highway from Polavaram Ch. 260000 to Marripudi Ch. 285500 of [NH-544G]Package-12 (NHAI) (619124) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (05/2027)	747.29 (626.83)	242.62	70.2
836	6L Access Controlled Greenfield Highway from Somavarappadu Ch.314.600 to Muppavaram Ch.343240 of [NH-544G] Package-14 (NHAI) (619125) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (10/2027)	1103.9 (943.66)	259.07	44.56
837	6L Access Controlled Greenfield Highway from Marripudi Ch. 285500 to Somavarappadu Ch. 314600 of [NH-544G] Package-13 (NHAI) (619126) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (04/2027)	976.41 (798.71)	370.82	73
838	6L of Naidupeta Junction - Turpukanupur Section from km 57.046 to km 91.927 (NHAI) (619140) (-) (-)	Andhra Pradesh	08/2022 (10/2023)	10/2025 (10/2027)	1398.84 (965.58)	374.07	48.9

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
839	Construction of four lane access controlled highway from Chillakuru cross road to Turpu KanupurPart 1 of Package - II km 0.000 131.500 of NH - 16 to km 23.770 on New NH-516W including six lane flyover and approaches on NH-16 length km 1.050 and six lane access controlled from Turpu Kanupur to Port South Gate Part 2 of Package - II km 23.770 to km 35.015 on New NH-516W in the state of Andhra Pradesh on HAM Mode under Bharatmala Pariyojana Phase I (NHA) (619141) (-) (-)	Andhra Pradesh	08/2022 (12/2023)	12/2025 (03/2026)	864.2 (844.39)	358.97	54.11
840	Balance works in AP Portion and punch list items in TN & AP portion of NH-205 (NHA) (619160) (-) (-)	Andhra Pradesh	10/2022 (07/2023)	01/2025 (01/2026)	166.52 (113.46)	98.52	100
841	Construction of 2-lane road of Potin to Pangin section of NH-13 from Km 163.59 to Km 206.66 Package-5 on EPC Mode in the State of Arunachal Pradesh under Arunachal Pradesh Package of Roads and Highways of SARDP-NE [Job No SARDP-NE/P-P/Pkg-A/NH-13/Ar.Pr./PWD/2018-19/116] (MoRTH) (617892) (-) (-)	Arunachal Pradesh	03/2019 (11/2020)	11/2023 (07/2026)	450.65 (450.65)	345.01	96.61
842	4-Laning of Itanagar to Bandardewa section of NH-415from km 40430 to km 51735 Package-Bon EPC Mode in the state of Arunachal Pradesh Job NO. 415/Ar. P/2020-21/031 (MoRTH) (618033) (-) (-)	Arunachal Pradesh	06/2020 (12/2021)	12/2024 (07/2026)	496.47 (496.47)	171.91	51.37
843	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang Package-III from design Km 60.000 to Km 121.500 Design Length 61.500 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Pkg-3 (NHIDCL) (618401) (-) (-)	Arunachal Pradesh	02/2024 (07/2025)	07/2028 (07/2028)	1418.67 (1418.67)	0	1.7
844	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang from Design Km 0.000 to Km 53.000 Design Length 53.000 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Package-I (NHIDCL) (618402) (-) (-)	Arunachal Pradesh	02/2024 (03/2025)	02/2028 (03/2028)	1262.43 (1262.43)	245.19	18.1
845	Construction of Intermediate Lane Road with hard shoulder from design Km 0.000 to Km 17.387 Total length 17.387 km of Hunli to Ithun Bridge section on NH-913 Frontier Highway in State of Arunachal Pradesh on EPC mode under NHO-NE (NHIDCL) (618403) (-) (-)	Arunachal Pradesh	02/2024 (01/2025)	01/2027 (01/2027)	275.5 (275.5)	0	54.11
846	Construction of Intermediate Lane Road with hard shoulder from design chainage Km 0.000 to Km 53.040 Existing Length68.500 Km & Total Design length 53.04 km of Tato to Monigong section of NH-913 Frontier Highway on Nafra Bomdila to Vijaynagar along China border in state of Arunachal pradesh on EPC mode (NHIDCL) (618404) (-) (-)	Arunachal Pradesh	12/2023 (05/2025)	11/2027 (11/2027)	625.61 (625.61)	0	21.97
847	Construction of Intermediate Lane of Pango to Jorging Road from 0000 to Design Km Design Km 40000 Design Length 40.00 Km, Pkg-I, Greenfield Alignment in the State of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (618405) (-) (-)	Arunachal Pradesh	01/2024 (01/2025)	07/2027 (07/2027)	898.19 (898.19)	0	39.8
848	Construction of Balance work of 2-Lane with PS of Joram Koloriang Road from existing Km122.600 to km138.00 [Design Km108.724 to Km123.714] in Arunachal Pradesh on EPC Mode under SARDP-NE Pkg-7 (NHIDCL) (618433) (-) (-)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (04/2026)	184.89 (184.89)	0	99.69
849	Roing-Hunli Road Greenfield Alignment Project (NHIDCL) (618434) (-) (-)	Arunachal Pradesh	02/2017 (03/2018)	03/2022 (10/2026)	1718.59 (1718.59)	189.24	82.32
850	Construction of 2-Laning with hard shoulders of Demwe-Brahmakund section of NH-13 from Ch.0.00 km to 18.464 km on EPC under SARDP-NE NHO-NE -Balance Work (NHIDCL) (618445) (-) (-)	Arunachal Pradesh	08/2020 (06/2025)	12/2027 (12/2027)	353.9 (353.9)	0	19.55
851	Improvement and Widening to 2 lane with paved Shoulder of NH-15 old NH-52 from Existing Km 770.600 Design Km 24.819 to Existing km 805.750 Design Km 59.885 Kamlang T-Junction to Chowkham, Existing Length 35.150 Km, Design Length-35.066 Km in the state of Arunachal Pradesh on EPC mode Pkg-2 (NHIDCL) (619014) (-) (-)	Arunachal Pradesh	12/2023 (02/2026)	02/2028 (02/2028)	316.73 (316.73)	0	11.74
852	Improvement and Widening to 2-lane with Paved Shoulder of NH-13 & 15 Old NH-52 from Existing Km 745.60 Design Km 0.000 to Existing km 770.600 Design Km 24.819 Brahmakund T-junction to Kamlang T-Junction, Existing Length 25.00 Km, Design Length 24.819 Km in the state of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (619248) (-) (-)	Arunachal Pradesh	12/2023 (06/2026)	06/2028 (-)	441.41 (441.41)	0	0
853	Construction of Mangaldoi Bypass NH-15 starting at Ch 26400 and terminating at Ch 41505 under Rangia NH Division L 15.105 Km in the State of Assam. Job No. 15/AS/2021-22/234 (MoRTH) (617895) (-) (-)	Assam	03/2022 (04/2023)	04/2025 (12/2026)	535.03 (535.03)	209.27	75.82

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
854	Construction of 4 lane Gauripur Bypass Starting bfrom Km 852.56 of NH-31Dumardoha Pt-II and Terminating at Km 862.17 Baladmara via. Khudimari Pt.- II, Fulkumari, Charaldanga, Sajuakuti,Geramari Pt.-III and finally meeting at km 862.17 of NH-17New/ NH-31Old in the State of Assam under EPC Mode Job no. 31/AS/ 2023-24/265 (MoRTH) (617896) (-) (-)	Assam	03/2024 (04/2025)	10/2026 (10/2026)	421.15 (421.15)	0	20.8
855	Construction of 2 lane Barpeta Bypass from Km 77900Baradi to Km 86150 Deurikuchi Length8.25Km on NH-427 in the state of Assam under EPC ModeJob No.427/AS/2022-23/245 (MoRTH) (618034) (-) (-)	Assam	03/2023 (02/2025)	08/2026 (08/2026)	173.65 (173.65)	11.38	20
856	Construction of new 2 Lane with paved shoulders of NH Standards from km 0.080 to km 11.690 L11.610 km in Majuli and from km 19.715 to km 27.484 L 7.769 km in Jorhat on the newly declared NH 715K and construction of 1.10 km flyover on NH-715 with its approaches and service roads L1.10 km, Total Length 20.479 km in the State of Assam Job No. 715K/AS/2023-24/256 (MoRTH) (618159) (-) (-)	Assam	02/2024 (09/2025)	03/2027 (03/2027)	382.1 (382.1)	26.05	6.3
857	Construction of 2 lane Major Bridge including approaches over Brahmaputra between Majuli on North Bank and Jorhat on South Bank from km. 11.690 to km. 19.715 length of bridge 6,812.5m Package - II on NH-715K in the state of Assam Job no. 715/AS/2020-21/213 (MoRTH) (618160) (-) (-)	Assam	03/2025 (12/2025)	12/2027 (12/2027)	1019.17 (1019.17)	0	3.25
858	4-L Bilasipara-Guwahati Package-10 (NHIDCL) (618282) (-) (-)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1264.9 (1264.9)	603.33	64.48
859	4-L Bilasipara-Guwahati Package-9 (NHIDCL) (618283) (-) (-)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1000.27 (1000.27)	490.64	59.78
860	Widening/Improvement to 4-Lane with paved shoulder from Km 99930 to Km 143680 Design Chainage 96000 to 139750 of Paikan to Dhupdhara Sahar of Bilasipura-Guwahati Road on NH-17 in the state of Assam on EPC mode under Bharatmala Pariyojana in Economic Corridors Project Length 43.750km under NHO-NE Package-8 (NHIDCL) (618284) (-) (-)	Assam	03/2023 (12/2023)	12/2026 (12/2026)	1457.59 (1457.59)	926.96	85.87
861	Construction of New 2-Lane Bridge with its approaches from km 0000 to Km 4385 across River Brahmaputra on NH-17 at Jogighopa in Assam on EPC mode (NHIDCL) (618286) (-) (-)	Assam	09/2021 (11/2021)	11/2024 (12/2026)	746.76 (746.76)	426.91	81.07
862	Widening/Improvement to 4-Lane with paved Shoulder from Ch. 25.633 Km to Ch. 52.470 Km Design Ch. 21.850 Km to Ch.48.670 Km for Package-2 of Bilasipura-Guwahati road NH-17 Section Near Mowatari, before Chapar Bypass to Tulungia junction with NH-17 in the state of Assam on HAM mode under NHO-NE Package-2 (NHIDCL) (618287) (-) (-)	Assam	11/2023 (12/2024)	06/2027 (06/2027)	1338.61 (1338.61)	0	12.45
863	Widening/Improvement to 4-Lane with Paved Shoulder from Ch.5.580 Km to Ch.25.633 Km Design Ch.0.000 Km to Ch.17.737km Km 901.100 to Km 921.145 of old NH-31 of Bilasipara- Guwahati road NH-17 Section Near Chirakuta to near Mowatari, before Chapar Bypass in the state ol Assam on HAM mode Package-1 (NHIDCL) (618288) (-) (-)	Assam	02/2024 (02/2025)	08/2027 (08/2027)	1081.15 (1081.15)	0	32.59
864	Construction and up gradation to 4-Lane of existing two lane with paved shoulder from Hapachara to Tulungia road of NH-117 of existing Km 0.00 to km 14.050 and Design Km 0.000 to km 14.660 under BMP on EPC mode (NHIDCL) (618289) (-) (-)	Assam	03/2020 (06/2020)	12/2022 (03/2026)	224.85 (224.85)	209.94	97.76
865	Construction of 4-Lane Panchgram Bypass from Design Chainage km 15500 on NH-37 Old NH-53 at Kalinagar Pt.-I Village to Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Package-2 (NHIDCL) (618308) (-) (-)	Assam	03/2023 (08/2024)	02/2027 (02/2027)	676.18 (728.97)	0	57.17
866	Widening/Improvement to 4-Laning and Greenfield alignment with Paved shoulder of Silchar-Badarpur Churaibari section of NH-37 & NH-8 from Design chainage 38.600 End point of proposed Badarpur Bypass to Km. 62.800 Start point of proposed Nilambazar/Cheragi Bypass in the state of Assam on HAM Mode Package-4 (NHIDCL) (618309) (-) (-)	Assam	02/2024 (08/2025)	08/2027 (08/2027)	1319.55 (1319.55)	0	25.16
867	Widening/Improvement to 4-L of Karimgani - sutarkandi section of NH 37 from design Ch 0020 Start of proposed Karimganj Bypass from NH -8 to design Chainage Km 14380 near Sutarkandi Spur Connectivity to Indo/Bangladesh Border on Silchar- Churaibari in the State of Assam on HAM Mode Package-7 (NHIDCL) (618310) (-) (-)	Assam	02/2024 (02/2025)	02/2027 (02/2027)	791.79 (791.79)	0.06	41.88

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
868	Widening/Improvement to 4-Lane with Paved shoulder for existing as well as Greenfield alignment of Badarpur Churaibari section of NH-8 from Design chainage 87.700 Chandkhira to Km. 106.500 Churaibari section Assam-Tripura border in the state of Assam on HAM Mode Package-6 (NHIDCL) (618311) (-) (-)	Assam	03/2024 (03/2025)	03/2027 (03/2027)	870 (870)	0	40.99
869	Widening/Improvement to 4-Lane with Paved Shoulder from existing road and Greenfield alignment form Design Ch. 62.800 start of proposed Nilambazar/Cheragi Bypass to Design Ch. 87.700 near Chandkhira Village of NH-8 on Silchar-Churaibari in the state of Assam on HAM Mode Package-5 (NHIDCL) (618312) (-) (-)	Assam	02/2024 (04/2025)	10/2027 (10/2027)	1258.13 (1258.13)	0	14.04
870	Widening/Improvement of Existing 2 lane to 4-Laning of Karimganj-Silchar section of NH-37 from Design Ch 0.000 near Silchar ISBT to Design Ch 15.970 near Kalinagar Pt I on NH-37 in Assam on HAM Mode Pkg-1 (NHIDCL) (618313) (-) (-)	Assam	03/2024 (09/2025)	09/2027 (09/2027)	1181.55 (1181.55)	0	41.26
871	4-Laning of Dhanehari Lailapur / Vairengte section from Existing Chainage km 12920 to km 43000 of NH 306 Design Chainage km 20000 to km 49360 on Silchar - Vairengte Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode. Project Length 29.360 km under NHO-NE Package-2 (NHIDCL) (618314) (-) (-)	Assam	03/2023 (02/2024)	08/2026 (08/2026)	1716.21 (1716.21)	970.37	81.65
872	4-Laning of Silchar - Dhanehari section from Existing Chainage km 263800 of NH 37 to km 12920 of NH 306 Design Chainage km 0000 to km 20000 on Silchar - Vairengte - Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode Package-1 (NHIDCL) (618315) (-) (-)	Assam	02/2023 (01/2024)	07/2026 (07/2026)	1256.9 (1256.9)	575.03	59.65
873	Dillai to Lahorijan Package-7 (NHIDCL) (618325) (-) (-)	Assam	11/2021 (01/2023)	07/2024 (04/2026)	204.1 (204.1)	142.21	0
874	Widening/Improvement to 4-Lane with Paved Shoulder from KM 38500 to Km 51246 Design Chainage 38500 to 50959 with proposed Daboka Bypass of Daboka- Parokhaowa of NH 29 on EPC under NHO-NE Package-1 (NHIDCL) (618326) (-) (-)	Assam	01/2023 (11/2023)	11/2025 (06/2026)	516.88 (516.88)	0	99.7
875	Improvement to 4-Lane with Paved Shoulder from existing km 260000 Design Ch.4560 km to existing km Ch.233000 D. Ch.24560 of Silchar near Nutan Dayapur village - Budha Nagar Section Length-20.00 Km of NH-37 under Package Silchar-Jiribam Pkg-1 in the state of Assam on HAM Mode (NHIDCL) (618331) (-) (-)	Assam	01/2024 (01/2025)	01/2028 (01/2028)	957.95 (957.95)	165.23	47.27
876	Widening/Improvement to 2-Lane Lane with Paved Shoulder from km 16900 Bogapani to km 27150 Golai Goan on existing Dibrugarh to Ledo section with proposed Digboi Bypass Green Field and Brownfield 2-LanePS of NH-315 OLD NH-38 in Tinsukia District under NHO- NE Package-4 (NHIDCL) (618339) (-) (-)	Assam	01/2023 (12/2023)	12/2025 (12/2026)	356.65 (356.65)	80.08	20.45
877	Widening/Improvement to 4-Lane with Paved Shoulder from km 626030 Nalani hulla Gaon to km 650450 Chotahapjan on existing Tinsukhia -Makum Bypass of NH-15 OLD NH-37 and Strengthening of existing NH-315 OLD NH-38 from Km 0000 Chotahapjan to Km 16900 Bogapani section 2-Lane PS in Assam on EPCMode under NHO-NE Package-3 (NHIDCL) (618340) (-) (-)	Assam	01/2023 (05/2023)	05/2025 (10/2026)	458.59 (458.59)	249.84	88.99
878	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 156.489 near P. Leikul to km 176.410 near Borowapu on EPC mode under NHO-NE Assam portion Package-10 (NHIDCL) (618351) (-) (-)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	890.33 (693.15)	604.86	90.5
879	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 136.500 near Hejaichak to km 156.489 near P. Leikul Package-9 on EPC mode under NHO-NE Package-9 (NHIDCL) (618352) (-) (-)	Assam	03/2023 (08/2023)	08/2025 (07/2026)	860.37 (614.43)	559.69	87.5
880	Widening & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 116.480 near Hangrum to km 136.500 near Hejaichak Package-8 on EPC mode under NHO-NE Package 8 (NHIDCL) (618353) (-) (-)	Assam	03/2023 (08/2023)	08/2025 (09/2026)	904.04 (904.04)	557.37	85.2
881	Wideinig & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 96.870 near Jiri River to km 116.550 near Hangrum Package-7 on EPC mode Package7 (NHIDCL) (618354) (-) (-)	Assam	12/2023 (03/2024)	03/2026 (12/2026)	846.82 (846.82)	0	90.36

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
882	Widening/Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Srirampur near Bhairiguri Village to Kachukhana Harichara Paglagaunj Package-I of Srirampur - Dhubri Section of NH-127B from existing Km 0.000 to Km 28.050 Design Km 0.000 to Km 27.650, Design Length27.650 Km under JICA ODA Loan assistance Phase-V -Balance work (NHIDCL) (618371) (-) (-)	Assam	03/2022 (11/2024)	11/2026 (11/2026)	613.89 (613.89)	384.24	89.5
883	Construction of 4-Lane Bridge including approaches over River Brahmaputra between Dhubri on North Bank,Assam and Phulbari on south Bank,Meghalaya on NH-127B under JICA ODA Loan assistance Phase-III (NHIDCL) (618373) (-) (-)	Assam	05/2019 (12/2020)	09/2028 (09/2028)	4997.04 (4997.04)	3033.59	77.14
884	4-Laning from Rangagara to Kaliabor Tiniali from km 297.00 to km 315.315 of NH-37 on EPC basis under SARDP-NE in state of Assam (NHIDCL) (618435) (-) (-)	Assam	01/2016 (10/2017)	04/2020 (07/2026)	386.51 (386.51)	360.25	97.13
885	4-Laning of Jamugurihat to end of Biswanath Chariali By-Pass from Km 182.000 to Km 208.000 of NH-52 on EPC mode in state of Assam under SARDP-NE (NHIDCL) (618436) (-) (-)	Assam	03/2015 (12/2016)	06/2019 (07/2025)	599 (599)	434.89	100
886	Construction of Balance Work of 4-Laning of NH-37 Section between End of Moran Bypass to Bogibeel junction near Lapetketa Km. 561.700-Km. 580.875 under SARDP-NE, Phase 'A' in the State of Assam on EPC mode Pkg-I Road works & Toll Plaza (NHIDCL) (618437) (-) (-)	Assam	01/2016 (09/2024)	03/2025 (08/2025)	274.34 (274.34)	96.67	100
887	4-Laning of NH-37 Section between Demow to End of Moran Bypass From Km. 534.800 to Km. 561.700 including Emergency Landing Facility ELF under SARDP-NE, Phase 'A' in the State of Assam on EPC mode (NHIDCL) (618438) (-) (-)	Assam	01/2016 (01/2023)	07/2024 (08/2025)	385.57 (385.57)	685.73	100
888	Construction of Balance Work of 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 453000 to Km 463000 10.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618439) (-) (-)	Assam	01/2024 (02/2024)	08/2024 (06/2026)	478.3 (478.3)	0	96.79
889	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 534.800, under SARDP- NE on EPC Mode in the state of Assam Pkg- IV Structures & Toll Plaza (NHIDCL) (618440) (-) (-)	Assam	01/2016 (10/2024)	10/2025 (07/2026)	187.09 (100.22)	0	58.19
890	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 501.800 11.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618441) (-) (-)	Assam	01/2016 (10/2024)	09/2025 (07/2026)	467.79 (476.5)	0	87.33
891	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 477.000 to Km 490800 13.800 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (618442) (-) (-)	Assam	01/2024 (02/2024)	08/2024 (06/2026)	358.72 (358.72)	398.28	100
892	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 463.00 to Km 477.000 14.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-II Road Works (NHIDCL) (618443) (-) (-)	Assam	01/2024 (02/2024)	08/2024 (03/2026)	438.44 (438.44)	0	95.86
893	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 453.000 to Km 490.800, under SARDP- NE , under EPC Mode in the state of Assam Pkg-IV Structures & Toll Plaza (NHIDCL) (618444) (-) (-)	Assam	01/2024 (02/2024)	08/2024 (07/2026)	279.01 (279.01)	398.54	94.73
894	Earthwork in Formation, Road Work, Construction of Bridges, Blanketing, P. Way Linking works including Supply of P. Way Fittings and Track Ballast in connection with Construction of Railway Siding from Jogighopa Railway Station to MMLP at Jogighopa from Ch. 00 to 3760 on Item Rate basis Package -3, Railway Siding from Jogighopa Railway Station to MMLP (NHIDCL) (618454) (-) (-)	Assam	02/2020 (12/2020)	06/2022 (09/2024)	693.97 (693.97)	41.78	93.23
895	Development of External Trunk Connectivity and Internal Infrastructure Works at Multi Model Logistics ParkMMLP at Jogighopa in the State of Assam on EPC Mode Package-I Road and Utility Works (NHIDCL) (618455) (-) (-)	Assam	02/2020 (09/2020)	04/2022 (09/2024)	693.97 (693.97)	310.1	100
896	Guwahati Ring Road in the State of Assam (NHAI) (618934) (-) (-)	Assam	08/2024 (01/2026)	01/2030 (01/2030)	5729.47 (5729.47)	328.42	0
897	2L with ES of Yagyi - Kalewa section from Milepost 40/0 to Milepost 115/5 in Myanmar (NHAI) (618958) (-) (-)	Assam	12/2017 (05/2018)	06/2023 (07/2027)	1200.14 (1200.14)	0	52

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
898	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 501.800 to Km 514.800 13.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-II Road Works (NHIDCL) (619013) (-) (-)	Assam	10/2014 (10/2024)	01/2026 (07/2026)	508.76 (542.87)	111.01	73.88
899	Construction of 4-Lane Badarpur Bypass from Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village to Design Chainage km 38600 on NH-37 Old NH-44 at Kandigram Chaita Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Pkg-3 (NHIDCL) (619057) (-) (-)	Assam	02/2023 (02/2024)	08/2026 (08/2026)	574.26 (574.26)	318.82	71.09
900	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 514.800 to Km 534.800 20.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (619060) (-) (-)	Assam	10/2014 (10/2024)	09/2025 (07/2026)	344.71 (619.7)	54.48	72
901	Balance work of 4L of NarimbangloJatinga Junction- Harangajoroad section from Km 0.000 to Km 49.230 of NH-27 (NHAI) (619089) (-) (-)	Assam	03/2022 (01/2023)	01/2026 (07/2026)	1909.98 (2745.74)	1386.87	94.59
902	Construction of proposed 4Lane Revelgunj bypass NH-19 in the State of Bihar on EPC mode connecting NH 19 to 85 origin (MoRTH) (617897) (-) (-)	Bihar	03/2022 (07/2023)	07/2025 (10/2026)	295.24 (295.24)	44.18	86.02
903	Widening & Strenthening from km132.895 to km 190.15 NH-80 (MoRTH) (617958) (-) (-)	Bihar	03/2021 (11/2022)	11/2024 (08/2026)	566.1 (566.1)	292.35	95.1
904	Gaya-Hisua-Rajgir-Nalanda-Biharsharif section km0.00 to 92.935 NH-82 (MoRTH) (617961) (-) (-)	Bihar	01/2014 (11/2016)	11/2019 (10/2026)	1408.85 (2138.16)	0	97
905	Rehabilitation and Upgrading to 2 lanes/2-lane with paved shoulders configuration and strengthening of of Birpur and Bihpur Section from km 0.0 to Km 106 of NH 106 under phase I of National Highways Interconnectivity Improvement Projects NHIP ICB No. NHIP-BR-106-7 [NHIP-BR-106-7] (MoRTH) (617966) (-) (-)	Bihar	01/2014 (10/2016)	10/2019 (07/2026)	780.77 (961.33)	0.04	99.74
906	Construction of 4 Lane ROB and its approaches at the level crossing LC No 29 B of Km 29 Ekangarsarai at NH 110 New NH 33 & Railway Km 32.63 at Fatwa FUT Islampur IPR section in the state of Bihar on EPC mode. (MoRTH) (617969) (-) (-)	Bihar	03/2023 (07/2024)	07/2026 (12/2026)	201.08 (201.08)	0.01	62
907	Construction of Bhabhua Bypass from Ch. 10800Design Ch. 10800 to Ch. 19860 Design Ch. 18150 and Chand Bypass from Ch. 38060 Design Ch. 36250 to Ch. 40460 Design Ch. 38650 and widening of existing road to 2 - lane with Paved shoulder from Ch. 40460 Design Ch. 38650 to Ch. 46860 Design Ch. 45050 of NH-219 Total length-16.150 Kmunder EPC mode in the state of Bihar (MoRTH) (618004) (-) (-)	Bihar	02/2022 (06/2026)	12/2027 (12/2027)	179.86 (179.86)	2.37	2
908	Sheohar-Sitamarhi Section km 40.000 to 79.400 km Lot-I (MoRTH) (618005) (-) (-)	Bihar	02/2016 (05/2016)	05/2018 (09/2026)	178.85 (278.53)	0	98.65
909	Improvement to Two lane with Paved Shoulder from Junction of NH22 near Hajipur to Junction of NH -122 at Bachhwara via Mahnar and Mohiuddin Nagar from Km 0.00 to Km 29.730 of NH 122 B in the State of Bihar. (MoRTH) (618073) (-) (-)	Bihar	02/2024 (08/2024)	02/2026 (02/2027)	226.16 (226.16)	0	53
910	Pre construction activity of NH 122B from km 0 to 72.348 and Improvement to two lane with paved shoulders of NH 122B from km 29.730 to km 72.348 in state of Bihar under EPC mode (MoRTH) (618074) (-) (-)	Bihar	02/2022 (05/2023)	11/2024 (08/2026)	624.43 (624.43)	154.25	95
911	Improvement to two lane with paved shoulders of BH WB Border Amdabad Manihari section from design Km 0.000 to Km 23.945 of NH 131 A Total length 23.945 Km under EPC mode in the state of Bihar (MoRTH) (618080) (-) (-)	Bihar	01/2022 (05/2025)	11/2026 (06/2027)	353.27 (353.27)	0	7
912	construction of Four-Lane of chausa-Buxar Bypass from Km 45.000 to Km 65.915 Package - 2 in the State of Bihar on EPC Mode. (MoRTH) (618120) (-) (-)	Bihar	09/2022 (01/2026)	01/2028 (01/2028)	1060.16 (1060.16)	0	4
913	Improvement to two lane with paved shoulders of NH-319A from km 0 to km 45 in state of Bihar under EPC mode (MoRTH) (618121) (-) (-)	Bihar	02/2022 (06/2023)	12/2024 (09/2026)	427.29 (427.29)	198.15	93

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
914	Pre-Construction activities from Km 134.000 to Km 190.233 of NH-333A and Construction of 4 no. of Bypasses at Katoria, Lakhpura, Banka & Panjwara total length-14.359 Km to two lane with paved shoulders standard in State of Bihar. (MoRTH) (618126) (-) (-)	Bihar	11/2022 (12/2024)	12/2026 (03/2027)	479.37 (479.37)	67.37	58.1
915	Estimate for Improvement to two lane with paved shoulder from Ramnagar to Roseda from km 3.500 to 43.000 of NH 527 E on EPC mode in State of Bihar (MoRTH) (618146) (-) (-)	Bihar	01/2022 (10/2024)	04/2026 (04/2027)	495.16 (495.16)	0	37
916	construction of a new 4 lane Parallel to existing MG Setu with its appooces from km 0.00 to km 14.500 across river Ganga on NH-19 at Patna in the state of Bihar. (MoRTH) (618228) (-) (-)	Bihar	02/2019 (03/2021)	09/2024 (09/2027)	2926.42 (2926.42)	0	74.93
917	Construction of a new 4-lane major bridge across river Kosi at Phulaut including Rehabilitation and upgradation of existing Birpur and Bihpur section of NH-106 from km 106.000 to km 136.000 to 2-lane with paved shoulders in the State of Bihar on EPC mode (MoRTH) (618234) (-) (-)	Bihar	09/2018 (06/2021)	06/2024 (02/2027)	1478.4 (1478.4)	901.32	97.5
918	Construction of New 4-Lane Bridge Parallel to existing Vikramashila Setufrom km 8920 to Km 13375including approach road 35m Naugachhia side &53 m Bhagalpur sideacross River Ganga on newly declared NH-131B at Bhagalpur in the State of Bihar (MoRTH) (618246) (-) (-)	Bihar	07/2020 (05/2023)	05/2027 (03/2029)	1110.23 (1110.23)	0	51.91
919	Construction of 6-Lane Elevated / Extra Dose Cable Bridge on River Ganga parallel to & Western side of Digha-Sonepur Rail cum-Road Bridge of NH 139W in the State of Bihar (MoRTH) (618250) (-) (-)	Bihar	01/2024 (05/2024)	11/2027 (12/2028)	3064.45 (3064.45)	0	17.24
920	Improvement and Up gradation to four lane with Paved shoulder configuration from Existing Km 0000 to Km 39500 design km 0500 to Km 40342, Design length km of NH 227A near Mehrauna GhatUP Bihar Border to Siwan on the state of Bihar on Hybrid Annuity Model HAM basis (MoRTH) (618251) (-) (-)	Bihar	03/2023 (09/2025)	03/2028 (03/2028)	1661.25 (1661.25)	0.83	7.89
921	Balance work - WB-10 Gandak Bridge Km 402.00 to Km 440.00 Devanpur - Kotwa (NHAI) (618569) (-) (-)	Bihar	11/2021 (07/2022)	01/2024 (02/2027)	210.05 (358.3)	181.96	64.05
922	Permanent rectification of 3 nos. of black spots in project Highway NH-27 of U.P border - Dewapur - Kotwa section from Km.360.915 to km.440.000 Total Length of 79.085 Km of NH-27& Permanent rectification of 5 nos. of black spots of project Highway NH-27 of Kotwa - Mehsi - Muzaffarpur Section from km.440.000 to km.520.000 Total length 80.00Km (NHAI) (618571) (-) (-)	Bihar	04/2022 (12/2023)	12/2025 (10/2026)	227.25 (321.23)	233.7	83
923	6L Greenfield Varanasi-Ranchi-Kolkata Highway from Pachmon village to Anarbansalea village From KM. 116000 to KM. 151200 Package-6 (NHAI) (618725) (-) (-)	Bihar	03/2023 (09/2025)	09/2027 (09/2027)	1915.99 (1920.21)	405.1	23.77
924	6L Greenfield Varanasi-Ranchi-Kolkata Highway from junction with Chandauli-Chainpur Road near Khainti village to junction with Bhabhua-Adhaura road near Palka village from Km. 27.000 to Km. 54.000 Pkg-2 (NHAI) (618726) (-) (-)	Bihar	03/2023 (10/2025)	10/2027 (10/2027)	1240.93 (1341.52)	244.38	25.37
925	6L Greenfield Varanasi-Ranchi-Kolkata Highway from junction with Bhabhua-Adhaura road in Bhairpur village to Konki village From KM. 54.000 to KM. 90.000Pkg-3 (NHAI) (618727) (-) (-)	Bihar	03/2023 (10/2025)	10/2027 (10/2027)	1576.94 (1711.44)	313.1	22
926	6L Bridge and its approaches across River Ganga as Part of Patna Ring Road NH-131G starting from Km 8.480 near Sherpur to Km 23.000 near Dighwara (NHAI) (618738) (-) (-)	Bihar	09/2022 (09/2023)	09/2027 (03/2029)	6291.69 (3351.62)	733.93	21.21
927	4L Greenfield Alignment of Amas to Shivrampur from 0.000 Km. to 55.002 Km. of NH 119 D Pkg-I (NHAI) (618739) (-) (-)	Bihar	02/2022 (03/2023)	03/2025 (07/2027)	1390.92 (1427.43)	604.49	54.1
928	4L Greenfield Alignment of Shivrampur to Ramnagar from Km. 55.002 to Km. 109.300 of NH 119 D Pkg-II (NHAI) (618740) (-) (-)	Bihar	02/2022 (07/2023)	07/2025 (11/2027)	1494.31 (1546.07)	664.55	50.15
929	4L Greenfield Alignment from Kalyanapur to Tal Dashraha of NH-119D Pkg-III (NHAI) (618741) (-) (-)	Bihar	03/2022 (02/2023)	02/2025 (03/2028)	1857.58 (1969.3)	929.35	33.48
930	Construction of 6-lane Greenfield corridor from Ramnagar to Kacchi Dargah NH-119D from Km 109700 to Km 122300, including widening of the existing NH-31 from Km 196700 to Km 198600, as part of the Amas-Darbhanga. (NHAI) (618742) (-) (-)	Bihar	01/2025 (04/2026)	04/2028 (04/2028)	1113.46 (1113.46)	12.43	0.5

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
931	Ara Bypass (NHAI) (618775) (-) (-)	Bihar	03/2025 (10/2025)	04/2027 (04/2027)	226.32 (226.32)	5.62	24.84
932	Construction of four laning of Bakarpur- Manikpur road section starting from village Chitarsenpur km 0000 and terminating at SH-74 near Manikpur 38814 at NH-139W under Bharatmalapariyona (NHAI) (618790) (-) (-)	Bihar	03/2023 (10/2024)	04/2027 (09/2027)	1422.37 (1537.99)	623.75	46.1
933	4L PS under NH configuration of Manikpur-Sahebganj of NH-139W (NHAI) (618791) (-) (-)	Bihar	10/2024 (01/2026)	12/2027 (12/2027)	1538.76 (1538.76)	564.37	26.6
934	Simaria Km. 206.050 to Khagaria Km. 266.282 (NHAI) (618840) (-) (-)	Bihar	12/2015 (10/2016)	04/2019 (10/2026)	664.02 (891.64)	813.98	97.72
935	4L Elevated Section and at-grade improvements at Begusarai town Simaria - Khagaria section from Km. 221.047 to Km. 225.302 of NH-31 (NHAI) (618841) (-) (-)	Bihar	10/2021 (06/2022)	12/2024 (08/2026)	491.04 (348.38)	348.04	95.72
936	Bakhtiyarpur-Rajauli Pkg-II from km. 54.405 to km.101.630 (NHAI) (618861) (-) (-)	Bihar	09/2020 (04/2021)	07/2023 (07/2026)	897.45 (1397.47)	914.25	97.85
937	Bakhtiyarpur-Rajauli Pkg-III from km. 101.630 to km.152.520 (NHAI) (618862) (-) (-)	Bihar	09/2020 (12/2021)	06/2024 (07/2026)	2156.22 (3046.61)	1815.2	99.14
938	Maheshkunt-Saharsa-Purnea Pkg I km 0.00 to km. 90.00 of NH-107 (NHAI) (618902) (-) (-)	Bihar	02/2017 (12/2019)	12/2021 (09/2026)	662.44 (1311.22)	1125.2	90.07
939	Maheshkunt -Saharsa-Purnea Pkg II (NHAI) (618903) (-) (-)	Bihar	03/2017 (12/2018)	12/2020 (09/2026)	1028.28 (1244.09)	1220.65	94
940	Chhapra - Hajipur from km. 143.200 to km. 209.200 (NHAI) (618904) (-) (-)	Bihar	07/2010 (01/2011)	07/2013 (04/2026)	2127.86 (2171.6)	526.04	89.81
941	Widening with additional 3L abetting Chhapra Bypass Section of NH-19 from Km. 143.200 to Km. 159.255 Pkg-1 (NHAI) (618905) (-) (-)	Bihar	02/2024 (08/2024)	08/2026 (10/2026)	470.5 (528.48)	287.52	73.26
942	4L Elevated Corridor and at-grade improvements from Design Ch0000 to Design Ch 19870 of Danapur Bihta Section, Design Ch0000 to Design Ch0231 connecting the existing RoB near Danapur station ,1.35 Km ramps and at-grade improvements to 4-lane section on Danapur side and Upgradation of existing Two lane carriageway to Four Lane carriageway from Design Ch19870 to Design Ch23500 of Bihta - Koilwar section (NHAI) (618914) (-) (-)	Bihar	10/2022 (03/2024)	09/2026 (08/2027)	4432.97 (2625.4)	1517.29	61.12
943	4L Greenfield starting from NH-30 near Saristabad Patna to Nathupur Project end point of Patna-Gaya-Dobhi Section of NH-83 (NHAI) (618917) (-) (-)	Bihar	07/2023 (03/2024)	08/2025 (09/2026)	488.24 (419.66)	101.06	87.03
944	4L of Siwan- Masrakh section of Ram Janki Marg from Km 230.385 to Km 281.391 of NH-227A (NHAI) (618926) (-) (-)	Bihar	08/2022 (11/2024)	11/2026 (11/2028)	1431.36 (1927.04)	502.89	10.33
945	Umagaon-Saharsa Package-IV Koshi Bridge & approach Road - Bheja-Bakaur (NHAI) (618953) (-) (-)	Bihar	02/2019 (02/2020)	08/2023 (03/2027)	1199.58 (1223.94)	1308	91.99
946	Umagaon - Saharsa Package - I Combined Umagaon-Kaluahi0.000KM to 21.609Km of NH227LSaharghat-Rahika0.000 Km to 26.130KM of NH227JRahika-Rampatti 0.00 KM to 15.00KM of NH527ABideshwarsthan-Bheja0.000KM to 25.915KM of NH527A. (NHAI) (618954) (-) (-)	Bihar	08/2022 (01/2025)	07/2027 (07/2027)	1473.2 (1703.02)	641.88	21.5
947	2L PS of Majhauri to Charout section from km. 0.00 to km. 63.655 (NHAI) (618955) (-) (-)	Bihar	01/2018 (11/2019)	11/2021 (07/2026)	638.29 (1067.51)	1096.09	99.8
948	Construction of Major Bridge over Baghmati and Lakhandei River along with Approaches from Design km.16.500 to km.21.500 (NHAI) (618956) (-) (-)	Bihar	02/2024 (10/2024)	04/2027 (03/2028)	498.97 (380.3)	43.95	25.03
949	4L of Greenfield Alignment from Km. 47.000 to Km. 89.210 of Balbhaddarpur to Bela Nawda Section of NH-119D (NHAI) (619127) (-) (-)	Bihar	03/2022 (03/2024)	03/2026 (03/2028)	2185.75 (2118.46)	717.01	29.13

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
950	Rehabilitation and Upgradation of Chorma - Bairstonia Section of National Highway No 227F to 2 lane with paved shoulders from Design Ch.0.000 to Ch. 34.566 (NHAI) (619136) (-) (-)	Bihar	06/2022 (02/2024)	01/2026 (07/2026)	610.78 (628.65)	336.7	100
951	Bakhtiyarpur Km 153.300 to Mokama Km 197.900 (NHAI) (619152) (-) (-)	Bihar	12/2015 (06/2017)	12/2019 (07/2026)	1182.94 (1898.84)	1797.43	99.95
952	Umagaon-Saharsa Package-V Bakaur-Parsarma-Bangaon-Bariyahi & Spur to Mahishi (NHAI) (619166) (-) (-)	Bihar	10/2022 (12/2023)	12/2025 (08/2026)	768.35 (968.42)	503.02	99.5
953	4L of Munger Mirzachauki section from Munger to Kharia village junction from Km 69520 to Km 95580 Pkg-1 (NHAI) (619289) (-) (-)	Bihar	01/2021 (03/2022)	03/2024 (10/2026)	1659.81 (1696.66)	670.56	82.72
954	Construction of Approach Road to Rail-cum- Road Bridge across river Ganga at Munger Ghat NH-333 B (NHAI) (619301) (-) (-)	Bihar	07/2013 (12/2018)	05/2021 (07/2026)	537.88 (633.91)	573.9	99.99
955	4L of Munger Mirzachauki section from start of existing Bhagalpur bypass to Rasulpur from Km 125000 to Km 157350 Pkg-3 (NHAI) (619305) (-) (-)	Bihar	01/2021 (04/2022)	04/2024 (12/2026)	1769.5 (2024.59)	672.67	77.3
956	4L of Munger Mirzachauki section from Km 95580 to Km 125000 Pkg-2 (NHAI) (619306) (-) (-)	Bihar	02/2021 (03/2022)	03/2024 (07/2026)	1020.84 (1235.65)	633.41	95.31
957	4L of Hajipur-Muzaffarpur Section of the existing NH-77 from Km. 0000 Ramashish Chowk to Km. 46300 and new bypass starting at Km. 46300 and connecting NH-28 of E-W Corridor at Km. 515045 (NHAI) (619317) (-) (-)	Bihar	08/2010 (08/2010)	02/2013 (08/2026)	2723.39 (2906.78)	2160.8	99.45
958	Bemetara Bypass NH 30 (MoRTH) (617908) (-) (-)	Chhattisgarh	01/2024 (04/2025)	04/2027 (04/2027)	161.96 (161.96)	0	42
959	Construction of 4 Nos Grade separator between km. 281.000 to km. 307.600 km. 286.400 kumhari km. 299.000 Transport Nagar km. 302.000 Power House km. 304.000 Chandra Moura Chowk to km. 305.000 supeia of NH-53 old NH-06 Raipur - Durg 4 Lane on EPC mode in the state of chhattisgarh job NO. NH-53old NH-06 CG-2017-18-56 (MoRTH) (617919) (-) (-)	Chhattisgarh	03/2018 (01/2019)	01/2021 (08/2025)	349.03 (349.03)	0	97.9
960	Up-gradation to Two/Four lane with paved shoulder Configuration of Kondagaon-Narayanpur from design ch. 0.00 - 48.693 Design Length 47.493 Km. 1.20 Km. retained on NH-130D under EPC mode in the State Chhattisgarh. (MoRTH) (617971) (-) (-)	Chhattisgarh	12/2022 (03/2025)	03/2027 (03/2027)	322.4 (322.4)	1.14	70
961	Upgradation to Two lane with Paved Shoulder Configuration of Narayanpur Kasturmeta pkg-II from design ch. 48.693 to 70.453 design length21.760 Km. on NH-130D under EPC mode in the state of Chhattisgarh. (MoRTH) (617972) (-) (-)	Chhattisgarh	12/2022 (12/2024)	06/2026 (-)	200.67 (200.67)	0	0
962	Upgradation of Ambikapur-Ramanujganj-Garwa road of NH-343, Package-III, Badki mahri village to Ramanujganj section from existing km 80.600 to km 110.330 Design Ch. 85.370 to Ch. 114.800 of total length 29.430 km to two lane with paved shoulders under corridor scheme under EPC Mode in the of Chhattisgarh (MoRTH) (618014) (-) (-)	Chhattisgarh	03/2022 (05/2025)	10/2026 (10/2026)	199.05 (199.05)	52.96	33.58
963	Upgradation of Keonchi - Ratanpur Road of NH 45 Package-I, from design chainage km 237.860 to km 273.200 of length 35.340 km to two lane with paved shoulders under Corridor scheme on EPC mode in the state of Chhattisgarh. (MoRTH) (618015) (-) (-)	Chhattisgarh	03/2022 (07/2024)	01/2026 (12/2026)	225.41 (228.93)	77.46	60
964	Upgradation of Ambikapur Ramanujganj - Garhwa Road NH 343 of Package-I, Rajpuri Khurd Village to Padih Village section from existing km 7.830 to km 57.650 Design Ch. 13.700 to Ch. 62.700 of total length 49.00 km to two lane with paved shoulders under EPC mode in the state of Chhattisgarh (MoRTH) (618016) (-) (-)	Chhattisgarh	03/2022 (05/2025)	05/2027 (05/2027)	397.44 (397.44)	56.95	26.26
965	Upgradation of Keonchi - Ratanpur Road of NH 45 Package-II, from design chainage km 278.75 to km 321.348 of length 42.598 km to two lane with paved shoulders under Corridor scheme on EPC mode in the state of Chhattisgarh. (MoRTH) (618017) (-) (-)	Chhattisgarh	03/2022 (07/2024)	01/2026 (12/2026)	286 (286)	87.54	60

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
966	Upgradation of Bilaspur-Takhatpur-Mungeli-Pandariya-Pondi Road on N.H.-130A Package IIIA Takhatpur By-pass from existing Ch. 26.542 to 32.093 [Design Ch. 18.700 to 25.900] & Mungeli By-pass from existing Ch. 45.786 to 56.275 [Design Ch. 29.600 to 51.600] and Package IIIB Pandariya By-Pass from existing Ch. 82.582 to 87.133 [Design Ch. 77.900 to 81.1000 & Pondi By-pass from existing Ch. 103.166 to 104.756 [Design Ch. 97.000 to 103.395] to two lane with paved shoulder configuration in the (MoRTH) (618018) (-) (-)	Chhattisgarh	03/2022 (01/2024)	07/2025 (12/2026)	351.19 (351.19)	11.63	11
967	Durg-Raipur Bypass Section Package - 1 from km. 0.00 to km. 44.50 near Tendesara to near Khatti Village (NHAI) (618589) (-) (-)	Chhattisgarh	06/2022 (07/2023)	07/2025 (03/2027)	1828 (1656.73)	1016.41	74.93
968	Durg-Raipur-Arang Package - 2 from km. 44.50 to km. 92.23 near Khatti Village to near Aurang (NHAI) (618590) (-) (-)	Chhattisgarh	06/2022 (06/2023)	05/2025 (03/2027)	1958.9 (1561.97)	1000.81	73.96
969	4L of Bilaspur to Urga km 0.00 to 70.2 of NH-130A (NHAI) (618639) (-) (-)	Chhattisgarh	04/2020 (03/2022)	03/2024 (07/2026)	1855.59 (2523.86)	1468.47	94.81
970	4L of Urga - Pathalgaon from Km. 70.200 to km. 157.745 of NH-130A (NHAI) (618640) (-) (-)	Chhattisgarh	03/2022 (02/2024)	08/2026 (08/2026)	2261.3 (2860.36)	1050.51	80.05
971	4L of Pathalgaon-Kunkuri-CG/JH Border section of NH-43 from Km. 00.000 to Km.104.250 (NHAI) (618646) (-) (-)	Chhattisgarh	08/2024 (04/2026)	04/2029 (04/2029)	3147.07 (3147.07)	0.03	0
972	Development of 6L of Jhanki Sargi Section Road from km 0.000 to km 42.800 of NH-130CD Pkg-CG-1 (NHAI) (618673) (-) (-)	Chhattisgarh	11/2021 (09/2022)	09/2024 (02/2027)	1368.19 (1129.14)	715.25	99.35
973	Development of 6L Sargi Basanwahi Section from km 42.800 to km 99.500 of NH-130CD Pkg-CG-2 (NHAI) (618674) (-) (-)	Chhattisgarh	12/2021 (01/2023)	01/2025 (07/2026)	1470.73 (1461.81)	757.59	100
974	Development of 6L of Basanwahi Marangpuri Section from km 99.500 to km 124.661 of NH-130-CD (NHAI) (618675) (-) (-)	Chhattisgarh	03/2022 (10/2023)	10/2025 (03/2027)	1307.16 (1303.63)	481.63	66.8
975	4 laning of Champa - Korba from km 0.00 to km 38.2 (NHAI) (618957) (-) (-)	Chhattisgarh	02/2021 (01/2022)	01/2024 (07/2026)	1002.33 (1304.47)	944.63	98.75
976	Balance Works of Rehabilitation and Up gradation of NH-43 New NH-30 from Krn 162120 to Krn 173500 Length 11.380 Km. Keshkal Bypass 4-Lane with Paved shoulder in the State Of Chhattisgarh under NHDP-IV through Engineering, Procurement & Construction EPC Basis (MoRTH) (619039) (-) (-)	Chhattisgarh	06/2025 (06/2026)	06/2028 (-)	307.96 (307.96)	0	0
977	4/6 Laning of Raipur-Simga Pkg-I from km. 0.00 to km. 48.58 (NHAI) (619103) (-) (-)	Chhattisgarh	10/2015 (04/2016)	04/2018 (07/2026)	1096.52 (1172.36)	905.25	100
978	4 Laning with PS of Pathrapalli-Katghora km 53.3 to km 92.6 Pkg-II of Bilaspur Kathghora (NHAI) (619167) (-) (-)	Chhattisgarh	12/2019 (12/2020)	12/2022 (07/2026)	865.1 (1275.26)	851.38	93.1
979	Balance Work Estimate of Rehabilitation and Up-gradation of NH- 43 from Km. 468.600 to Km. 531.250 Pathalgaon to kunkuri Section to two-lane with paved shoulder in the State of Chhattisgarh on SBD mode under NHO under Annual plan 2025-26 (MoRTH) (619347) (-) (-)	Chhattisgarh	03/2026 (06/2026)	06/2028 (-)	201.16 (201.16)	0	0
980	Widening of Existing Road from Intermediate Lane 2-lane to 4-lane Between Km 19.994 to Km 35.180 of NH-848A Rakholi-Khadoli-Velugam Section in U.T. of Dadra and Nagar Haveli and Daman and Diu (MoRTH) (619183) (-) (-)	Dadra & Nagar Haveli and Daman & Diu	10/2022 (02/2024)	06/2026 (07/2026)	198.06 (239.57)	75.95	80
981	Development of 6L UER II [Package - I] NH-1 Near Bakoli till Karala Kanjhawala Road from km. 0.70 to km.15.00 (NHAI) (618509) (-) (-)	Delhi	07/2020 (10/2021)	10/2023 (06/2026)	2089.94 (2203.45)	1825.54	99.99
982	8L of Dwarka Expressway Pkg-II RuB near Dwarka Sector 21-DL/HR Border from 5.300 Km.to 9.500 Km. of NH-248BB (NHAI) (619090) (-) (-)	Delhi	01/2018 (10/2019)	10/2021 (06/2026)	2067.67 (2670.22)	2341.79	100

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
983	Dwarka Expressway from Km -0.600 to Km 5.300 - Pkg-I Shivmurti Chowk-RuB near Dwarka Sector 21 (NHAI) (619202) (-) (-)	Delhi	03/2018 (09/2020)	09/2022 (06/2026)	2144.67 (3929.5)	3329.23	98.8
984	4-Laning from End of Zuari approaches to Start of Margao Bypass section of NH-66 from Km 536.800 to Km 543.450 (MoRTH) (617941) (-) (-)	Goa	07/2024 (02/2026)	02/2028 (02/2028)	398.25 (398.25)	0	0.5
985	Construction of Six lane Elevated Corridor from Km. 508.000 to Km. 513.150 including approaches on NH-66 (MoRTH) (617942) (-) (-)	Goa	04/2023 (04/2024)	04/2026 (10/2026)	641.46 (641.46)	0	97.1
986	4-laning of Navelim to Cuncolim Section of NH-66 from Km 554.245 to Km 561.480 on HAM Mode (MoRTH) (617943) (-) (-)	Goa	12/2024 (04/2026)	10/2028 (10/2028)	746.75 (746.75)	0	0
987	Construction of 4L Flyover from MES College Junction to Bogmalo Junction on NH-566 from Km. 7.106 to Km. 10.460 and 4L VUP at Queeny Nagar Junction from Km. 3.330 to Km. 4.550 (NHAI) (618609) (-) (-)	Goa	01/2024 (08/2024)	07/2026 (05/2027)	463.08 (316.28)	168.21	57.3
988	Up-gradation of Dhoraji-Jamkandorna-Kalavad Section of NH-927D from Design Chainage km 0/00 to km 58/115 to Two lane with PS configuration in the State of Gujarat on EPC (MoRTH) (617906) (-) (-)	Gujarat	10/2022 (01/2025)	01/2027 (01/2027)	246.6 (291.19)	0	35
989	Work of 6 laning/Construction of elevated corridor from km 0/0 to 10/170 Narol Junction to Sarkhej junction including 4 lane Shastri Bridge on Sabarmati river on NH 47 in the State of Gujarat on HAM mode (MoRTH) (617916) (-) (-)	Gujarat	03/2024 (08/2025)	02/2028 (02/2028)	1295.39 (1295.39)	0	30
990	Construction of new 4 lane major bridge with approaches on Sabarmati River near Dharoi at Km. 82/00 to 86/00 Design length 3.300 km on NH-58 in the State of Gujarat on Hybrid Annuity Mode HAM (MoRTH) (617926) (-) (-)	Gujarat	03/2024 (08/2025)	08/2027 (08/2027)	398.4 (398.4)	0	44
991	Widening to 2LPS between Km 0/0 to 56/0 Khokhara Gujarat Border Vijayanagar Antrasuba Mathasur road of NH 58 in the State of Gujarat (MoRTH) (617927) (-) (-)	Gujarat	03/2024 (09/2025)	09/2027 (09/2027)	699.19 (699.19)	0	35
992	Widening 2 lane to 4-lane from KM 92/320 to Km 115/320 Vav Chokdi-Satlasana to to Vrundavan Chokdi, Kheralu on NH-58 in the State of Gujarat. (MoRTH) (617928) (-) (-)	Gujarat	03/2022 (03/2024)	03/2026 (07/2026)	151.13 (171.27)	0	98
993	Work of development and construction of elevated corridorfrom km 38/660 to km 42/690 Iscon junction to start point of approach of sanand flyover of NH-147 in the sate of Gujarat (MoRTH) (617976) (-) (-)	Gujarat	03/2023 (06/2024)	06/2026 (08/2026)	530.2 (530.2)	58.29	90
994	Upgradation to two lane with paved Shoulder Configuration from Km. 0/00 to 47/000 of NH 351 Mahuva to Badhada section in the State of Gujarat (MoRTH) (618022) (-) (-)	Gujarat	12/2022 (02/2024)	08/2025 (12/2026)	173.06 (219.08)	22.63	74
995	Upgradation of Mehsana-Visnagar-vadnagar-Kheralu-Idar section from km 0/00 to 81/300 of NH 168G Mehsana to Idar in the State of GujaratTotal Length 81.300 Km on Hybrid Annuity Mode HAM (MoRTH) (618107) (-) (-)	Gujarat	02/2024 (12/2025)	06/2028 (06/2028)	1155.21 (1155.21)	378.6	16
996	Up-gradation and strengthening to 2lanePS from Km 95/500 to km 129/775 of Nh 168G Idar-Bhiloda-Samlaji in the state of Gujarat Length 34.275 km (MoRTH) (618108) (-) (-)	Gujarat	09/2022 (12/2023)	12/2025 (12/2026)	237.28 (237.28)	0	63
997	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-26 Ch.696890 to Ch.726390 (NHAI) (618459) (-) (-)	Gujarat	09/2020 (12/2022)	08/2024 (02/2027)	1555.2 (1556.4)	1273.31	81.6
998	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-28 Ch.756052 to Ch.781282 (NHAI) (618460) (-) (-)	Gujarat	09/2020 (11/2021)	11/2023 (04/2026)	1263.38 (1266.98)	934.98	100
999	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-31 Ch.824920 to Ch.844382 [Junction near Pratap nagar Village - Junction near Dodka Village] (NHAI) (618462) (-) (-)	Gujarat	11/2019 (05/2021)	05/2023 (06/2026)	1644.85 (1651.14)	1297.47	100
1000	Vadodara Mumbai Expressway Kim to Ankleshwar Phase IA - Pkg V (NHAI) (618463) (-) (-)	Gujarat	02/2018 (11/2019)	10/2021 (07/2026)	1324.84 (2807.48)	1471.27	91.34

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1001	Vadodara Mumbai Expressway Jujuwa - Gandeva from Km. 154.600 to Km. 190.000 Phase-I Package-VIII (NHAI) (618466) (-) (-)	Gujarat	07/2023 (08/2024)	03/2026 (11/2026)	3834.24 (3820.2)	197.98	4.85
1002	Vadodara Mumbai Expressway Karvad - Jujuwa from Km. 128.000 to Km. 154.600 Phase-I Package-IX (NHAI) (618467) (-) (-)	Gujarat	07/2023 (04/2024)	10/2025 (07/2027)	2594.17 (2587.04)	226.62	21.75
1003	Ahmedabad - Dholera Pkg III from km. 48.52 to km. 71.06 [Vejalka Village - Start of DSIR zone] (NHAI) (618503) (-) (-)	Gujarat	05/2020 (07/2021)	07/2023 (07/2026)	1034.04 (1155.41)	1125.55	100
1004	Ahmedabad - Dholera Pkg IV from km. 71.06 to km. 109.019 [Start of DSIR zone - Adhelai Village] (NHAI) (618504) (-) (-)	Gujarat	05/2020 (12/2021)	12/2023 (07/2026)	1181.76 (1358.73)	1222.65	97.99
1005	Balance work of Six Laning of Shamlaji-Motachiloda from Km. 401.200 to Km.494.410 section Design Chainage Km.447.385 to Km 540.595, Length- 93.210 Km of old NH-8 NH-48 in the state of Gujarat on single Percentage Item Rate Contract (NHAI) (618507) (-) (-)	Gujarat	06/2024 (08/2024)	06/2025 (07/2026)	466.8 (501.48)	577.31	91.8
1006	Construction of Additional Structures including Approaches in Vadodara Surat Section of NH48 between existing Km. 108.000 to Km. 250.000 (NHAI) (618508) (-) (-)	Gujarat	03/2024 (01/2025)	01/2027 (06/2027)	907.39 (907.39)	346.17	48.73
1007	6L with PS of Samakhiyali to Santalpur section from km. 339.700 to Km. 430.100 of NH-27 (NHAI) (618564) (-) (-)	Gujarat	01/2023 (12/2023)	12/2025 (03/2027)	1553.76 (34.34)	28.59	64.52
1008	Sanchole - Santalpur from km 99.000 - km 130.073 of NH-754K AJ-RGBS-Package-4 (NHAI) (618615) (-) (-)	Gujarat	02/2020 (03/2021)	03/2023 (07/2026)	778.15 (835.55)	764	99.7
1009	4L of Dhrol bypass section of NH-151A Approx. length 5.7 Km & widening upto 4 laning of missing link of Amran section of NH-151A Approx. length 6.55 Km from existing Ch. 42000 to 48500 of ongoing Dhrol-Bhadra-Pipaliya section of NH-151A (NHAI) (618616) (-) (-)	Gujarat	03/2024 (02/2025)	02/2027 (02/2027)	625.58 (455.54)	140.05	32.1
1010	Upgradation to 4L PS from Bhimasar, Junction of NH-41 to Anjar- Bhuj upto Airport Junction from Km 0.000 to Km 65.478 of NH-341 (NHAI) (618787) (-) (-)	Gujarat	03/2022 (01/2023)	06/2025 (03/2027)	1373.06 (1687.25)	837.7	96
1011	Kodinar - Veraval Package VI from km. 221.610 to km. 263.00 of NH-8E & km. 120.900 to km. 121.150 of NH-8D (NHAI) (618833) (-) (-)	Gujarat	02/2016 (02/2018)	07/2020 (07/2026)	894.01 (1127.42)	730.04	98.79
1012	4L PS Divided Carriageway from Patan Near Rajpur to Gojariya From Km 52.000 to Km 128.940 of NH-68 (NHAI) (618901) (-) (-)	Gujarat	12/2021 (03/2023)	03/2025 (10/2026)	1181.34 (1098.23)	923.85	87.12
1013	4L PS from Ch. 94.030 in Jabugam Village to Ch. 132.320 in Dhamasiya Village of NH-56 Pkg-III (NHAI) (618930) (-) (-)	Gujarat	03/2023 (11/2025)	11/2027 (11/2027)	1188.46 (898)	147.42	23.82
1014	4L PS from Ch. 179.780 in Bitada/Movi Village to Ch. 208.900 in Nasarpore Village of NH-56 Pkg-V (NHAI) (618931) (-) (-)	Gujarat	03/2023 (11/2025)	11/2027 (11/2027)	764.02 (566.96)	79.56	7.59
1015	Construction of 4 lane with PS Idar-Badoli bypass section from design km 81/300 to km 95/500 of NH 168G in the State of Gujarat (MoRTH) (619061) (-) (-)	Gujarat	03/2025 (05/2026)	05/2028 (05/2028)	705.09 (705.09)	0	4
1016	Widening to 6L of Existing 4L Jetpur - Gondal - Rajkot Section from Km. 117.600 to Km. 185.00 on NH-27 (NHAI) (619087) (-) (-)	Gujarat	03/2022 (09/2023)	09/2025 (01/2027)	2070.44 (1390.29)	1048.83	73.08
1017	Four Laning of Una to Kodinar from km. 180.478 to km. 221.610 Package-V (NHAI) (619145) (-) (-)	Gujarat	02/2016 (02/2017)	08/2019 (07/2026)	877.71 (1126.66)	1008.77	100
1018	Kagvadar - Una Package-IV (NHAI) (619146) (-) (-)	Gujarat	02/2016 (03/2017)	09/2019 (07/2026)	750.53 (955.78)	833.12	97.93
1019	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-27 Ch.729.700 to Ch.756.052 (NHAI) (619197) (-) (-)	Gujarat	09/2020 (02/2022)	02/2024 (06/2026)	1185.69 (1259.27)	1037.33	97.21

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1020	Delhi-Amritsar-Katra Expressway Phase-I Pkg-I from Jussur Kheri on NH-KMP Expressway to Junction with Rohtak-Panipat road NH-709 near Rukhi Paani village Km 0000 to Km 34000 (NHAI) (618482) (-) (-)	Haryana	12/2020 (12/2021)	12/2023 (07/2026)	1866.49 (2429.9)	1609.72	99.91
1021	Delhi-Amritsar-Katra Expressway Phase-I Pkg-II from Junction with Rohtak-Panipat road NH-709 near Rukhi Paani village to Junction with Jind-Panipat road NH-352A near Gangana village Km 34000 to Km 60800 (NHAI) (618483) (-) (-)	Haryana	12/2020 (01/2022)	01/2024 (07/2026)	1533.87 (1792.53)	1176.23	99.89
1022	Construction of Additional Structures, Improvement of Service Road & Maintenance of Six Lane Gurgaon-Jaipur Section of NH-48 old NH-8 between km 42700 to km 107100 in the State of Haryana (NHAI) (618506) (-) (-)	Haryana	05/2024 (05/2025)	05/2027 (05/2027)	401.74 (240.02)	116.43	56.05
1023	Gohana - Sonipat PKG-2 (NHAI) (618580) (-) (-)	Haryana	01/2019 (07/2020)	07/2022 (07/2026)	1275.31 (1957.44)	1225.85	97.86
1024	4L Greenfield Jalbhera Shahbad section from km. 0.000 to km. 22.850 of NH-152G (NHAI) (618788) (-) (-)	Haryana	03/2022 (06/2023)	05/2025 (08/2026)	927.22 (1173.66)	544.51	87.05
1025	4L Bhiwani-Hansi road section of NH-148B (NHAI) (618792) (-) (-)	Haryana	11/2022 (12/2023)	12/2025 (08/2026)	1330.23 (1144.21)	455.02	99.5
1026	Jagadhari - Tajewala from Km -0.175 to 32.337 km of NH-344 (NHAI) (618936) (-) (-)	Haryana	03/2022 (02/2023)	02/2025 (03/2027)	1269.5 (919.43)	708.89	67.8
1027	4L PS of Ambala Ring Road of New NH-44 (NHAI) (619080) (-) (-)	Haryana	02/2023 (10/2023)	10/2025 (09/2026)	1093.35 (1225.41)	590.67	88.77
1028	4L of Jind-Gohana road Package-1 from km. 0.00 to km. 40.601 of NH-352 A under NHO (NHAI) (619092) (-) (-)	Haryana	01/2019 (07/2020)	07/2022 (07/2026)	994.22 (1606.82)	1064.47	99.97
1029	4/6L of Gurgaon - Pataudi - Rewari from km. 0.00 to km.43.87 of NH-352W (NHAI) (619132) (-) (-)	Haryana	05/2020 (11/2021)	11/2023 (08/2026)	1810.04 (1917.5)	1267.19	76.98
1030	Karnal ring road Lot-4/Pkg-1 (NHAI) (619201) (-) (-)	Haryana	11/2022 (08/2023)	08/2025 (10/2026)	1741.45 (2041.54)	831.11	96.42
1031	Rehabilitation and Upgrading of NH-707 OLD 72-B Package - 2 Hewna to Ashyari (MoRTH) (618051) (-) (-)	Himachal Pradesh	04/2020 (03/2021)	03/2023 (12/2025)	242.8 (220.95)	145.49	98.38
1032	Improvement/construction of existing CL-5 Road to NH Intermediate lane specification with hard shoulder from Km 166.000 to 203.77 net Length 37.770 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh on EPC mode under project Deepak, BRO (MoRTH) (618215) (-) (-)	Himachal Pradesh	06/2021 (06/2024)	06/2027 (06/2027)	274.36 (194)	0	22.26
1033	Improvement/construction of existing CL-5 Road to NH Intermediate lane specification with hard shoulder from Km 133.000 to 166.000 net Length 33.000 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh on EPC mode under project Deepak, BRO (MoRTH) (618216) (-) (-)	Himachal Pradesh	03/2021 (07/2023)	06/2026 (09/2027)	230.55 (203.15)	31.4	23.24
1034	Improvement/construction of existing Class-5 Road to NH Intermediate lane specification with hard shoulder from existing Km 76/340 to 134/940 Design chainage from Km 76/300 to 133/000 net Length 56.700 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh Package I (MoRTH) (618217) (-) (-)	Himachal Pradesh	03/2021 (05/2023)	05/2026 (08/2027)	314.67 (244.15)	93.27	60.02
1035	Rehabilitation and Upgradation to 2-lane configuration of Kalwahn-Mandi Section km 208.950 to 250.592 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-3 (MoRTH) (618230) (-) (-)	Himachal Pradesh	08/2020 (10/2022)	04/2025 (12/2026)	314.32 (314.32)	0	70.39
1036	Rehabilitation and Upgradation to 2-lane configuration of Hamirpur-Karnohal Section km 141.00 to 181.00 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-1 (MoRTH) (618231) (-) (-)	Himachal Pradesh	08/2020 (06/2022)	12/2024 (09/2026)	371.93 (371.93)	198.34	93.61

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1037	Rehabilitation and Upgradation to 2-lane configuration of Karnohal- Kalwahn Section km 181.00 to 208.950 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-2 (MoRTH) (618232) (-) (-)	Himachal Pradesh	08/2020 (11/2023)	05/2026 (12/2026)	251.62 (190.02)	75.89	58
1038	Construction of missing link from Birhu to Lathiani from Km 35/550 Design chainage Km 0.000 to Km 42/800 Design Chainage Km 8.153on NH-503A including Lathiani Bridge on back water of Govindsagar and its approaches in Himachal Pradesh. (MoRTH) (618253) (-) (-)	Himachal Pradesh	06/2023 (03/2026)	03/2029 (03/2029)	870.95 (896.86)	0	0
1039	Nerchowk km 190.000 to Pandoh including Pandoh bypass km221.305 (NHAI) (618850) (-) (-)	Himachal Pradesh	03/2016 (01/2018)	07/2020 (07/2026)	1464.12 (1651.67)	1567.12	100
1040	Pandoh bypass 221.305 to Takoli 242.000 of NH-21 in the state of Himachal Pradesh (NHAI) (618851) (-) (-)	Himachal Pradesh	06/2017 (03/2018)	09/2021 (03/2027)	3419.95 (4465.94)	2881.19	95.65
1041	4L Sundar Nagar Bypass from Km.173.900 to Km.179.600 of NH-21 (NHAI) (618852) (-) (-)	Himachal Pradesh	02/2022 (06/2022)	06/2024 (07/2026)	191.11 (192.11)	182.26	100
1042	Rehabilitation and Upgradation to 4L configuration & Strengthening of Sihuni to Rajol from Km 51.000 to Km 72.000 of NH-154 Package-IIA (NHAI) (618878) (-) (-)	Himachal Pradesh	03/2022 (09/2023)	09/2025 (09/2026)	696.65 (776.59)	493.1	98.58
1043	Rehabilitation and Upgradation to 2L PS configuration & Strengthening of Padhar to Bijni section from Km 180.000 to Km 202.815 of NH-154 Pkg-VA (NHAI) (618879) (-) (-)	Himachal Pradesh	06/2022 (11/2024)	11/2026 (11/2026)	930.86 (930.86)	665.28	99.19
1044	Rehabilitation and Up-gradation to 4L configuration & Strengthening of Thanpuri to Paror section from Km 85.135 to Km 100.840 of NH-154 Pkg-IIC (NHAI) (618880) (-) (-)	Himachal Pradesh	07/2022 (03/2024)	12/2025 (04/2027)	815.68 (666.79)	486.73	54.91
1045	4L PS bijni to mandi section from Km 202.815 to Km 208.000 of NH-20 New NH-154 of Pathankot-Mandi Package-VB (NHAI) (618881) (-) (-)	Himachal Pradesh	02/2023 (03/2025)	09/2027 (09/2027)	1113.02 (1112.39)	525.23	34.57
1046	Rehabilitation and Up-gradation of existing road to 2L PS from End of Hamirpur Bypass near Chilbahal to Bhangbar section from Km. 138.295 to Km.175.270 of NH-88 Pkg-IV (NHAI) (618888) (-) (-)	Himachal Pradesh	03/2022 (04/2023)	04/2025 (08/2026)	1146.19 (1358.62)	987.23	95.72
1047	4L of Bhangbar Near Ranital to Kangra Bypass Section of Old NH-88 New NH-303,503 up to Intersection with NH-154 from Km 175.270 to Km 193.400 Pkg-VB (NHAI) (618889) (-) (-)	Himachal Pradesh	03/2021 (12/2022)	12/2024 (09/2026)	1322.95 (1829.49)	1101.15	97.45
1048	2L PS of Hamirpur Bypass from Km 121.175 to Km.138.295 of NH-103&3 (NHAI) (618890) (-) (-)	Himachal Pradesh	08/2022 (10/2023)	10/2025 (09/2026)	739.39 (754.82)	369.59	93.25
1049	4L PS from Kalar Bala Village to Nauni Chowk of NH 205 from Km 41.000 to Km 58.450 (NHAI) (618891) (-) (-)	Himachal Pradesh	01/2024 (05/2025)	05/2027 (09/2027)	1244.43 (786.91)	117.5	30.43
1050	4 Lane with Paved Shoulder from Dareota Village to Kalar Bala NH 205, Design Chainage -Km 33185 to Km 41000, Design Length-7.815 Km Package-IIB (NHAI) (618892) (-) (-)	Himachal Pradesh	06/2025 (06/2026)	06/2028 (06/2028)	992.85 (992.85)	5.15	0
1051	4L of Kathlighat to Shakral Village from Km 128.835 to Km 146.300 of NH- 5 Shimla Bypass - Pkg I (NHAI) (618921) (-) (-)	Himachal Pradesh	03/2022 (04/2023)	04/2026 (07/2027)	1703.48 (2648.8)	1139.72	63.14
1052	4L of Shakral Village to Dhalli Section from Km 146.300 to Km 156.560 Shimla Bypass - Pkg II and Shimla connectivity from Km 0.000 to Km 0.725 of NH-5 (NHAI) (618922) (-) (-)	Himachal Pradesh	04/2022 (03/2024)	03/2027 (12/2027)	1956.26 (2880.72)	1452.65	63.17
1053	Solan - Kaithlighat Section of NH-22 Now NH-5 from Km. 106.139 to Km.129.05 (NHAI) (619003) (-) (-)	Himachal Pradesh	03/2018 (11/2018)	05/2021 (11/2026)	881.74 (1519.53)	1345.12	90.11
1054	4L of HP/Punjab Border - Mo from km. 11.00 to km. 42.00 of Old NH-20 New NH-154 Package-IA (NHAI) (619153) (-) (-)	Himachal Pradesh	03/2021 (05/2022)	05/2024 (10/2026)	1002.11 (1363.04)	819.71	67.66

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1055	Construction of Shopian Bypass on NH-444 taking off from existing chainage Km 36500 and re-joining at km 47588 of existing Chainage New Design Ch. From km 28000 to km 36925 as 2- lane with paved shoulder in the UT of Jammu & Kashmir on EPC mode. (MoRTH) (618038) (-) (-)	Jammu and Kashmir	03/2024 (01/2026)	01/2028 (-)	224.44 (224.44)	0	3
1056	Widening and strengthening to 2 lane with paved shoulder from existing Ch. Km 56720 to Km 100820 and Design Ch. From Km 62600 to Km 106360 Total Length43.760 Km on SRINAGAR -BARAMULA URINH-01 in the UT of Jammu & Kashmir under project BEACON, Border Roads Organization BRO on EPC mode. (MoRTH) (618201) (-) (-)	Jammu and Kashmir	09/2023 (11/2024)	11/2026 (06/2027)	702.1 (702.1)	0	51
1057	Construction of 2 lane with paved shoulders Baramulla Bypass Greenfield bypass from existing Ch. Km 47020 to Km 56720 and Design Ch. From 48500 to 62600 Total length 14.100 km on road Srinagar Baramulla Uri NH-01 in the UT of Jammu & Kashmir under Project.Package-III (MoRTH) (618202) (-) (-)	Jammu and Kashmir	03/2023 (09/2024)	09/2026 (07/2027)	992.43 (992.43)	98.99	46.8
1058	Construction of 4 lane with paved shoulder Pattan bypass Greenfield bypass from existing Ch. Km 24320 to Km 33760 and Design Ch. from Km 24400 to Km 35300, total length 10.900 km on road SrinagarBaramulla Uri NH-01 in the UT of Jammu & Kashmir under Project BEACON, Border Roads Organization BRO on EPC mode. Package-II (MoRTH) (618203) (-) (-)	Jammu and Kashmir	03/2023 (08/2024)	07/2026 (02/2027)	980.21 (980.21)	131.91	57
1059	Construction of realignment between Pandrass- Pashkyun Total length 27.10 km on road Zozila-Kargil -Leh NH-1 to 2 lane specifications i.e. Drass alignment 9.30 km Kharboo realignment 6.30 km & Kargil alignment 11.50 km under project Vijayak BRO in the UT of Ladakh on EPC Mode (MoRTH) (618204) (-) (-)	Jammu and Kashmir	11/2021 (06/2023)	06/2025 (07/2027)	426.15 (426.15)	112.2	54.89
1060	Construction of 4 lane with paved shoulder from Existing Ch. 14200 to 24320 Design Ch. 14200 to 24400, Ch. 33760 to 42780 Design Ch. 35300 to 44294 & Ch. 43440 to 47020 Design Ch. 44958 to 48500 Delina Flyover including construction of flyover length 1.704 km of total length 22.736 kms in AOR of 760 BRTF on road SRINAGAR BARAMULA URI NH-01 in the UT of Jammu & Kashmir under project BEACON, Border Roads Organization BRO Package-IJob No NH-1-J&K-2022-23-110 (MoRTH) (618205) (-) (-)	Jammu and Kashmir	06/2022 (08/2023)	08/2025 (08/2026)	823.46 (823.46)	292.48	85.5
1061	Widening and Strengthening of Rafiabad-Kupwara-Chowkibal-Tangdhar-Chamkot NH-701 road from design Ch. From 0000 to 51000 to two lanes with paved shoulders under Project Beacon in the UT of Jammu & Kashmir on EPC mode Package-I. (MoRTH) (618206) (-) (-)	Jammu and Kashmir	03/2024 (11/2024)	05/2027 (-)	1404.94 (1404.94)	143.99	41.7
1062	Rehabilitation and upgradation to 2 lane with paved shoulder from existing chainage Km 166.100 to Km 192.98 design chainage Km 146.700 to Km 162.800 including construction of Bhimber Gali Tunnel Total Length of Tunnel 1.100 Km under 31 BRTF on Akhnoor-Poonch Roads on EPC mode NH-144A Package-VII (MoRTH) (618221) (-) (-)	Jammu and Kashmir	09/2021 (07/2024)	07/2026 (07/2027)	734.64 (734.64)	0	50.03
1063	Widening and Strengthening up gradation to 2 lane with paved shoulder from existing chainage Km 192.98 to Km 229.820 design chainage Km 162.800 to Km 198.18 under 31 BRTF on Akhnoor-Poonch Road NH-144A in the UT of Jammu and Kashmir under Project Sampark Border Roads Organisation BRO on EPC Mode Package-VIII Job No NH-144A-J&K-2022-2023-111 (MoRTH) (618222) (-) (-)	Jammu and Kashmir	10/2022 (01/2024)	01/2026 (12/2026)	562.45 (562.45)	158.52	71.27
1064	Rehabilitation and up-gradation to 2 lane with paved shoulder from existing chainage km 64535 to km 85385 Design chainage km 55800 to km 74350 under 13 TF on Akhnoor-Poonch road NH-144A under Project Sampark BRO in the UT of Jammu & Kashmir on EPC mode Package-III Job no NH-144A-J&K-2019-20-79 (MoRTH) (618223) (-) (-)	Jammu and Kashmir	03/2020 (09/2021)	09/2023 (12/2026)	152.93 (152.93)	77.62	90.06
1065	Rehabilitation and up-gradation to 2 lane with paved shoulder from existing chainage km 49150 to km 64535 Design chainage km 46.450 to km 55.800 including construction of Sungal Tunnel Total length of Tunnel 2.79 km under 13 TF on Akhnoor-Poonch road NH-144A under Project Sampark BRO in the UT of Jammu & Kashmir on EPC mode Package-II Job no NH-144A-J&K-2019-20-78 (MoRTH) (618224) (-) (-)	Jammu and Kashmir	03/2020 (08/2021)	08/2024 (07/2026)	796.97 (796.97)	440.97	92.1
1066	Rehabilitation and up-gradation to 2 lane with paved shoulder from existing chainage km 134950 to km 166100 Design chainage km 116980 to km 146700 under 31 TF on Akhnoor-Poonch road NH-144A in the UT of Jammu & Kashmir under Project Sampark BRO on EPC mode Package-VI Job no NH-144A-J&K-2021-22-106 (MoRTH) (618225) (-) (-)	Jammu and Kashmir	07/2021 (07/2022)	07/2024 (12/2026)	395.25 (395.25)	156.58	89.2
1067	Rehabilitation and upgradation to 2 lane with paved shoulder from existing chainage Km 30.053 to Km 49.150 design chainage Km 30.000 to Km 46.450 including Kandi Tunnel under 31 BRTF on Akhnoor-Poonch Road NH-144A Under Project Sampark in the UT of Jammu & Kashmir EPC modePackage-I Job no NH-144A-J&K-2020-21-83. (MoRTH) (618226) (-) (-)	Jammu and Kashmir	07/2020 (11/2022)	11/2024 (09/2026)	272.49 (272.49)	160.08	95.27

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1068	Up-gradation to 2-lane with Paved Shoulder from Km 12.850 to Km20.300 of 7.450Km length on Goha-Khellani section and a link road to Goha village of 2.016 km on NH-244 in UT of Jammu and Kashmir on EPC Mode Pkg-1 (NHIDCL) (618394) (-) (-)	Jammu and Kashmir	07/2020 (10/2020)	04/2022 (10/2026)	228.39 (225.37)	176.58	94.26
1069	Construction & Upgradation to 2-lane with paved shoulder from Design Ch. Km 51700 at Premnagar km 66315 to Km 66535 New Thatri at Start of Km 83rd, Tunnel Km 82665 of 14.835 Km design length on Chenani-Sudhmahadev-Goha Khellani-Kishtwar-Vailoo Donipawa-Ashajipora section of NH-244 in the UT of J&K on EPC Mode under NHO-Gen Pkg - 2 (NHIDCL) (618395) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	02/2023 (10/2026)	512.43 (512.43)	164.66	53.49
1070	Widening and Up-gradation to 2-Lane with Paved Shoulder of configuration and geometric improvement from Km 0.000 to Km 16.990 on Chenani Sudhmahadev section of NH-244 in UT of Jammu and Kashmir to be executed on EPC basis (NHIDCL) (618397) (-) (-)	Jammu and Kashmir	03/2018 (11/2018)	11/2020 (12/2025)	255.9 (255.9)	242.42	94.06
1071	Up-gradation to 2-lane with Paved Shoulder from Km 20.300 to Km 29.030 of 8.730 Km length on Goha-Khellani section on NH-244 in UT of Jammu and Kashmir on EPC Mode Package II (NHIDCL) (618398) (-) (-)	Jammu and Kashmir	07/2020 (10/2020)	04/2022 (06/2026)	210.79 (210.79)	190.26	96.95
1072	Construction of Kishtwar bypass with 2 lane with paved shoulder from Design Km. 80.675 Dulhasti to km 95.550 Bandarkoot of 14.88 km & a link road to Kishtwar town from 0000 to 1.871 of length1.871 Km on Khellani - Kishtwar - Chattroo section in UT of Jammu and Kashmir on EPC Mode Pkg-4 (NHIDCL) (618399) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	08/2023 (06/2027)	859.67 (859.67)	360.47	50.64
1073	Construction & Upgradation to 2-lane with paved shoulder from Design Km 67.805 at the end of Km 83rd Tunnel near Dhrabshalla Ex. Km 83905 to Km 80.675 start of Kishtwar Bypass - Dulhasti Ex. Km 970751 of 12.870 Km length on chenani-Sudhmahadev-Goha Khellani-Kishtwar-vailoo-Donipawa-Ashajipora seition of NH-244 in the UT of J&K on EPC Mode under NHO-Gen Pkg-3 (NHIDCL) (618400) (-) (-)	Jammu and Kashmir	03/2021 (07/2021)	12/2022 (08/2025)	398.51 (398.51)	120.09	98.55
1074	Up-gradation to 4-lane with Paved Shoulder of Jammu-Akhnoor road section of NH-144A from Ganesh Vihar Km 6.000 to Khati Chowk Km 26.350 in UT of Jammu and Kashmir on EPC basis Pkg-3A (NHIDCL) (618406) (-) (-)	Jammu and Kashmir	03/2018 (07/2019)	07/2021 (11/2026)	322.49 (322.49)	388.64	92.21
1075	Jammu-Akhnoor Road Pkg-I (NHIDCL) (618407) (-) (-)	Jammu and Kashmir	03/2018 (01/2023)	01/2025 (10/2026)	245.3 (245.3)	97.2	75.29
1076	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XV [Junction with Hiranagar Road near village Gurha Baidaran to Junction with Jammu Ring Road NH-244A near Jakh village from Km 468100 to Km 503250] (NHAI) (618494) (-) (-)	Jammu and Kashmir	10/2021 (09/2022)	09/2024 (12/2026)	2714.95 (3716.56)	1833.59	89.52
1077	4/6L Access Control Expressway from Design Chainage Km 515.000 to 528.300 Kunjwani to Sidhra Section of NH-44 and from Design Chainage Km 550.900 to Km 566.520 Domel to Katra Section Phase II-Package XVII (NHAI) (618495) (-) (-)	Jammu and Kashmir	06/2022 (06/2023)	06/2025 (08/2027)	2894.74 (2894.74)	996.74	66.17
1078	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XVI Existing Jakh Vijaypur-Kunjwani section of NH-44 including spur Connectivity to Jammu Airport NH-144A [Km 503500 to km 514500] (NHAI) (618496) (-) (-)	Jammu and Kashmir	09/2021 (09/2022)	09/2024 (09/2026)	1821.72 (2522.56)	1237.76	94.14
1079	Delhi Amritsar Katra Expressway Phase-II Pkg XVIII Development and Upgradation of Four lane Access Control Expressway from Design Chainage KM 530.00 to KM 545.300 Sidhra to Domel Section of NH-44 (NHAI) (618497) (-) (-)	Jammu and Kashmir	12/2022 (11/2023)	11/2025 (06/2027)	975.38 (975.38)	606.46	67.5
1080	4L Ring road/bypass around Srinagar city from km 0.000 to km 42.100 Phase-I (NHAI) (618541) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	02/2024 (10/2026)	2919.96 (2604.76)	1829.2	88.5
1081	4L of existing Wayul Ganderbal Pandach Soura section of old NH-1 as a part of Srinagar Ring Road Phase IIA (NHAI) (618542) (-) (-)	Jammu and Kashmir	12/2024 (05/2026)	05/2028 (05/2028)	827.98 (827.98)	262.83	0
1082	4L of twin tube tunnel configuration including approaches from Marog to Digdol from Km.154.210 to Km.158.650 North Bound and from Km.155.940 to Km.160.260 South Bound of Ramban to Banihal Pkg-I of Old NH-1A New NH-44 (NHAI) (618543) (-) (-)	Jammu and Kashmir	07/2021 (08/2022)	08/2025 (12/2027)	1912.17 (1034.3)	404.01	30.5
1083	4L twin tube tunnel including approaches from Digdol to Khuni Nallah North Bound connecting with existing major bridge on NB and South Bound connecting with Tunnel T4 ,Single tube tunnel of Ramban to Banihal Pkg-II of Old NH-1A New NH-44 (NHAI) (618544) (-) (-)	Jammu and Kashmir	07/2021 (02/2022)	06/2024 (09/2026)	1401.87 (1020.99)	1053.1	87.1

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1084	4L of Km.165.092 to Km.171.855 North Bound and from Km.166.895 to Km.173.638 South Bound, excl. certain reaches of North Bound and South Bound of Ramban to Banihal Pkg-III of Old NH-1A New NH-44 (NHAI) (618545) (-) (-)	Jammu and Kashmir	07/2021 (02/2022)	08/2024 (06/2027)	614.48 (444.76)	306.05	42.8
1085	2L NH-1 from km 8.660 to km 33.775 Sumbal to Wayul to 4L dual carriageway NH standard as part of Srinagar Ring Road PhaseII [Design Ch. 41.907 to Ch. 66.609] (NHAI) (618547) (-) (-)	Jammu and Kashmir	11/2022 (12/2023)	06/2026 (06/2027)	961 (643.64)	459.97	53.28
1086	Construction of twin tube tunnels on Jammu Kashmir Ring Road NH-244A Between Design Ch. 50600 to 51700 and design Ch. 53535 to 55700 on EPC mode under residual NHDP component of Bharatmala Pariyojna (NHAI) (618549) (-) (-)	Jammu and Kashmir	11/2022 (06/2023)	06/2025 (12/2026)	242.65 (731.59)	677.46	83.87
1087	Corridor Efficiency Improvement including removal of black spots in Lakhanpur - Samba section of NH-44 from Chainage Km. 16.300 to Km. 74.100 (NHAI) (618550) (-) (-)	Jammu and Kashmir	06/2022 (12/2022)	06/2024 (12/2026)	855.74 (215.68)	203.36	74.63
1088	Upgradation and Strengthening of Chenani to Nashri Section via Patnitop of NH244 from Km 0.000 to Km 39.100 (NHAI) (618967) (-) (-)	Jammu and Kashmir	03/2024 (08/2024)	08/2026 (03/2027)	295.06 (295.06)	176.11	64.18
1089	Construction/upgradation to 2-lane with paved shoulder from Design Km 95.55 Bandarkoot to Km. 111.06 Chataroo of 15.52 Km length on Khellani-Kishtwar-Chataroo section on NH-244 in UT of Jammu and Kashmir on EPC Mode Pkg-5 (NHIDCL) (619038) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	02/2023 (03/2026)	497.09 (497.09)	270.8	99.97
1090	Widening and Strengthening of existing paveemnt to two lane with paved shoulders from km 116.00 to km 176.355 of NH-75E in the State of Jharkhand on EPC mode. (MoRTH) (618060) (-) (-)	Jharkhand	01/2022 (01/2023)	07/2024 (07/2026)	315.21 (315.21)	143.35	87
1091	Widening to 2-lane with paved shoulder from km 0.00 to 44.00 Kuru-Ghaghra section of NH-143A including re-construction of culverts and bridges. (MoRTH) (618084) (-) (-)	Jharkhand	02/2020 (08/2021)	08/2023 (09/2026)	153.01 (133.67)	100.77	95
1092	Widening and Strengthening/Reconstruction to Two Lane with Paved Shoulder/ Two Lane with paved shoulders with service road from km 0000 to km 42250 excluding design Ch. 03220 to 04200 & 28350 to 29060 of NH-320G in the state of Jharkhand under EPC mode (MoRTH) (618123) (-) (-)	Jharkhand	03/2022 (08/2023)	08/2025 (-)	423.18 (423.18)	5.46	0.01
1093	Construction of 2- Lane with paved shoulder from km 56.45 Dharampur More to 93.050 Pakur of NH-333A in the State of Jharkhand on EPC mode (MoRTH) (618127) (-) (-)	Jharkhand	03/2023 (11/2025)	05/2027 (05/2027)	255.73 (255.73)	10.06	10.4
1094	Widening and Reconstruction to 4-lane/4-lane with service road including structures from Pokharia More at Km 47.600 Ex. Km 50.230 to Govindpur at km 62.949 Ex. Km 65.325 of Nh-419 in the State of Jharkhand on EPC mode. (MoRTH) (618242) (-) (-)	Jharkhand	05/2022 (01/2024)	01/2026 (01/2027)	300.46 (300.46)	86.07	52.14
1095	Construction of Six lane elevated flyover including reconstruction/rehabilitation of existing pavement from Km 426230 to Km 430500 Length 4.27 Km at Nirsa in the Barwa Adda Panagarh section of NH-19 from Km.398.240 to Km.521.120 including Panagarh Bypass in the State of Jharkhand on EPC Mode. (NHAI) (618534) (-) (-)	Jharkhand	01/2025 (02/2026)	08/2028 (08/2028)	470.75 (470.75)	0.04	0
1096	Construction of Six lane elevated flyover including reconstruction/rehabilitation of existing pavement from Km 406100 to Km 411150 Length 5.05 Km at Gobindpur area in the Barwa Adda Panagarh section of NH-19 from Km.398.240 to Km.521.120 including Panagarh Bypass in the State of Jharkhand on EPC Mode. (NHAI) (618535) (-) (-)	Jharkhand	01/2025 (09/2025)	03/2028 (03/2028)	687.77 (442.52)	66.59	16.1
1097	4 Lane of CG/JH Border-Gumla from km 0.000 to km 32.370 of NH-43 in the State of Jhrkhand (NHAI) (618641) (-) (-)	Jharkhand	08/2024 (02/2026)	02/2028 (02/2028)	1325.8 (1325.8)	292.91	5.73
1098	4L of Palma to Gumla from km. 26.00 to km. 89.170 of NH-23 (NHAI) (618642) (-) (-)	Jharkhand	03/2020 (04/2022)	03/2024 (07/2026)	1882.93 (1895.75)	1369.19	99.89
1099	4L of Ormanjhi-Gola section from Km 81.450 to Km 53.600 of NH- 320BPKG-II (NHAI) (618644) (-) (-)	Jharkhand	02/2022 (06/2023)	06/2025 (12/2026)	1214.93 (1462.19)	993.58	86.57
1100	4L of Gola-BokaroJaina More section from Km 53.600 to Km 21.110 of NH-320PKG-1 (NHAI) (618645) (-) (-)	Jharkhand	02/2022 (06/2023)	06/2025 (10/2026)	1007.97 (1030.64)	609.9	78.1

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1101	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Donoreshan village to junction with NH-20 in Bongabar village from km 288.600 to km 325.500 Pkg -11 (NHAI) (618729) (-) (-)	Jharkhand	03/2023 (07/2026)	07/2028 (-)	1856.12 (1856.12)	261.76	0
1102	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Deoria village to Donoreshan village from km 253.000 to km 288.600 Pkg -10 (NHAI) (618730) (-) (-)	Jharkhand	03/2023 (05/2026)	05/2028 (05/2028)	1546.27 (1546.27)	82.65	3.96
1103	6L Greenfield Varanasi- Ranchi- Kolkata Highway from junction with NH-20 in Bongabar village to junction with NH-30 in Lepo village from km 325.500 to km 358.500 Pkg -12 (NHAI) (618733) (-) (-)	Jharkhand	03/2023 (07/2026)	07/2028 (-)	1525.52 (1525.52)	218.27	0
1104	4L Elevated corridor of Kalimandir-Dimna Chowk-Baliguma Jamshedpur Section of NH-33 New NH-18 from km 241940 to km 251961 Length 10.021 km (NHAI) (618736) (-) (-)	Jharkhand	03/2024 (09/2024)	03/2027 (03/2027)	936.26 (832.2)	310.35	46.79
1105	Grade separated Interchanges at Km. 113.730 junction with Ranchi Hazaribagh Road & Km. 139.225 junction with Ranchi Jamshedpur road on 4L Ranchi Bypass of NH-33 (NHAI) (618737) (-) (-)	Jharkhand	01/2025 (12/2025)	12/2027 (12/2027)	303.53 (5.58)	4.98	0
1106	4L from Km 147.450 Bhogu to Km 196.870 Sankha on NH-75 Sec-III (NHAI) (618830) (-) (-)	Jharkhand	10/2022 (11/2023)	11/2025 (03/2027)	1517.87 (1652.09)	1103	76.95
1107	4L from Km 95.400 Udaipura to Km 147.450 Bhogu on NH-75 Sec-II (NHAI) (618831) (-) (-)	Jharkhand	03/2023 (10/2024)	10/2026 (03/2027)	1436.8 (1301.54)	419.61	27.9
1108	4L from Km 55.00 Kuru to Km 95.400 Udaipura on NH-75 Sec-I (NHAI) (618832) (-) (-)	Jharkhand	02/2024 (01/2026)	01/2028 (01/2028)	1274.82 (1274.82)	231.62	9.66
1109	Barhi-Koderma Section of NH31 km 0.00 - km 27.5 (NHAI) (618863) (-) (-)	Jharkhand	02/2017 (11/2019)	08/2024 (07/2026)	662.44 (826.59)	824.95	98.5
1110	4L of NH-80 from km 215.00 to km 260.00 Mirza Chauki to Farkka Pkg-I (NHAI) (618947) (-) (-)	Jharkhand	03/2018 (12/2021)	07/2023 (10/2026)	1504.8 (1508.21)	1029.73	91.83
1111	4L of Basukinath- Deoghar Section of NH-114A (NHAI) (618949) (-) (-)	Jharkhand	09/2022 (12/2023)	12/2025 (08/2026)	1444.94 (1553.76)	723.48	90.02
1112	Construction of Bypass to NH-114A Connecting NH-333 and NH-133 Deoghar Bypass from design km 0.000 to design Km 49.000 (NHAI) (618950) (-) (-)	Jharkhand	11/2024 (01/2026)	01/2028 (01/2028)	1565.47 (1565.47)	55.24	9
1113	Construction of bypass around Chatra Town on NH-22 old NH-99 in the state of Jharkhand under EPC Mode (MoRTH) (619005) (-) (-)	Jharkhand	03/2023 (01/2026)	01/2028 (01/2026)	235.42 (199.2)	0.86	12
1114	Construction of Elevated corridor from Km. 135.650 to 136.300 on 63, from Km. 249 to Km. 250.050 on old NH-4 and from Km. 192.910 to Km. 193.350 on NH-218 from decongestion of traffic in Ranichennamma circle in Hubli city in the state of Karnataka on EPC basis (MoRTH) (617935) (-) (-)	Karnataka	08/2020 (06/2021)	06/2024 (11/2026)	298 (349.49)	232.09	65
1115	Construction of Srinivasapura Bypass from existing Km 453.890 Design Ch. 0000 to existing Km 461.450 Design Ch 10080 on NH-69 in the State of Karnataka Under NH O in EPC mode under Annual Plan 2022-23 NH-69-KNT-2022-23-966 dated 22.11.2022 (MoRTH) (617950) (-) (-)	Karnataka	11/2022 (07/2025)	01/2027 (01/2027)	204.42 (204.42)	0	20
1116	Construction of Chintamani Bypass from Design Ch.0000 Existing Ch.428880 to Design Ch.15400 Existing Ch.444010 on NH-69 in the State of Karnataka in EPC Mode under NHO Annual Plan 2022-23. NH-69-KNT-2022-23-989 dated 24.03.2023 (MoRTH) (617951) (-) (-)	Karnataka	03/2023 (01/2026)	07/2027 (07/2027)	314.55 (314.55)	4.03	10
1117	Widening to two lane with paved Shoulders from Km 40.00 to Km 75.00 Existing chainages of Mangalore - Tumkur section of NH-73 in the State of Karnataka on EPC Mode under Annual Plan 2021-22 Job No NH-73-KNT-2021-22-945 (MoRTH) (617955) (-) (-)	Karnataka	03/2022 (03/2023)	03/2025 (12/2026)	718.52 (718.52)	308.99	84
1118	Construction of Major Bridge at Km.180.865 across river Krishna on NH 167 Hagari Jadcherla section (MoRTH) (617989) (-) (-)	Karnataka	03/2019 (05/2019)	11/2021 (04/2027)	157.32 (187.61)	103.33	69

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1119	Widening of existing 2 lane to 4 lane with paved shoulder from Designed km 25.15 to km 56.70 Except Km 52.70 to 53.50 of NH-169 Nellisara Camp to Thirthahalli of NH-169 on Shimoga-Mangalore section in the state of Karnataka on EPC mode under Annual plan 2022-23 NH-169-KNT-2022-23-978 dated 08.03.2023 (MoRTH) (617997) (-) (-)	Karnataka	03/2023 (02/2026)	02/2028 (02/2028)	538.71 (538.71)	14.63	6
1120	Widening to existing 2 lane with paved Shoulder to 4 Lane with paved shoulder from design Km 153.00 to 168.27 Mala Gate to Karkala of NH -169 on Shimoga - Mangalore section in the state of Karnataka on EPC mode under Annula Plan 2021-22 Job No. NH-169-KNT-2021-22-949 (MoRTH) (617998) (-) (-)	Karnataka	03/2022 (02/2023)	02/2025 (11/2026)	177.94 (177.94)	115.6	83
1121	Widening to 2LPS from Km 67 to Km 115 on Kadur-Hosadurga section NH 173 in the state of Karnataka NH-173-KNT-2022-23-980 dated 13.03.2023 (MoRTH) (617999) (-) (-)	Karnataka	03/2023 (10/2024)	05/2026 (04/2027)	471.62 (471.62)	91.74	69.54
1122	Widening to 2-Lane with Paved Shoulders from Km 116.800 to 149.070Design Changes on Hosadurga - Holalkere Section of NH-173 in the State of Karnataka on EPC mode under Annual Plan 2021-22 Job no. NH-173-KNT-2021-22-946 (MoRTH) (618000) (-) (-)	Karnataka	03/2022 (10/2022)	02/2024 (06/2026)	170.34 (147.39)	106.96	100
1123	Widening to 2LPS from Km 71.00 to 104.00 Existing chainages Sarjapur to Pattadakallu on Bhanapur to Gaddanakeri section NH-367 in the State of Karnataka under NHO on EPC mode under Annual Plan 2022-23 NH-367-KNT-2022-23-972 dated 08.02.2023 (MoRTH) (618027) (-) (-)	Karnataka	02/2023 (03/2024)	03/2026 (12/2026)	445.62 (445.62)	0	90
1124	Construction of Bypass at Kuknoor, Yelburga, Gajendragada of Bhanapur Gaddanakeri section of NH-367 in the State of Karnataka under NHO on EPC mode under Annual Plan 2022-23. NH-367-KNT-2022-23-973 dated 08.02.2023 (MoRTH) (618028) (-) (-)	Karnataka	02/2023 (06/2025)	06/2027 (06/2027)	333.96 (333.96)	63.57	36
1125	Widening to 4 lane from Km. 133.00 to 158.04 design Chainage Km. 130.88 to 155.145 Shirur Cross to Gaddankeri of NH-367 in the State of Karnataka on EPC mode. Job No. NH-367-KNT-2021-22-930 (MoRTH) (618029) (-) (-)	Karnataka	01/2022 (01/2023)	01/2025 (03/2027)	350.69 (312.06)	199.09	81.62
1126	Widening to 2 lane with paved shoulder from Km. 103.225 Pattadakal to Km. 133.00 Shirur cross of NH-367 in the state of Karnataka on EPC Mode.Job No. NH-367-KNT-2021-22-934 (MoRTH) (618030) (-) (-)	Karnataka	02/2022 (11/2022)	05/2024 (12/2026)	264.14 (264.14)	3.78	0
1127	Balance work of Construction of Two/Four lane with paved shoulder from Km 422.000 to 523.600 Chitradurga to Shivamogga of NH-13 in the state of Kanataka on EPC mode. (MoRTH) (618031) (-) (-)	Karnataka	01/2021 (12/2021)	12/2025 (08/2026)	516.96 (516.96)	121.75	98
1128	Widening to Two Lane with Paved Shoulders from KB Cross to Chunchanahalli ie., Design Ch. 485240 Km Existing Km 494.000 to Design Ch. 523393 Km Existing km 533.152 & From Design Ch. 530393 Existing Km 540.175 to Design Ch. 534476 Existing Km 544.200 at Nelligere of NH-150A on EPC mode under Annual Plan 2022-23 NH-150A-KNT-2022-23-977 dated 08.03.2023 (MoRTH) (618086) (-) (-)	Karnataka	03/2023 (07/2025)	01/2027 (01/2027)	617.28 (617.28)	7.59	48.5
1129	Widening to intermediate/two lane to 2 lane with paved shoulder from Existing chanages Km 112.750 to 142.00 Liingasur to Mudabal cross & from Km. 147.070 to Km. 149.070 Maski city limit of Jewargi Chamrajnagar setion of NH-150A in the state of Karnataka on EPC mode. Job No. NH-150A-KNT-2021-22-951 (MoRTH) (618087) (-) (-)	Karnataka	03/2022 (01/2023)	07/2024 (08/2026)	255.88 (255.88)	182.8	96
1130	Widening to Two Lane with Paved Shoulders from Km 0.00 Design Chainage 0.00 to Km 23.338 Design Chainage 23310 of NH-166E MH/KNT Border- Kanamadi- Bijjargi-Tikota section in the state of Karnataka in EPC Mode under Annual plan 2022-23 NH-166E-KNT-2022-23-974 (MoRTH) (618095) (-) (-)	Karnataka	02/2023 (09/2024)	03/2026 (03/2027)	196.05 (196.05)	0	71
1131	Widening to 4 lane from Km 51.60 to 76.20 Hebri to Parkala and from Km 85.20 to 88.90 Karavali junction to Malpe of Thirthahalli-Udupi-Malpe Section of NH-169A in the State of Karnataka on EPC Mode under Annual plan 2021-22 Job No. NH-169A-KNT-2021-22-927 (MoRTH) (618109) (-) (-)	Karnataka	01/2022 (12/2022)	12/2024 (11/2026)	355.72 (355.72)	215.43	88.33
1132	Widening to 2 Lane with Paved Shoulders from design Km 103.200 Existing Km 103.200 to design Km 116.700 Existing Km 118.470 on AP/KNT Border to Sira Section of NH-544E in the State of Karnatakaon EPC mode under Annual plan 2022-23 (MoRTH) (618147) (-) (-)	Karnataka	01/2023 (03/2024)	09/2025 (08/2026)	166.58 (166.58)	42.48	65

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1133	Widening to 4LPS of NH-548B from Km 80.000 Near Murgundi to Km 140.200 Near Chikkodi excluding length from Km 118.450 to Km 128.450 in the State of Karnataka under NH O on EPC Mode under Annual Plan 2022-23 - Package 1 NH-548B-KNT-2022-23-979 dated 09.03.2023 (MoRTH) (618148) (-) (-)	Karnataka	03/2023 (04/2026)	04/2028 (04/2028)	785.79 (785.79)	6.15	0
1134	Widening to two lane with paved shoulders from Km 0.00 to 102.310 Design Chainage of NH-548B Murrum-Maharashtra Border in the State of Karnataka (MoRTH) (618149) (-) (-)	Karnataka	02/2023 (01/2025)	01/2027 (01/2027)	957.09 (957.09)	288.15	60.21
1135	Widening to 4LPS of NH-548B from Km 118.450 Near Shirguppi to Km 128.450 Near Ankali in the State of Karnataka under NH O on EPC Mode Under Annual Plan 2022-23 NH-548B-KNT-2022-23-982 (MoRTH) (618151) (-) (-)	Karnataka	03/2023 (05/2026)	05/2029 (-)	1084.29 (1084.29)	0	0
1136	Construction of 2 Lane with paved shoulder from km 55.6 to km 90.7 existing chainages of NH-766C complete Realignment of 13.76 km with 2 major Bridges across Sharavathi Backwaters on EPC mode under Annual Plan 2022-23 in the state of Karnataka NH-766C-KNT-2022-23 dated 14.10.2022 (MoRTH) (618184) (-) (-)	Karnataka	01/2023 (02/2024)	02/2026 (12/2027)	313.56 (313.56)	151.04	65
1137	Widening to 2LPS from Km 0.000 to 37.850 Except Ex. Km 24.45 to 27.20 of NH-766c Byndoor-Ranebennur Section in the state of Karnataka on EPC Mode under Annual Plan 2022-23 NH-766C-KNT-2022-23-969 dated 30.12.2022 (MoRTH) (618185) (-) (-)	Karnataka	12/2022 (08/2025)	08/2027 (08/2027)	394.95 (394.95)	0	12
1138	Widening to two lane with paved shoulder of NH-73New spur road Ujire - Dharmasthala - Periyashanthi in the State of Karnataka under NHO on HAM Mode Job No. NH-73Spur-KNT-2023-24-996 (MoRTH) (618189) (-) (-)	Karnataka	01/2024 (11/2025)	11/2027 (11/2027)	613.65 (613.65)	0	23.16
1139	4/6L of Bangalore - Pune Section of bypass connecting Dharwad - Hubli from km. 403.80 to km. 433.20 (NHAI) (618517) (-) (-)	Karnataka	12/2021 (03/2023)	09/2025 (05/2027)	1135.39 (763.36)	744.25	83.19
1140	Davanagere - Haveri of NH-48 Old NH-4 from km. 260.00 to km. 338.923 (NHAI) (618518) (-) (-)	Karnataka	01/2017 (01/2018)	07/2020 (09/2026)	1454.67 (1805.84)	1273.49	98.87
1141	4L of km 0.00 to km 42.00 of Dobbaspeta to Doddaballapura Bypass section of NH-648 old NH-207] [Bangalore Ring Road Pkg 1] (NHAI) (618520) (-) (-)	Karnataka	08/2020 (04/2021)	04/2023 (08/2026)	1438.74 (1786.57)	1228.99	99.2
1142	6L of MH/KN Border Nimbal Village to KN/TS Border Singnodi Village from Km. 26.000 to Km. 97.000 in Gulbarga of NH-150C Pkg-II (NHAI) (618630) (-) (-)	Karnataka	02/2022 (12/2022)	06/2025 (11/2026)	2355.56 (1923.3)	964.75	79.87
1143	4 Lane with PS from Des. Ch 228.500 to Des. Ch. 273.400 of Belgaum-Hungund-Raichur Section of NH 748 A Package-6 (NHAI) (618649) (-) (-)	Karnataka	03/2023 (11/2024)	11/2026 (06/2027)	1246.15 (1012.78)	381.27	53.8
1144	4 Lane with PS from Des. Ch 89.900 to Des. Ch. 136.100 of Belgaum-Hungund-Raichur Section of NH-748A Package-3 (NHAI) (618650) (-) (-)	Karnataka	01/2024 (04/2025)	04/2027 (02/2028)	1363.9 (1219.62)	302.3	22.5
1145	4 Lane with PS from Des. Ch 43.800 to Des. Ch. 89.900 of Belgaum-Hungund-Raichur Section of NH-748A Package-2 (NHAI) (618651) (-) (-)	Karnataka	02/2024 (03/2025)	02/2027 (07/2027)	1427.88 (1293.94)	594.55	48.8
1146	4LPS Access Controlled Highway of Bellary Bypass Balance work from Ch. 254750 to Ch. 266837 and construction of 4LPS from Ch. 277.690 to Ch. 278.690 at D. Hirehal Village Balance work of NH 150A of Bellary Byrapura Section (NHAI) (618697) (-) (-)	Karnataka	02/2024 (08/2024)	07/2026 (10/2027)	626.01 (284.05)	112.21	38.08
1147	4L of Addahole Near Gundya to Bantwal Cross section Pkg-02 from Design Km 270.270 to Design km 318.55 including flyover at Kalladka Town including approaches from Km. 311.57 to Km. 313.67 of NH-75 Old NH-48 (NHAI) (618702) (-) (-)	Karnataka	12/2020 (11/2021)	11/2023 (12/2026)	1660.19 (1318.24)	1451.9	94.21
1148	Bangalore-Nidagatta Pkg. I (NHAI) (618706) (-) (-)	Karnataka	02/2018 (05/2019)	11/2021 (07/2026)	3496.01 (4087.42)	4315.22	99.19
1149	Additional works under BM1 to ensure road safety under 6L of Bengaluru Mysuru Access control with close toll from Km.17.300 to Km.136.300 of NH-275 (NHAI) (618707) (-) (-)	Karnataka	11/2024 (01/2026)	01/2028 (05/2028)	738.37 (738.37)	17.91	9.67

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1150	4L of Left-Over Works of Hospet-Bellary -Karnataka/AP border from Km.280.080 Dec.Ch. to Km.375450Des.Ch. of NH-63 New-67 (NHAI) (618709) (-) (-)	Karnataka	03/2023 (05/2023)	05/2025 (04/2028)	1340.15 (992.6)	922.07	91.67
1151	Belakeri Port to Kumta - Sirsi road from km 0.00 - km 4.265 of Belekeri Port Road Link Rd. and km 4.965 - km 60.00 of SH-69 (NHAI) (618799) (-) (-)	Karnataka	03/2018 (12/2020)	12/2022 (08/2026)	456.79 (456.79)	471.29	94.98
1152	4L PS from near Hemmige Village Periyapatna - Hassan Road Jn. to near Hunsur - KR Nagar Jn section from Km. 144.900 to Km. 169.000 of NH-275 Pkg. III (NHAI) (618870) (-) (-)	Karnataka	02/2023 (04/2025)	04/2027 (01/2028)	883.62 (1726.65)	437.77	24.27
1153	4L PS from Near Guddehosur to Start of Kushalnagara Bypass to near Hemmige Village Periyapatna - Hassan Road Jn from Km. 122.200 to Km. 144.900 of NH-275 Pkg. II (NHAI) (618871) (-) (-)	Karnataka	02/2023 (12/2025)	12/2027 (04/2028)	909.86 (896.42)	313.21	13.61
1154	4L PS from near Hunsur - KR Nagar Junction to near Yalachahalli village KR Nagara - Yelawala Road Junction fcrom Km 169.000 to Km 195.550 of NH-275 Pkg-IV (NHAI) (618872) (-) (-)	Karnataka	02/2023 (04/2025)	04/2027 (03/2028)	1062.76 (952.03)	272.54	18.13
1155	4L PS from near Yalachahalli village KR Nagara - Yelawala Road junction to Srirangapatna Bypass Near Paschima Vahini from km 195.550 to Km 214.535 of NH-275 Pkg-V (NHAI) (618873) (-) (-)	Karnataka	01/2023 (04/2025)	04/2027 (03/2028)	1272.71 (1203.2)	462.59	16.45
1156	4L of Bettadahalli- Shivamogga section from Km.170.415 to km. 226.750 of NH-206 Tumkur- Shivamogga Pkg-IV (NHAI) (618887) (-) (-)	Karnataka	01/2019 (10/2021)	10/2023 (03/2027)	2082.98 (2545.11)	1621.81	83.78
1157	4L of Sannur to Bikarnakatte section from Km 691.350 to Km 736.362 of NH-169 Karkala - Mangalore Package-III (NHAI) (618896) (-) (-)	Karnataka	03/2021 (10/2022)	10/2024 (04/2027)	1386.41 (2038.71)	1213.06	76.1
1158	4L Expressway from Km 26.400 to km 53.500 of Malur to Bangarpet section of Bangalore-Chennai Expressway Phase-I Package-II (NHAI) (619065) (-) (-)	Karnataka	12/2020 (09/2021)	09/2023 (09/2026)	1745 (1729.63)	1103.13	99.8
1159	Tumkur - Nelamangala 6L (NHAI) (619071) (-) (-)	Karnataka	03/2021 (08/2022)	08/2025 (03/2027)	2032.15 (1664.2)	1069.89	61.16
1160	Bangalore/TN border to Hoskote (NHAI) (619072) (-) (-)	Karnataka	02/2022 (02/2023)	02/2025 (11/2026)	1181.68 (1297.76)	1150.16	94.89
1161	4L of 42.000 to km 80.00 of Dodaballapur Bypass to Hoskote section of NH-648 Old NH-207 [Bangalore Ring Road Pkg 2] (NHAI) (619073) (-) (-)	Karnataka	02/2020 (02/2021)	02/2023 (08/2026)	1317.74 (1846.52)	1304.65	99.2
1162	Goa / Karnataka Km.93.700 to Kundapur Km.283.30 (NHAI) (619096) (-) (-)	Karnataka	07/2012 (03/2014)	08/2016 (07/2026)	1644.92 (1990.99)	1848.87	97.94
1163	4 Lane with PS from Des. Ch 182.300 to Des. Ch. 228.500 of Belgaum-Hungund-Raichur Section of NH 748 A Package-5 (NHAI) (619106) (-) (-)	Karnataka	03/2023 (11/2024)	11/2026 (08/2027)	1141.88 (868.65)	254.24	37.9
1164	4 Lane with PS from Des. Ch 136.100 to Des. Ch. 182.300 of Belgaum-Hungund-Raichur Section of NH-748A Package-4 (NHAI) (619107) (-) (-)	Karnataka	02/2024 (09/2025)	09/2027 (04/2028)	1311.41 (1123.35)	227.3	13.18
1165	4 Lane with PS from Des. Ch 0.000 to Des. Ch. 43.800 of Belgaum-Hungund-Raichur Section of NH-748A Package-1 (NHAI) (619108) (-) (-)	Karnataka	02/2024 (06/2025)	06/2027 (10/2027)	1452.43 (1256.55)	490.31	38.45
1166	Hassan km 184.912 to Maranahally km 230.060 of NH - 75 in Karnataka (NHAI) (619117) (-) (-)	Karnataka	12/2015 (03/2017)	03/2019 (07/2026)	1021.57 (1091.4)	1068.77	97.8
1167	Nidagatta-Mysore Pkg II (NHAI) (619120) (-) (-)	Karnataka	02/2018 (12/2019)	06/2022 (07/2026)	2919.8 (4113.89)	3713.89	99.19
1168	Yekkambi-Haveri (NHAI) (619138) (-) (-)	Karnataka	09/2021 (03/2022)	03/2024 (01/2028)	309.9 (309.9)	94.8	24.7

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1169	BRT Tiger Reserve Boundary Km.287.500 to Bangalore Section Km.458.420 of NH-209 in Karnataka (NHAI) (619150) (-) (-)	Karnataka	04/2016 (08/2017)	08/2019 (07/2026)	2082.69 (2859.93)	2242.71	99.7
1170	Belgaum-Khanapur Pkg I Km 0.000-Km 30.800 of NH-4A (NHAI) (619164) (-) (-)	Karnataka	03/2018 (03/2019)	09/2021 (03/2027)	1214.3 (1195.74)	917.82	75.63
1171	6L of MH/KN Border Nimbal Village to KN/TS Border Singnodi Village from Km. 97.000 to Km. 162.500 in Yadgir of NH-150C Pkg-III (NHAI) (619211) (-) (-)	Karnataka	03/2022 (04/2023)	10/2025 (11/2026)	2104.7 (2065.83)	983.95	73.9
1172	4L of Channarayapatna Bypass and Hassan Bypass with structures in Devihalli - Hassan section (NHAI) (619214) (-) (-)	Karnataka	04/2020 (01/2021)	01/2023 (10/2026)	688 (684.54)	600.43	82.34
1173	4L Tumkur-Shimoga Pkg-I from Mallasandra to Karadi village of NH-206 from Km. 12.300 to Km. 65.195 (NHAI) (619218) (-) (-)	Karnataka	02/2018 (10/2019)	10/2021 (07/2026)	1364.14 (1692.12)	1336.5	100
1174	4L of Tumkur-Shimoga Pkg-II from Km 65.195 Karadi to Km 121.900 Banawara of NH-206 (NHAI) (619219) (-) (-)	Karnataka	02/2018 (10/2019)	10/2021 (12/2026)	1505.85 (1989.89)	1297.99	99.98
1175	Tumkur-Shimoga Pkg-III from Km 121.900 Banawara to Km 170.415 Bettadahalli of Old NH-206 (NHAI) (619220) (-) (-)	Karnataka	02/2018 (03/2021)	03/2023 (12/2026)	1444.5 (1834.81)	872.92	98
1176	Widening to 2 Lanes with paved shoulders from Km.87/000 to 133/720 Nattukal to Thanau Jn. in Palakkad of NH-966 Old NH-213 on EPC mode Basis under NHO Annual Plan 2016-17 in the state of Kerala (MoRTH) (618070) (-) (-)	Kerala	02/2017 (08/2017)	08/2019 (06/2026)	294.28 (315.63)	0	98
1177	6L of Chengala - Neeleshwaram from km. 56.200 to km. 93.468 (NHAI) (618595) (-) (-)	Kerala	06/2020 (10/2021)	04/2024 (03/2027)	1746.45 (2538.06)	1447.31	90.82
1178	6L of Taliparamba to Muzhappilangad from Km 134.650 to Km 170.6 of NH-66 (NHAI) (618596) (-) (-)	Kerala	08/2020 (11/2021)	05/2024 (01/2028)	2714.6 (3557.65)	2020.24	83.4
1179	6L of Azhiyur-Vengalam from km. 189.200 to km. 230.400 of NH-66 (NHAI) (618597) (-) (-)	Kerala	10/2020 (10/2021)	07/2024 (03/2028)	3205.77 (3898.46)	2406.73	60.07
1180	6L Minor Bridge Paloli Palam at km. 203.160 & Major Bridge Morad at km. 204.895 and allied works (NHAI) (618598) (-) (-)	Kerala	03/2020 (12/2020)	06/2022 (07/2026)	210 (216.94)	190.46	100
1181	6L of Ramanatukkara Junction to start of Valanchery bypass section of NH-66 (NHAI) (618599) (-) (-)	Kerala	01/2021 (01/2022)	07/2024 (07/2026)	4924.11 (4919.46)	3635.17	100
1182	6L of Valanchery bypass to Kappirikkad of NH 66 from km. 298500 to km 335850 (NHAI) (618600) (-) (-)	Kerala	02/2021 (01/2022)	07/2024 (07/2026)	4023.94 (4023.94)	2476.49	100
1183	6L of Kappirikkad to Thalikulam section from km 335.85 to km 369.015 of NH - 66 old NH-17 (NHAI) (618601) (-) (-)	Kerala	06/2021 (09/2022)	01/2025 (06/2027)	4225.59 (4225.59)	3329.11	95.27
1184	6L of Thalikulam to Kodugallur section from km 369.015 to km 397.850 of NH - 66 old NH-17 (NHAI) (618602) (-) (-)	Kerala	06/2021 (09/2022)	02/2025 (06/2027)	4302.06 (4302.06)	3312.67	94.55
1185	6L of Kodugallur to Edappally section from km 397.750 to km 423.780 of NH - 66 old NH-17 (NHAI) (618603) (-) (-)	Kerala	11/2021 (10/2022)	04/2025 (05/2027)	3465.82 (3606.2)	2171.55	70.99
1186	Aroor-Thuravoor Thekku (NHAI) (618604) (-) (-)	Kerala	08/2022 (02/2023)	01/2026 (12/2026)	2429.52 (2382.83)	1791.8	91.27
1187	Thuravoor Thekku-Paravoor (NHAI) (618605) (-) (-)	Kerala	09/2021 (03/2022)	09/2024 (05/2027)	2878.97 (2638.67)	2495.62	80.85
1188	Paravoor-Kottankulangara (NHAI) (618606) (-) (-)	Kerala	12/2021 (08/2022)	02/2025 (03/2027)	3273.61 (3200.24)	2858.39	71.2

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1189	Kottankulangara- Start of Kollam Bypass (NHAI) (618607) (-) (-)	Kerala	06/2021 (04/2022)	10/2024 (03/2027)	2842.14 (3680.49)	2373.25	73.89
1190	Widening/Development of Existing NH-85 from Km 0.000 to Km 124.636 section to 2L/LPS section in the state of Kerala on EPC Mode under Bharatmala Pariyojana (NHAI) (618708) (-) (-)	Kerala	09/2022 (06/2023)	06/2025 (03/2027)	1187.47 (1265.47)	778.5	66.88
1191	Kozhikode Bypass Calicut Bypass Vengalam Jn. to Ramanattukara Jn. (NHAI) (619098) (-) (-)	Kerala	02/2018 (02/2021)	02/2023 (07/2026)	1424.77 (2139.18)	1064.53	98.75
1192	6L of Perole Nileswhar town to Taliparamba from Km 94.248 to Km 134.650 of NH-66 (NHAI) (619206) (-) (-)	Kerala	06/2020 (10/2021)	01/2024 (03/2027)	3041.65 (3867.66)	2526.41	86.65
1193	Start of Kollam Bypass - Kadambattukonam (NHAI) (619207) (-) (-)	Kerala	06/2021 (10/2022)	03/2025 (06/2027)	2641.37 (3309.06)	1990.7	81.8
1194	Kadambattukonam-Kazhakuttom (NHAI) (619208) (-) (-)	Kerala	12/2021 (07/2022)	01/2025 (05/2027)	3635.64 (3526.33)	2124.09	44.34
1195	Kargil Zanskar Road (NHIDCL) (618408) (-) (-)	Ladakh	03/2021 (07/2021)	01/2023 (08/2026)	398.37 (398.37)	325.95	95.02
1196	Widening & Up-gradation to 2 lane with Paved shoulder of NH-301 Kargil- Zanskar Road from Design km 57.000 Ex. Km. 57.905 to Km 87.000 Ex. Km. 88.2491 of 30.000 Km length Pkg-III (NHIDCL) (618409) (-) (-)	Ladakh	03/2021 (07/2021)	01/2023 (07/2026)	381.01 (381.01)	299.33	89.3
1197	Widening & Up-gradation to 2 lane with paved shoulder of NH-301 Kargil- Zanskar Road from Design Km .30.040 Ex. Km. 30.000 to Design Km 57.000 Ex. Km. 57.905 of 26.960 Km length Pkg-II (NHIDCL) (618410) (-) (-)	Ladakh	03/2021 (07/2021)	01/2023 (10/2026)	404.89 (404.89)	359.99	84.68
1198	Construction of Rewa Bypass to 4-lane with paved shoulder along with service road from Ratahara Chowk to Chorhata Chowk Road section of NH-30 from km 00.000 to 19.200 in the State of Madhya Pradesh on Hybrid Annuity Mode HAM. (MoRTH) (617909) (-) (-)	Madhya Pradesh	03/2024 (02/2025)	02/2027 (02/2027)	648.05 (648.05)	0	50
1199	Rehabilitation and upgradation Umaria to Shahdol section of NH-78 from Existing Km. 68/4 to Km. 142/2 to 2LPS including construction of Birshinghpur and Shahdol Bypass on EPC mode under NHDP-IVA (MoRTH) (617911) (-) (-)	Madhya Pradesh	03/2015 (08/2015)	07/2017 (08/2026)	511.83 (613.16)	0	94.5
1200	Upgradation and reconstruction of Shahpura-Dindori Section of NH 45 from Km 103.700 Design to Km 164.580 Design including 3 bypasses Total length 60.88km to Two lane with paved shoulder configuration along with One time improvement in 03 nos of bypassed built-up areas in a total length of 12.341 km in the State of Madhya Pradesh on EPC mode (MoRTH) (617914) (-) (-)	Madhya Pradesh	03/2022 (01/2024)	12/2025 (06/2027)	241.23 (250.09)	0	32.52
1201	Upgradation of Dindori-Sagartola-kabichabutra MP-CG border section of NH -45 from km 000Design to km 77.00 Design to Two lane with paved shoulder configration along with one time improvement in 04 nos. of bypaased built-up areas in a total length of 9.1 km in the state of Madhya Pradesh on EPC mode. (MoRTH) (617915) (-) (-)	Madhya Pradesh	01/2022 (09/2023)	09/2025 (07/2026)	329.14 (319.09)	0	100
1202	Upgradation & widening of Jharkheda- Berasia - Dholkhedi from design km 0000 to km 87900 Design length 87.90km of NH-346 including 3 nos. bypasses of 13.10 Km in the State of Madhya Pradesh under EPC mode. (MoRTH) (618019) (-) (-)	Madhya Pradesh	03/2022 (05/2023)	05/2025 (09/2026)	365.21 (365.21)	0	89
1203	Rehabilitation & Upgradation of KurwaiMungaoliChanderi Road section of NH-346, from Design Chainge 0.000 to 81.300 Km Total length 83.1 km to Two lane with paved shoulder configuration along with One time improvement in 07 nos of bypassed built-up areas in a total length of 22.615 km in the state of Madhya Pradesh on EPC mode. (MoRTH) (618020) (-) (-)	Madhya Pradesh	03/2022 (02/2023)	02/2025 (12/2026)	386.49 (386.49)	164.41	67.57
1204	Up-gradation of Pichhore- Dinara section of NH-346 from Km 292.750 to 334.550 to two lane with paved shoulders in the state of Madhya Pradesh on EPC mode (MoRTH) (618021) (-) (-)	Madhya Pradesh	02/2024 (12/2025)	06/2027 (06/2027)	425.97 (425.97)	0	31.29
1205	Rehabilitation & Upgradation of existing intermediate lane to two Lane with paved shoulder from km. 0.600 Gulganj bypass on NH-34 to km. 43.00 Barna River length 42.400 km. on Gulganj-Amanganj-Pawai-Katni NH43 Extn. in the state of Madhya Pradesh on EPCmode. (MoRTH) (618035) (-) (-)	Madhya Pradesh	03/2023 (11/2024)	05/2026 (12/2026)	275.4 (275.4)	0	54.25

All Ongoing Projects							JUNE 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1206	Upgradation and reconstruction of existing intermediate lane to two Lane with paved shoulder configuration from km. 43.00 Barna River to km. 77.00 ken river length 34.00 km. on Gulganj-Amanganj-Pawai-Katni NH43 Extn. along with One time improvement in 01 no. of bypassed built-up area in a total length of 1.585 km in the state of Madhya Pradesh on EPCmode. (MoRTH) (618036) (-) (-)	Madhya Pradesh	03/2023 (11/2024)	11/2026 (03/2027)	315.55 (315.55)	0	40.02
1207	Upgradation and reconstruction of Dindori - Mandla Section of NH 543 from Km 77100 Design to Km 170580 Design Total length 93.48km to Two lane with paved shoulder configuration along with One time improvement in 04 nos of bypassed built-up areas in a total length of 7.23 km in the state of Madhya Pradesh on EPC mode (MoRTH) (618043) (-) (-)	Madhya Pradesh	03/2022 (01/2024)	07/2026 (09/2026)	492.12 (523.71)	0	88
1208	Upgradation of Shahdol- Sagartola Section of NH 543 from km 0000 to km 69400 to 2 lane with paved shoulders under Hybrid Annuity Mode HAM in the State of Madhya Pradesh (MoRTH) (618044) (-) (-)	Madhya Pradesh	02/2024 (03/2026)	03/2028 (-)	851.4 (851.4)	0	0
1209	Construction of Kaithi-Padaria Kala bypass, Patna-Tamoli bypass, Jaso bypass and Nagod bypass total length 15.44 Km to 2-lane with paved shoulders flexible pavement on NH-943 in the State of Madhya Pradesh on EPC Mode. (MoRTH) (618068) (-) (-)	Madhya Pradesh	03/2022 (10/2023)	10/2025 (12/2026)	158.36 (158.36)	0	60
1210	Upgradation of Nasrullagani-Rehti-Budhni Sction to 2-lane with paved shoulder from Km 0150 to Km 50500 of NH-146B in the state of Madhya Pradesh on EPC mode. (MoRTH) (618085) (-) (-)	Madhya Pradesh	12/2021 (04/2023)	10/2024 (08/2026)	305.12 (293.74)	0	89.07
1211	Construction of Kasrawad bypass, Selani bypass, Khargone bypass & Bistan bypass Total length. 31.950 km Section of NH-347 C to Two lane with paved shoulder configuration in the State of Madhya Pradesh on EPC mode. (MoRTH) (618129) (-) (-)	Madhya Pradesh	03/2023 (12/2024)	12/2026 (12/2026)	467.93 (467.93)	0	86.03
1212	Construction of Morena bypass, Ambah bypass & Porsa bypass Totat length 27.16 km Section of NH-552 Ext. to TWo lane with paved shoulder configuration in the state of Madhya Pradesh on EPC mode (MoRTH) (618156) (-) (-)	Madhya Pradesh	02/2023 (10/2024)	10/2026 (10/2026)	492.66 (492.66)	0	73.5
1213	Construction of Ater realignment & Bhind bypass Total length. 21.50 km Section of NH-552Extn. to Two lane with paved shoulder configuration in the State of Madhya Pradesh on EPC mode. (MoRTH) (618157) (-) (-)	Madhya Pradesh	03/2023 (12/2024)	06/2026 (12/2026)	348.06 (348.06)	0	79
1214	Upgradation of Goras to Shyampur Road section of NH-552 Ext., from Design Chainge 48.400 to 111.800 Km Total length 63.40 km to two lane with paved shoulder configuration along with One time improvement of 8.91 km in the state of Madhya Pradesh on EPC mode (MoRTH) (618158) (-) (-)	Madhya Pradesh	03/2023 (12/2024)	12/2026 (12/2026)	416.96 (416.96)	0	15.49
1215	Construction of Two lane with paved shoulder configuration of Shujalpur Bypass section of NH-752C from km 33100 Design to km. 42570 Design total design length 10.470 km in the State of Madhya Pradesh on EPC mode. (MoRTH) (618170) (-) (-)	Madhya Pradesh	03/2023 (03/2024)	09/2025 (12/2026)	214.07 (214.07)	0	41.59
1216	Work of Upgradation of Jirapur-Pachore Road including Pachore, Jirapur, Chhapiheda & Khujner Bypasses from 0000 to 58790 Design Length 58.79 Km section of NH-752C to 2LPS in the State of Madhya Pradesh under EPC mode (MoRTH) (618171) (-) (-)	Madhya Pradesh	03/2022 (01/2024)	01/2026 (12/2026)	352.69 (352.69)	0	57.26
1217	Bypass on Western side of Gwalior City (NHAI) (618619) (-) (-)	Madhya Pradesh	03/2025 (01/2026)	01/2028 (01/2028)	998.95 (998.95)	195.11	0
1218	Additional works 2VUPs, MR-10 junction flyover and underpass in Six lane Indore-Dewas section of NH-52 in the state of Madhya Pradesh on EPC Mode (NHAI) (618620) (-) (-)	Madhya Pradesh	08/2022 (01/2023)	07/2024 (03/2027)	207.77 (211.27)	142.54	79.72
1219	Indore - Edlabad Pkg-II [Tejajinagar to Balwara] (NHAI) (618621) (-) (-)	Madhya Pradesh	03/2022 (01/2023)	01/2025 (10/2026)	1162.8 (1530.82)	811.16	87.3
1220	4L of Indore - Boregaon Pkg-III [Balwara to Dhangaon] from km. 42.260 to km. 82.660 of NH347BG & 753L (NHAI) (618622) (-) (-)	Madhya Pradesh	01/2021 (04/2022)	04/2024 (10/2026)	1001.69 (888.81)	825.56	90.5
1221	4L Boregaon Buzurg to Shahpur Pkg I of Boregaon Buzurg to Muktainagar of NH 753L (NHAI) (618623) (-) (-)	Madhya Pradesh	11/2022 (02/2024)	01/2026 (10/2026)	1504.37 (1132.34)	527.34	90.1
1222	4L Greenfield Rudhi to Deshgaon Pkg V of Betul-Khandwa/Deshgaon (NHAI) (618654) (-) (-)	Madhya Pradesh	11/2022 (10/2023)	10/2025 (08/2027)	521.21 (469.68)	199.48	63.79

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1223	2L PS of Roshni to Ashapur Section of NH-347B from Design KM Ch. 89.900 to 114.000 KM Package III of Betul Khandwa (NHAI) (618655) (-) (-)	Madhya Pradesh	03/2024 (08/2024)	08/2026 (08/2026)	200.99 (120.75)	126.72	98.26
1224	4L from km 0.000 to 42.040 Bhopal Ratnaigiri Tiraha to Vidisha Morikodi (NHAI) (618661) (-) (-)	Madhya Pradesh	10/2024 (11/2025)	11/2027 (11/2027)	1032.3 (1038.18)	178.3	17.11
1225	4L Vidisha Gyaraspur section of NH-146 from Design Chainage km 59475 existing chainage km 81240 to Design Chainage km 88361 existing chainage km 110.315 (NHAI) (618662) (-) (-)	Madhya Pradesh	10/2024 (03/2026)	03/2028 (03/2028)	980.2 (980.2)	96.41	11.1
1226	i 4L Vidisha to Hinotiya from km 0.000 to Km 27.000 Vidisha Mehulwa-Talbehat Pkg-I Section of NH- 346 and ii 4L Vidisha to Morikori from Km 39.000 to 59.476 section of NH-146 (NHAI) (618663) (-) (-)	Madhya Pradesh	09/2022 (12/2023)	12/2025 (12/2026)	1003.87 (941.12)	398.13	90.04
1227	Berkhedi to Godpehra on NH-44 Sagar link road (NHAI) (618664) (-) (-)	Madhya Pradesh	02/2022 (11/2022)	11/2024 (12/2026)	524.84 (471.31)	385.96	92.05
1228	4- Laning of Mohari to Satai Ghat section NH-934 from Km 50300 to Km 89875 Total length 39.575 km Package-2 in the State of Madhya Pradesh on EPC Mode (NHAI) (618666) (-) (-)	Madhya Pradesh	08/2022 (08/2024)	08/2026 (08/2026)	710.92 (539.08)	505.77	95.66
1229	4L of near Satai Ghat to Chowka section of NH-34 from D. Ch. 89.875 to D. Ch. 145.000 Package-3 (NHAI) (618667) (-) (-)	Madhya Pradesh	10/2024 (10/2025)	10/2027 (10/2027)	1005.59 (882.21)	193.1	34.92
1230	4-lanning of Rahatgarh to Berkhedi section of NH-146 from Design Ch 124470 to Ch. 134.549 (NHAI) (618671) (-) (-)	Madhya Pradesh	03/2025 (12/2025)	12/2027 (12/2027)	618.33 (342.69)	53.13	12.07
1231	4-lanning of Gyaraspur to Rahatgarh section of NH-146 from Design Ch. 88361 to Ch 124470 in the state of MP on HAM mode (NHAI) (618672) (-) (-)	Madhya Pradesh	10/2024 (11/2025)	11/2027 (11/2027)	903.44 (592.44)	169.75	33.14
1232	Outer Ring Road of Jabalpur Town from Manegaon to NH-45 Pkg-2 (NHAI) (618684) (-) (-)	Madhya Pradesh	11/2022 (03/2024)	03/2026 (03/2027)	917.26 (786.47)	512.57	75.61
1233	Outer Ring Road of Jabalpur Town from NH45 to Kushner Pkg-3 (NHAI) (618685) (-) (-)	Madhya Pradesh	09/2022 (03/2024)	03/2026 (12/2026)	911.24 (773.23)	552	79.8
1234	Outer Ring Road of Jabalpur Town from Kushner to Amjhar Road including Airport Connectivity Pkg-IV (NHAI) (618686) (-) (-)	Madhya Pradesh	08/2022 (03/2024)	03/2026 (11/2026)	612.94 (509.82)	363.91	79.63
1235	Outer Ring Road of Jabalpur Town from Barela to Manegaon Pkg-1 (NHAI) (618687) (-) (-)	Madhya Pradesh	09/2022 (03/2023)	03/2025 (08/2026)	652.33 (651.88)	483.18	89.72
1236	Outer Ring Road of Jabalpur Town from Amjhar Road including Airport Connectivity to barela Pkg-V (NHAI) (618688) (-) (-)	Madhya Pradesh	10/2024 (10/2025)	10/2027 (10/2027)	794.7 (539.9)	84.37	30.26
1237	Indore - Harda Pkg-I [Indore to Raghav Garh from km. 0.25 to km. 26.903] (NHAI) (618694) (-) (-)	Madhya Pradesh	01/2022 (11/2022)	10/2024 (07/2026)	1011.29 (813.03)	687.94	93.84
1238	4L of Chandesara to Khedakhajuriya from Km. 0.000 to - 750 & Km 0.000 to km 41.400 of NH-148NG Pkg-I (NHAI) (618735) (-) (-)	Madhya Pradesh	12/2021 (09/2022)	05/2024 (09/2026)	909.84 (976.55)	587.8	99
1239	2L PS of Hinotiya-Mehulwa section of NH-346 from Km. 27.000 to Km 75.700 Vidisha Mehulwa-Talbehat Pkg-II Section of NH- 346 (NHAI) (618751) (-) (-)	Madhya Pradesh	10/2022 (09/2023)	09/2025 (03/2027)	581.65 (592.71)	273.54	69.04
1240	Itarsi Km. 63.000 to Betul Km. 137.000 of NH-69 in Madhya Pradesh (NHAI) (618762) (-) (-)	Madhya Pradesh	08/2017 (02/2018)	02/2020 (07/2026)	950.27 (788.33)	663.67	100
1241	Balance works of 4 lane divided carriageway of Missing Link section of NH-39 Rewa Bypass from junction with NH 30 near Bela to Junction with MPRDC ring road near Silpara on SH 9 design length 13.100 km on EPC Mode under Bharatmala Pariyojana in the State of Madhya Pradesh (NHAI) (618784) (-) (-)	Madhya Pradesh	08/2023 (04/2024)	04/2026 (01/2027)	355.36 (355.36)	238.95	84.44

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1242	Construction of 6 lane Indore western bypass from km 0000 to Km 34000 Pkg -I in the State of Madhya Pradesh on Hybrid Annuity Mode under NHO (NHAI) (618932) (-) (-)	Madhya Pradesh	02/2024 (01/2026)	12/2027 (12/2027)	1534.7 (1472.68)	655.83	22.96
1243	Construction of 6 lane Indore western bypass from km 34000 to Km 64000 Pkg-II in the state of Madhya Pradesh on Hybrid Annuity Mode under NHO (NHAI) (618933) (-) (-)	Madhya Pradesh	03/2024 (02/2026)	02/2028 (02/2028)	1430.56 (1430.56)	662.12	17.5
1244	4L of Budhni to Shahganj Bypass End Package-III of NH-146B from Km. 73.750 to Km. 102.000 (NHAI) (618962) (-) (-)	Madhya Pradesh	03/2024 (08/2025)	08/2027 (05/2027)	1102.97 (770.21)	174.55	27.25
1245	Construction work of 4-laning of Shahganj bypass end to Badi Package-IV of NH-146B from design km 102.000 to design km 142.357 Design length 40.357 km (NHAI) (618963) (-) (-)	Madhya Pradesh	02/2024 (03/2025)	03/2027 (03/2027)	784.14 (836.64)	318.15	50.13
1246	4 Laning of Sandalpur to Nasrullaganj Pkg-1 section of NH-146B Length 43.2 Km. (NHAI) (618964) (-) (-)	Madhya Pradesh	03/2025 (01/2026)	01/2028 (01/2028)	1425.98 (1425.98)	197.48	10.9
1247	Six laning with both sides Service Road of Ayodhya Bypass from Design Km 0000 near Ashram Tiraha on NH-46 to Km 16439 end at Ratnagiri Tiraha on Nh-146 (NHAI) (618966) (-) (-)	Madhya Pradesh	02/2024 (08/2025)	08/2027 (08/2027)	1123.17 (1103.22)	141.71	20.09
1248	Upgradation of Sarvardewla to Pal MP/MH Border Road section of NH-347 C from Design Chainge km 81.600 to 137.400 Total length 55.80 km to two lane with paved shoulder configuration along with One time improvement of 1 .95 km in the State of Madhya Pradesh on EPC mode. (MoRTH) (619007) (-) (-)	Madhya Pradesh	03/2023 (01/2026)	01/2028 (-)	461.23 (461.23)	0	0
1249	Dhangaon - Borgaon section km 81.000 to km 139.000 [Indore - Edlabad Pkg IV] (NHAI) (619100) (-) (-)	Madhya Pradesh	01/2020 (08/2021)	08/2023 (08/2026)	866 (1185.04)	746.36	99.8
1250	Indore - Harda Pkg-II [Raghavgarh to Nanasa from km. 29.30 to km. 92.30] (NHAI) (619114) (-) (-)	Madhya Pradesh	01/2023 (03/2024)	03/2026 (11/2027)	1081.51 (1146.63)	369.26	40.25
1251	Construction of 6 lane flyover from Khapari ROB to Mihan Interchange design chainage km 8760 to 11450 L- 2.69 km and upgradation of existing 4L PS road to 6LPS with service road by flexible pavement design chainage km 11450 to 14500 L- 3.05 [total project length 5.74 km] in section of Nagpur - Hyderabad NH-44 Old NH-7 in Nagpur district in the state of Maharashtra on HAM mode. (MoRTH) (617912) (-) (-)	Maharashtra	03/2024 (10/2025)	10/2027 (10/2027)	619.55 (619.55)	0	8.24
1252	Construction of New Four Lane Bypass to Parbhani City Parwa to Asola Km 463/265 to Km 481/180 Design Ch. 19220 to Ch. 34434 Length-15.214 Km section of NH-61 on EPC mode in the State of Maharashtra. (MoRTH) (617932) (-) (-)	Maharashtra	03/2022 (07/2023)	10/2024 (10/2026)	496.64 (496.64)	0	70.14
1253	Nasratpur to Barasgaon section of NH-61 2L / 4L PS from Km.514/00 to 558/200 (MoRTH) (617934) (-) (-)	Maharashtra	07/2017 (09/2017)	09/2019 (08/2026)	406.54 (406.54)	0	95.84
1254	Udgir Raavi Degloor Aadampur phata to Sagroli fata (MoRTH) (617937) (-) (-)	Maharashtra	11/2024 (04/2026)	04/2028 (-)	809.77 (809.77)	0	12
1255	Rehabilitation And Upgradation to four lane with paved shoulder configuration from km 24350 to km 61875 Jawale - Borgaon Kale of NH-63 in the State of Maharashtra on EPC mode under Annual Plan 2024-25 Total length - 37.525 Km. (MoRTH) (617938) (-) (-)	Maharashtra	12/2024 (09/2025)	03/2027 (03/2027)	574.18 (574.18)	7.49	20
1256	Balance work of NH-66 from design Km 84/00 to Km 87/100 Indapur Bypass and Km 91/600 to Km 99/100 Mangaon Bypass to four lane with paved shoulder in State of Maharashtra under NHO on EPC Mode. (MoRTH) (617945) (-) (-)	Maharashtra	03/2025 (10/2025)	04/2027 (04/2027)	354.21 (354.21)	0	66.44
1257	Kashedi to Parshuram Ghat section of NH-66 from Km 161/600 - Km 205/400 - 4L PS (MoRTH) (617946) (-) (-)	Maharashtra	03/2016 (02/2018)	02/2020 (12/2025)	1142.62 (1142.62)	0	97.5
1258	Arawali Kante section of NH-17New NH-66 4L PS from Km.241/300 to 281/300 (MoRTH) (617947) (-) (-)	Maharashtra	03/2016 (11/2017)	11/2019 (03/2026)	1006.99 (1443.09)	0	80.06
1259	Kante - Wakad section of NH-66 4L PS from Km.281/300 to 332/200 (MoRTH) (617948) (-) (-)	Maharashtra	03/2016 (11/2017)	11/2019 (11/2025)	1117.75 (2020.56)	375.93	90.14
1260	Kopargaon to Savali Vihir section (MoRTH) (617965) (-) (-)	Maharashtra	06/2022 (01/2023)	07/2024 (08/2026)	195.38 (195.38)	0	90.5

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1261	Rehabilitation, upgradation & widening of existing highway to 2L/4LPS Rigid Pavement of NH 160 section- Phaltan to Mhaishal near Karnataka Border including Tasgaon Bypass, from existing chainage Km 301/430 to Km 458/415 in the State of Maharashtra- Package-II & Package III combined- starting from existing chainage Km 341/300 to Km 394/130 and design chainage Km 340/250 at Dahiwadi Village to Km 392/950 ending at Vita Village in the State of Maharashtra on EPC Mode. (MoRTH) (617978) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	631.76 (631.76)	187.59	85
1262	Rehabilitation, upgradation & widening of existing highway to 2L/4LPS Rigid Pavement of NH 160 section- Phaltan to Mhaishal near Karnataka Border including Tasgaon Bypass, from existing chainage Km 301/430 to Km 458/415 in the State of Maharashtra. Package-I starting from existing chainage Km 301/430 at Phaltan Village Junction of Phaltan Baramati Road Design Chainage -301/430km & ending at existing chainage Km 341/300 Dahiwadi Village Bus Stop Design chainage Km 340466km in the S (MoRTH) (617979) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (11/2026)	533.76 (533.76)	0	72.05
1263	Rehabilitation/ Upgradation of existing Highway to four lane standards in Kurkheda town from km.413257 to km 410775, Two lane in Shankarpur Gurnuli km 42400 to km 43100 section and Reconstruction of Major Bridge at Ch. 448558 Bhuti Nallah and Ch. 411695 Sati River bridge, Minor Bridge at Ch. 411477 and Ch. 405800 Lendhari Bridge of NH 543 Bhamhapuri-wadsa-kurkheda-korchi-Deori-Amgaon road on EPC mode in the State of Maharashtra (MoRTH) (618042) (-) (-)	Maharashtra	03/2022 (11/2023)	05/2025 (12/2026)	163.86 (163.86)	0	42.78
1264	Widening, Reconstruction & Up-gradation to 2 lane with Paved Shoulder/Four Lane configuration for the work of Ahmednagar to Sabalkhed & Ashti to Chinchpur Section of NH-561 from Design km 2915 to km 37728 & Design km 55100 to km 70000 in the State of Maharashtra on EPC mode. Length 49.713 km (MoRTH) (618047) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	657.16 (657.16)	0	83.46
1265	Up-gradation to 2/4 lane with paved shoulder configuration of NH-652 from Tuljapur Naldurg-Akkalkot road Chainage from Km. 00.000 to km 30.982 in the State of Maharashtra on EPC mode. (MoRTH) (618049) (-) (-)	Maharashtra	03/2024 (01/2025)	07/2026 (08/2026)	183.41 (183.41)	64.87	98
1266	Construction of four-lane Concrete Road from Police Headquarter Gondia City to Rawanwadi Village Birsi Airport Junction from design km 0.000 to km 15.781 existing km 39/720 of NH-753 to existing Km 8/400 of NH 543 on sections from Kohmara-Goregaon- Police HeadquarterKaranja - Collector Office Square - Balaghat T Point- Rawanwadi- Rajegaon of NH-753 and NH-543 in Gondia District in the state of Maharashtra. Total Length of the project 15.781 Km. (MoRTH) (618059) (-) (-)	Maharashtra	02/2023 (02/2024)	08/2025 (10/2026)	328.11 (328.11)	0	34.15
1267	Strengthening, Widening & Up-gradation of newly declared NH-761 from NH-61Junction-BelheAlkutiDevibhoyareNighojShirur, from Design chainage Km 0.000 to Km 37.970 from Single/Intermediate/2L to 2LPS in the State of Maharashtra on EPC Mode Length 37.970 Km (MoRTH) (618061) (-) (-)	Maharashtra	03/2024 (03/2025)	09/2026 (09/2026)	386.16 (386.16)	57.06	62.5
1268	Rehabilitation/Upgradation of existing Highway to 2LPS/4 lane of Dhawali to Rajoli from Design Km.149476 to 163476 existing Km.150000 to 164000, Pandhasala to Mohadongri from design Km.170476 to 181476 existing Km.171000 to 182000, Ambeshivni Fata to Bodli from design Km.183476 to 185476 existing Km.184000 to 186000 and Made Tukum to Gadchiroli from design Km.188476 to 189476 existing Km.188000 to 18900 having length 28 km of NH-930 of Dhawali to Gadchiroli road in the (MoRTH) (618065) (-) (-)	Maharashtra	03/2022 (03/2024)	09/2025 (10/2026)	316.44 (316.44)	0	34.1
1269	Nandurshingote to Kolhar (MoRTH) (618088) (-) (-)	Maharashtra	09/2024 (06/2025)	12/2026 (12/2026)	325.79 (325.79)	23.01	37.74
1270	Rehabilitation & Up-gradation of Mudkhed to Nanded section from Km. 372000 to Km 388400 of NH 161A i.e. Nanded-Bhokar-Himayatnagar-Kinwat-Mahur-Arani Road Design chainage from Km 372000 Mudkhed to Km 387650 Nanded of NH 161A Length 15.65 Km to 2/4Lane with paved shoulders configuration in the State of Maharashtra on EPC mode. (MoRTH) (618089) (-) (-)	Maharashtra	03/2022 (04/2023)	04/2025 (10/2026)	206.54 (206.54)	0	65.14
1271	Pen to Khopoli 2LPS (MoRTH) (618094) (-) (-)	Maharashtra	03/2018 (06/2018)	12/2019 (12/2025)	369.39 (369.39)	333.1	86.3
1272	Rehabilitation and Up-gradation to 2 lane road with paved shoulders configuration for the balance work of 13 km length on Helwak-Patan-Karad section Km. 85000 to 133 417 of NH-166E in the state of Maharashtra on EPC mode. (MoRTH) (618096) (-) (-)	Maharashtra	02/2024 (10/2024)	04/2026 (12/2026)	181.45 (181.45)	0	87
1273	Guhagar - Rampur - 2L-PS - km 0/00 Guhagar to 26/230 Rampur and 40/00 Mirjoli to 53/600 Sati on NH-166E (MoRTH) (618097) (-) (-)	Maharashtra	01/2017 (06/2017)	06/2019 (08/2025)	407.2 (407.2)	0	91.89

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1274	Upgradation of existing 2 lane flexible pavement to 2 lane paved shoulders rigid pavement from design chainage Km 66.00 to Design Km 82.440 Start of Kolhapur Municipal corporation near Phulewadi to kale, design length 16.440 Km section on Talere Gaganbawada-Kolhapur road NH 166G in the state of Maharashtra on EPC mode (MoRTH) (618098) (-) (-)	Maharashtra	03/2021 (11/2022)	05/2024 (08/2026)	167.97 (167.97)	0	93.75
1275	Strengthening and Widening of road Sakoli- Wadsa-Armori-Gadchiroli-Ashti- Allapalli - Sironcha National highway NH 353C in Km 262/00 to 321/00 including 16 minor Bridges and 2 Major Bridge Total length 59 Km section from repanpalli to sironcha in Gadchiroli Dist in the State of Maharashtra. (MoRTH) (618133) (-) (-)	Maharashtra	03/2021 (06/2022)	05/2024 (03/2027)	280.57 (280.57)	0	65
1276	Rehabilitation /Upgradation from Lagam to Alapalli section Desing Km. 199/400 to km 227/400 Length 28.0 Km to 2 lane with Paved Shoulders/ 4 lane configuration section of NH-353 C Sakoli-Wadsa-Armori-Gadchiroli-Ashti-Alapalli Sironcha in Gadchiroli District on EPC mode in the state of Maharashtra. (MoRTH) (618134) (-) (-)	Maharashtra	02/2023 (09/2024)	09/2026 (09/2026)	459.39 (459.39)	0	81.42
1277	Rehabilitation and Up-gradation of Jarud - Sirsala section of NH-361F km 59500 to km11500 to Two lane with paved shoulder/ Four Lane in the state of Maharashtra on EPC mode Length 55.5 Km. (MoRTH) (618137) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	540.35 (540.35)	139.11	63.67
1278	Widening, Reconstruction & Up-gradation to 2 lane with Paved Shoulder/Four Lane configuration for the work of Sautada to Shirapur Section of NH-561 from Design km 86300 to km 125589 in the state of Maharashtra on EPC mode. Design length 39.289 km (MoRTH) (618138) (-) (-)	Maharashtra	03/2024 (05/2025)	11/2026 (11/2026)	349.57 (349.57)	0	54.04
1279	Rehabilitation and Up-gradation of Gangakhed Loha section of NH-361F from Km 169/00 to 210/00 to two lane with paved shoulder/ four lane configuration in the state of Maharashtra on EPC mode Length - 41.00 Km. (MoRTH) (618139) (-) (-)	Maharashtra	03/2024 (04/2025)	09/2026 (09/2026)	355.12 (355.12)	0	43.46
1280	Rehabilitation and Up-gradation of i. Deogaon phata to Digras phata Ch. 0/000 to 15/000 & Selu to Borgavhan Ch 20/900 to 35/800 [Length 29.9km] ii. Injegaon Dhamoni to Pohner Phata Ch.58/200 to Ch. 83/700 [Length25.5 km] and iii. Pohner phata to Pathri Design Ch. 42/700 to 58/200 [Length 15.5 km] sections of NH-548B to Two lane with paved shoulder configuration in the state of Maharashtra on EPC mode Total project length 70.9 Km. (MoRTH) (618150) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	761.83 (761.83)	0	15
1281	Mhaswad to Tembhurni section of NH-548C - 2L PS (MoRTH) (618152) (-) (-)	Maharashtra	01/2017 (08/2017)	07/2019 (08/2026)	488.6 (488.6)	0	96.19
1282	Satara to Mhaswad (MoRTH) (618153) (-) (-)	Maharashtra	01/2017 (08/2017)	08/2019 (08/2026)	653.46 (653.46)	7.34	98.08
1283	Rehabilitation & upgradation of Jamkhed to Sautada Section of NH548 D from km 195.375 to km 208.774, Length 13.399 Km to 2L PS /4L configuration with rigid pavement in the state of Maharashtra on EPC mode. (MoRTH) (618154) (-) (-)	Maharashtra	03/2022 (01/2023)	07/2024 (06/2026)	157.62 (157.62)	0	68.93
1284	Development/Widening of Talegaon Chakan Shikrapur Nhavara Section of NH-548D from existing chainage km. 54/000 to 82/300 and Design chainage Km. 54/000 to 82/120 Shikrapur to Nhavara Section to 2LPS/4L Configuration on EPC Mode in the State of Maharashtra. (MoRTH) (618155) (-) (-)	Maharashtra	03/2024 (01/2025)	07/2026 (09/2026)	396.17 (396.17)	95.2	76.2
1285	Paithan - Shirur section 2LPS Km 0.0 to 55.00 (MoRTH) (618172) (-) (-)	Maharashtra	03/2017 (06/2017)	06/2019 (10/2026)	341.8 (341.8)	0	82
1286	Shirur-Kharda section from 55937 km to 114486 km to 2LPS/4L (MoRTH) (618173) (-) (-)	Maharashtra	02/2017 (06/2017)	06/2019 (08/2026)	381.77 (381.77)	0	83.93
1287	Rehabilitation and Upgradation to two lane with paved shoulder configuration of NH-752G from Sakri to Pimpalner Section Design Ch km 0000 to Ch km 21411 in the state of Maharashtra on EPC Mode. Length 21.411 km. (MoRTH) (618174) (-) (-)	Maharashtra	03/2024 (04/2025)	10/2026 (10/2026)	226.58 (226.58)	0	100
1288	Rehabilitation and Upgradation of Satana to Mangrul Chandwad Section of NH752 G Design Ch Km 64.000 to Ch Km 101.140 two lane with paved shoulder/four lane configuration in the state of Maharashtra on EPC mode. (MoRTH) (618175) (-) (-)	Maharashtra	03/2022 (05/2023)	05/2025 (08/2026)	428.8 (428.8)	0	93.46

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1289	Rehabilitation and upgradation from ch km 50/200 to 56/800 and km 62/600 to 100/403 of Kolde to Visarwadi Near Junction with NH-6 section of NH 752G total length 44.40 to two-lane with paved shoulder / four lanes in the State of Maharashtra on EPC mode. (MoRTH) (618176) (-) (-)	Maharashtra	03/2025 (01/2026)	01/2028 (-)	349.08 (349.08)	25.6	35.45
1290	Pal Phata Phulambri - Khultabad 2LPS (MoRTH) (618177) (-) (-)	Maharashtra	03/2018 (06/2018)	12/2019 (12/2025)	227.19 (227.19)	0	95.29
1291	Widening and strengthening of Gangakhed to Kingaon section of NH-752K in Km 38/750 to 72/304 Flexible Pavement Length33.554 km to 2-lane configuration on EPC mode in the State of Maharashtra. (MoRTH) (618178) (-) (-)	Maharashtra	02/2024 (12/2024)	06/2026 (10/2026)	162.67 (162.67)	0	72
1292	Rehabilitation and Upgradation of Shewali phata to Kalambhir section i.e. Km 0443 to Km 4500 & Nizampur to Chadwel section i.e. Km 13485 to Km 26265 Length16.317 Km excluding 2 Major Bridges with approaches Km 13735 to Km 14095 & Km 19660 to Km 20030 of NH 753B to 2LPS Configuration in the State of Maharashtra on EPC Mode. (MoRTH) (618179) (-) (-)	Maharashtra	03/2024 (08/2024)	02/2026 (07/2026)	181.58 (181.58)	0	97
1293	Pune raigarh District Border To Mangaon Ch 69000 to 103775 NH-753F (MoRTH) (618180) (-) (-)	Maharashtra	03/2018 (06/2018)	12/2019 (07/2026)	223.46 (223.46)	0	89.08
1294	Rehabilitation and Up-gradation to 2 lane with paved shoulder configuration of Mahud Sangola road NH 965 G 159400 to 161900and 162400 to 183960 Design Chainage from km. 32/300 to km. 34/800 and km. 35/800 to km. 56/860 Rigid Pavement on EPC mode in the State of Maharashtra. (MoRTH) (618188) (-) (-)	Maharashtra	02/2023 (11/2023)	05/2025 (07/2026)	253.78 (253.78)	0	99.75
1295	Balance work of Rehabilitation and Up-gradation to 2-lane road with paved shoulders configuration for NH- 965DD from Pacharal-Mandangad-Mhapral-Rajewadi Upto Junction of NH-66 Ch-22700 to 75100 Km and Ambadave connector Birth place of Dr. Babasaheb Ambedkar Ch-0000 to 7325 Km length Km 59.725 in the state of Maharashtra on EPC mode. Balance Work (MoRTH) (618198) (-) (-)	Maharashtra	03/2018 (01/2022)	01/2024 (08/2026)	388.93 (341.69)	0	93.07
1296	Rehabilitation, Upgradation & Widening of existing Highway to Rigid Pavement 2 Lane with Paved Shoulder of NH 965DD from Lonand Shirval-Bhor Mandangad-Pchral Section ShindewadiPhata to Varandah Ghat Dist Border from Km 33/550 to 92/550 in the state of Maharashtra on EPC mode. (MoRTH) (618199) (-) (-)	Maharashtra	02/2023 (07/2024)	07/2026 (10/2026)	723.13 (723.13)	0	53.5
1297	Vadodara Mumbai Expressway Phase II - Pkg XIII [Km. 26.582 to Km. 50.700] Shirsad - Masvan (NHAI) (618469) (-) (-)	Maharashtra	06/2020 (02/2022)	02/2024 (07/2026)	3536.9 (4679.54)	1844.7	90.86
1298	Vadodara Mumbai Expressway Phase II - Pkg XIV [Km. 3.000 to Km. 20.200 of Spur] Shirsad - Akloli (NHAI) (618470) (-) (-)	Maharashtra	05/2021 (11/2022)	05/2024 (07/2026)	2058.79 (2324.72)	634.54	98
1299	Vadodara Mumbai Expressway Phase II - Pkg XV [Km. 20.200 to Km. 43.000 of Spur] Akloli - Amne (NHAI) (618471) (-) (-)	Maharashtra	05/2021 (11/2022)	05/2024 (07/2026)	2610.88 (2918.39)	622.23	91.5
1300	Vadodara Mumbai Expressway Phase II - Pkg XVI [Km. 43.000 to Km. 69.800 of Spur] Amne - Bhoj (NHAI) (618472) (-) (-)	Maharashtra	06/2021 (11/2022)	10/2024 (07/2026)	4051.8 (4315.56)	982.89	90.7
1301	Vadodara Mumbai Expressway Phase II - Pkg XVII [Km. 69.800 to Km. 79.783 of Spur] Bhoj - Morbe (NHAI) (618473) (-) (-)	Maharashtra	09/2021 (01/2023)	07/2025 (07/2026)	2208.68 (2463.02)	889.44	85.79
1302	Upgradation & rehabilitation of Service Roads on both sides in urban areas of Pune City on PuneSatara section of NH48 (NHAI) (618511) (-) (-)	Maharashtra	01/2025 (06/2025)	06/2027 (06/2027)	604.59 (388.78)	66.29	22.96
1303	Tunnel at Khambataki Ghat Section and its approaches from existing Km. 771.730 to existing Km. 782.000 (NHAI) (618512) (-) (-)	Maharashtra	11/2017 (02/2019)	02/2022 (10/2026)	907.03 (816.12)	677.98	89.16
1304	6L of Kagal-Satara section from Km 592.500 to Km 658.000 of NH-48 Pkg-I (NHAI) (618513) (-) (-)	Maharashtra	12/2021 (01/2023)	01/2025 (02/2027)	2111.95 (1435.46)	634.07	45.47
1305	6L of Kagal-Satara section from Km 658.000 to Km 725.000 of NH-48 Pkg-II (NHAI) (618514) (-) (-)	Maharashtra	12/2021 (12/2022)	12/2024 (12/2026)	2330.71 (317.4)	205.24	73.96

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1306	4L of Indora Chowk to Pachpaoli and Agrasen Chowk - Ashoka Chowk (NHAI) (618557) (-) (-)	Maharashtra	03/2023 (07/2023)	06/2026 (07/2026)	1038.84 (918.53)	685.21	84
1307	6L of Gonde Km. 439.038 to Pimpri Sado Km. 459.905 section of NH-848 Old NH-3 (NHAI) (618585) (-) (-)	Maharashtra	02/2024 (10/2024)	04/2027 (11/2027)	856.93 (718.84)	142.38	38
1308	Improvement and strengthening of existing 2 lane stretch to 2-Lane with PS 1.5m on both sides on Ghoti-Sinnar section of NH-160A using Thin White Topping 200mm thick in the State Of Maharashtra on EPC Mode (NHAI) (618586) (-) (-)	Maharashtra	03/2025 (06/2025)	06/2026 (08/2026)	254.78 (147.64)	115.05	77
1309	4L Mitigation Measure structures on CH/MH Border to Wainganga Bridge Section of NH-6 New NH-53 (NHAI) (618588) (-) (-)	Maharashtra	02/2021 (11/2021)	11/2023 (07/2026)	540.24 (468.92)	464.28	99.79
1310	Balance work of 4L Panvel to Indapur section of NH-66 Old NH- 17 from km 0.000 Panvel to km 42.300 Kasu (NHAI) (618594) (-) (-)	Maharashtra	12/2022 (03/2023)	10/2024 (07/2026)	329.82 (196.87)	185.79	96.89
1311	Four laning from Dive Ghat Km. 220.900 to Hadapsar Km. 234.150 of Mohol Alandi section Pkg VI of NH-965 (NHAI) (618626) (-) (-)	Maharashtra	12/2023 (10/2024)	10/2026 (04/2027)	819.52 (400)	122.8	64.95
1312	Construction of 7 Nos of Standalone safety structures/works at different locations on various NHs (NHAI) (618627) (-) (-)	Maharashtra	01/2025 (07/2025)	01/2027 (01/2027)	168.52 (112.03)	26.55	33.35
1313	Strengthening of Existing Alignment of Pandharpur Town Part Bypassed Section of NH 965 from KM 36.230 to KM 44.230 from Chh. Shivaji Maharaj Chowk to Wakhari (NHAI) (618628) (-) (-)	Maharashtra	08/2022 (11/2023)	10/2025 (03/2027)	150.21 (87.59)	65.36	48
1314	Loha-Waranga Section of NH-361 from km 187.800 to km 244.369 (NHAI) (618653) (-) (-)	Maharashtra	03/2018 (03/2019)	03/2021 (12/2026)	1236.08 (3466.58)	1503.55	96.22
1315	Bodhre - Dhule (NHAI) (618693) (-) (-)	Maharashtra	02/2021 (01/2022)	07/2024 (08/2026)	1344.78 (1292.7)	785.93	97.69
1316	Upgradation of 2L/4L with Paved Shoulder of Shirwal-Lonand Section from KM 159900 To KM 188025 of NH-965DD Section I and 2L With Paved Shoulder of Lonand-Satara Section from KM 51500 To KM 96246 Of NH-965D Section II in Satara District in the State of Maharashtra on EPC Mode under NHO- (NHAI) (618754) (-) (-)	Maharashtra	03/2025 (06/2025)	06/2027 (06/2027)	538.11 (307.24)	160.27	41.08
1317	Up-gradation to Four Lane with Paved Shoulder configuration of the highway starting from existing km 88.400 Savali Vihir to km 163.400 start of Ahmednagar bypass Design Length 75.000 km section of NH-160 in the State of Maharashtra under Bharatmala Pariyojana on EPC Mode (NHAI) (618766) (-) (-)	Maharashtra	10/2024 (04/2025)	04/2027 (04/2027)	862 (617.93)	298.23	48.55
1318	4L of Ratnagiri - Kolhapur section from km 67.140 to km 112.340 of NH-166 Pkg II (NHAI) (618836) (-) (-)	Maharashtra	02/2022 (05/2023)	05/2025 (03/2027)	1985.38 (1798)	1235.29	79.98
1319	4L of Ratnagiri - Kolhapur section from km 112.340 to km 145.300 of NH-166 PkgIII (NHAI) (618837) (-) (-)	Maharashtra	02/2022 (05/2023)	05/2025 (03/2027)	1939.23 (1910.41)	1078.85	67.57
1320	4L of Nagpur-Katol Section from Km. 13.00 to Km. 62.900 of NH-353J (NHAI) (618937) (-) (-)	Maharashtra	02/2021 (10/2021)	10/2023 (10/2026)	1166.96 (1432.82)	1182.28	81.54
1321	Construction of Standalone Flyover cum ROB from Design Ch.66.600 to Design Ch.68.800 in Gadchandur Town on NH-353B (NHAI) (618939) (-) (-)	Maharashtra	02/2025 (07/2025)	07/2027 (07/2027)	191.31 (107.76)	33.97	36.99
1322	Rehabilitation and Up gradation of Charthana Jintur Section of NH 752 I Km 25100 to 47100 to 2 Lane with Paved Shoulder configuration Flexible Pavement in the state of Maharashtra on EPC mode. Reg- Resubmission of Annual Plan Estimate. (MoRTH) (619008) (-) (-)	Maharashtra	03/2025 (01/2026)	07/2027 (07/2026)	157.69 (157.69)	0.01	51
1323	Construction of six lane Flyover at Katraj junction at Km, 3/880 of NH 548-DD Vadgaon - Katraj - Kondhwa - Mantarwadi Chowk - Loni Kalbhor - Theur Phata - Lonikand Road in Pune Dist of the State of Maharashtra. On Engineering Procurement and construction EPC Basis mode L.1.326 Km, (MoRTH) (619042) (-) (-)	Maharashtra	02/2021 (03/2022)	02/2026 (02/2023)	163.51 (163.51)	0	83.19
1324	Satara Km 725.000 to Pune Km 865.350 of NH - 4 New NH - 48 in Maharashtra (NHAI) (619069) (-) (-)	Maharashtra	09/2009 (10/2010)	05/2022 (10/2026)	361.72 (425.51)	384.55	99.05

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1325	Balance works of 4L Panvel Indapur section of NH66 old NH17 from km 42.300 kasu to km 84.600 Indapur (NHAI) (619095) (-) (-)	Maharashtra	06/2022 (11/2022)	05/2024 (07/2026)	546.44 (472.1)	420.7	81.63
1326	4L of Ratnagiri - Kolhapur section of NH-166 from km 0.000 to km 19.769 and km 31.000 to km 67.140 Pkg I (NHAI) (619149) (-) (-)	Maharashtra	02/2022 (11/2022)	11/2024 (11/2026)	1774.03 (2108.41)	1427.82	93.75
1327	4L of Baramati to Indapur Pkg-II from km. 41.400 to km. 84.550 of NH-965G Saint Tukaram Marg (NHAI) (619163) (-) (-)	Maharashtra	01/2021 (09/2021)	09/2023 (12/2026)	1471.32 (1297.48)	1071	86.2
1328	Vadodara Mumbai Expressway Phase II - Pkg XII [Km. 50.700 to Km. 77.000] Masvan - Ganjad (NHAI) (619198) (-) (-)	Maharashtra	08/2020 (03/2022)	03/2024 (07/2026)	1711.38 (2388.52)	979.41	99.38
1329	Vadape to Thane from km 539.202 to km 563.000 section of NH-3 new NH-848 (NHAI) (619203) (-) (-)	Maharashtra	03/2018 (01/2019)	07/2021 (07/2026)	1252.92 (1371.27)	491.81	80.78
1330	Capacity Augmentation in the stretch of Pimpri Sado Vadape section of NH848 Km. 460900 to Km. 537000 by Construction of Slip/Service Road on either side at various locations total length 25.140 Km LHSRHS, Flyover 2 x 25m at Borivali Junction Km. 528550 & LVUP 1 x 15m at Sherekarpada Km. 528800 (NHAI) (619204) (-) (-)	Maharashtra	12/2025 (04/2026)	10/2027 (10/2027)	372.03 (372.03)	0	1
1331	Dharampuri-Lonand from km. 117.00 to 166.40 Pkg-IV on Mohol-Alandi Section (NHAI) (619210) (-) (-)	Maharashtra	01/2021 (09/2021)	09/2023 (07/2026)	1411.71 (1358.68)	1471.41	97.4
1332	Construction of 6 Lane Elevated corridor from KM 612582 to KM 617540 including construction of Service Roads in Kolhapur City on NH -48 in the State of Maharashtra on EPC mode under NHO (NHAI) (619298) (-) (-)	Maharashtra	02/2026 (06/2026)	06/2029 (06/2029)	1039 (1039)	0	0
1333	Construction of a 6-Lane Elevated Corridor from Km 593766 to Km 596620 Including Construction of Service Roads in Kagal City on NH-48 in the State of Maharashtra on EPC Mode. (NHAI) (619299) (-) (-)	Maharashtra	03/2026 (06/2026)	06/2028 (06/2028)	357.99 (357.99)	0	0
1334	Construction of Four Lane Nagpur-Katol section of NH-353J including Mitigation Structures from Design Ch. 37000 to Ch. 45990 Tiger Corridor-I Mitigation Structures from Design Ch. 37000 to Ch. 45990 Tiger Corridor-I in the State of Maharashtra on EPC Mode (NHAI) (619300) (-) (-)	Maharashtra	01/2026 (06/2026)	12/2027 (12/2027)	300.68 (300.68)	0	0
1335	Widening/Improvement of existing 2-Lane road to 4-Lane Divided Highway from Sekmai to Nilakuthi section of Imphal-Kohima Road Design Chainage from Km 297700 to Km 308729 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5B (NHIDCL) (618298) (-) (-)	Manipur	03/2021 (07/2021)	01/2023 (09/2026)	211.7 (211.7)	254.22	93.54
1336	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Daili to Kuraopokpi section of Imphal-Kohima road NH-02 Design Chainage from Km 274610 to Km 287000 in the state of Manipur on EPC mode Pkg-4B (NHIDCL) (618299) (-) (-)	Manipur	09/2020 (12/2024)	06/2026 (01/2027)	268.98 (268.98)	0	56.16
1337	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Taphukuki to Daili section of Imphal-Kohima road NH-02 Design Chainage from Km 262175 to Km 274610 in the state of Manipur on EPC mode Pkg-4A (NHIDCL) (618300) (-) (-)	Manipur	09/2020 (10/2020)	04/2022 (08/2026)	379.39 (379.39)	312.58	91.39
1338	Widening/Improvement of existing 2-lane to 4-Lane Divided Highway from Kuraopokpi to Sekmai section of Imphal-Kohima Road Design Ch. km 287.00 to 297.700 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5A (NHIDCL) (618301) (-) (-)	Manipur	09/2020 (02/2025)	08/2026 (08/2026)	228.97 (228.97)	114.62	48.31
1339	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 16.900 to Km 30.970 of NH-202 in the state of Manipur on EPC mode Package-2 (NHIDCL) (618302) (-) (-)	Manipur	03/2020 (07/2020)	06/2022 (08/2026)	256.04 (256.04)	0	98.12
1340	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 0.000 to Km 16.900 of NH-202 in the state of Manipur on EPC mode Package-1 (NHIDCL) (618303) (-) (-)	Manipur	03/2020 (07/2020)	06/2022 (08/2026)	222.77 (222.77)	0	88.96

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1341	Widening/Improvement to 2 Lane with earthen shoulder of Jessami to Laynen bridge Nagaland border section of NH-29 of Imphal -Ukhrul - Jessami Economic Corridor from km 0.000 to km 11.009 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-7 (NHIDCL) (618304) (-) (-)	Manipur	03/2023 (12/2024)	06/2026 (02/2027)	164.89 (164.89)	127.59	26.67
1342	Widening/Improvement to 2 lane with earthen shoulder of Marrem Khullen to Jessami section of NH-202 of Imphal - Ukhrul - Jessami Economic Corridor from Design Chainage km 95.700 to km 140.180 in the State of Manipur on EPC mode under Bharatmala Pariyojana under NHO-NE Package-6 (NHIDCL) (618305) (-) (-)	Manipur	03/2023 (12/2024)	12/2026 (08/2027)	554.66 (554.66)	221.02	24.43
1343	Widening/Improvement to 2 lane with earthen shoulder of Choithar to Marrem Khullen section of NH-202 of Imphal Ukhrul Jessami Economic Corridor from Design Chainage km 53.110 to km 95.700 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-5 (NHIDCL) (618306) (-) (-)	Manipur	03/2023 (05/2025)	03/2027 (08/2027)	564.05 (564.05)	172.98	14.5
1344	Widening to 2 lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 169570 Near Nungkao vllage under Tamenglong District to km 205974 near Jiribam Bridge under Jiribam district under NHO-NE PKG-7 (NHIDCL) (618333) (-) (-)	Manipur	01/2023 (12/2023)	12/2025 (12/2026)	760.16 (760.16)	424.3	92.52
1345	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 131.280 to km 169.570 on EPC mode in Manipur under NHO-TSP PKG-6 (NHIDCL) (618334) (-) (-)	Manipur	12/2021 (02/2023)	02/2025 (09/2026)	504.76 (504.76)	325.89	95.2
1346	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from Km 101280 Near Khongsang Village to Km 131280 near Puilon Kambiron Village on EPC Mode in Manipur PKG-5 (NHIDCL) (618335) (-) (-)	Manipur	12/2021 (11/2022)	05/2024 (08/2026)	410.68 (410.68)	345.66	90.61
1347	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 66.110 km to 101.280 Km Existing Chainage km 67.496 to km 103.557 on EPC Mode in Manipur PKG-4 (NHIDCL) (618336) (-) (-)	Manipur	09/2021 (06/2022)	12/2023 (07/2026)	579.63 (579.63)	404.8	85.98
1348	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 33.000 km to 66.390 Km Existing Chainage from km 33.395 to km 67.496 on EPC Mode in Manipur PKG-3 (NHIDCL) (618337) (-) (-)	Manipur	03/2021 (09/2021)	03/2023 (03/2026)	467 (467)	593.44	86.33
1349	Widening to 2-Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 15.940 km to 33.120 Km Existing Chainage Km 15.946 to Km 33.395 Total length17.180 Km in the State of Manipur on EPC mode PKG-2 - Balance Works & Rectification works (NHIDCL) (618338) (-) (-)	Manipur	03/2021 (03/2025)	03/2026 (08/2026)	195.14 (195.14)	161.96	92.99
1350	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from Design Chainage 69.875 Km to 121.769 Km in the State of Manipur on EPC mode Package-3 (NHIDCL) (618344) (-) (-)	Manipur	03/2021 (08/2021)	08/2023 (12/2026)	673.27 (673.27)	563.27	84.72
1351	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section from Km 48.587 to Km 69.875 in the State of Manipur on EPC mode under NHO Package-2B (NHIDCL) (618345) (-) (-)	Manipur	06/2020 (08/2020)	08/2022 (08/2026)	365.53 (365.53)	195.73	88.2
1352	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 32.835 to km 48.587 in the State of Manipur on EPC mode under NHO Package-2A (NHIDCL) (618346) (-) (-)	Manipur	04/2020 (07/2020)	06/2022 (07/2026)	232.99 (232.99)	155.44	100
1353	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 13.747 to km 32.835 in the State of Manipur on EPC mode under NHO Package-1B (NHIDCL) (618347) (-) (-)	Manipur	04/2020 (07/2020)	06/2022 (07/2026)	241.52 (241.52)	164.85	100
1354	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from km 130.000 to km 141.029 Package-4B in the State of Manipur on EPC Mode (NHIDCL) (618348) (-) (-)	Manipur	06/2020 (11/2025)	11/2026 (11/2026)	177.76 (177.76)	97.93	7.45
1355	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from Design Chainage km 118850 to km 130000 Package-4A in the State of Manipur on EPC Mode (NHIDCL) (618349) (-) (-)	Manipur	04/2020 (08/2025)	08/2026 (08/2026)	204.12 (204.12)	0	24.66

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1356	Construction of of 2 -Lane with paved shoulders road from Tamenglong-Tousem-Lisang-Mahur Road NH-137 starting near Dialong Village from km 10.000 at Dialong to km 31.430 near Old Tamenglong , near Barak River on EPC Mode Package-2 (NHIDCL) (618355) (-) (-)	Manipur	07/2021 (09/2021)	03/2023 (03/2026)	483.87 (483.87)	372.1	95.28
1357	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur in the state of Manipur from km 31.430 at Old Tamenglong to km 43.480 ending near Phelong on EPC Mode Package-3 (NHIDCL) (618356) (-) (-)	Manipur	03/2021 (06/2021)	12/2022 (04/2026)	234.08 (234.08)	201.13	98.5
1358	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 in Manipur starting from km 54.180 near Azuram to km 80.630 near Mandeu on EPC Mode Package 5 (NHIDCL) (618357) (-) (-)	Manipur	09/2021 (11/2021)	05/2023 (01/2026)	477.86 (477.86)	330.12	84.87
1359	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 starting from km 80.630 near Mandeu to km 96.870 near Jiri River on EPC Mode Package-6 (NHIDCL) (618358) (-) (-)	Manipur	09/2021 (11/2021)	05/2023 (12/2025)	311.18 (311.18)	231.08	87.3
1360	Construction of 2-laning with Hard shoulder of Ukhrul Tolloi - Tadubi section of NH-102A from Design Chainage km 9450 to km 50850 in the State of Manipur on EPC mode under NHO-NE Package-2 (NHIDCL) (618387) (-) (-)	Manipur	03/2023 (03/2024)	03/2026 (12/2026)	578.98 (578.98)	267.11	80.02
1361	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 50.850 km to 81.870 km in the State of Manipur on EPC mode under NHO-TSP Package -3 (NHIDCL) (618388) (-) (-)	Manipur	09/2021 (07/2023)	01/2025 (07/2026)	315.56 (315.56)	251.46	91.11
1362	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 81.870 km to 105.825 km in the State of Manipur on EPC mode under NHO-TSP Package -4 (NHIDCL) (618389) (-) (-)	Manipur	09/2021 (08/2022)	02/2024 (08/2026)	310.76 (310.76)	255.6	97
1363	Improvement of existing road to 2 laning with Hard Shoulders of Maram-Peren section Package-1B, length- 17.660 km from Design Chainage 22.340 km to 40.000 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618415) (-) (-)	Manipur	02/2021 (06/2021)	12/2022 (03/2026)	188.36 (188.36)	0	100
1364	Improvement of existing road to 2 laning with Hard Shoulders of Maram -Peren section Package-1A, length- 22.340Km from Design Chainage 0.000 km to 22.340 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618416) (-) (-)	Manipur	02/2021 (06/2021)	12/2022 (03/2027)	226.32 (226.32)	189.26	75.08
1365	Rehabilitation and Up-gradation of Nongstoin Wahkaji section of Project Road Km 0000 to Km 43060 to Intermediate Lane with earthen shoulder under SARDP-NE Phase-A in the State of Meghalaya on EPC mode. Job No- SARDP-NE ong-Don-Maw/MG/2020-21/294 (MoRTH) (617885) (-) (-)	Meghalaya	08/2020 (02/2022)	08/2023 (07/2026)	302.88 (302.88)	187.77	99.1
1366	Improvement and Widening two lannig with paved Shoulder of NH 127B from km 31.500 Goeragre to km 63.224 Package-II in state of Meghalaya (MoRTH) (618076) (-) (-)	Meghalaya	12/2023 (05/2025)	05/2027 (-)	504 (350.67)	0	2.5
1367	Improvement and Widening of National Highway No. 127B Darugiri - Songsak - Williamnagar Junction Section to two lane with paved shoulder from design Km 0000 to Km 36635 Design length 36.635 Km existing Km 112000 to Km 151060 of NH-1278 under Bharatmala Pariyojana Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618294) (-) (-)	Meghalaya	03/2023 (09/2025)	09/2027 (09/2027)	801.07 (801.07)	176.12	26.08
1368	Improvement/Widening of New NH-217 Dainadubi-Darugiri section to Two lane with paved shoulder in Meghalaya from design Km 0000 to Km 40840 existing Km 8600 to Km 53000 of Old NH-62 under BMP Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618295) (-) (-)	Meghalaya	03/2023 (03/2025)	03/2027 (03/2027)	705.83 (705.83)	0	45.52
1369	Improvement/Widening to 2-L with Paved Shoulder/ 4-Laning of NH-40 section from Km 151330 to Km 163400 design Km 63.530 to Km 71.520 including Dawki Bridge of length 368 m between Shillong-Dawki under JICA ODA Loan assistance Phase-II Pkg-5 -Balance work (NHIDCL) (618374) (-) (-)	Meghalaya	07/2020 (05/2024)	11/2026 (11/2026)	284.21 (284.21)	170.81	41.92
1370	Improvement/Widening to 2-Lane with Paved Shoulder from design Km 45.760 to Km 63.530 between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance work Pkg-4 (NHIDCL) (618375) (-) (-)	Meghalaya	07/2020 (04/2024)	04/2026 (10/2026)	445.51 (445.51)	42.39	53.21

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1371	Improvement/Widening to 2-Lane with Paved Shoulder between Shillong-Dawki road up to Bangladesh Border from design Km 10.670 to Km 37.550 under JICA ODA Loan assistance Phase-II -Balance Work-Pkg-2 (NHIDCL) (618376) (-) (-)	Meghalaya	07/2020 (02/2024)	08/2026 (12/2026)	525.67 (525.67)	0	51.02
1372	Improvement/Widening to 2-L with Paved Shoulder/4-L from Km 81740 to Km 93490 design Km 0000 to Km 10670 of NH-40 New NH-106 & 206 section & 4-L from design Km 0.00 to Km 0.930 of NH-44 section between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance Work Pkg-1 (NHIDCL) (618377) (-) (-)	Meghalaya	07/2020 (10/2023)	10/2025 (06/2026)	351.12 (351.12)	0	100
1373	Rehabilitation and up gradation of Nongstoin-Rambrai-Kyrshai road up to Meghalaya-Assam border from Km 0.335 to km 34.039 to 2-Lane under NHO - NE in the State of Meghalaya Package-1 (NHIDCL) (618418) (-) (-)	Meghalaya	09/2021 (05/2022)	05/2024 (12/2026)	359.86 (359.86)	299.18	83.02
1374	Construction of 2-Lane with paved shoulders of Shillong Western Bypass starting from NH-06 near Ladumsaw existing Km 60.900 of old NH40 to NH106 old NH 44E Package-III, from km 24700 to km 38256 under SARDP-NE PHASE A in the state of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618419) (-) (-)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	562.48 (562.48)	254.54	52
1375	Construction of 2 lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw existing km 60.900 of old NH-40 to NH-106 old NH-44E, Package-II km 12800 to km 24700 under SARDP-NE Phase A in the State of Meghalaya on EPC Mode (NHIDCL) (618420) (-) (-)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	686.03 (686.03)	435.15	49.82
1376	Construction of 2-Lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw Existing km 60.900 of old NH-40 to NH106 old NH-44E, km 0000 to km 12800 Package-I under SARDP-NE PHASE A in the State of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618421) (-) (-)	Meghalaya	03/2023 (09/2024)	09/2026 (09/2026)	620.3 (620.3)	304.5	73.13
1377	4-Laning of Vairengte - Chhimluang section Package-3 of NH-306 from Existing Chainage km 43000 to Km 59700 Design Chainage km 46000 to km 60850 on Silchar - Vairengte- Sairang road in the State of Mizoram under Bharatmala Pariyojna under NHO-NE. Package-1&2 in Assam state (NHIDCL) (618316) (-) (-)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	491.39 (491.39)	237.85	17.86
1378	4-Laning of chhimluang-Kolasib from section pkg-4 of NH-306 & NH-6 existing chainage km 59700 to km 86000 design chainage km 61000 to km 77500 on Silchar-vairengte-sairang road in the state of Mizoram under Bharatmala Pariyojna on EPC mode Vairengte - Sairang Pkg-4 (NHIDCL) (618317) (-) (-)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	561.91 (561.91)	0	17.12
1379	4-Laning of Kolasib - Sethawn section Package-5 of NH-6 from Existing Chainage km 86000 to km 107850 Design Chainage km 77500 to km 95500 on silchar - voirengte - sairang road under Bharatmala Pariyojna on EPC mode under NHO-NE Vairengte - Sairang Pkg-5 (NHIDCL) (618318) (-) (-)	Mizoram	11/2021 (07/2025)	07/2027 (06/2027)	720.4 (720.4)	247.14	11.86
1380	4-Laning of Sethawn - N. Kawnpui section Package-6 of NH-6 from Existing Chainage km 107850 to km 126315 Design Chainage km 95500 to km 111850 on Silchar-Vairengte- Sairang road, Vairengte - Sairang Pkg-6 (NHIDCL) (618319) (-) (-)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	595.65 (595.65)	173.14	6.72
1381	Construction of 4-Laning of N. Kawnpui N. Mualvum Mualkhang via Khamrang Village section Package-7 of NH-6 from Existing Chainage km 127200 to km 142000 Design Chainage km 111850 to km 123400 on Silchar - Vairengte - Sairang road in the State of Mizoram on EPC mode (NHIDCL) (618320) (-) (-)	Mizoram	02/2024 (10/2025)	10/2028 (-)	866.32 (866.32)	0	18.9
1382	Construction of 4-Laning of West Serawlg-Sairang section of NH-6 from Existing Chainage km 142000 to km 158900 Design Chainage km 123400 to km 136260 on Silchar - Vairengte - Sairang road in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-8 (NHIDCL) (618321) (-) (-)	Mizoram	02/2024 (11/2025)	11/2028 (-)	875.79 (875.79)	0	13.95
1383	Construction of Twin Tube Uni-directional Aizawl Bypass Tunnel of 2.5 km and its approaches of 2.1 km from km 10.600 to km 15.200 on Sarrang - Phaibawk section of NH-6 in the State of Mizoram on EPC Mode under NHO-NE Package-2 (NHIDCL) (618323) (-) (-)	Mizoram	01/2024 (12/2025)	12/2028 (-)	1313.28 (1313.28)	0	0
1384	Construction of 2-lane Aizawl Bypass from km 15.200 to km 34.500 Package-3 on Sairang - Phaibawk section of NH-6 in the State of Mizoram under Bharatmala Pariyojna on EPC Mode under NHO-NE (NHIDCL) (618324) (-) (-)	Mizoram	02/2023 (10/2025)	11/2028 (-)	720.72 (720.72)	0	15.1

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1385	Construction of 2-laning with hard shoulder of Lunglei to Chhumkhum from Design Chainage Km 0.000 to Km 37.420 of NH-302 [Lunglei-Tlabung] Package-A (NHIDCL) (618362) (-) (-)	Mizoram	03/2021 (06/2021)	12/2022 (11/2026)	698.45 (698.45)	552.89	64.78
1386	Construction of 2-laning with hard shoulder configuration of Chhumkhum to Tlabung from Design Chainage Km 37.420 to Km 74.950 of NH-302 in Mizoram under Bharatmala Pariyojana on EPC mode [Pkg-B] (NHIDCL) (618363) (-) (-)	Mizoram	06/2021 (07/2021)	01/2023 (12/2026)	740.58 (740.58)	494.49	61.34
1387	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 208. 000 to Km 250.000 Package-5 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-5 (NHIDCL) (618379) (-) (-)	Mizoram	09/2019 (10/2019)	04/2023 (06/2026)	752.89 (752.89)	125.64	95.35
1388	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 125. 000 to Km 166 Package-3 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-3 (NHIDCL) (618380) (-) (-)	Mizoram	09/2019 (10/2019)	04/2023 (06/2026)	867.09 (867.09)	159.55	97.51
1389	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 339.00 to km 380.00 Siaha on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-8 (NHIDCL) (618383) (-) (-)	Mizoram	09/2019 (03/2020)	09/2023 (06/2026)	637.06 (637.06)	101.89	99.82
1390	2-laning of Zorinpui - Longmasu section of NH-502A from km 0.000 to km 28.244 in the State of Mizoram on EPC mode under NHO-NE, stretch of IMBR (NHIDCL) (618452) (-) (-)	Mizoram	02/2023 (12/2024)	12/2026 (07/2027)	781.85 (781.85)	48.14	4.71
1391	Up-gradation to 2 lane with paved shoudters of Pawlrang - Rulchawm section- of NH-102B of Aizawl - Imphal Economic Corridor from Existing Chainage km 72.030 to km 104.129 including 2.459 km re-alignment section from Tuivai River to Rulchawm connecting km 48.150 of NH-6 [Design Chainage km 68.170 to km 98.579] in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-3 Keifang- Tuivai Pkg-3 (NHIDCL) (619010) (-) (-)	Mizoram	12/2021 (11/2023)	05/2025 (07/2026)	500.88 (500.88)	442.08	99.52
1392	Balance work of widening to two laning/re-alignment and geometric improvement from Km. 11000 to Km. 114618 with rectification of damaged stretches and provision of protection works in vulnerable location of NH-44 in the State of Mizoram. (MoRTH) (619321) (-) (-)	Mizoram	10/2025 (05/2026)	05/2028 (-)	170.96 (170.96)	0	2
1393	Bangalore Chennai Expressway Phase-II Pkg-I from km.71.000 to Km 96.000 Bethamangala in the state of Karnataka to Byreddypalli (NHAI) (619199) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	12/2020 (10/2022)	10/2024 (10/2022)	1410.01 (1410.01)	736.08	99.05
1394	6L Aluru - Jakuva Section of NH-130CD Road from km 365.033 to km 396.800 Pkg. 1 (NHAI) (618681) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	02/2021 (03/2022)	03/2024 (07/2026)	1216.12 (1241.66)	697.95	99.63
1395	Bangalore Chennai Expressway Phase-III Package I Gudipala to Walajahpet from Km 156.000 to Km 180.000 (NHAI) (618477) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	10/2020 (05/2022)	05/2024 (08/2026)	1481.87 (1481.87)	746.73	99.02
1396	6L of Veera Kaveri Raja Puram to Pondavakkam from km 61.380 to km 96.040 of NH 716B Pkg-III (NHAI) (618634) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	03/2021 (01/2023)	01/2025 (09/2026)	1439.77 (1439.77)	808.45	98.89
1397	Walajahpet/Ranipet to TN/AP Border Section of from Km.106.800 to Km.133.36 NH-4 (NHAI) (618769) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	12/2024 (09/2025)	09/2027 (09/2027)	1338.14 (1214.7)	240.71	13.45
1398	6L of Kumarajapet to Veera Kaveri Raja Puram from km 43.800 to km 61.380 of NH-716B Pkg-II (NHAI) (618772) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	02/2021 (10/2023)	10/2025 (09/2026)	702.52 (799.36)	405.81	98.91
1399	6 laning of Balance Work of Chennai - Tada from km. 21.40 to km. 54.40 (NHAI) (619077) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	12/2017 (03/2018)	03/2020 (07/2026)	464.62 (472.37)	389.75	100
1400	Khammam-Devarapalle Pkg III [4L Access Controlled Greenfield from Chintagudem village to Recherla village Design Chainage 63117 to 105236] (NHAI) (618747) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	01/2021 (09/2022)	09/2024 (07/2026)	829.5 (1227.07)	649.48	98.82
1401	4L Access Controlled Greenfield Highway section on NH-163G Khammam Vijayawada from Remidicherla village at Design Ch. 280.200 Km to Jakkampudi village on NH-16 at Design Ch. 309.909 Km Package-III (NHAI) (618818) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	03/2023 (10/2025)	05/2027 (12/2027)	1183.23 (1225.14)	228.66	4.37

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1402	4L Access Controlled Greenfield Highway section on NH-163G Khammam Vijayawada from BrahmanapalliK village at Design Ch. 250.400 Km to Remidicherla village at Design Ch. 280.200 KmPackage-II (NHAI) (619143) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	03/2023 (03/2025)	03/2027 (06/2027)	826.01 (862.58)	165.28	23.73
1403	6L Access Controlled Greenfield Highway of Julekal village to Dinnevarapadu village from Km 242.200 to Km 280.400 Pkg-2 (NHAI) (619212) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	01/2022 (01/2023)	01/2025 (04/2027)	1227.57 (1315.87)	528.05	68.53
1404	Widening/Improvement to 4-Lane with Paved Shoulder from km 55000 Nagabang Gamsuk to km 82514 Oyan in the State of Assam and Arunachal Pradesh on EPC mode under Bharatmala Pariyojna of Length 27.514 Km Package-3 (NHIDCL) (618359) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	03/2023 (09/2024)	03/2027 (03/2027)	665.47 (665.47)	373.06	96.7
1405	6L of Aurangabad to Bihar-Jharkhand border Chordaha section from km. 180.000 to km. 209.827 of NH-2 PKG-01 (NHAI) (618531) (-) (-)	Multi-States (Bihar, Jharkhand)	02/2021 (12/2024)	12/2026 (12/2026)	1054.46 (786.81)	201.3	33.24
1406	6L Greenfield Varanasi-Ranchi-Kolkata Highway from Anarbansalea village to Sagrapur village From KM. 151200 to KM. 184700Package-7 (NHAI) (618724) (-) (-)	Multi-States (Bihar, Jharkhand)	03/2023 (07/2025)	06/2027 (06/2027)	1719.2 (1723.42)	322.79	25.19
1407	6L Greenfield Varanasi- Ranchi- Kolkata Highway from Sonepurbigha village to junction with NH- 22 Chatra Bypass near Chatra from km 184.700 to km 222.000Pkg - 8 (NHAI) (618732) (-) (-)	Multi-States (Bihar, Jharkhand)	03/2023 (05/2026)	05/2028 (05/2028)	1728.17 (1728.17)	114.23	3.94
1408	Hariharganj to Parwa Mode section from km 23.284 to km 57.049 of NH-98 (NHAI) (618951) (-) (-)	Multi-States (Bihar, Jharkhand)	09/2020 (03/2022)	02/2024 (07/2026)	1125.78 (1186.56)	830.06	91.3
1409	4L of Sahibganj - Manihari Ganga Bridge including Manihari Bypass (NHAI) (618952) (-) (-)	Multi-States (Bihar, Jharkhand)	10/2016 (11/2020)	10/2024 (12/2026)	1954.77 (1978.01)	2008.25	86.54
1410	Six Laning of Bihar - Jharkhand Border Chordaha - Gorhar section of NH-2 from km 249.525 to km 320.810 (NHAI) (619078) (-) (-)	Multi-States (Bihar, Jharkhand)	12/2017 (06/2019)	11/2021 (12/2026)	1772.7 (1689.17)	1273.56	78
1411	4L of Munger Mirzachauki section from Km 157350 to Km 193931 Pkg-4 (NHAI) (619307) (-) (-)	Multi-States (Bihar, Jharkhand)	02/2021 (08/2022)	08/2024 (08/2026)	1376.56 (1481.58)	893.28	92
1412	Six Laning of Varanasi to Aurangabad from km. 786.00 to km. 978.40 of Old NH-2 (NHAI) (618530) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	02/2009 (09/2011)	03/2014 (07/2026)	3241.56 (3241.56)	2858.26	99.75
1413	6L Greenfield Varanasi-Ranchi-Kolkata Highway from junction with NH-19 & Varanasi Ring Road near Rewasa village to junction with Chandauli-Chainpur road near Khainti village from Km. 0.000 to Km. 27.000 - Pkg-1 (NHAI) (618728) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	03/2023 (11/2024)	11/2026 (05/2027)	1433.39 (1564.15)	561.54	45.02
1414	Construction of additional 3-Lane Bridge over River Ganga for connection between Buxar and Bharauli on NH-922 in the State of Uttar Pradesh and Bihar on Hybrid Annuity Mode (NHAI) (618882) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	03/2024 (08/2025)	02/2028 (02/2028)	531.61 (444.92)	46.76	20.16
1415	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package III [from Pindari km 78.150 to Rawalganj Bypass Km 117.120] on EPC Mode in the state of Uttar Pradesh. (NHAI) (619154) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	10/2022 (08/2023)	08/2025 (10/2026)	1493.5 (1493.59)	1042.03	83
1416	4L of Kishanganj - Bahadurganj section from Km. 0.000 to Km. 23.649 & interchange at Start Point Length - 1.200 Km of NH-27 (NHAI) (618584) (-) (-)	Multi-States (Bihar, West Bengal)	01/2025 (12/2025)	12/2027 (12/2027)	962.84 (855.56)	179.31	18.31
1417	Vadodara Mumbai Expressway Talsari to Karvad Phase IB - Pkg X [Km 103.400 to Km 128.000] (NHAI) (619064) (-) (-)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	10/2020 (03/2022)	03/2024 (12/2027)	1909.74 (2652.24)	1096.51	36.23
1418	Dwarka Expressway Pkg-III Delhi/HR Border to Start of RoB Gurugram (NHAI) (618577) (-) (-)	Multi-States (Delhi, Haryana)	01/2018 (11/2018)	11/2020 (05/2024)	2228.26 (2298.37)	1759.52	100
1419	Balance work of 2L PS from Km 30.800 to Km 70.800 and 2L with Rigid Carriageway from Km 70.800 to km 84.120 of Khanapur- KA/GOA Border section of NH-4A (NHAI) (618942) (-) (-)	Multi-States (Goa, Karnataka)	01/2022 (11/2022)	05/2024 (03/2027)	226.76 (149.44)	110.31	84.7
1420	Bal. Works of Fagne Km. 510.000 to Maharashtra/Gujarat Border Km. 650.794 (NHAI) (618637) (-) (-)	Multi-States (Gujarat, Maharashtra)	12/2019 (09/2020)	09/2022 (12/2026)	1654.07 (1672.89)	1416.49	97.66

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1421	Delhi-Amritsar-Katra Expressway Phase-I Pkg-V from Junction with Ambala-Kaithal-Hissar road NH-152 near Kharak Pandwa village to Junction with Patiala-Samana-Patran road SH-10 near Ghagga village Km 120250 to Km 157920 (NHAI) (618486) (-) (-)	Multi-States (Haryana, Punjab)	01/2021 (05/2022)	05/2024 (07/2026)	1741.86 (2281.02)	1431.89	98.7
1422	4L Ismailabad to Ambala Section of NH-152 Lot-4/Package-1 (NHAI) (619093) (-) (-)	Multi-States (Haryana, Punjab)	02/2023 (12/2023)	12/2025 (02/2027)	609.32 (454.34)	203.25	75.05
1423	6L of Ambala-Chandigarh greenfield section from Km. 0.000 to Km. 25.000 with 4L spur to Lalru from Km. 0.000 to Km. 5.828 & spur to PR-7 road from Km. 0.000 to Km. 11.157 (NHAI) (619134) (-) (-)	Multi-States (Haryana, Punjab)	03/2022 (10/2023)	10/2025 (09/2026)	1641.66 (1904.79)	1258.95	85.5
1424	6L access Controlled Greenfield Highway from Adhoya Musalmana to Sadopur section of Shamli -Ambala Package-III Design Ch. Form km 84.400 to km 121.786 (NHAI) (619216) (-) (-)	Multi-States (Haryana, Punjab)	05/2022 (05/2023)	05/2025 (12/2026)	1491.72 (1122.86)	724.49	79.56
1425	Additional Structures on 6LGurgaon-Jaipur Section of NH-48 between KM 42.700 to KM 273.00 (NHAI) (618505) (-) (-)	Multi-States (Haryana, Rajasthan)	08/2022 (12/2022)	06/2024 (08/2026)	409.64 (290.64)	199.54	88.9
1426	4 laning of Aligarh-Palwal Section from Km. 46.390 Design Chainage to Km. 69.110 Terminating at junction EPE Package-II from Kurana- Eastern Peripheral Expressway of NH-334D (NHAI) (618691) (-) (-)	Multi-States (Haryana, Uttar Pradesh)	03/2024 (08/2025)	08/2027 (08/2027)	939.17 (903.94)	246.86	12.5
1427	6L access Controlled Greenfield Highway from Ranipur Barsi to Adhoya Musalmana section of Shamli -Ambala Package-II Design Ch. Form km 45.500 to km 84.400 (NHAI) (618723) (-) (-)	Multi-States (Haryana, Uttar Pradesh)	06/2022 (05/2023)	05/2025 (02/2027)	1554.21 (1241.89)	825.78	79.1
1428	Construction of Greenfield Connectivity to Jewar International Airport from DND-Faridabad-Ballabgarh Bypass KMP Link - Spur to Delhi Mumbai Expressway (NHAI) (619068) (-) (-)	Multi-States (Haryana, Uttar Pradesh)	07/2022 (06/2023)	06/2025 (04/2027)	2920.69 (3485.77)	1756.53	74.08
1429	2L/4L of Hoshiarpur to Una section including Hoshiarpur Bypass of NH 503A (NHAI) (618907) (-) (-)	Multi-States (Himachal Pradesh, Punjab)	03/2023 (05/2025)	05/2027 (05/2027)	571.34 (481.88)	257.77	26.18
1430	4L Poanta SahebMednipur from Km. 435.65 to km. 458.65 of NH-07Pkg-1 (NHAI) (619291) (-) (-)	Multi-States (Himachal Pradesh, Uttarakhand)	03/2022 (05/2023)	05/2025 (07/2026)	524.54 (657.32)	319.77	94.25
1431	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XIV from Junction with Pathankot-Gurdaspur road NH-54 near Balsua to Junction with Hiranagar Road near village Gurha Baildaran km 423500 to km 468100 (NHAI) (619066) (-) (-)	Multi-States (Jammu and Kashmir, Punjab)	10/2021 (09/2022)	09/2024 (10/2026)	3044.02 (3707.91)	1773.85	83.6
1432	Barwa Adda Km. 398.240 to Panagarh Km. 521.120 (NHAI) (618533) (-) (-)	Multi-States (Jharkhand, West Bengal)	08/2010 (04/2014)	09/2016 (08/2026)	1560.39 (1568.22)	1690.95	100
1433	6L Greenfield Varanasi- Ranchi- Kolkata Highway from junction with NH-320 in Lepo village to Kamlapur villageJH/WB border from km 358.500 to km 387.200 Pkg -13 (NHAI) (618734) (-) (-)	Multi-States (Jharkhand, West Bengal)	03/2023 (09/2025)	09/2027 (09/2027)	1154.49 (1319.18)	308.02	23.23
1434	2L PS of JH / WB Border km. 70.524 - Purulia km.84.400 & Purulia km. 94.30 - Chandil Junction with NH-33 km. 153.705 of Old NH-32 (NHAI) (618909) (-) (-)	Multi-States (Jharkhand, West Bengal)	03/2018 (12/2019)	08/2022 (10/2026)	1652.4 (1771.88)	1649.25	97.65
1435	4L of NH-80 section of Mirza Chauki to Farakka section from existing km 190.00 to design km 200.75 junction at km 3.100 of NH 133 B and from existing km 260.00 to existing km 283.00 design km 274.133 in the state of Jharkhand package - II (NHAI) (618948) (-) (-)	Multi-States (Jharkhand, West Bengal)	02/2025 (02/2026)	01/2028 (01/2028)	782.18 (782.18)	202.69	5.64
1436	Six Laning of KT/KL Border Thalapaddy -Chengala from Km. 17.200 to Km. 57.20 (NHAI) (619205) (-) (-)	Multi-States (Karnataka, Kerala)	05/2020 (11/2021)	05/2024 (07/2026)	1981.07 (2681.48)	1699.07	100
1437	6L from Sankeshwar Bypass to MH-KNT Border from Km. 555.017 to Km. 592.853 of NH-48 Pkg-II (NHAI) (618516) (-) (-)	Multi-States (Karnataka, Maharashtra)	01/2022 (10/2022)	04/2025 (05/2027)	1388.7 (1066.86)	1156.86	84.8
1438	Akkalkot MH/KN border New Greenfield corridor from Km 512.000 to Km 548.400 of NH-150C part of Akkalkot KN/TS Border section Package XIV (NHAI) (618636) (-) (-)	Multi-States (Karnataka, Maharashtra)	03/2023 (10/2024)	10/2026 (06/2027)	1370.75 (1403.49)	300.25	53.31
1439	Bangalore Ring Road STRR-NH-948A- Package-I of Phase-III from Belagondapalli TN to TN/KNT border from km 144.480 to 179.969 (NHAI) (618519) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	03/2022 (05/2023)	05/2025 (12/2026)	1260.74 (1218.47)	764.03	90.68

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1440	Hosur to Dhamrapuri Pkg-1 [Neraluru - Thorapalli Agraharam] (NHAI) (618581) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	10/2021 (10/2022)	10/2024 (01/2027)	1757.27 (1828.66)	1459.22	78.7
1441	6L of MH/KN Border Nimbal Village to KN/TS Border Singnodi Village from Km. 162.5 to Km. 203.100 in Raichur of NH-150C Pkg-IV (NHAI) (618631) (-) (-)	Multi-States (Karnataka, Telangana)	03/2022 (11/2022)	05/2025 (08/2026)	1499.73 (1457.48)	840.3	99.51
1442	6L Access Controlled Greenfield Highway of Nandinne village to Julekal village from Km 202.900 to Km 242.200 Pkg-1 (NHAI) (618632) (-) (-)	Multi-States (Karnataka, Telangana)	02/2022 (01/2023)	01/2025 (08/2026)	972.06 (1044.06)	459.45	91.47
1443	Thalassery Mahe Bypass Km 170.600 to Km 189.200 of NH-17New NH-66 in Kerala (NHAI) (619097) (-) (-)	Multi-States (Kerala, Puducherry)	09/2017 (12/2017)	05/2020 (07/2026)	1181.12 (1573.18)	1534.73	100
1444	4L Shahpur to Muktainagar from Km. 186.000 to km 216.278 of NH 753L Pkg II of Boregaon Buzurg to Muktainagar (NHAI) (619101) (-) (-)	Multi-States (Madhya Pradesh, Maharashtra)	12/2022 (03/2024)	03/2026 (10/2026)	784.35 (659.52)	330.42	64
1445	Construction of 26 VUPs, Major Bridge, Service Road etc. on Lalitpur-Sagar-Lakhnadon section of NH-44 NS (NHAI) (618556) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	02/2023 (03/2024)	03/2026 (07/2026)	665.91 (665.91)	559.45	97.4
1446	4L of Chowka to Kaimaha near MP/UP Border section NH-34 from D. Ch. 145.000 to D. Ch. 197.266 excluding existing Chhatarpur bypass from D. Ch. 160.307 to D. Ch. 168.630 Package-4 (NHAI) (618668) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	10/2024 (09/2025)	09/2027 (09/2027)	996.5 (846.68)	288.69	44.92
1447	4L of Bamni - Rajura - Warur - Devada upto M.S. Border of NH - 930D from km 19.000 to km 51.985 (NHAI) (618941) (-) (-)	Multi-States (Maharashtra, Telangana)	03/2022 (03/2024)	03/2026 (12/2026)	968.05 (1187.19)	805.71	73.73
1448	Viluppuram Km.0.000 to Puducherry Km.29.000 (NHAI) (618844) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (11/2021)	11/2023 (09/2026)	1358.31 (1162.44)	526.4	98.32
1449	Puducherry Km.29.000 to Poondiyanakupam Km.67.000 (NHAI) (618845) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (11/2021)	11/2023 (09/2026)	1588.4 (1415.9)	460.39	98.75
1450	Sattanathapuram to Nagapattinam from Km 123.800 to Km 179.555 (NHAI) (618847) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (10/2020)	10/2022 (12/2026)	2899.77 (2899.77)	1593.32	85
1451	6L with access control provision Saharanpur bypass to Ganeshpur section from 13.89 Km to 41.820 Km of Delhi- Dehradun Economic Corridor package-2 (NHAI) (618711) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	04/2022 (11/2022)	11/2024 (07/2026)	796.65 (560.03)	507.68	99.29
1452	4-laning of Pilibhit - Sitarganj from Km. 32.500 to Km. 70.800 Pkg-2 of NH-30 (NHAI) (618783) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	01/2023 (03/2024)	03/2026 (10/2027)	1471.19 (1471.19)	456.76	42.88
1453	Road Safety Improvement of Critical Junctions on MuzaffarnagarHaridwar Section of NH-334 from Km 143000 to Km 196000 (NHAI) (618886) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	04/2025 (10/2025)	10/2027 (10/2027)	238.66 (0.1)	33.07	20.5
1454	Improvement & Up-gradation of NH-734 Section of Moradabad-Thakurdwara Kashipur including Moradabad & Kashipur Bypass Package-III Kashipur Bypass Length 14.490 Km., Starts from Ch. 38770 and ends at Ch. 53260 existing Ch. 05560 (NHAI) (618928) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	02/2023 (03/2024)	09/2025 (03/2027)	936.12 (717.5)	369.85	53.84
1455	4/6L of Spur to Haridwar Greenfield from Km. 0.000 to Km. 50.70 (NHAI) (618969) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	11/2021 (02/2023)	02/2025 (09/2026)	2155.95 (2612.3)	1540.17	91.95
1456	4L of Haridwar-Nagina section from km. 0.00 to km. 71.614 of NH-74 (NHAI) (619217) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	12/2015 (01/2018)	07/2020 (07/2026)	1659.12 (1622.49)	1540.99	99.85
1457	Widening of existing Single lane / Intermediate lane road to 2 lane from Km 101 to Km 125 of NH 61 (MoRTH) (617886) (-) (-)	Nagaland	06/2020 (06/2024)	06/2026 (03/2027)	252.2 (252.2)	0	44.46
1458	Widening to Existing single lane /intermediate lane to 2 lane from Km185.00 to Km 220.00 of NH-61 New NH-02 in the state of Nagaland. (MoRTH) (618072) (-) (-)	Nagaland	03/2021 (07/2022)	07/2024 (03/2026)	297.25 (297.25)	155.15	100

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1459	Construction of 2-lane with Paved shoulder of Kohima- Bypass Road Connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29, NH-39New NH-02 from Design Km 32.00 to Design Km 43.454Design Length-11.454 Km in the State of Nagaland under SARDP-NE on EPC Mode Package-IV (NHIDCL) (618290) (-) (-)	Nagaland	07/2020 (10/2020)	04/2022 (12/2026)	202.36 (202.36)	102.12	46.77
1460	Construction of 2-lane with Paved shoulder of Kohima-Bypass Road connecting NH-39 New NH-02, NH150New NH-02, NH7-61 New NH-29 and NH-39 New NH-02 from Design km 21.000 to km 32.268 [Design length11.268 km] in the state of Nagaland Under SARDP-NE on EPC Mode Package- 3 (NHIDCL) (618291) (-) (-)	Nagaland	07/2020 (06/2023)	06/2025 (12/2026)	159.85 (342.29)	123.42	39.54
1461	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting New NH-02 and New NH-29 from Design Km 10.500 to design Km 21.000 [Design Length-10.500 km] including TUNNEL of 500m at Ch. 11.000 in the state of Nagaland Under SARDP-NE on EPC Mode Package-2 (NHIDCL) (618292) (-) (-)	Nagaland	07/2020 (10/2020)	10/2022 (10/2027)	277.44 (277.44)	198.97	69.76
1462	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29 and NH-39New NH-02 from design Km 0.00 to Km 10.500 in the State of Nagaland under SARDP-NE on EPC Mode Package-1 -Balance work (NHIDCL) (618293) (-) (-)	Nagaland	07/2020 (11/2023)	11/2026 (11/2026)	232.29 (350.88)	116.76	27.24
1463	Balance work of Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 old NH-150 from existing km 98.380 near Chizami vill. to km120.367 Nagaland/Manipur Border [Design km 95.700 to design km 117.200] [Design Length 21.500 km] in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode Package-V under NHO (NHIDCL) (618296) (-) (-)	Nagaland	03/2020 (11/2023)	11/2025 (07/2026)	330.8 (330.8)	0	98.39
1464	Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 Old NH-150 from existing Km 30.474 Near Kidwema road Chakahabama to existing Km 53.220 Near Kikruma Village Design Km 29.60 to Km 51.50 Design length-21.90 Km in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode under NHO Package-II -Balance work (NHIDCL) (618297) (-) (-)	Nagaland	03/2020 (01/2024)	01/2026 (12/2026)	355.79 (355.79)	0	43.13
1465	4-Laning of Balance work of Dimapur-Kohima Road from design km 152.490 to km 166.700 Existing km 156.000 to km 172.900 Excluding Dimapur & Kohima Bypass under SARDP-NE Package-III (NHIDCL) (618328) (-) (-)	Nagaland	03/2016 (09/2023)	09/2025 (07/2026)	562.98 (794.75)	535.96	84.32
1466	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-I Design Chainage 0000 Km to 34795 Km, in the State of Nagaland on EPC mode under NH O-NE (NHIDCL) (618364) (-) (-)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	430.24 (430.24)	0	87
1467	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-III Design Chainage 69875 Km to 106816 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618365) (-) (-)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	497.18 (497.18)	0	85.67
1468	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-II Design Chainage 34795 Km to 69875 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618366) (-) (-)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	442.54 (442.54)	0	58.5
1469	Construction of 2 laning with Hard shoulder of Peren-Dimapur section on NH 129A from Design Km 146.208 to Km 163.592 Length- 17.384 km in the state of Nagaland on EPC mode under NHO-TSP Package-III (NHIDCL) (618413) (-) (-)	Nagaland	02/2021 (06/2023)	06/2025 (07/2026)	177.77 (199.02)	0	95.62
1470	Construction of Balance work for 2-lane with hard shoulder of Peren- Dimapur section on NH-129A from Design Km 126.775 to Km 146.208 Length 19.433 Km in the state of Nagaland on EPC mode under NHO-TSP Package-II (NHIDCL) (618414) (-) (-)	Nagaland	01/2021 (09/2023)	09/2025 (09/2025)	258.52 (258.52)	135.86	96.53
1471	Construction of 2-lane with hard shoulders of Merangkong-Tamlu-Mon road Wakching Twon portion on EPC basis from existing Chainage Km 59000 to Km 73640 [Design Km. 59000 to Km, 72450] Design length - 13.450 Km under SARDP-NE package-V Balance work (NHIDCL) (618422) (-) (-)	Nagaland	03/2021 (09/2023)	09/2025 (07/2026)	161.73 (161.73)	101.21	99.75
1472	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon MTM Road from existing Km 20.456 to Km 41.065 Design Km. 20 to Km. 40.0 Design Length-20.000 Km in the State of Nagaland under SARDP-NE Phase-A Pkg-2 Balance work (NHIDCL) (618423) (-) (-)	Nagaland	03/2018 (08/2023)	08/2025 (03/2026)	215.79 (215.79)	173.12	100



All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1473	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon Road on EPC Basis from existing road Km. 76.640 to Km 98.065 Design chainage Km. 63.800 to Km. 86.835 Design Length-23.035 Km in the state of Nagaland under SARDP-NE PKG-IV Balance work (NHIDCL) (619059) (-) (-)	Nagaland	03/2018 (09/2023)	09/2025 (12/2026)	323.98 (323.98)	143.39	79.03
1474	New construction of Major Bridge with Approaches from Km 0.000 to 1.200 Madhopur -Badabanta section of NH-20 under NHO in Annual Plan 2022-23 in the State of Odisha (MoRTH) (617898) (-) (-)	Odisha	03/2023 (04/2025)	10/2027 (10/2027)	199.5 (199.5)	0.32	0
1475	Widening and Strengthening to 4LPS/2LPS from km 0.000 to 35.800 Kuakhia - Mangalpur section of NH 20 in the state of Odisha on Annual Plan 2021-22 (MoRTH) (617899) (-) (-)	Odisha	03/2022 (02/2024)	02/2026 (11/2026)	636.1 (636.1)	296.22	56.11
1476	construction or By-pass road on NH-26 for Nabrangpur Town (MoRTH) (617902) (-) (-)	Odisha	03/2023 (12/2024)	12/2026 (12/2026)	168.95 (168.95)	10.62	35
1477	Construction of Bypass road to Balangir town from km 72/400 Desing km 0/0 to km 79/800 Design km 11/670 of NH-26 in the State of Odisha. (MoRTH) (617904) (-) (-)	Odisha	02/2022 (04/2023)	10/2025 (07/2026)	238.78 (238.78)	6.79	55
1478	Construction of 4 lane ROB with approaches in lieu of LC No. RV-172 at km 176.00 of NH-201 present NH-26 at Kesinga including land acquisition in the state of Odisha on EPC mode under Annual Plan 2021-22 (MoRTH) (617905) (-) (-)	Odisha	12/2021 (05/2023)	05/2025 (10/2026)	324.09 (324.09)	88.48	70.09
1479	Widening and Strengthening to 2LPS including LA from km 318.970 to 353.450 Balikuda-Mulkani Section of NH-55 under NHO in Annual Plan 2022-23 in the State of Odisha. Job No. NH-55-OD-2022-23-656 (MoRTH) (617920) (-) (-)	Odisha	01/2022 (06/2025)	06/2027 (06/2027)	511.54 (511.54)	0	3
1480	Widening and strengthening to 2LPS including LA of Kandarpur-Balikuda from km 277/500 to 318/970 of NH-55 in the State of Odisha under Annual Plan 2021-22. (MoRTH) (617921) (-) (-)	Odisha	03/2022 (06/2023)	06/2025 (11/2026)	499.79 (499.79)	131.36	60.65
1481	Construction of Jharsuguda Bypass including Land acqusition on NH-49 from km 258.636 to km 283.300 design chainage 258.636 to km 289.876 under NHO in Annual Plan 2022-23 for the state of Odisha Job No.NH-49-OD-2022-23-655 (MoRTH) (617922) (-) (-)	Odisha	09/2021 (01/2025)	07/2027 (07/2027)	587.1 (587.1)	52.51	23
1482	Construction of Daspalla Bypass from km 195.250 To 200.635 of NH-57 including land acquisition in the state of Odisha on EPC mode under Annual Plan 2022-23. (MoRTH) (617923) (-) (-)	Odisha	02/2023 (05/2025)	05/2027 (05/2027)	155.97 (155.97)	50.04	25
1483	Construction of Bypass to Khordha town from Km 294/000 to 300/300 on NH-57 including LA in the State of Odisha on EPC mode. (MoRTH) (617925) (-) (-)	Odisha	02/2022 (05/2023)	11/2024 (07/2026)	157.49 (157.49)	33.67	92
1484	Construction of Bypass on NH-59 from Km 336/350 to 349/910 13.56 km near Berhampur town including 4-lane RoB in the state of Odisha. (MoRTH) (617930) (-) (-)	Odisha	03/2021 (03/2022)	12/2025 (12/2026)	196.94 (196.94)	59.54	70
1485	Construction of four lane ROB and its approaches in lieu of existing Level Crossing No. RV-71 at km 435 on NH-217 New NH-353 at Khariar including land acquisition under NHO in Annual Plan 2021-22 for the state of Odisha for F.Y. 2021-22 to F.Y 2033-34 (MoRTH) (618003) (-) (-)	Odisha	11/2021 (06/2023)	12/2024 (07/2026)	154.49 (154.49)	25.17	90
1486	Widening & strengthening to 2LPS from km 0,000 to 40.000 Dhaugaon- Podamari section of NH 326 in the State of Odisha under Annual Plan 2021.22. (MoRTH) (618012) (-) (-)	Odisha	03/2022 (02/2024)	02/2026 (12/2026)	186.52 (186.52)	46.39	60
1487	Construction of Dharmagarh Bypass on NH-130C including land acquisition in the state of Odisha on EPC Mode under Annual plan 2022-23. (MoRTH) (618079) (-) (-)	Odisha	03/2023 (04/2025)	10/2026 (10/2026)	172.66 (172.66)	0	15
1488	Widening to 2 lane with paved shoulded of Jareikela Jharkhand/Odisha Border - Dhabaleswar section from 0/0 to 36/0 of NH-320D in the State of Odisha under Annual Plan 2021-22. (MoRTH) (618122) (-) (-)	Odisha	03/2022 (10/2024)	10/2026 (10/2026)	172.09 (172.09)	0	32
1489	Bhadrak KM 136.500 to Baleshwar KM 199.141 (NHAI) (618523) (-) (-)	Odisha	11/2014 (03/2019)	09/2021 (11/2026)	844.67 (1394.82)	783.79	91.32

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1490	Construction of 6-lane flyover at Ainthapali junction and a 2-lane ROB LHS on NH-53 Earlier NH-6 in Sambalpur, on EPC mode in Odisha under NHO (NHAI) (618591) (-) (-)	Odisha	03/2024 (06/2024)	12/2026 (12/2026)	374.17 (211.74)	106.42	50.87
1491	Balance work of 8 nos. of Elephant Underpasses EUPs, 1 no. of Vehicular Underpass VUP, 1 nos. of Light Vehicular Underpass LVUP, 1 nos. of Pedestrian Underpass PUP, 1 nos. of Foot Over Bridge FOB and A2 side approach of Jharpokharia Flyover at Km.215.270 in Baharagora-Singhara section of NH-49 (NHAI) (618592) (-) (-)	Odisha	09/2023 (11/2024)	05/2026 (10/2027)	320.64 (244.85)	54.79	22.85
1492	Balance work of Rehabilitation and Upgradation to four laning of Baharagora Singhara section of NH-49 from Km.229.727 to Km.238.990 Length 9.263 Km. including construction of five nos. of Elephant Underpasses EUP and fourteen nos. of Animal Underpasses AUP inside the buffer zone of Similipal Tiger Reserve Area in Bangriposi Ghat section in the State of Odisha on EPC Mode (NHAI) (618593) (-) (-)	Odisha	03/2025 (05/2025)	11/2027 (11/2027)	263.32 (163.07)	13.82	9.8
1493	6L Greenfield Kaliagura Baunsagar Section of NH-130-CD Road from km 249000 to km 293000 Package OD-5 (NHAI) (618677) (-) (-)	Odisha	09/2021 (05/2022)	05/2024 (11/2026)	1539.75 (1918.49)	998.13	96.8
1494	6L Greenfield Baunsagar - Baraja Section of NH-130-CD Road from km 293000 to km 338500 Package OD-6 (NHAI) (618678) (-) (-)	Odisha	08/2021 (06/2022)	05/2024 (07/2026)	1265.59 (1635.44)	969.31	99.4
1495	6L Greenfield Kandili - Aluru Section of NH-130-CD Road from km 342500 to km 365033 Package-OD-8 (NHAI) (618680) (-) (-)	Odisha	12/2021 (10/2022)	10/2024 (07/2026)	1492.74 (1912.84)	1064.81	99.9
1496	6L Flyover including RE Wall approaches with Flexible Pavement in the Elephant Corridor of Angul Sambalpur Section of NH-42 New NH-55 Km.202.533 (NHAI) (618704) (-) (-)	Odisha	09/2023 (06/2024)	01/2027 (07/2026)	150.86 (106.32)	106.14	99.99
1497	4L Godibandha to Ballhar Chhak, Ballhar Chhak to Banarpal & Banarpal to Start of Angul bypass at Km.314.130 to Km.321.035 of NH53, at Km.75.200 to Km.84.000 of NH149 & at Km.84.000 to Km.86.100 of NH55 (NHAI) (618705) (-) (-)	Odisha	12/2024 (02/2026)	02/2028 (02/2028)	973.12 (973.12)	238.15	4.2
1498	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.39.000 to Km.60.00 Package-3 (NHAI) (618820) (-) (-)	Odisha	03/2023 (12/2023)	12/2025 (02/2027)	861.84 (938.55)	390.03	91.8
1499	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km 18.00 to Km 39.00 in the State of Odisha on HAM mode Package-2 (NHAI) (618821) (-) (-)	Odisha	03/2023 (12/2023)	12/2025 (08/2026)	920.47 (950.4)	421.6	91
1500	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.0.00 to Km.18.00Package-1 (NHAI) (618822) (-) (-)	Odisha	03/2023 (12/2023)	12/2025 (08/2026)	929.91 (869.45)	398.91	92.3
1501	3L Major Bridge over River Brahmani at Km. 401.250 Duburi - Chandikhole Section of NH-200 New NH -53 (NHAI) (618908) (-) (-)	Odisha	04/2022 (08/2022)	01/2025 (09/2027)	153.61 (103.68)	73.59	38
1502	6L of Badakumari - Karki Section from Km 179.000 to km 226.500 of NH-130-CD Package OD-3 (NHAI) (619109) (-) (-)	Odisha	03/2021 (04/2022)	04/2024 (07/2026)	1101.76 (1374.43)	713.4	99.7
1503	Four Laning of Angul to Sambalpur from Km.112.000 to Km.265.000 (NHAI) (619118) (-) (-)	Odisha	09/2016 (03/2017)	08/2019 (07/2026)	2510.04 (2632.91)	2459.45	99.98
1504	Cuttack-Angul Section of NH-42 New NH-55 from km 0.400 to km 60.200 Pkg-I in the State of Odisha (NHAI) (619119) (-) (-)	Odisha	10/2017 (01/2018)	07/2020 (09/2026)	999.32 (1178.31)	1128.44	99
1505	4 Laning of Talcher to end of Kamakhyanagar Bypass km 8.844 - km 15.725 of NH-149 and km 301.875 - km 335.946 of NH-53 Pkg-I (NHAI) (619157) (-) (-)	Odisha	01/2018 (02/2019)	08/2021 (10/2026)	795.18 (810.71)	713.62	99
1506	4 Laning of Duburi Chandikhole from km 388.376 to km 428.074 Pkg-III (NHAI) (619158) (-) (-)	Odisha	01/2018 (02/2020)	08/2022 (10/2026)	789 (907.61)	724.86	86
1507	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.60.000 to Km.76.646 Package-4 (NHAI) (619181) (-) (-)	Odisha	03/2023 (11/2024)	10/2026 (10/2027)	882.45 (1009.92)	196.63	33.02

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1508	6L of Hatibena - Badakumari Section from Km 146.50 to km 179.00 of NH-130-CD Package OD-2 (NHAI) (619213) (-) (-)	Odisha	02/2021 (03/2022)	03/2024 (07/2026)	791.17 (1070.63)	733.58	99.95
1509	Cuttack-Angul Section of NH-42 New NH-55 from Km.60.200 to Km. 112.000 Pkg-II in the State of Odisha (NHAI) (619215) (-) (-)	Odisha	10/2017 (03/2018)	09/2020 (09/2026)	991.41 (1168.82)	1083.76	99.66
1510	Development to 4-lane with paved shoulder for the road section Talwandi Sabo-Raman road to refinery Road junction with Bathinda Dabwali Road of NH-254 from existing Km 131.600 to Km 155.650 Design Km 131600 to km 155600 in the State of Punjab. Job No NH-254-PB-2022-23-565 (MoRTH) (618010) (-) (-)	Punjab	03/2023 (05/2025)	11/2026 (11/2026)	546.67 (546.67)	0	45
1511	Work of Widening/upgradation of 2-Lane with paved shoulder of Sri Muktsar Sahib to Malout road from Km 279.400 to Km 307.060 section of NH-354 in the State of Punjab on EPC mode. Job No. NH-354-PB-2021-22-555 (MoRTH) (618023) (-) (-)	Punjab	03/2022 (10/2023)	04/2025 (03/2026)	152.58 (152.58)	0	100
1512	Up-gradation to two lane with paved shoulder configuration of NH-354 Section Arifkes-Ferozepur-Muktsar-Malaut from Km 201.500 to Km 212.500 & Km 229.690 to Km 269.960 and strengthening of existing pavement from Km 212.500 to Km 229.690 excluding Km 218.500 to 223.690 of NH-354 on EPC Mode in the State of Punjab. Job No. NH-354-PB-2020-21-532 (MoRTH) (618024) (-) (-)	Punjab	03/2021 (10/2023)	04/2025 (09/2026)	263.19 (263.19)	0	83
1513	Delhi-Amritsar-Katra Expressway Phase-I Pkg-VIII from Junction with Ludhiana-Malerkotla SH-11 near Bhogiwal village to Junction with Ludhiana-Moga road NH-5 near Mullanpur Dakha Km 225770 to km 260860 (NHAI) (618488) (-) (-)	Punjab	12/2020 (03/2023)	03/2025 (12/2026)	1895.74 (2034.94)	1274.51	31.08
1514	Delhi-Amritsar-Katra Expressway Phase-I Pkg-IX from Junction with Ludhiana-Moga road NH-5 near Mullanpur Dakha to Junction with Jalandhar - Moga road NH-703 near Kang Sahibu village Km 260860 to km 303900 (NHAI) (618489) (-) (-)	Punjab	12/2020 (07/2022)	07/2024 (03/2027)	1851.47 (2407.14)	1934.7	73.35
1515	Delhi-Amritsar-Katra Expressway Phase-I Pkg-X from Jn. with Jalandhar - Moga road NH-703 to Jn. with Jalandhar-Kapurthala road NH-703A and to Jn. with Kapurthala - Sultanpur Lodhi road NH-703A km 000 to km 24000 to Amritsar connectivity (NHAI) (618490) (-) (-)	Punjab	12/2020 (07/2022)	07/2024 (07/2026)	2177.54 (2062.74)	1524.23	62.99
1516	Delhi-Amritsar-Katra Expressway Phase-I Pkg-XI from Junction with Jalandhar - Kapurthala road NH-703A near khojewal village to Junction with Amritsar-Mehta-SriHargobindpur-Tanda road NH-503A near SriHargobindpur Km 319400 to km 362420 (NHAI) (618491) (-) (-)	Punjab	03/2021 (11/2022)	11/2024 (12/2026)	2175.35 (2206.71)	1377.13	43.45
1517	Delhi-Amritsar-Katra Expressway Phase-I Pkg-XII from Junction with Amritsar-Mehta-SriHargobindpur-Tanda road NH-503A near SriHargobindpur to Junction with Pathankot-Gurdaspur road NH-54 near Gurdaspur Km 362420 to km 397700 (NHAI) (618492) (-) (-)	Punjab	03/2021 (02/2025)	02/2027 (06/2027)	1734.18 (1538.47)	773.53	27.52
1518	Delhi-Amritsar-Katra Expressway Phase-I Spur-I from Jn. with Kapurthala - Sultanpur Lodhi Road NH-703A near Isharwal village to Jn. with Kapurthala - Tarn Taran road NH-703AA near Goinwal Sahib [Km 24000 to Km 41000 of Amritsar connectivity] (NHAI) (618493) (-) (-)	Punjab	12/2021 (04/2023)	04/2026 (03/2028)	2165.23 (1519.6)	603.8	33.49
1519	Greenfield connectivity from Govindsar village on Delhi Amritsar Katra Expressway to Talwara village on NH-44 Pathankot by-pass (NHAI) (618551) (-) (-)	Punjab	11/2024 (07/2025)	07/2027 (07/2027)	666.81 (690.47)	215.06	28.5
1520	Development of 6L Greenfield Jalandhar Bypass starting from Kahlwan NH-03 ending at Kang Sahbu NH-703 via Sarmastpur NH-44 - Madara NH-03 - Khajurla NH-44 (NHAI) (618552) (-) (-)	Punjab	03/2021 (01/2023)	01/2025 (06/2027)	1754.84 (2167.39)	1252.02	54.01
1521	6L of Jodhpur Romana Bathinda - Mandi Dabwali Punjab Haryana Border section of NH-54 from km. 0.000 to km. 27.400 of NH-54 (NHAI) (618610) (-) (-)	Punjab	05/2020 (08/2023)	08/2025 (07/2026)	789.26 (1318.91)	688.68	99
1522	6L Amritsar-Bathinda Greenfield section from village Tiba on NE-5A to Jn. with Moga Jalandhar road NH-703 near Dharamkot from km 0.000 to km 39.000 of NH-754A Pkg-1 (NHAI) (618617) (-) (-)	Punjab	03/2021 (11/2022)	11/2024 (12/2027)	1229.38 (1549.32)	969.03	71.6
1523	6L Amritsar-Bathinda Greenfield section from Jn. with Bhagta Bhai Ka-Bhadaur Road near Dyalpura Bhai Ka to Jn. with Mandi Dabwali Bathinda Road on NH-54 near Sangat Kalan from km 93.000 to km 154.866 of NH-754A Pkg-3 (NHAI) (618618) (-) (-)	Punjab	03/2021 (06/2024)	06/2026 (07/2027)	2029.17 (2677.23)	1440.11	72

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1524	6L Access Controlled Ludhiana-Bathinda Greenfield highway from Jn. with Amritsar-Bathanda Greenfield Road NH-754A near Rampura Phul to Jn. with Moga-Barnala Road NH-703 near village Tallewal from Km 0.0 to Km 30.3 of NH-754AD Pkg-1 (NHAI) (618647) (-) (-)	Punjab	06/2021 (09/2023)	09/2025 (10/2026)	906.51 (1020.52)	687.75	81.5
1525	Development of 6-lane Greenfield Southern Ludhiana Bypass from intersection with NH-44 near Village Rajgarh to intersection with Delhi Katra Expressway NE-5 near Village Ballawal, km 0000 to km 25240 (NHAI) (618648) (-) (-)	Punjab	11/2024 (03/2026)	03/2028 (03/2028)	1424.55 (1424.55)	145.14	3.54
1526	Moga - Bagha Purana - Bajakhana from km. 0.00 to km. 43.32 (NHAI) (618764) (-) (-)	Punjab	05/2020 (12/2022)	12/2024 (12/2026)	1032.59 (1264.17)	787.04	76
1527	4L of Greenfield section from Sirhind to Mohali (NHAI) (618776) (-) (-)	Punjab	03/2022 (05/2023)	05/2025 (09/2026)	1237.65 (1301.15)	1383.52	96.78
1528	4/6L Greenfield LudhianaRupnagar highway from Jn. with NE-5 village near to ManewalLudhiana to Jn. with NH-205 near Bheora Village Rupnagar from Km 66.0 to Km 91.0 i/c spur to Kharar from Km 0.0 to Km 19.5 with Ludhiana bypass of NH-205K Pkg-3 (NHAI) (618785) (-) (-)	Punjab	07/2021 (02/2023)	02/2025 (12/2026)	1501.02 (1815.13)	1158.7	79.86
1529	4L of Phagwara - Hoshiarpur (NHAI) (618786) (-) (-)	Punjab	11/2022 (03/2025)	03/2027 (07/2027)	1196.38 (1503.79)	535.6	20.03
1530	4L of Fazilka to Abohar section of NH-07 including construction of Greenfield Abohar & Fazilka Bypasses (NHAI) (618793) (-) (-)	Punjab	03/2023 (04/2024)	04/2026 (07/2027)	1409.88 (1674.04)	881.3	67
1531	Amritsarairport Junction - Ramdas from km. 100.835 to km. 139.813 Pkg - IV (NHAI) (618794) (-) (-)	Punjab	12/2020 (03/2022)	09/2023 (09/2026)	524.88 (416.58)	394.14	96
1532	Amritsar Bypass Pkg III from km. 71.496 to km. 105.158 (NHAI) (618795) (-) (-)	Punjab	02/2021 (08/2022)	08/2024 (12/2026)	1474.77 (1228.42)	1222.73	82.3
1533	4L of Beas-Mehta-Batala-Dera Baba Nanak from intersection with Jalandhar-Amritsar Highway NH-3 near Beas till start of Batala Bypass near Village Acchhal from Km. 0.000 to Km. 31.300 Pkg-1 (NHAI) (618809) (-) (-)	Punjab	08/2021 (06/2023)	06/2025 (05/2027)	809.51 (966.99)	669.72	67.8
1534	4L of existing Beas Baba Bakala - Dera Baba Nanak Section from start of Batala Bypass till intersection with Ajnala Gurdaspur Highway NH 354 near Dera Baba Nanak from Km. 31.300 to Km. 69.100 with Additional batala Bypass Pkg-II (NHAI) (618810) (-) (-)	Punjab	10/2021 (06/2023)	06/2025 (03/2027)	1003.38 (993.6)	792.5	80.7
1535	4L of Amritsar-Ghoman - Tanda - Una Section from Km 8.270 to Km 54.000 of NH-503A Package-I (NHAI) (618906) (-) (-)	Punjab	12/2020 (06/2022)	06/2024 (03/2027)	857.91 (1443.47)	754.44	68.4
1536	6L Amritsar-Bathinda Greenfield section from Jn. with Moga Jalandhar road NH-703 near Dharamkot to Jn. with Bhagta Bhai Ka-Bhadaur Road near Dyalpura Bhai Ka from km 39.000 to km 93.000 of NH-754A Pkg-2 (NHAI) (619099) (-) (-)	Punjab	03/2021 (06/2024)	06/2026 (06/2027)	1801.37 (2172.71)	1268.39	64.6
1537	6L Access Controlled Ludhiana-Bathinda Greenfield highway from Jn. with Moga-Barnala Road NH-703 near village Tallewal to Jn. with Delhi-Katra Expressway NE-5 near Ludhiana village Ballawal from Km 30.300 to Km 75.543 of NH-754AD Pkg-2 (NHAI) (619105) (-) (-)	Punjab	07/2021 (09/2025)	09/2027 (09/2027)	1555.13 (1564.66)	698.87	23.56
1538	Delhi-Amritsar-Katra Expressway Phase-I Spur-III from Junction with Amritsar-Jalandhar road NH-3 near Bhishambarpura to Junction with Amritsar-Anjala road NH-354 near Amritsar Airport [Km 71000 to Km 99000 of Amritsar connectivity] (NHAI) (619200) (-) (-)	Punjab	03/2021 (11/2022)	10/2024 (10/2027)	1641.75 (1951.7)	1345.26	33.58
1539	4/6L Greenfield Ludhiana Rupnagar highway from Jn. with NE-5 village near to ManewalLudhiana to Jn. with NH-205 near Bheora Village Rupnagar from Km. 0.00 to Km. 37.7 including spur to Kharar with Ludhiana bypass of NH-205K Pkg-1 (NHAI) (619318) (-) (-)	Punjab	05/2021 (12/2022)	12/2024 (12/2027)	1368.91 (1382.48)	530.32	15.31
1540	Beaver Gomti 4LPS from km 58.245 to km 108.600 Pkg-I (MoRTH) (617887) (-) (-)	Rajasthan	12/2020 (10/2021)	10/2023 (07/2026)	379.23 (379.23)	206.48	100
1541	Widening of Pachpadra-Bagundi Section to 4 Lane from Km 73/60 to 95/70 of NH-25 on EPC mode in the state of Rajasthan. (MoRTH) (617901) (-) (-)	Rajasthan	01/2022 (12/2022)	12/2024 (07/2026)	194.88 (194.88)	55.29	98.58

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1542	Construction of 2 lane with paved shoulder for the work of Development of remaining sections of NH-325 Balotra to sanderao via Jalore to 2 lane with paved shoulder configuration by Construction of Byasses for town portions1 Asotra- Brahmdham bypass 2Siwana Bypass 3 Mokalsar Bypass 4 Major realignment at Kathadi 5 Major realignment at Bishangarh 6 Jalore Bypass 7 Ahore Town portion 8 Dujana Bypass in the state of Rajasthan on EPC Mode (MoRTH) (618011) (-) (-)	Rajasthan	12/2021 (05/2022)	05/2024 (10/2026)	411.44 (411.44)	85.69	91.36
1543	Upgradation to Two-lane with paved shoulder of Hanumangarh to Kenchiyan section from Km 0.000existing chainage-Km 23.200 to Km 49.605existing chainage-Km 74.645 of NH-54 in the State of Rajasthan on EPC mode. (MoRTH) (618069) (-) (-)	Rajasthan	03/2022 (10/2024)	10/2026 (10/2026)	334.64 (334.64)	0	70
1544	Up-gradation to 2 lane with paved shoulder from Neechli Oden Nathdwara at Design Km 88.800 existing km 55.95 to Bhatewar at Design Km 142.028 existing km 0.00 of NH-162E in the State of Rajasthan on EPC mode. (MoRTH) (618092) (-) (-)	Rajasthan	02/2023 (10/2024)	10/2026 (10/2026)	606.61 (606.61)	0	60.39
1545	Upgradation to 2-Lane with Paved Shoulder from Design Km 36300 to Design Chainage 47918 and from Design Ch 69900 to Design Ch 83940 of NH-248A Natni Ka Bara in the State of Rajasthan on EPC Mode. (MoRTH) (618117) (-) (-)	Rajasthan	02/2024 (11/2024)	05/2026 (08/2026)	154.89 (154.89)	15.13	23
1546	Construction of 2 lane with Paved Shoulder for Northern Bypass Phase-II of Kota city in the State of Rajasthan. (MoRTH) (618200) (-) (-)	Rajasthan	03/2022 (10/2023)	04/2025 (11/2026)	317.74 (317.74)	6.14	48.9
1547	Balance work of Rehabilitation and Up-gradation to 4-Lane configuration of Ras-Beawar Section Km 00.000 to km 30.050 of NH-158 in the State of Rajasthan under Green National Highway Corridor Project GNHCP. (MoRTH) (618235) (-) (-)	Rajasthan	01/2025 (06/2025)	12/2026 (12/2026)	278.1 (278.1)	82.5	53.45
1548	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-10 Ch. 292.950 to Ch. 319.400 [End of Interchange on NH-166 near village Mui to Hardeoganj village near Indergarh] (NHAI) (618457) (-) (-)	Rajasthan	11/2019 (05/2021)	05/2023 (08/2026)	1272.97 (1265.16)	1150.12	95.25
1549	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-15 Ch. 419.000 to Ch.427.300 [Junction with NH-12 near village Ummedpura to Major bridge over Takli river near Nayagaon Jageer village] (NHAI) (618458) (-) (-)	Rajasthan	07/2020 (07/2021)	01/2024 (07/2026)	1854.68 (1854.68)	1495.49	95.52
1550	Sangariya near Chautala-Rasisar near Bikaner section of NH-754K Phase-I AJ/SR-Package-7 (NHAI) (618611) (-) (-)	Rajasthan	02/2019 (06/2021)	06/2023 (07/2026)	520.63 (548.42)	450.58	100
1551	Deogarh near Dhandhaniya-Rajasthan/Gujarat Border Phase-I AJ/DRGB-Package-6 (NHAI) (618612) (-) (-)	Rajasthan	10/2019 (08/2021)	08/2023 (07/2026)	846.59 (740.62)	704.71	100
1552	Deogarh near Dhandhaniya-Rajasthan/Gujarat Border Phase-I AJ/DRGB-Package-7 (NHAI) (618613) (-) (-)	Rajasthan	10/2019 (07/2021)	07/2023 (07/2026)	662.08 (597.77)	561	99.2
1553	6L access controlled Highway from Km 40080 to Km 86513 Mator to Barodameo Section (NHAI) (618757) (-) (-)	Rajasthan	09/2022 (03/2024)	03/2026 (06/2027)	2010.2 (1565.88)	708.28	37.27
1554	6L accesscontrolled highway from km 0000 to km 40080 Paniyala to Mator Section of Paniyala-Barodameo ICR (NHAI) (618758) (-) (-)	Rajasthan	09/2022 (09/2024)	09/2026 (09/2026)	1764.86 (1239.24)	558.32	41.25
1555	Tanot -Ramgarh-Bhadasar-Jaisalmer NH-68 and BhadasarMokal-Sarkaritala up to Pakistan Border NH-968 Pkg-BM/5 (NHAI) (618796) (-) (-)	Rajasthan	02/2018 (04/2019)	04/2021 (07/2026)	828.58 (830.37)	694.47	100
1556	Mayjilar Jaisalmer with Jaisalmer Bypass Link Road Section of NH-11 Part of BM-7 & Sundra Myajilar Ambsingh ki Dhani Road part of Munabao Tanot project NH-70 (NHAI) (618797) (-) (-)	Rajasthan	03/2025 (12/2025)	12/2027 (12/2027)	1237.71 (927.02)	76.97	18.56
1557	4L of Karwar Km. 281.980 of NH-62 Nagaur road to Dangiyavas of Jodhpur Ring Road Pkg-II (NHAI) (618838) (-) (-)	Rajasthan	11/2021 (08/2022)	08/2024 (07/2026)	736.75 (512.77)	470.4	100
1558	Construction of Four lane Elevated Structure at Raniwada Circle in Sanchoe City on NH-68 (NHAI) (618853) (-) (-)	Rajasthan	01/2024 (07/2024)	07/2026 (07/2026)	353.3 (241.34)	184.84	86.18

All Ongoing Projects							JUNE 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1559	Construction of two lane with paved shoulder of Ghatol Bypass from km 133.250 to km 140.950 of NH-56 old NH No. 113 on EPC mode in the State of Rajasthan. (MoRTH) (619251) (-) (-)	Rajasthan	03/2025 (03/2026)	09/2027 (-)	170.49 (170.49)	0	11
1560	Upgradation of 6 laned Jaipur- Kishangarh section of NH-48 from km 274100 to 363885 involving construction of flyovers and Service road in Rajasthan On Engineering, Procurement & Construction EPC Mode (NHAI) (619270) (-) (-)	Rajasthan	03/2026 (07/2026)	01/2029 (-)	910.91 (910.91)	0	0
1561	Construction of Elevated Corridor at Kherwara Town on Udaipur Ratanpur Shamlaji Section of NH-48 in Udaipur District in the State of Rajasthan on EPC mode (NHAI) (619271) (-) (-)	Rajasthan	03/2026 (07/2026)	01/2029 (-)	363.89 (363.89)	0.38	0
1562	Construction of two lane with paved shoulder Gangtok Bypass Road from Ranipool to Burtuk Ch 0.00 Km to 23.316 L23.316 Km in the State of Sikkim (MoRTH) (618071) (-) (-)	Sikkim	10/2021 (05/2022)	05/2024 (12/2026)	385.15 (342.89)	0	90
1563	Construction/Up gradation of Existing road to 2 Lane with Paved Shoulder including Geometric Improvement from Ranipool to Pakyong Balance work from Km 2.000 to 16.167 of NH-717-A on EPC basis under SARDP-NE Phase A in the State of Sikkim (NHIDCL) (618426) (-) (-)	Sikkim	03/2018 (01/2023)	07/2024 (12/2026)	264.84 (380.94)	0.17	87.03
1564	Realignment of NH-717A from Design Ch.0.00 Km 77.800 of NH-10 to Design Ch.2.00 Km 3.100 of NH-717A with two lane paved shoulder including Major Bridge of 680 m in the State of Sikkim on EPC Mode-COS work (NHIDCL) (618428) (-) (-)	Sikkim	01/2021 (04/2021)	04/2023 (05/2026)	264.84 (380.94)	70.7	100
1565	Construction & Upgradation of existing road to 2-lane with paved shoulder from New Rolep Bridge at km 37.600 to Chochenpheri at km 52.00 in the section of Rongli to Chochenpheri of NH 717B Pkg-II C (NHIDCL) (618446) (-) (-)	Sikkim	10/2020 (05/2021)	05/2024 (09/2026)	493.42 (478.79)	0.03	79.13
1566	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Helipad near Menla at Km 82000 to Menla at Km 94030 of Rhenock-Menla Spur NH-717B Package-IIIB on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618447) (-) (-)	Sikkim	01/2021 (02/2021)	02/2024 (05/2027)	410.6 (379.3)	0	82.64
1567	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Chochenpheri at Km 52000 to Helipad near Menla at Km 82000 of Rhenock-Menla Spur NH-717B Package-IIIA on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618448) (-) (-)	Sikkim	10/2020 (12/2020)	12/2023 (05/2027)	816.79 (786.6)	32.28	64.31
1568	Construction & Upgradation of existing road to 2-lane with paved shoulder from km27.200 End of Rongli bypass to km37.600New Rolep Bridge of Rhenok-Menla spur NH-717B on EPC Mode under SARDP-NE Phase-A in Sikkim Pkg-II B (NHIDCL) (618449) (-) (-)	Sikkim	07/2020 (10/2020)	04/2023 (09/2026)	230.45 (244.91)	0	86.19
1569	Rehabilitation & Upgradation of existing road to 2-lane with paved shoulder including geometric improvement of section from start of Rabangla km33.600 to km58.840 under SARDP-NE Phase A Pkg- IV (NHIDCL) (618450) (-) (-)	Sikkim	07/2020 (10/2020)	05/2022 (12/2026)	292.8 (292.8)	1.91	65.15
1570	Construction of Bypass to Madurai Achambathu Viratipathu in between km 6/850 10/382 of NH 49 Extn New NH 85 including Land Acquisition on Engineering, Procurement & Construction EPC basis Contract under NH O Annual Plan 2021-22 in the state of Tamil Nadu job No.NH-49 Extn New NH 85 - TN-2021-22-997 (MoRTH) (617962) (-) (-)	Tamil Nadu	03/2022 (09/2024)	08/2026 (08/2026)	238.97 (260.07)	126.43	94
1571	Bangalore Chennai Expressway Phase-III Package II Walajahpet to Arakkonam from Km 180.000 to Km 204.500 (NHAI) (618478) (-) (-)	Tamil Nadu	01/2021 (07/2022)	07/2024 (08/2026)	1106.65 (1106.65)	591.91	93.04
1572	Bangalore Chennai Expressway Phase-III Package III Arakkonam to Kancheepuram from Km 204.500 to Km 230.000 (NHAI) (618479) (-) (-)	Tamil Nadu	12/2020 (08/2022)	07/2024 (12/2027)	1525.1 (1525.1)	360.65	53.56
1573	Construction of Trumpet Interchange Connecting Bangalore Chennai Expressway km.261705 to km. 262800 with Maduravoyal to Walajapet Section of NH 48 near Sriperumbudur Toll Plaza at km. 35700 (NHAI) (618480) (-) (-)	Tamil Nadu	05/2023 (02/2024)	08/2025 (10/2026)	162.55 (162.56)	52.47	38.52
1574	4L Bangalore-Chennai Expressway from Km. 230.000 to Km. 261.705 of Kancheepuram to Sriperumbudur Section Phase-III/Package-IV (NHAI) (618481) (-) (-)	Tamil Nadu	02/2021 (07/2022)	07/2024 (10/2026)	3605.73 (3605.73)	930.29	89.97
1575	Karaipettai to Walajapet from Km 71.015 to 107.091 (NHAI) (618521) (-) (-)	Tamil Nadu	08/2018 (02/2019)	02/2021 (07/2026)	766.51 (766.51)	613.5	93.55

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1576	Balance Works for six laning of Sriperumbudur to karaipettai section of NH-4 New NH-48 from 37000 Existing Km 37000 to Km 71015 Existing Km 71000 in Tamilnadu on EPC mode underNHDP Phase-V (NHAI) (618522) (-) (-)	Tamil Nadu	06/2024 (01/2025)	10/2026 (03/2027)	411.16 (411.16)	134.48	36.64
1577	Improving the Alignment of Thoppur Ghat Section from Km 158.500 to Km 165.100 in Dharmapuri - Salem Section of NH-44 (NHAI) (618561) (-) (-)	Tamil Nadu	03/2024 (03/2025)	03/2028 (03/2028)	904.99 (731.09)	209.58	45.13
1578	4L of Madurai Ring Road Phase 1 [Vadipatti-Thamrapatti] from km 0.00 - km 29.960 (NHAI) (618563) (-) (-)	Tamil Nadu	12/2018 (03/2020)	03/2022 (07/2026)	900.05 (900.05)	903.4	99.25
1579	4L of left-over works including additional structures from Kerala/Tamil Nadu border to Kanyakumari Section from Km 43.0 to Km 96.174 of NH66 (NHAI) (618608) (-) (-)	Tamil Nadu	11/2022 (08/2023)	08/2025 (11/2026)	1564.23 (1263.42)	961.9	80.68
1580	6L of Pondavakkam to Kannigaipair from km 96.040 to km 116.100 of NH 716B Pkg-IV (NHAI) (618635) (-) (-)	Tamil Nadu	02/2021 (01/2023)	01/2025 (12/2027)	1359.81 (1359.81)	409.22	40.88
1581	4L of Thirumangalam to Vadugapatti section from km 0.000 to km 36.000 of NH-744 (NHAI) (618744) (-) (-)	Tamil Nadu	03/2022 (02/2023)	02/2025 (07/2026)	1076.97 (791.6)	679.49	95.51
1582	Melur - Pilayarpatti - Karaikudi from km 99.920 of NH 38 to km 12.9 of NH 383 Ext. (NHAI) (618756) (-) (-)	Tamil Nadu	12/2018 (03/2020)	03/2022 (07/2026)	1103.86 (1085.41)	956.43	97.32
1583	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package II from Km 4.604 to Km 9.700 (NHAI) (618800) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1616.97 (1616.97)	239.48	18.13
1584	Construction of New Double Tier 4-lane Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from Km -0342 to Km 20223 Package 1 from Km -0342 to Km 4604 (NHAI) (618801) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1388.59 (1388.59)	268.23	22.8
1585	Poondiyankuppam Km.67.000 to Sattanathapuram Km.123.800 (NHAI) (618846) (-) (-)	Tamil Nadu	03/2018 (01/2022)	01/2024 (09/2026)	2565.63 (2319.35)	1207.03	99.8
1586	4L of Madathukulam - Pollachi from km. 74.38 to km. 116.95 of old NH-209 New NH-83 (NHAI) (618894) (-) (-)	Tamil Nadu	01/2019 (12/2020)	12/2022 (07/2026)	1772.13 (1772.13)	1061.26	95.52
1587	Kamalapuram to Oddanchatram from km. 0.00 to km. 35.822 (NHAI) (618895) (-) (-)	Tamil Nadu	01/2019 (01/2021)	01/2023 (08/2026)	1319.42 (1319.42)	649.69	92.49
1588	Balance Works for Four laning of Vikravandi to Sethiyathope section from Km 0.0 to Km 65.96 of NH-45C in Tamil Nadu under NHDP Phase-IV on EPC mode (NHAI) (618898) (-) (-)	Tamil Nadu	01/2025 (06/2025)	06/2027 (06/2027)	1163.17 (834.46)	235.05	33.64
1589	Kallagam km.38.700 to Meensurutti Km.98.433 of NH-227 in Tamil Nadu (NHAI) (618899) (-) (-)	Tamil Nadu	02/2018 (04/2019)	04/2021 (07/2026)	1499.12 (1499.12)	1111.8	100
1590	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package IV from Km 14.185 to Km 20.593 (NHAI) (619045) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1205.4 (1210.21)	86	8.58
1591	6-laning of Krishnagiri Km.0.000 to Walajahpet Km.148.300 section on NH-46 under NHDP-V (NHAI) (619074) (-) (-)	Tamil Nadu	12/2009 (06/2011)	12/2013 (07/2026)	1673.17 (781.74)	701.37	99.99
1592	Chengapalli km 102.035 to Neelambur Km144.680 and Madukkarai Km 170.880 to Walayar K183.010 Package No. NS-2/BOT/TN-08 (NHAI) (619086) (-) (-)	Tamil Nadu	10/2009 (09/2010)	03/2013 (10/2026)	852 (285.55)	6.93	100
1593	Thorapalli - Agraharam - Jittandahalli Section from km 23.350 to km 60.100 [Hosur to Dhamrapuri Pkg-2] (NHAI) (619094) (-) (-)	Tamil Nadu	02/2019 (12/2021)	12/2023 (12/2026)	1243.57 (1272.11)	827.88	77.57
1594	4L of Padalur - Trichy section from km. 285.00 to km. 325.00 of NH - 45 Pkg VI-C (NHAI) (619113) (-) (-)	Tamil Nadu	12/2005 (11/2006)	05/2009 (02/2026)	555.8 (235.8)	235.51	100

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1595	Mahabalipuram - Pondicherry Pkg-I [Mamallapuram to Mugaiyur] (NHAI) (619129) (-) (-)	Tamil Nadu	02/2019 (05/2022)	05/2024 (01/2027)	1360.54 (1477.94)	897.36	58.65
1596	Mahabalipuram - Pondicherry Pkg-II [Mugaiyur to Marakkanam] (NHAI) (619130) (-) (-)	Tamil Nadu	02/2019 (12/2023)	12/2025 (03/2027)	1116.13 (1463.75)	771.85	53.41
1597	Four Laning of Chettikulam to Natham section of NH-785 (NHAI) (619131) (-) (-)	Tamil Nadu	03/2018 (11/2018)	11/2020 (06/2026)	837.61 (823.93)	641.93	99.75
1598	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package III from Km 9.700 to Km 14.185 (NHAI) (619139) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1299.36 (1299.36)	189.12	17.24
1599	4 Laning of Paramakudi to Ramanathapuram Section of NH-87 Old NH-49 (NHAI) (619156) (-) (-)	Tamil Nadu	07/2025 (05/2026)	05/2028 (06/2028)	1853.16 (1853.16)	159.26	0
1600	Access Controlled Highway of 4 Lane with Paved Shoulders from Tiruvallur Design Chainage Km 1756 to TN/AP Broder Design Chainage Km 6151 of NH-716 Chennai-Tirupati Package-1 (NHAI) (619161) (-) (-)	Tamil Nadu	03/2024 (12/2024)	12/2026 (03/2027)	1376.1 (1247.7)	180.68	40.8
1601	Balance works of four lane from km 43.950 Thiruvallur Bypass to km 61.470 Veppampattu Bypass passing through Thannerkulam, Thozur and Sevapet Bypass 17.520 kms of Tirupathi- Tiruttani- Chennai section of NH 205 (NHAI) (619222) (-) (-)	Tamil Nadu	03/2022 (09/2022)	09/2024 (07/2026)	467.99 (699.68)	594.43	97.92
1602	6-laning of km 9.900 to km 19/948 Aramgarh to Shamshabad Section of Hyderabad-Bangalore section of NH-44 Under NHO EPC basis in the state of Telangana (MoRTH) (617913) (-) (-)	Telangana	01/2018 (05/2018)	05/2020 (06/2026)	283.15 (300.7)	480.41	92.62
1603	Widening to two/four lane with paved shoulder from Km.180.600 to Km.223.000 of NH-63 on Nizamabad-Jagadapur road on EPC mode under NHO in the state of Telangana. (MoRTH) (617936) (-) (-)	Telangana	10/2016 (03/2017)	03/2019 (-)	253.99 (183.26)	0	100
1604	6-Laning of Pune-Hyderabad Section of NH-65 from Km 493/0 to Km 524/0 from Sangareddy X Roads to Madinaguda in the State of Telangana (MoRTH) (617939) (-) (-)	Telangana	03/2023 (07/2024)	07/2026 (08/2026)	1297.75 (1297.75)	0	44.73
1605	Rehabilitation and Upgradation of LB-Nagar to Malkapur section to 6-Lane main carriageway with service roads, drains cum footpath, including VUPs and widening of Minor bridge & road safety provisions from Km. 15/00 to Km 40/00 of NH-65 Old NH-9 under NH O for the year 2020-21 in the state of Telangana on EPC Mode. (MoRTH) (617940) (-) (-)	Telangana	03/2021 (07/2022)	07/2024 (07/2026)	545.11 (545.11)	290.36	82.28
1606	Construction of six lane elevated corridor from km 7.950 Uppal to km 14.200 of NH-163 to De-Congest the urban limits of Hyderabad-Bhoopalapatnam section on EPC mode in the state of Telangana (MoRTH) (617980) (-) (-)	Telangana	03/2018 (07/2018)	07/2020 (10/2026)	626.76 (626.76)	19.3	53.01
1607	Widening & Strengthening of Existing 2LPS to 4 lane PS from Km 150000 to Km 159000 and Km 165400 to Km 186000 of NH-163 old NH-202 under NH O for the year 2020-21 on EPC Mode in the state of Telangana. (MoRTH) (617983) (-) (-)	Telangana	03/2021 (07/2022)	07/2024 (07/2026)	317.19 (300.56)	190.76	90
1608	Rehabilitation and upgradation of NH-167 from design km 113.900 to 154.479 Mallepally Haliya section to two lane with paved shoulders on EPC mode in the stte of Telangana (MoRTH) (617994) (-) (-)	Telangana	02/2018 (06/2018)	11/2019 (12/2025)	294.13 (257.61)	244.16	88.22
1609	Widening to Two Lane with Paved Shoulders from Km 67.000 to Km 114.425 of Kalwakurthy- Mallapally Section of NH 167 Erstwhile section of SH 18 in the State of Telangana on EPC mode under NH O Annual Plan 2016-17 (MoRTH) (617995) (-) (-)	Telangana	01/2017 (05/2017)	05/2019 (12/2026)	300 (300)	175.12	99.2
1610	Construction of 4-lane flyover at Amberpet-X road, Hyderabad on NH-202 in the State of Telangana (MoRTH) (618001) (-) (-)	Telangana	05/2018 (06/2021)	06/2023 (06/2026)	216.53 (265.88)	172.02	92.1
1611	Rehabiitation and upgradation from km 121/000 to 154/000 Nakrekal to Mallampally section of NH-365 to 2 lane with paved shoulders in the state of Telangana in the EPC mode (MoRTH) (618025) (-) (-)	Telangana	03/2018 (06/2018)	12/2019 (09/2026)	192.67 (192.67)	141.82	96

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1612	Widening to two lane with paved shoulders from Km 0/000 to Km 45/946 of Nizampet-Narayankhed-bidar section of NH-161B in the state of Telangana under Annual Plan 2021-22 on EPC mode under NHO (MoRTH) (618091) (-) (-)	Telangana	03/2022 (02/2024)	02/2026 (03/2027)	512.98 (512.98)	151.45	46
1613	Widening to two lane with paved shoulders from Km 0/000 to Km 79/300 of Kalwakurthy - Kollapur section of NH-167K in the state of Telangana under annual plan 2021-22 on EPC mode under NHO. (MoRTH) (618104) (-) (-)	Telangana	03/2022 (07/2023)	07/2025 (07/2026)	886.69 (886.69)	620.25	86.74
1614	Widening and strengthening to 4 lane / 2-lane with paved shoulders of Mahabubnagar - Chincholi section from km 60/255 to Km 102/834 of NH-167N in the State of Telangana on EPC mode. (MoRTH) (618105) (-) (-)	Telangana	03/2022 (10/2023)	10/2025 (11/2026)	631.49 (631.49)	125.34	30.8
1615	Widening and Strengthening to 2/4 lane with paved shoulders of Mahabubnagar Chincholi section from Km 0/0 to Km 60/255 of NH-167N in the state of Telangana under Annual plan 2021-22 on EPC modepackage-I under NHO Job No.167N-TS-2021-22-75 (MoRTH) (618106) (-) (-)	Telangana	01/2022 (01/2023)	01/2025 (05/2026)	703.68 (703.68)	304.65	90.69
1616	Widening to 2 lane with paved shoulders from 0.00 to 32.970 ofAdilabadto Bela section of NH 353B in the State of Telangana (MoRTH) (618130) (-) (-)	Telangana	10/2022 (05/2024)	05/2026 (11/2026)	490.92 (490.92)	0	77.79
1617	Widening to two/four lane with paved shoulders from Km.34.250 to Km.71.830 of NH-365A on Kodad-Khammam-Kurvi road. (MoRTH) (618140) (-) (-)	Telangana	10/2022 (02/2025)	01/2027 (01/2027)	445.76 (445.76)	18.32	9.39
1618	Widening and Improvement of existing carriage way to 2 lane with paved shoulders from Km. 86/160 to 131/730 of Jangaon-Duddeda section of NH-365B in the State of Telangana on EPC Mode (MoRTH) (618141) (-) (-)	Telangana	01/2022 (12/2022)	12/2024 (12/2026)	423.48 (423.48)	184.83	77.77
1619	Widening to Two lane with paved shoulders from 106/830 to 158/496 of Yellareddy-Rudrur Section of NH-765D in the state of Telangana on EPC mode under NHO under Annual plan 2022-23 (MoRTH) (618182) (-) (-)	Telangana	10/2022 (07/2024)	07/2026 (07/2026)	499.88 (499.88)	197.25	66.68
1620	Widening to 2 lane with paved shoulders from Km 62/920 to km 106/830 of Medak - Yellareddy section in the State of Telangana under Annual Plan 2022-23 on EPC mode under NHO (MoRTH) (618183) (-) (-)	Telangana	10/2022 (08/2024)	08/2026 (08/2026)	399.01 (399.01)	0	69.6
1621	Rehabilitation and Up-gradation of Valigonda to Thorrrur Section to Two Lane with Paved Shoulders from Km 39.180 to Km 108.300 of NH-930P in the State of Telangana on Engineering, Procurement and Construction EPC Basis (MoRTH) (618186) (-) (-)	Telangana	01/2022 (12/2022)	12/2024 (09/2026)	549.28 (549.28)	325.77	94.68
1622	Widening to two lane with paved shoulders of 'Bodhan Basar Bhainsa ' section from Km 38/900 to 95/300 of NH-161BB in the state of Telangana under Annual Plan 2021-22 on EPC Mode under NH O. (MoRTH) (618190) (-) (-)	Telangana	03/2022 (03/2023)	03/2025 (07/2026)	644.45 (644.45)	403.3	98.6
1623	Widening to 2 lane with Paved Shoulders of Siddipet-Elkathurthy section from Km 69/978 to km 133/619 of NH-765DG in the State of Telangana under Annual plan 2021-22 on EPC mode (MoRTH) (618196) (-) (-)	Telangana	01/2022 (12/2022)	09/2024 (12/2026)	578.85 (578.85)	0	85
1624	Widening to 2 lane with Paved Shoulders of Medak - Siddipet section from Km 0/0 to km 69/978 of NH-765DG in the State of Telangana under Annual plan 2021-22 on EPC mode (MoRTH) (618197) (-) (-)	Telangana	01/2022 (01/2023)	01/2025 (12/2026)	882.18 (882.18)	383.75	74.06
1625	Improvement of Geometrics of Kalkallu to Gundla Pochanpalli from Km 454.00 to Km 471.00 of NH-44 (NHAI) (618558) (-) (-)	Telangana	03/2022 (01/2023)	01/2025 (03/2027)	955.49 (903.17)	454.5	36.5
1626	6L of existing 4L from Gundlapochampally to Bowenpally from km 471.300 to km 481.331 of NH-44 (NHAI) (618559) (-) (-)	Telangana	12/2021 (08/2022)	07/2024 (12/2026)	521.53 (528.21)	257.31	50.5
1627	Improvement of Geometrics of Thondupally to Kothur from Km 22.300 to Km 34.14 of NH-44 (NHAI) (618560) (-) (-)	Telangana	03/2022 (03/2023)	09/2024 (09/2026)	541.58 (527.43)	74.01	17.05

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1628	Khammam-Devarapalle Pkg I [4L Access Controlled Greenfield from Thallampadu village to Somavaram village Design Chainage 0000 to 33604] (NHAI) (618746) (-) (-)	Telangana	01/2021 (10/2022)	10/2024 (10/2026)	797.36 (1337.18)	684.51	96.4
1629	4L of Karimnagar-Warangal section from km 49.500 to km 117.820 of NH-563 (NHAI) (618765) (-) (-)	Telangana	03/2022 (07/2023)	07/2025 (08/2026)	2146.86 (2486.51)	1268.13	92.4
1630	4L Access Controlled Greenfield Highway Section Mancherial Warangal from Pangidipalle village at Design Ch. 72.350 Km to Oorugonda village at Design Ch. 112.240 KmPackage-III (NHAI) (618811) (-) (-)	Telangana	03/2023 (10/2025)	10/2027 (01/2028)	1183.71 (1170.64)	163.15	5
1631	4L Access Controlled Greenfield Section Mancherial Warangal from Puttapaka village at Design Ch. 35.300 Km to Pangidipalle village at Design Ch. 72.350 KmPackage-II (NHAI) (618812) (-) (-)	Telangana	01/2023 (06/2025)	06/2027 (12/2027)	1129.33 (1145.41)	209.45	8.05
1632	4L Access Controlled Greenfield Section Mancherial Warangal from Narva village at Design Ch. 3.834 Km to Puttapaka village at Design Ch. 35.300 Km Package-I (NHAI) (618813) (-) (-)	Telangana	03/2023 (12/2024)	12/2026 (10/2027)	1127.9 (1104.27)	160.54	10.23
1633	4L Access Controlled Greenfield Highway section on NH163G Warangal-Khammam from Oorugonda village in Hanamkonda District at Design Ch. 112.240 Km to Venkatpur village in Warangal District at Design Ch. 150.240 KmPackage-I (NHAI) (618814) (-) (-)	Telangana	03/2023 (06/2025)	06/2027 (05/2028)	1142.6 (1140.82)	147.2	0
1634	4L Access Controlled Greenfield Highway section on NH-163G Warangal-Khammam from Venkatpur village in Warangal District at Design Ch. 150.240 Km to Thallasenkesa village in Mahabubabad District at Design Ch. 189.650 kmPackage-II (NHAI) (618815) (-) (-)	Telangana	03/2023 (04/2024)	04/2026 (03/2027)	1092.88 (1083.11)	377.96	74.43
1635	4L Access Controlled Greenfield Highway section on NH-163G Warangal-Khammam from Thallasenkesa village at Design Ch. 189.650 km to V.Vekatayapalem village in Khammam District at Design Ch. 220.480 KmPackage-III (NHAI) (618816) (-) (-)	Telangana	03/2023 (07/2025)	07/2027 (07/2027)	1105.25 (1098.05)	168.17	10.06
1636	4L Access Controlled Greenfield Highway section on NH-163G Khammam Vijayawada from V. Venkatayapalem village at Design Ch. 220.480 Km to BrahmanapalliK village at Design Ch. 250.400 Km Package-I. (NHAI) (618817) (-) (-)	Telangana	03/2023 (03/2025)	03/2027 (06/2027)	973.45 (1021.96)	270.95	44
1637	Hyderabad - Maneguda (NHAI) (618944) (-) (-)	Telangana	10/2021 (11/2024)	11/2026 (05/2027)	958.86 (1218.49)	408.06	21.84
1638	4L of Kodad Design Km 0.00/Existing Km 185.00 of NH-65 to Khammam Design Km 31.800/Existing Km 29.400 of NH-365A (NHAI) (618945) (-) (-)	Telangana	01/2021 (01/2022)	05/2024 (07/2026)	1149.17 (1606.99)	871.58	99.98
1639	Upgradation to Two Lane with Paved Shoulders from Km 0.000 to Km 41.920 Green Field Alignment of Gowrelly to Valigonda Section of NH-930P in the State of Telangana on EPC Mode under Annual Plan 2022-23 (MoRTH) (619009) (-) (-)	Telangana	11/2022 (05/2026)	04/2028 (03/2028)	690.33 (690.33)	0	0
1640	Khammam-Devarapalle Pkg II [4L Access Controlled Greenfield from Somavaram village to Chintagudem village Design Chainage 33604 to 63117] (NHAI) (619128) (-) (-)	Telangana	01/2021 (09/2022)	09/2024 (07/2026)	615.78 (981.64)	524.03	98.02
1641	Thanamcherla-Jamandlapally 2LPS (NHAI) (619165) (-) (-)	Telangana	11/2013 (03/2014)	02/2023 (07/2026)	177.18 (18.65)	8.3	100
1642	Rehabilitation and upgradation of NH-221 from km 121/0 to 165/0 Rudrampur to Bhadrachalam section to two lane with paved shoulder under NHDPIV in the state of Telangana through EPC mode (MoRTH) (619193) (-) (-)	Telangana	01/2015 (02/2015)	02/2017 (07/2026)	295.47 (334.82)	375.14	82.76
1643	Construction of 4 lane Bypass to Nalgonda Town Iroon Km 000 Existing Ch. 181590 to Km 14.00 Existing Ch. 28/685 ol Nakrekal to Nagarjunsagar Section of NH -565 in the State of Telangara on EPC under Annual Plan 2024 -25 (MoRTH) (619253) (-) (-)	Telangana	10/2024 (10/2025)	10/2027 (10/2027)	516.17 (516.17)	0	49.34
1644	Rehabilitation and up-gradation of road from km 16.077 to km 43.935 total length 27.858 km of Lalchara-Kanchanpur section via Shivbari on NH-44A to 2 lane with paved shoulder in the state of Tripura on EPC Mode Pkg-2 under BharatMala Pariyojana Manu-Simlung -2 (NHIDCL) (618307) (-) (-)	Tripura	02/2022 (01/2023)	01/2025 (01/2026)	456.88 (456.88)	0	54.56

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1645	Improvement & widening of existing NH-08 to 4-lane with Paved Shoulder from Champak Nagar to Khayerpur section design Km 242500 to Km 261610 in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618350) (-) (-)	Tripura	12/2023 (09/2024)	09/2026 (03/2027)	920.66 (920.66)	0	48.3
1646	Improvement and Widening to 2-lane with paved shoulder of road from design Km 72.000 Pati Chhari to design Km 107.654 Harina Total length 35.654 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-4 (NHIDCL) (618367) (-) (-)	Tripura	01/2024 (12/2024)	12/2026 (06/2027)	726.9 (726.9)	259.36	9.33
1647	Improvement and Widening to 2-lane with paved shoulder of road from design Km 36.000 Rangamati to design Km 72.000 Pati Chhari Total length 36.000 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-3 (NHIDCL) (618368) (-) (-)	Tripura	01/2024 (09/2024)	09/2026 (05/2027)	670.9 (670.9)	0	14.5
1648	Improvement and Widening to 2-lane with paved shoulder of road from existing Km 438.170 Khowai Chowmuhani to existing Km 439.410 South Pulinpur of NH-08 and from design Km 0.000 South Pulinpur to design Km 36.00 near Rangamati of NH 208 on Khowai Teliamura- Harina section Total length 37.24 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-2 (NHIDCL) (618369) (-) (-)	Tripura	01/2024 (09/2024)	09/2026 (03/2027)	657.21 (657.21)	0	60.5
1649	Improvement and Widening to 2-lane with paved shoulder of road from Km 101.300 to km 127.319 Total Length 26.019 Km i.e. the Khowai Teliamura-Amarpur-Harina-Sabroom section of NH 208 in the state of Tripura on EPC under JICA ODA Loan Phase VI Package-1 (NHIDCL) (618370) (-) (-)	Tripura	01/2024 (07/2024)	07/2026 (04/2027)	431.78 (431.78)	0	63.15
1650	Rehabilitation and up-gradation of road from design km 25.250 to km 36.460 Total lenth 11.210 km of Kailashahar-Kurti Bridge section on NH-208A to 2-lane with paved shoulder on EPC basis under NHO Package-III- Balance Work (NHIDCL) (618385) (-) (-)	Tripura	02/2020 (09/2024)	03/2026 (03/2026)	174.43 (174.43)	0	41.9
1651	Melaghar-Srimantapur section on NH-08 Spur from Km 23 to Km 34.500 11.5 Km and overlay from Km 20.30 to Km 22.00 1.7 Km Total Length 13.2 Km (NHIDCL) (618411) (-) (-)	Tripura	01/2023 (05/2023)	11/2024 (08/2026)	195.95 (195.95)	92.61	72.48
1652	Construction of 4-Lane with paved shoulder Agartala bypass Western side, length 25.402 km connecting NH-8 near Amtali to NH-108B near Lembuchhera in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618417) (-) (-)	Tripura	03/2023 (03/2024)	03/2027 (03/2027)	2026.05 (2026.05)	487.38	9.2
1653	Rehabilitation and upgradation to four lane road from km 70.500 to km 78.600 of NH-92 under EPC mode in the State of Uttar Pradesh (MoRTH) (617963) (-) (-)	Uttar Pradesh	01/2022 (01/2025)	01/2027 (07/2027)	296.02 (351.78)	0	33
1654	Widening to Four Lane rigid pavement configuration from Km 90.00 to Km 100.800 on NH-96 Km 42.0 to Km 53.300 as per new NH-330,design length of 11.300 km under EPC mode in the state of Uttar Pradesh. (MoRTH) (617964) (-) (-)	Uttar Pradesh	12/2022 (11/2024)	11/2026 (11/2026)	309.63 (309.63)	38.08	31
1655	Balance work of Construction of Ring Road for Raebareli City on eastern side of NH-24B Phase-1 on EPC mode. (MoRTH) (618009) (-) (-)	Uttar Pradesh	12/2019 (10/2020)	04/2022 (09/2026)	319.96 (347.8)	0	95
1656	Construction of Balrampur bypass with 2L flexible pavement configuration from km.223.000 of NH-330 to km.328.300 of NH-730 under EPC mode (MoRTH) (618054) (-) (-)	Uttar Pradesh	12/2022 (08/2024)	02/2026 (08/2026)	515.69 (515.69)	118.72	54
1657	Construction of Pratapgarh Bypass Extension connecting NH-31 to NH-330 on EPC mode in the State of Uttar Pradesh. (MoRTH) (618055) (-) (-)	Uttar Pradesh	10/2022 (01/2024)	06/2025 (09/2026)	225.17 (225.17)	0	75
1658	Improvement and Up-gradation to two Lane with Paved Shoulder Configuration from existing km. 420.00 Shohratgarh to km. 454.00 Uska Bazar of NH-730 in the state of Uttar Pradesh EPC basis (MoRTH) (618056) (-) (-)	Uttar Pradesh	01/2022 (03/2024)	09/2025 (12/2026)	509.65 (484.42)	115.2	60
1659	Construction of Shohratgarh Bypass on NH-730 under EPC mode in the State of Uttar Pradesh (MoRTH) (618057) (-) (-)	Uttar Pradesh	10/2022 (11/2023)	05/2025 (12/2026)	189.31 (189.31)	0	52
1660	Widening & Strenghteningof section from Bharthana chowk to Kodarkoot km.0.00 to km.40.00 of NH-91-A on EPC mode (MoRTH) (618063) (-) (-)	Uttar Pradesh	03/2020 (03/2023)	09/2024 (09/2026)	262.37 (343.77)	115.38	94

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1661	Construction of Amethi bypass Part-II at km.30.050 of NH-931 under EPC mode in the state of Uttar Pradesh (MoRTH) (618066) (-) (-)	Uttar Pradesh	12/2022 (02/2025)	02/2027 (02/2027)	283.86 (283.86)	38.69	48
1662	Rehabilitation & Up-gradation from design Km. 0.000 to Km. 69.280 of NH-931 Pratapgarh - Amethi - Gauriganj -Musafirkhana to two lane with paved shoulder on Engineering, Procurement & Construction EpC mode in the State of Uttar Pradesh (MoRTH) (618067) (-) (-)	Uttar Pradesh	05/2023 (11/2025)	11/2027 (11/2027)	1086.3 (1086.3)	0	9
1663	Construction of two lane with paved shoulder from existing Km.0.000 to Km.55.610 design km. 0.000 to km. 54.048 of NH-124D (MoRTH) (618075) (-) (-)	Uttar Pradesh	12/2021 (02/2024)	02/2026 (09/2026)	840.93 (773.58)	204.84	75
1664	Construction of Mariahu Bypass with four lane paved shoulder configuration Km. 53.540 to Km.59.200 of NH-135A on EPC mode in the state of Uttar Pradesh (MoRTH) (618081) (-) (-)	Uttar Pradesh	03/2023 (02/2024)	02/2026 (09/2026)	438.24 (362.39)	0	55
1665	Widening & Upgradation to four lane configuration from Km.34.900 Bhadohi to km.73.134 Jaunpur of NH-135A on EPC mode (MoRTH) (618082) (-) (-)	Uttar Pradesh	03/2021 (11/2022)	05/2024 (09/2026)	395.62 (392.03)	0	94
1666	Improvement and upgradation to two lane with paved shoulder configuration from existing km 90.00 to 130.00 Design length 39.15 of NH-227A near Sikriganj to Barhalganj in the State of UP on EPC Mode. (MoRTH) (618111) (-) (-)	Uttar Pradesh	08/2021 (12/2023)	06/2025 (07/2026)	403.36 (345.34)	0	96
1667	Improvement and up-gradation of NH-227B 84 Kosi Parikrama Marg Package I, from km 228.920 Jagarnathpur to Km 235.960/0.000 MakhaudaDham to Km 29.000 Sarpur in the State of Uttar Pradesh on EPC basis (MoRTH) (618112) (-) (-)	Uttar Pradesh	03/2022 (05/2025)	11/2026 (11/2026)	912.5 (912.5)	1.9	7
1668	Improvement and up-gradation of NH-227B 84 Kosi Parikrama Marg Package III, from Km.47.800 Gosaiganj to Km.73.300 Bikapur in the State of Uttar Pradesh on EPC basis. (MoRTH) (618113) (-) (-)	Uttar Pradesh	03/2022 (05/2025)	11/2026 (11/2026)	587.97 (587.97)	61.19	43.46
1669	Improvement and up-gradation of NH-227B 84 Kosi Parikrama Marg PackageV, from Design Km.140.960 Patranga to Km.160.200 Bahuvan Madar Majha on EPC mode in the State of Uttar Pradesh (MoRTH) (618114) (-) (-)	Uttar Pradesh	03/2023 (02/2026)	08/2028 (08/2028)	1192.33 (1192.33)	0	4
1670	Improvement and Up-gradation from Km. 73.300 Bikapur to Km.140.960 Patranga of NH-227B 84 Kosi Parikrama Marg to 2LPS along with Parikrama Path (MoRTH) (618116) (-) (-)	Uttar Pradesh	11/2022 (01/2026)	01/2028 (01/2028)	1679.75 (1679.75)	142.53	40.45
1671	Rehabilitation and upgradation from km 51.600 to km 75.700 of NH-321G Nuhkhas to Etah section to two lane with paved shoulder configuration under EPC mode in the State of Uttar Pradesh (MoRTH) (618124) (-) (-)	Uttar Pradesh	01/2022 (02/2024)	08/2025 (09/2026)	343.54 (343.54)	84.43	65
1672	Improvement and up-gradation to 2LPS of NH-227B 84-Kosi Parikrama Marg PackageVI, Design Km 160200 Bahuvan Madar Majha to Km 224040 Jagarnathpur under HAM (MoRTH) (618162) (-) (-)	Uttar Pradesh	05/2023 (01/2026)	01/2028 (01/2028)	2008.7 (2008.7)	0	18
1673	Rehabilitation and Up-gradation from km. 0000 to km.40390 of NH-730S MaharajganjNichloulThuthibari to two lane with paved shoulders in the State of U.P. on Engineering, Procurement & Construction EPC Basis. (MoRTH) (618163) (-) (-)	Uttar Pradesh	03/2023 (06/2024)	12/2025 (12/2026)	809.25 (603.19)	0	59
1674	Construction of four lane highway with paved shoulder from Km.74.700 to Km.112.950 of NH-731A i/c Yamuna Bridge on HAM in the state of Uttar Pradesh. (MoRTH) (618164) (-) (-)	Uttar Pradesh	03/2022 (06/2024)	06/2026 (07/2026)	1141.67 (1157.31)	0	91
1675	Construction of 4-lane highway with paved shoulders from Km 49.155 to Km 74.700 of NH-731A on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) (618165) (-) (-)	Uttar Pradesh	01/2022 (02/2024)	01/2026 (07/2026)	1156.72 (1156.72)	0	100
1676	Construction of 4-lane green field highway from Km. 35.000 to Km. 49.155 of NH-731A with paved shoulders on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) (618166) (-) (-)	Uttar Pradesh	01/2022 (10/2023)	10/2025 (07/2026)	697.66 (697.66)	0.04	100
1677	Widening to four lane with paved shoulder from Design Km.49.200 to Km.89.285 of NH-731B on EPC mode in the state of Uttar Pradesh (MoRTH) (618168) (-) (-)	Uttar Pradesh	03/2022 (01/2024)	01/2026 (01/2027)	917.91 (965.3)	134.41	56

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1678	Construction of Two Lane with paved shoulder highway from Design Ch.0.000 to Ch.49.200 of NH-731B on EPC Mode (MoRTH) (618169) (-) (-)	Uttar Pradesh	03/2022 (11/2023)	11/2025 (07/2026)	640.18 (602.76)	265.25	97.68
1679	Rehabilitation and upgradation of Salon - Jais - Jagdishpur Road section of NH-931A, from design Chainage km 0.000 to km 5.740 to four lane divided carriageway and from design Chainage km 5.740 to km 53.500 to two lane with paved Total length km 53.500 along with One time improvement in 04 no's of realigned/bypassed built-up areas in a total length of 9.732 km in the state of Uttar Pradesh on EPC mode (MoRTH) (618187) (-) (-)	Uttar Pradesh	05/2023 (10/2025)	10/2027 (10/2027)	947.15 (947.15)	0	8
1680	Construction of 6-lane bridge on Ganga on NH-96 and its approaches in Phaphamau Allahabad on EPC mode (MoRTH) (618233) (-) (-)	Uttar Pradesh	07/2018 (02/2021)	02/2024 (09/2026)	1948.25 (1465.41)	0	90.2
1681	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Bewar-naer Karri village section Km0.00 to Km30.00 Pakage-I of NH-92 in state of Uttar Pradesh undergreen national Highway Corridor Project GNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618240) (-) (-)	Uttar Pradesh	04/2020 (09/2022)	03/2024 (07/2026)	236.47 (236.47)	0	100
1682	Construction of Basti Ring Road Phase-I with 4L configuration for Basti City in the state of Uttar Pradesh on HAM mode (MoRTH) (618243) (-) (-)	Uttar Pradesh	12/2022 (06/2025)	06/2027 (06/2027)	1138.72 (1138.72)	0.07	35
1683	Construction of Raebareli Ring Road Phase-2 with four Lane configuration for Raebareli City in the state of Uttar Pradesh on Hybrid Annuity Model HAM basis (MoRTH) (618244) (-) (-)	Uttar Pradesh	03/2022 (05/2025)	05/2027 (05/2027)	1273.72 (1273.72)	0	54
1684	Construction of 4 lane Mirzapur bypass including bridge over river Ganga from km 0.000 to km 15.000 of NH 135A in the State of Uttar Pradesh on HAM Mode. (MoRTH) (618247) (-) (-)	Uttar Pradesh	03/2024 (01/2026)	01/2029 (01/2029)	1708.62 (1708.62)	0	5.5
1685	Widening to 4 lane from km. 139.00 to km 179.20 of NH-135A Pkg-III Jaunpur Akbarpur section and Akbarpur bypass on Hybrid Annuity Mode in the state of Uttar Pradesh. (MoRTH) (618248) (-) (-)	Uttar Pradesh	05/2023 (01/2026)	01/2028 (01/2028)	1653.15 (1653.15)	0	21.06
1686	Widening to 4 lane from km. 108.50 to km 139.00 of NH-135A Pkg-II Jaunpur Akbarpur section on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) (618249) (-) (-)	Uttar Pradesh	03/2023 (03/2025)	03/2027 (03/2027)	1511.57 (1511.57)	0	36.02
1687	Improvement and Up-gradation to two Lane with Paved Shoulder/Four Lane configuration from existing Km 130.000 to Km 191.000 design km 131.500 to Km 188.735, Design length 57.235 Km of NH-227A near Barhalganj to Mehrauna Ghat in the state of Uttar Pradesh on Hybrid Annuity Model HAM basis (MoRTH) (618252) (-) (-)	Uttar Pradesh	01/2022 (11/2024)	05/2027 (05/2027)	974.19 (1344.61)	0.99	58
1688	Construction of Salempur bypass to 4LPS from km 64.000 of NH-727A Km 171.00 of Sonauli Balia Marg, old SH-01, near Mahadahan Chauraha to km 61.500 of NH-727B Km 178.500 of Sonauli Balia Marg, old SH-01, near near Ahirauli Village under Hybrid Annuity Mode HAM in the State of Uttar Pradesh (MoRTH) (618260) (-) (-)	Uttar Pradesh	03/2022 (11/2025)	11/2027 (11/2027)	1348.06 (1348.06)	0	35
1689	Construction of Deoria Bypass from existing Km. 27.140 to existing Km. 46.780 Design Km. 49.109 on NH727A Design length 21.969 Km. to four lane with paved shoulder configuration under Hybrid Annuity Mode HAM in the State of Uttar Pradesh (MoRTH) (618262) (-) (-)	Uttar Pradesh	03/2023 (08/2025)	07/2027 (07/2027)	1734.7 (1734.7)	0	10
1690	Rehabilitation and Up-gradation to 2LPS from Km. 0.000 to Km. 7.800 and Km. 35.400 to Km. 52.345 Design length 24.745 Km., except Bihar portion of NH-727B Tamkuhiraj to Bihar Border and Bihar Border to Majhauri on EPC mode in the State of Uttar Pradesh (MoRTH) (618263) (-) (-)	Uttar Pradesh	03/2023 (01/2025)	07/2026 (08/2026)	701.02 (701.02)	0	81.18
1691	Widening and Strengthening to two Lane with Paved Shoulder/Four Lane with paved shoulder configuration from km. 61.500 of NH-727B near Nawalpur km 178.500 of Sonauli Balia Marg, Old SH-01 i.e. end point of Salempur Bypass to km. 106.495 of NH-727B near Sikanderpur under EPC mode (MoRTH) (618264) (-) (-)	Uttar Pradesh	05/2023 (12/2025)	05/2028 (05/2028)	2061.86 (2061.86)	0	37
1692	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Miranpur Katra to radhaita section of NH-730CKm.114.000 to Km 137.250package-III in state of Uttar Pradesh undergreen national Highway Corridor ProjectGNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618265) (-) (-)	Uttar Pradesh	04/2020 (07/2022)	07/2024 (08/2026)	172.5 (169.56)	0	91

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1693	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Bewar-Allahaganj- section of NH-730C Km.0.000 to Km 52.770 pakage-I in state of Uttar Pradesh undergreen national Highway Corridor Project GNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618266) (-) (-)	Uttar Pradesh	04/2020 (11/2022)	11/2024 (08/2026)	325.24 (340.16)	0	99
1694	Widening/Upgradation to four lane configuration of Shahjahanpur-Bisalpur section from km 0.00 to km 47.026 of NH-731K on Hybrid Annuity Mode in the state of Uttar Pradesh. (MoRTH) (618267) (-) (-)	Uttar Pradesh	03/2023 (05/2026)	05/2028 (05/2028)	1590.2 (1590.2)	0	0
1695	6L Elevated Kanpur - Lucknow Exeressway Pkg-1 from Km. 10980 to Km. 28500 (NHAI) (618499) (-) (-)	Uttar Pradesh	12/2021 (02/2023)	07/2025 (07/2026)	1972.94 (1943.27)	770.81	100
1696	Construction of 4L Connector from Delhi Meerut Expressway Km 50.000 of Pkg IV to Km 8.520 of NH-235 Pkg-5 (NHAI) (618500) (-) (-)	Uttar Pradesh	09/2021 (03/2022)	03/2024 (07/2026)	1081.39 (1116.19)	442.98	78
1697	Varanasi Ring Road Pkg-II connecting Sandaha Village km 11.70 / NH-29 with Revasa Village km 818.80 / NH-2 (NHAI) (618529) (-) (-)	Uttar Pradesh	12/2017 (02/2019)	02/2022 (10/2026)	1991.71 (1832.66)	1750.54	96.15
1698	Construction of Ring Road around Kanpur from Ch.68.650 to Ch.93.209 Jarkala to Pakari Package-IV in State of Uttar Pradesh. (NHAI) (618536) (-) (-)	Uttar Pradesh	02/2023 (12/2024)	06/2027 (06/2027)	1603.53 (1192.16)	249.74	37.65
1699	Construction of Ring Road around Kanpur from Km.000 to Km. 23.325 Chachendi Sachendi I to Maharajpur Package-I (NHAI) (618537) (-) (-)	Uttar Pradesh	01/2023 (12/2023)	06/2026 (02/2027)	1753.75 (1311.7)	453.73	61.21
1700	Construction of Ring Road around kanpur from Ch.51.200 to Ch. 68.650 Badarka to Harbanch-Uchti Pkg-III (NHAI) (618538) (-) (-)	Uttar Pradesh	09/2023 (01/2025)	07/2027 (07/2027)	1792.68 (1126.75)	261.94	32.78
1701	Construction of Ring Road Kanpur from Ch. 32.090 to Ch.51.200 Transganaga to Sathara Package-II B (NHAI) (618539) (-) (-)	Uttar Pradesh	08/2024 (03/2025)	09/2027 (09/2027)	1089.41 (1106.92)	48.77	17.25
1702	Construction of Ring Road around Kanpur from Ch.23.325 to Ch.32.090 Chaudhariya to Transganga Package-IIA (NHAI) (618540) (-) (-)	Uttar Pradesh	08/2024 (11/2025)	10/2027 (04/2028)	1089.41 (977.45)	249.69	49.1
1703	Construction of left out portion of Agra Inner Ring Road connecting village Deori to NH-44 village Bad from Km. 0.000 to Km. 7.772 (NHAI) (618554) (-) (-)	Uttar Pradesh	07/2022 (03/2023)	09/2024 (08/2026)	879.26 (787.58)	629.11	93.8
1704	4L Green Field Northern East side Gorakhpur Bypass 26.616 Kms starting from NH-29E Chainage 83.308 and end at NH-28 Chainage 285.100 (NHAI) (618566) (-) (-)	Uttar Pradesh	02/2023 (01/2024)	01/2026 (01/2027)	1973.98 (1244.44)	1010.31	72
1705	4/6L of Northern Ayodhya Bypass starting Km. 112.540 and ending Km. 139.928 north of existing NH-27 part-1 and part-2 south of NH-27 from km 0.000 to km 5.000. (NHAI) (618567) (-) (-)	Uttar Pradesh	08/2024 (07/2025)	01/2028 (01/2028)	2289.34 (1834.25)	268.81	33.12
1706	4/6L Southern Ayodhya Bypass from Km 5.000 to Km 37.172 starting near Km. 112.540 and ending at Km. 153.281 of NH-27 (NHAI) (618568) (-) (-)	Uttar Pradesh	08/2024 (03/2025)	09/2027 (09/2027)	2541.13 (1983.05)	312.39	39.03
1707	4 -Laning of MP/UP Border to Kabarai section of NH-34&35 from km 197.000 to km 242.991 Length 45.991 Km Sagar-Kabrai Package-5 under Bharat Mala Pariyojana EC in MP & UP on HAM (NHAI) (618669) (-) (-)	Uttar Pradesh	10/2022 (02/2025)	02/2027 (01/2027)	1632.93 (1425.43)	529.81	60.02
1708	4 lanning of Aligarh Palwal section from km 0.00 to km 46.39 package -1 from khereshwar junction-kurana of NH33D , including khair & jattari bypass in the state of UP on HAM mode (NHAI) (618690) (-) (-)	Uttar Pradesh	03/2024 (03/2025)	03/2027 (03/2027)	1663.38 (1685.69)	553.34	19.5
1709	Aligarh-Kanpur Pkg I [Aligarh-Bhadwas] (NHAI) (618692) (-) (-)	Uttar Pradesh	03/2018 (02/2019)	06/2022 (08/2026)	1226.64 (2069.6)	1359.14	100
1710	DL/UP Border - EPE Crossing Pkg-02 (NHAI) (618710) (-) (-)	Uttar Pradesh	09/2020 (05/2021)	11/2023 (07/2026)	2002.79 (1889.78)	1739.68	100

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1711	6L access Controlled Greenfield Highway from Gogwan Jalalpur Shamli to Ranipur Barsi Saharanpur of Shamli -Ambala section Package-I Design Ch. Form km 00.600 to km 45.500 (NHAI) (618722) (-) (-)	Uttar Pradesh	06/2022 (05/2023)	05/2025 (03/2027)	1843.59 (1247.55)	759.25	67.4
1712	4L Spur of Meerut-Garh-Mukteshwar section connecting NH-119 and NH-58 bypassing Meerut Town of NH 709 A (NHAI) (618761) (-) (-)	Uttar Pradesh	10/2021 (02/2023)	02/2025 (07/2026)	991.89 (977.73)	861.63	96.98
1713	Four laning of Agra-Aligarh Section from Km. 0.000 Junction of NH-34 Aligarh Km 144.60 to Km. 28.000 near Asroi village in Hathras of NH-509 Package-I (NHAI) (618768) (-) (-)	Uttar Pradesh	06/2024 (03/2026)	03/2028 (11/2028)	1309.08 (1309.08)	305.43	1.99
1714	4L of Bareilly-Pilibhit-Sitarganj from Km. 0.000 to Km. 32.500 of NH-30 Pkg-1 (NHAI) (618782) (-) (-)	Uttar Pradesh	02/2023 (03/2024)	03/2026 (03/2027)	1394.14 (1394.14)	606.2	63.4
1715	4L of Sonauli - Gorakhpur (NHAI) (618798) (-) (-)	Uttar Pradesh	12/2021 (03/2023)	03/2025 (09/2026)	2555.5 (2275.43)	1326.61	89
1716	2L PS Greenfield bypass lalganj ajhara, mohanganj and Raniganj on Raebareli - Jaunpur Section Design km 0.00 to Km 53177 of NH-31 (NHAI) (618842) (-) (-)	Uttar Pradesh	12/2024 (06/2026)	06/2028 (-)	1280.68 (1280.68)	186.29	0
1717	Construction of two lane with paved shoulders bypass to Mungrabadshapur town starting from near Kodahu at Km 47/225 of NH-319D and ending near Nauwadandi at Km 219/720 of NH-31 under NHO in the state of Uttar Pradesh on EPC mode (NHAI) (618843) (-) (-)	Uttar Pradesh	02/2025 (09/2025)	03/2027 (09/2027)	197.6 (165.28)	53.53	17.22
1718	Construction of Underpass beneath airport runway on NH-31 old NH-56 for proposed expansion of runway of Babatpur Airport Varanasi (NHAI) (618848) (-) (-)	Uttar Pradesh	02/2025 (09/2025)	09/2027 (09/2027)	649.44 (649.44)	0.09	6.7
1719	Improvement and Up-Gradation of Existing Road to 4L PS from Km 123.650 to 175.080, from Start of Shahabad Bypass to End of Hardoi bypass of NH 731 Pkg-2B (NHAI) (618856) (-) (-)	Uttar Pradesh	09/2022 (11/2023)	11/2025 (03/2027)	1101.79 (1212.26)	486.98	68.8
1720	Improvement and Up-Gradation of Existing Road to 4L PS from Km 88.750 to 123.650, from Start of Shahjahanpur Bypass to start of Shahabad bypass of NH 731Pkg.-2A (NHAI) (618858) (-) (-)	Uttar Pradesh	09/2022 (01/2024)	01/2026 (03/2027)	955.34 (955.34)	348.38	70.56
1721	Improvement and Up-Gradation of Existing Road to 4L PS from Km 229.070 to 260.800, End of Hardoi District to Lucknow Ring road of NH 731 Pkg-4 (NHAI) (618859) (-) (-)	Uttar Pradesh	09/2021 (10/2022)	10/2024 (07/2026)	575.66 (553.61)	390.09	99.33
1722	Four Lane Highway from Chandan Nagar Existing Km. 59.025 of NH 530B/Design Km. 179.5000 to Bareilly BypassStartExisting Km. 59.025 of NH 530B/Design Km. 218.000 Section of NH 530B, in the State of Uttar Pradesh on HAM Mode under NHO (NHAI) (618866) (-) (-)	Uttar Pradesh	12/2024 (11/2025)	11/2027 (11/2027)	2077 (1112.44)	438.93	30.3
1723	4L Kasganj-Badaun Section from Km. 123.100 to Km. 179.500 Pkg-III of NH530B (NHAI) (618867) (-) (-)	Uttar Pradesh	03/2023 (05/2025)	05/2027 (12/2027)	2009.11 (1936.61)	549.05	37.03
1724	4L from Devinagar Bypass End Existing Km. 208.000 of NH 530B/Design Km. 66.000 to Kasganj Bypass End Existing Km.150.100 of NH 530B/ Design Km. 123.100 of NH 530B (NHAI) (618868) (-) (-)	Uttar Pradesh	03/2023 (06/2024)	06/2026 (12/2026)	2289.52 (2223.71)	1027	70.02
1725	Construction of 4/6 lane Highway of Southern Bareilly Bypass, starting at Ch. 237000 of NH 530 near Jhumka chauraha, Dhantiya village and ending at Ch. 267000 of NH 30 near Invertis University including Trumpet Interchange (NHAI) (618869) (-) (-)	Uttar Pradesh	12/2024 (12/2025)	06/2028 (06/2028)	1122.02 (1869.59)	603.36	15.48
1726	Construction of Four Lane Highway form Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package I [from Hridaipur km 0.000 to Shahapur km 42.500] on EPC Mode in the state of Uttar Pradesh. (NHAI) (618883) (-) (-)	Uttar Pradesh	10/2022 (07/2023)	07/2025 (08/2026)	1706.47 (1579.59)	1440.46	100
1727	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package II [from Shahapur km 42.500 to Pindari km 78.150] on EPC Mode in the state of Uttar Pradesh. (NHAI) (618884) (-) (-)	Uttar Pradesh	10/2022 (10/2023)	10/2025 (07/2026)	1493.65 (1311.44)	757.69	96.29

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1728	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package IV [from Buxur Spur of length km 17.270 on EPC Mode in the state of Uttar Pradesh. (NHAI) (618885) (-) (-)	Uttar Pradesh	10/2022 (06/2023)	06/2025 (07/2026)	617.88 (549.02)	282	91.1
1729	Varanasi Gorakhpur Section Packege IV from km. 149.540 to km. 215.160 Mau- Gorakhpur (NHAI) (618893) (-) (-)	Uttar Pradesh	04/2015 (04/2017)	10/2019 (08/2026)	2966.63 (3475.65)	3453.91	97.35
1730	4L Greenfield Western Side spur of Rampur-Rudrapur Section from Km 0.000 to Km 13.700 connecting NH-24 to NH-87 bypassing rampur town (NHAI) (618911) (-) (-)	Uttar Pradesh	12/2021 (05/2023)	11/2024 (02/2027)	646.27 (637.83)	369.67	63.79
1731	4L Behsuma at Km 39.250 Ex. Km 39240 To Bijnor at Km 78.810 Ex. Km 86590 Design Length 39.560 Km of NH-119 Pkg-II (NHAI) (618923) (-) (-)	Uttar Pradesh	03/2023 (05/2024)	05/2026 (12/2026)	2158.2 (2553.12)	1195.23	70.12
1732	2L PS of Najibabad Kotdwar section from 112.575 to Km. 138.635 of NH 119 (NHAI) (618924) (-) (-)	Uttar Pradesh	10/2021 (03/2024)	09/2025 (10/2026)	188.87 (99.2)	50.34	55.9
1733	Bijnor-Kotawali (NHAI) (618925) (-) (-)	Uttar Pradesh	02/2021 (11/2021)	05/2023 (07/2026)	300.58 (334.48)	296.47	99.02
1734	4L of Moradabad-Thakurdwara-Kashipur Section from Km. 0.000 to Km. 38.77 of NH-734 Pkg-II (NHAI) (618927) (-) (-)	Uttar Pradesh	10/2022 (03/2024)	03/2026 (06/2027)	2006.82 (1890.05)	969.49	52.68
1735	4L of Moradabad western side spur connecting NH-734 & NH-24 from Km. 0.000 to Km. 33.200 Pkg-I (NHAI) (618929) (-) (-)	Uttar Pradesh	11/2022 (09/2023)	09/2025 (12/2026)	1841.92 (1843.54)	1120.76	81.48
1736	4 Lane Inner Ring Road around Allahabad City Pkg-2 Prayagraj Southern Bypass 43.200 - 50.860 (NHAI) (618960) (-) (-)	Uttar Pradesh	08/2023 (12/2023)	06/2026 (06/2027)	1377.51 (1007.62)	447.26	44.64
1737	4 Lane Inner Ring Road around Allahabad City Pkg-1 Prayagraj Southern Bypass 34.400 43.200 (NHAI) (618961) (-) (-)	Uttar Pradesh	02/2025 (12/2025)	12/2027 (12/2027)	775.94 (498.97)	42.97	18.5
1738	6L access control Greenfield highway of Vill-Khyawari to Vill-Latifpur at Saharanpur Bypass from Km. 82.000 to Km. 119.790 Pkg-4 (NHAI) (618968) (-) (-)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (07/2026)	1428.19 (1439.35)	1394.44	99.24
1739	6L access control Greenfield highway of Vill-Lohadda to Vill-Karaunda Mahajan from Km. 27.000 to Km. 56.500 Pkg-2 (NHAI) (618970) (-) (-)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (07/2026)	1335.45 (1335.38)	1253.61	98.06
1740	4L of Najibabad Bypass from Km. 105.423 to Km. 118.373 excluding 2.45 Km. of NH-74 Bypass of NH-119 (NHAI) (619162) (-) (-)	Uttar Pradesh	01/2022 (12/2022)	06/2024 (07/2026)	578.02 (566.9)	440.68	100
1741	6L access controlled Greenfield highway of Junction of EPE Vill.-Mavikalan to Vill.-Lohadda from Km. 0.000 to Km. 27.000 Pkg-1 (NHAI) (619168) (-) (-)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (07/2026)	1602.48 (1497.94)	1419.77	99.29
1742	Construction of Four Lane Gola Flyover at Km 99.850 of NH 730 Major Junction with State Highways -93 of Engineering, Procurement and Construction EPC mode in the State of Uttar Pradesh. (MoRTH) (619194) (-) (-)	Uttar Pradesh	03/2025 (05/2026)	10/2027 (10/2027)	168.05 (168.05)	0	2
1743	6L access-controlled highway from Ganeshpur tonear Mohand of Ganeshpur Dehradun section from Km.0 to Km.8.3 of NH-72A Package-1 (NHAI) (619308) (-) (-)	Uttar Pradesh	11/2020 (10/2021)	10/2023 (07/2026)	836.24 (835.74)	811.84	98.92
1744	Landslide treatment work on NH 58 from Kodyala Km. 266.130 to Devprayag Km. 296.925 10 location under EPC mode in the State of Uttarakhand on EPC Mode (MoRTH) (617888) (-) (-)	Uttarakhand	01/2023 (02/2024)	02/2025 (07/2026)	192.54 (192.54)	0	99
1745	Treatment of landslide zone from location no. 01 to 28 km 62.860 to 152.750 on NH-12509 in the State of Uttarakhand under EPC mode in NHO Annual Plan 2022-23 (MoRTH) (617889) (-) (-)	Uttarakhand	11/2022 (06/2023)	06/2024 (07/2026)	192.22 (192.22)	0	98.5

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1746	Construction of Champawat Bypass with two lane with paved shoulder configuration starting from existing chainage 121.700 to existing chainage 129.450 Design Length 9.847 of NH-125 in District-Champawat in the state of Utrrakhand on EPC mode. (MoRTH) (617890) (-) (-)	Uttarakhand	02/2025 (01/2026)	12/2027 (-)	220.89 (220.89)	0	8
1747	Construction of 2 lane with paved shoulder of Kund Bypass from Design Km 35.130 to Km 47.700 existing Km 33.130 to Km 41.260 of NH-109 in the State of Uttarakhand (MoRTH) (617929) (-) (-)	Uttarakhand	02/2018 (05/2018)	05/2020 (12/2026)	247.41 (247.41)	114.6	73.5
1748	Construction of Rudraprayag tunnel of length 900.30 MTR including approaches and one major bridge on river Alaknanda connecting NH-107/old-109 to NH-07old-58 on EPC mode in the state of Uttarakhand. (MoRTH) (617967) (-) (-)	Uttarakhand	02/2021 (01/2023)	07/2025 (07/2026)	251.88 (251.88)	0	99
1749	Construction & Widening Including Augustmuni Bypass Ch-16.545 to Ch - 19.890 to 2L/PS from Km 16.545-Km 33.130 & 45.980 -57.975 Augustmuni to Kund & Guptkashi to Sitapur on NH 109 in UK (MoRTH) (617968) (-) (-)	Uttarakhand	03/2017 (02/2018)	02/2020 (03/2024)	418.89 (418.89)	0	95
1750	Rehabilitation and upgradation of 2 lane with paved shoulder from existing km. 195.175 to km. 220.000 Design Chainage km71.300 to Km. 95.947 Excluding existing chainage Km 200.300 to Km 202.400 Design chainage Km 76.400 to Km 78.400 on Dharasu to Yamunotri Road of NH- 134 Old NH-94 (MoRTH) (617974) (-) (-)	Uttarakhand	05/2025 (10/2025)	04/2028 (-)	344.73 (344.73)	0	53.74
1751	Widening to 2 Lane from Existing Chainage Km 74.700 Km 100.660 Design Chainage Km 53.365 to Km 78.785 on NH- 507 in the State of Uttarakhand. (MoRTH) (618039) (-) (-)	Uttarakhand	01/2024 (10/2025)	04/2028 (-)	346.82 (346.82)	0	31.75
1752	Rehabilitation and Upgradation to Two lanes with Paved Shoulders configuration and Strengthening from Km 175.00 to Km 196.00 Gumkhal to Satpuli of NH-119 New NH-534 in the State of Uttarakhand under NHO Annual Plan 2021-22 under EPC mode (MoRTH) (618040) (-) (-)	Uttarakhand	03/2022 (01/2025)	01/2027 (-)	452.81 (452.81)	0	42
1753	Rehabilitation and upgrading to two lanes with paved shoulders and Strengthening of Kotdwar-Pauri-Srinagar road section from Km 232.00 to 274.470 on NH-119 New 534 Paidul to Srinagar in the State of Uttarakhand on EPC Mode under NHO Annual Plan 2021-22. (MoRTH) (618041) (-) (-)	Uttarakhand	02/2022 (12/2025)	12/2027 (-)	299.31 (299.31)	0	2
1754	Rehabilitation and up-gradation to 2-lane configuration of Bageshwar to Kangarchina road from km 129.600 to Km 161.600 Existing Chainage 136.00 to Km 169.00 of NH-309Ain the State of Uttarakhand Package-IV under NHO Annual Plan 2021-22 (MoRTH) (618119) (-) (-)	Uttarakhand	03/2022 (08/2024)	02/2027 (-)	472.23 (472.23)	0	65
1755	Widening to 2-lane with Hard Shoulder configuration of Mana Ch. 0.00 to Mana Pass Ch. 50.987 road on NH-07 under Bharatmala Pariyojna in the state of Uttarakhand under Annual Plan 2022-23 length 50.987 (MoRTH) (618207) (-) (-)	Uttarakhand	10/2022 (10/2023)	10/2027 (10/2028)	573.96 (573.96)	0	21.03
1756	Construction & up gradation of existing road to 2-Lane with paved shoulder from existing chainage km 468000 to km 489350 Design Chainage km 465150 to km 471500 of NH-07 Old NH-58 including Joshimath bypass on EPC mode in the state of Uttarakhand Length 6.35 km (MoRTH) (618209) (-) (-)	Uttarakhand	03/2022 (09/2022)	09/2025 (08/2027)	258.85 (258.85)	0	37.23
1757	Rehabilitation and upgradation of Askot-Lipulekh on EPC Basis for Phase-I Existing Km 72.00 to 107.620 Design Chainage Km 21330 to Km 56935 under Project Hirak of BRO in the state of Uttarakhand under Bharatmala Pariyojna Phase-I on EPC Mode Length-35.605 Km CA No EPC/MORT&H/HRK/01/2021-22 (MoRTH) (618210) (-) (-)	Uttarakhand	09/2020 (12/2021)	12/2023 (07/2026)	603.92 (603.92)	0	81.17
1758	Improvement/construction of 2-lane with paved shoulder of Askote Llipulekh road from Tawaghat village to Budhi village design km. 56935 to km 95748 and from end of Tunnel portal to Kali Mandir design km 113828 to km. 133078 [total design length 58.063 km] under project Hirak of BRO in the state of Uttarakhand under Bharatmala Pariyojna on EPC Mode (MoRTH) (618211) (-) (-)	Uttarakhand	05/2022 (11/2024)	11/2026 (11/2026)	649.6 (649.6)	0	30.76
1759	STABILIZATION OF LAND SLIDE AND SLOPE PROTECTION AT KM 11.00 TO KM 11.08, 29,730 KM TO 30,060 KM, 30,400 KM TO 31,060 KM, 34,750 KM TO 35,300 KM, 38,950 KM TO 39,030 KM & 39,460 KM TO 39,540 KM TWO LOC CLUBBED, KM 40,400 TO KM 40,650, KM 43,500 KM 43,680, 52,460 RISHIKESH - DHARASU ROAD NH-94 ON EPC MODE IN THE STATE OF UTTARAKHAND. NOSE OF LAND SLIDE - 12 NOS (MoRTH) (618212) (-) (-)	Uttarakhand	01/2024 (10/2025)	04/2027 (-)	197.26 (197.26)	0	22

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1760	Rehabilitation and Upgradation of road Rishikesh Dharasu Old NH-94 with 2-lane with paved shoulder from km 76.000 to km 110.000 Design Chainage from km 74.733 to km 107.347 32.614 km including construction of Kamand re-alignment from existing Chainage Km 105.200 to Km 108.600 design chainage Km 103.436 to Km 105.949 - total length 2513 mtrs and land slide treatment work between design chainage Km 73.800 to Km 74.00 200m on EPC mode under improvement to NH connectivity to Chardham in (MoRTH) (618213) (-) (-)	Uttarakhand	03/2018 (01/2019)	01/2021 (07/2026)	273.76 (273.76)	0	96.46
1761	Rehabilitation and upgradation to 2 lane / 2 lane with paved shoulder configuration for design chainage km 107.347 to km 129.208 & km 133.878 to km 138.570 existing chainage km 110.000 to km 133.020 & km 137.330 to km 142.028 and land slide treatment at existing km 138.500 Design chainage km 134.970 of NH -94 on EPC mode under improvement to NH connectivity to Chardham in the state of Uttarakhand. (MoRTH) (618214) (-) (-)	Uttarakhand	03/2018 (01/2019)	07/2021 (06/2024)	346.5 (346.5)	0	100
1762	Rehabilitation & upgradation of existing road to 2-lane with hard shoulder from Joshimath km 0.00 to Saraihotra km 29.725 road on NH-107B under Bharatmala Pariyojna on EPC mode in the state of Uttarakhand (MoRTH) (618218) (-) (-)	Uttarakhand	10/2022 (05/2023)	05/2025 (03/2027)	338.38 (338.38)	0	80
1763	Upgradation to 2-lane with Hard shoulder configuration of Suraihotra Ch. 29.725 km to Malari Ch. 60.550 km road on NH- 107B under in the state of Uttarakhand. (MoRTH) (618219) (-) (-)	Uttarakhand	10/2022 (05/2024)	05/2026 (12/2026)	292.76 (292.76)	0	76.67
1764	Construction, Operation & Maintenance of 2-L Bi-directional Silkyara Bend- Barkot Tunnel with escape passage including approaches Tunnel-4.531 & Approach road- 0.328 on Dharasu-Yamunotri section b/w Chainage 25.400km and 51.00km falling along NH-134 Old NH-94 on EPC mode (NHIDCL) (618390) (-) (-)	Uttarakhand	03/2018 (07/2018)	07/2022 (03/2027)	1383.78 (1383.78)	830.46	73.5
1765	Construction for Mitigation Measures of 5 Nos. Landslides, 05 No. Sinking Zones and 01 No. Bridge from Ch. 450.00 to Ch. 468.00 18 Km. Length on NH-07 Package-III (NHIDCL) (618391) (-) (-)	Uttarakhand	12/2023 (06/2024)	12/2025 (02/2027)	250.33 (250.33)	0	87.57
1766	Construction for Mitigation Measures of 5 Nos. Landslides, 5 Nos. Sinking Zones in between Ch. 433.00 to 450.00 BANERPANI VILLAGE on NH-07 on EPC mode in the state of Uttarakhand Package-2 (NHIDCL) (618392) (-) (-)	Uttarakhand	12/2023 (12/2024)	06/2026 (01/2027)	259.64 (259.64)	0	64.23
1767	Construction for Mitigation Measures of 10 Nos. Landslides, 01 No. Sinking Zones and 1 No. of Minor Bridge in between at Ch. Km 368.00 to Km 433.00 on NH-07 on EPC Mode in Uttarakhand Package-1 (NHIDCL) (618393) (-) (-)	Uttarakhand	12/2023 (06/2024)	12/2025 (02/2024)	216.68 (216.68)	113.17	98.61
1768	4L of Haridwar Nagina section Design Ch. LME from km 13.829 to km 17.110 & km 26.077 to km 27.508 and Design Ch. RME from km 13.839 to km 17.120 & km 26.078 to km 27.509 of EUP mitigation measures on NH74 (NHAI) (618875) (-) (-)	Uttarakhand	11/2021 (08/2022)	02/2024 (12/2026)	183.92 (142.11)	115.42	70.42
1769	Construction of 4-lane connectivity to Banbasa ICP at India Nepal border from NH-09 old NH-125 Sitarganj-Tanakpur at Km 40.00 near Jagbuda bridge under Bharatmala Priyojana of NH-109D on EPC mode in the State of Uttarakhand (NHAI) (619142) (-) (-)	Uttarakhand	06/2022 (03/2023)	09/2024 (04/2027)	216.97 (237.01)	213.92	75.24
1770	Upgradation and 4L of Haridwar Bypass from Km 0.000 Km 188.100 of NH-58 to Km. 15.100 Km 5.100 of NH 74 PKg-1 (NHAI) (619155) (-) (-)	Uttarakhand	11/2021 (10/2022)	10/2024 (11/2026)	1602.89 (1423.89)	770.27	79.75
1771	4L Medinipur to Ballupur from Km. 458.65 to Km. 487.65 of NH-07Pkg-2 (NHAI) (619292) (-) (-)	Uttarakhand	03/2022 (02/2023)	02/2025 (07/2026)	1092.9 (1072.5)	736.71	93.9
1772	Construction of 4 Lane Access Controlled Bypass for Dehradun on NH307 from Design Chainage km 0050 Jhajra on NH-07 to Design Chainage km 12220 Asharori on EPC Mode in the State of Uttarakhand under NHO (NHAI) (619293) (-) (-)	Uttarakhand	12/2023 (04/2025)	04/2027 (04/2027)	715.97 (337.11)	179.03	58.09
1773	Road Safety Improvement of existing four lane section of Dehradun-Lal Tappar-Nepali Farm Section of NH-7 and Nepali Farm-Motichur NH-34 on EPC Mode in Uttarakhand under NHO. (NHAI) (619294) (-) (-)	Uttarakhand	05/2025 (02/2026)	08/2028 (08/2028)	720.67 (388.19)	2.7	5.02
1774	Four/Six laning of Bhaniyawala-Jollygrant-Rishikesh spur section of NH-07 from Km. 0.000 to Km 19.780 (NHAI) (619295) (-) (-)	Uttarakhand	02/2023 (12/2025)	11/2027 (11/2027)	742.43 (664.92)	12.47	0

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1775	Construction of additional major Bridge with 4- lane configuration of length 1.48 km on NH-60 NH-14 over River Kangshabati from Km. 117.770 to Km 119.250 and additional major Bridge with 4- lane configuration of length 0.900 km on NH-60 NH-14 over River Shilabati from Km. 173.220 to Km 174.120 in the district of Paschim Medinipur of West Bengal under Annual Plan for FY 2023-24 on EPC mode. Job No 014-W8-2023-24/527 . (MoRTH) (617893) (-) (-)	West Bengal	11/2023 (11/2025)	05/2028 (05/2028)	304.83 (304.83)	0.04	0
1776	Construction or 4 lane Raniganj Bypass of length 5.261 km on NH-60 new NH-14 from km 273.00 of NH to km 478.18 of NH-2 New NH 16 in paschim Bardhaman, West Bengal in EPC Mode- reg. Job No. 014-WB-2022-23/514 (MoRTH) (617894) (-) (-)	West Bengal	03/2023 (03/2024)	03/2026 (05/2027)	410.83 (410.83)	174.31	67.28
1777	Construction of ROB and its approaches in lieu of LC No. 10/B/T at Km 307.050 of NH-60. (MoRTH) (617931) (-) (-)	West Bengal	03/2016 (08/2023)	08/2025 (03/2027)	155.87 (138.57)	0	16.84
1778	Construction of new road at the missing link portion of NH-81 along approved alignment between Harishchandrapur and Eastern approach of Kalindri Bridge from Km 46.550 to Km 59.697 in the district of Malda. Job No-081-WB-2015-16/400 (MoRTH) (617960) (-) (-)	West Bengal	08/2016 (11/2016)	11/2018 (10/2026)	271.17 (291.2)	216.61	85.08
1779	Development to 4/6-lanning of NH-31 New NH-10 with both side service roads from km 569.258 to km 581.030 end of AH-02 project on NH- 31 near Shivmandir to Sevoke Army Cantonment in districts of Darjeeling and Jalpaiguri in the state of West Bengal on EPC Mode Job No. 010/WB/2021-22/490 (MoRTH) (618227) (-) (-)	West Bengal	03/2022 (03/2023)	09/2025 (03/2027)	995.04 (1059.2)	578.55	73.5
1780	Construction & upgradation of existing road to 2-lane with paved shoulder including geometric improvement of Kafer- Lava More section from km 40.00 to km 61.100 of NH717-A on EPC under SARDP-NE A in state of West Bengal Pkg-VA (NHIDCL) (618427) (-) (-)	West Bengal	06/2020 (10/2020)	04/2023 (07/2026)	311.02 (273.78)	6.12	95.98
1781	Construction & upgradation of existing road to 2-lane with paved shoulder including geometric improvement of sect. from Pedong bypass to Reshi Border km 79.700 to km 96.254 of NH-717A under SARDP-NE-A on EPC as part of Alternate connectivity to Gangtok Lava More-Reshi Border Pkg-VB (NHIDCL) (618429) (-) (-)	West Bengal	06/2020 (10/2020)	04/2022 (08/2026)	345.38 (395.59)	418.73	97.2
1782	Construction of alternative highway to Gangtok in Sikkim via Bagrakot -Chuikhim-Nimbong -Kafer-Bakhim-Algarah-Rhenock in the State of West Bengal and from Rhenok-Rorathang-Pakyong along with spur from Aritar-Rolep-Menla in the State of Sikkim from Km 0.00 to Km 13.00 of Bagrakot -Kafer section of NH 717A on EPC Mode under Phase-A of SARDP-NE in the State of West Bengal PKG- IVA (NHIDCL) (618430) (-) (-)	West Bengal	03/2018 (10/2019)	04/2022 (08/2026)	402.94 (402.94)	0.39	99.23
1783	Construction of alternative highway to Gangtok in Sikkim via Bagrakot -Chuikhim-Nimbong -Kafer-Bakhim-Algarah-Rhenock in the State of West Bengal and from Rhenok-Rorathang-Pakyong along with spur from Aritar-Rolep-Menla in the State of Sikkim from Km 13.00 to Km 25.60 of Bagrakot -Kafer section of NH 717A on EPC Mode under Phase-A of SARDP-NE in the State of West Bengal PKG- IVB (NHIDCL) (618431) (-) (-)	West Bengal	03/2018 (10/2020)	04/2023 (07/2026)	295.97 (295.97)	0	97.73
1784	Binnaguri Bypass-Descoped portion of Ghoshpukur-Dhupguri Section of NH-31Dpkg-1 (NHAI) (618572) (-) (-)	West Bengal	03/2025 (11/2025)	11/2027 (11/2027)	309.99 (306.02)	2.17	2.58
1785	Balance Works of 4L of NH-31D from Km. 113.200 to Km. 154.854 Package-II A Ghoshpukur-Salsalabari Section (NHAI) (618574) (-) (-)	West Bengal	11/2023 (12/2024)	06/2027 (06/2027)	1818.46 (962.31)	457.52	58.15
1786	6L Elevated Kona Expressway from Km. 0.145 to Km. 7.337 of NH-117 (NHAI) (618808) (-) (-)	West Bengal	03/2023 (06/2024)	12/2026 (12/2027)	1212.56 (1203.11)	428.26	39.98
1787	4 laning of Barasat - Barajaguli Section of NH-12 from Km. 31.000 to Km. 48.679 in the district of North 24 - Parganas (NHAI) (618823) (-) (-)	West Bengal	02/2024 (08/2024)	02/2026 (10/2027)	352.01 (346.39)	87.41	41.67
1788	Development to 4-laning of the de-scoped stretches from Km 115.342 to Km 191.700 of NH-34 in Nadia District 3.962 & Murshidabad District 5.538 pertaining to Krishnagar to Berhampore section of NH-34 New NH-12 , in the state of West Bengal under NHO. (NHAI) (618824) (-) (-)	West Bengal	03/2024 (07/2024)	01/2026 (06/2027)	201.1 (197.74)	56.97	54.02
1789	Bridge over Ganga River at d/s of Farraka Barrage including Approaches connecting Farakka-Raiganj (NHAI) (618825) (-) (-)	West Bengal	08/2018 (12/2018)	12/2021 (09/2026)	622.04 (646.1)	623.69	96.71
1790	4L of Purulia Bypass section from Km 84.030 to Km 94.345 of NH-32 (NHAI) (618910) (-) (-)	West Bengal	01/2021 (02/2022)	08/2023 (09/2026)	557.55 (562.57)	488.7	94.12

All Ongoing Projects

JUNE 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1791	Construction of Dubrajpur Bypass with 4-lane configuration of length 5.676 km on NH-60 new NH-14 from design chainage 0.00 existing km 316.135 on NH-60 to design chainage 5.676 existing km 320.980 on NH-60 in the district of Birbhum, West Bengal under Annual Plan 2022-23 in EPC Mode- reg. Job. No. 014-WB-2022-23/518 (MoRTH) (619004) (-) (-)	West Bengal	03/2023 (12/2025)	12/2027 (12/2027)	560.79 (560.79)	0.03	5.5
1792	Slope protection and landslide mitigation at 4 vulnerable locations km 1.950 to Km 2.100, km 11.100 to 11.450, km 22.435 to km 22.485 and km 22.610 to km 22.680 within Sevoke-Rangpo section of NH-10 old NH-31A in Darjeeling & Kalimpong district in the State of West Bengal on EPC mode (NHIDCL) (619187) (-) (-)	West Bengal	02/2024 (06/2025)	06/2027 (06/2027)	152.27 (152.27)	0	32.21
	Total (1022)				969676.90000000 1	448972.5	
	Department of Telecommunications						
	Telecommunication						
1793	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance [Erstwhile NICF]) (709859) (-) (-)	Delhi	10/2014 (04/2018)	02/2020 (06/2026)	248.2 (248.2)	237.43	98
1794	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598) (-) (-)	Meghalaya	09/2019 (09/2020)	03/2022 (06/2026)	971.96 (180.46)	167.23	99.84
1795	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase 1 Upgradation (Department of Telecommunications [DoT]) (617413) (-) (-)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	04/2022 (05/2024)	05/2025 (12/2026)	1884.6 (1884.6)	376.8	98.28
1796	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 (Department of Telecommunications [DoT]) (701599) (-) (-)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	05/2018 (09/2021)	03/2023 (11/2026)	1577.57 (604.6)	480.91	88
1797	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha (Department of Telecommunications [DoT]) (701602) (-) (-)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	11/2021 (05/2022)	11/2023 (01/2027)	3685 (1448.61)	1100.41	81.2
1798	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (09/2026)	1255.49 (276.62)	237.98	99.6
1799	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajastha and Uttar Pradesh (Department of Telecommunications [DoT]) (704495) (-) (-)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	12/2019 (03/2021)	03/2022 (06/2026)	421.65 (228.94)	152.96	99
1800	Amended BharatNet Program - KTK, GOA, PY (Department of Telecommunications) (108841) (-) (-)	PAN India	08/2023 (06/2025)	06/2028 (-)	3742 (3742)	435.31	0
1801	Saturation 4G mobile coverage of Uncovered Villages through USOF (Department of Telecommunications [DoT]) (400013) (-) (-)	PAN India	07/2022 (07/2022)	06/2024 (03/2027)	26316 (15392.8)	8553.1	85
1802	4G Services by BSNL (Department of Telecommunications [DoT]) (701593) (-) (-)	PAN India	11/2020 (11/2020)	03/2024 (03/2026)	28466 (19592)	9142.63	98.4
1803	BharatNet (Department of Telecommunications [DoT]) (706775) (-) (-)	PAN India	07/2017 (10/2011)	08/2023 (03/2027)	61109 (188000)	48809.69	99.98
1804	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (709856) (-) (-)	PAN India	05/2023 (05/2023)	08/2024 (06/2026)	645.13 (645.13)	407.15	92.1
1805	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. (BSNL) (709857) (-) (-)	PAN India	05/2023 (06/2023)	06/2025 (09/2026)	24544.55 (24544.5)	9143.48	98.41

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1806	Amended BharatNet Program - UP (East) (Department of Telecommunications) (222253) (-) (-)	Uttar Pradesh	08/2023 (02/2025)	02/2028 (-)	5008 (5008)	502	0
1807	Amended BharatNet Program - UP (West) (Department of Telecommunications) (708687) (-) (-)	Uttar Pradesh	08/2023 (02/2025)	02/2028 (-)	1917 (1917)	183.16	0
	Total (15)				161792.15	79930.24	
	Department of Water Resources, River Development & GR						
	Waste & Water						
1808	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616600) (-) (-)	Bihar	10/2017 (03/2022)	02/2025 (12/2026)	413.29 (413.29)	126.67	97
1809	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616611) (-) (-)	Bihar	08/2017 (07/2019)	12/2025 (09/2026)	824 (824)	403.34	59
1810	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh Patna under Hybrid annuity based PPP mode Namami Gange Programme (NMCG1) (616612) (-) (-)	Bihar	08/2017 (07/2019)	12/2025 (-)	578.89 (578.89)	171.79	55
1811	Sewer Network, SPS and STP at Begusarai (National Mission for Clean Ganga) (616615) (-) (-)	Bihar	03/2010 (03/2018)	04/2025 (12/2026)	230.06 (230.06)	261.82	97
1812	Sewer Networks, SPS and STP at Hajipur (National Mission for Clean Ganga) (616616) (-) (-)	Bihar	03/2010 (03/2018)	06/2025 (12/2026)	305.19 (305.19)	346.46	95
1813	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme (National Mission for Clean Ganga) (616594) (-) (-)	Uttar Pradesh	05/2020 (04/2023)	04/2025 (12/2026)	842.25 (842.25)	208.64	84
1814	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP (National Mission for Clean Ganga) (616605) (-) (-)	Uttar Pradesh	05/2020 (11/2024)	12/2024 (03/2027)	690.71 (690.71)	34.79	56
1815	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP (National Mission for Clean Ganga) (616604) (-) (-)	West Bengal	05/2018 (12/2021)	03/2025 (08/2026)	154.73 (154.73)	102.04	94
	Total (8)				4039.12	1655.55	
	Water Resources						
1816	Sardar Gouthu Latchanna Thotapalli Barrage Project (Water Resources-AP) (400100) (-) (-)	Andhra Pradesh	04/2005 (01/2006)	12/2019 (06/2026)	353.05 (1023.24)	879.15	95.88
1817	Gundlakamma project (Water Resources-AP) (400101) (-) (-)	Andhra Pradesh	04/2005 (04/2005)	12/2019 (03/2027)	397.41 (697.39)	624.78	98.3
1818	Polavaram Irrigation Project (Water Resources-AP) (701415) (-) (-)	Andhra Pradesh	01/2009 (11/2009)	04/2022 (03/2026)	10151.04 (55548.9)	27726.15	86.14
1819	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370) (-) (-)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 (256.16)	44.7	55.44
1820	Kelo Irrigation Project (Water Resources-CT) (400111) (-) (-)	Chhattisgarh	04/2008 (04/2008)	12/2019 (06/2026)	459.97 (727.04)	620.15	73
1821	Kudali Irrigation Project (Department of Water Resources, River Development & GR) (701399) (-) (-)	Chhattisgarh	04/2009 (12/2009)	12/2025 (03/2026)	382.29 (382.29)	249.06	86.31
1822	Sardar Sarovar Project (Narmada and Water Resources, Water Supply and Kalpsar Department-GJ) (701372) (-) (-)	Gujarat	04/1996 (04/1996)	12/2019 (03/2026)	20718.17 (33412.5)	31943.15	93.7
1823	Subernarekha Multipurpose Project, Jharkhand (Department of Water Resources-JH) (701376) (-) (-)	Jharkhand	04/2011 (01/2012)	12/2019 (03/2026)	3807.77 (9579.58)	6040.27	70
1824	Upper Tunga Irrigation Project (Water Resources-KA) (701377) (-) (-)	Karnataka	04/2014 (04/2014)	12/2019 (03/2026)	770.16 (1606.07)	1515.6	99.32
1825	Bargi Diversion Project Phase - IV [km. 154 to km 197] (Water Resources-MP) (400115) (-) (-)	Madhya Pradesh	04/2008 (01/2009)	12/2019 (03/2026)	751.03 (893.35)	814.02	75

All Ongoing Projects

JUNE 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1826	Bargi Diversion Project Phase - III [km. 104 to km 154] <i>(Water Resources-MP)</i> (400116) (-) (-)	Madhya Pradesh	04/2007 (04/2007)	12/2019 (12/2026)	1229.15 (1399.7)	2240.05	81.52
1827	Bodwad Parisar Sinchan Yojna <i>(Department of Water Resources-MH)</i> (617422) (-) (-)	Maharashtra	05/2002 (01/2017)	07/2027 (-)	1923.81 (1923.81)	1949.56	49.52
1828	Waghur Project <i>(Department of water resources-MH - II)</i> (701383) (-) (-)	Maharashtra	04/1996 (04/1996)	12/2019 (03/2026)	1058.99 (1758.51)	1634.36	89.57
1829	Gosikhurd Project <i>(Department of water resources-MH - II)</i> (701386) (-) (-)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2028)	7196.47 (12770.1)	14385.73	72.65
1830	Aruna Medium Irrigation Project <i>(Department of water resources-MH - II)</i> (701391) (-) (-)	Maharashtra	04/2009 (01/2010)	12/2019 (12/2025)	210.45 (1472.14)	1734.71	100
1831	Lower Pedhi Project <i>(Department of water resources-MH - II)</i> (701396) (-) (-)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2026)	255.97 (1480.7)	3066.05	65
1832	Nardave Medium Irrigation Project <i>(Department of water resources-MH - II)</i> (701398) (-) (-)	Maharashtra	04/2009 (04/2009)	12/2019 (06/2026)	211.46 (781.85)	879.16	74
1833	Thoubal Multipurpose Project <i>(Water Resources Department-MN)</i> (701400) (-) (-)	Manipur	04/1997 (04/1997)	12/2019 (12/2026)	1449.44 (1822.24)	1848.17	99
1834	North Koel Reservoir Project <i>(Department of Water Resources, River Development & GR)</i> (701412) (-) (-)	Multi-States (Bihar, Jharkhand)	08/2017 (01/2021)	03/2021 (03/2026)	1622.27 (2430.76)	172.97	44
1835	Ken-Betwa Linking Development Project <i>(Department of Water Resources, River Development,)</i> (701530) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	NA (03/2022)	03/2029 (-)	21030 (21030)	8530.86	0
1836	Integrated Anandpur Barrage Project <i>(Water Resources-OR)</i> (603945) (-) (-)	Odisha	04/1997 (01/1998)	12/2019 (06/2026)	567.03 (2990.05)	2776.23	62.85
1837	Subernarekha Project, Odisha <i>(Department of Water Resources, River Development & GR)</i> (701402) (-) (-)	Odisha	12/1995 (01/1998)	12/2019 (03/2026)	3055.88 (7023.19)	8289.65	95.5
1838	Kanupur Irrigation Project <i>(Irrigation and CAD-TG)</i> (701404) (-) (-)	Odisha	04/2003 (01/2004)	12/2019 (06/2026)	989.43 (2301.28)	2804.16	79.5
1839	Relining of Rajasthan feeder and Sirhind Feeder canal <i>(Department of Water Resources-PB)</i> (701410) (-) (-)	Punjab	02/2016 (04/2018)	06/2021 (06/2026)	1441.26 (2462.16)	2342.05	95
1840	Shahpur Kandi Dam Project <i>(Department of Water Resources-PB)</i> (701411) (-) (-)	Punjab	02/2010 (04/2018)	06/2022 (06/2026)	2285.81 (2715.7)	2201.94	88
1841	Sri Ram Sagar Project Stage - II <i>(Irrigation and CAD-TG)</i> (400102) (-) (-)	Telangana	04/1996 (04/2005)	12/2019 (12/2025)	736.13 (949.87)	971.47	97
1842	Indiramma Flood Flow Canal Project <i>(Irrigation and CAD-TG)</i> (400103) (-) (-)	Telangana	04/1996 (01/2006)	12/2019 (12/2026)	1331.3 (5940.09)	4491.08	92
1843	J. Chokka Rao Devadula Lift Irrigation Scheme <i>(Irrigation and CAD-TG)</i> (701405) (-) (-)	Telangana	04/2006 (04/2006)	12/2019 (12/2025)	8200.71 (14730)	4841.09	87.7
1844	Rajiv Bhima Lift Irrigation Scheme <i>(Irrigation and CAD-TG)</i> (701406) (-) (-)	Telangana	04/2007 (01/2008)	12/2019 (03/2026)	1402 (2509.66)	1839.76	100
1845	Morna [Gureghar] Irrigation Project <i>(Department of Water Resources, River Development & GR)</i> (701395) (-) (-)	Uttar Pradesh	04/2007 (12/2007)	12/2025 (-)	219.9 (219.9)	115.2	31.5
1846	Madhya Ganga canal Phase-II <i>(Irrigation & Water Resources-UP)</i> (701408) (-) (-)	Uttar Pradesh	04/2008 (04/2008)	12/2019 (12/2025)	1060.67 (4417.21)	4575.74	82.39
1847	Jamrani Dam Multipurpose Project <i>(Irrigation-UK)</i> (613787) (-) (-)	Uttarakhand	10/2023 (11/2023)	06/2029 (-)	2584.1 (2584.1)	1307.15	26.22
	Total (32)				98109.28	143454.17	



- Note:
- The projects with IDs 617933, 617917, 617944, 617957, 617981, 617993, 617977, 617982, 618006, 618007, 618046, 618062, 618090, 618136, 618144, 618181, 618167, 618192, 618208, 618220, 618229, 618342, 618343, and 618432 have not been published in the current month's Flash Report due to inconsistencies in the Cumulative Expenditure data and will be published once the data is rectified.



सत्यमेव जयते

Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <https://paimana-proj.mospi.gov.in/>
